


APPENDIX B
TRANSECT SHEETS

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/14/2008	Completion Date:	8/14/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

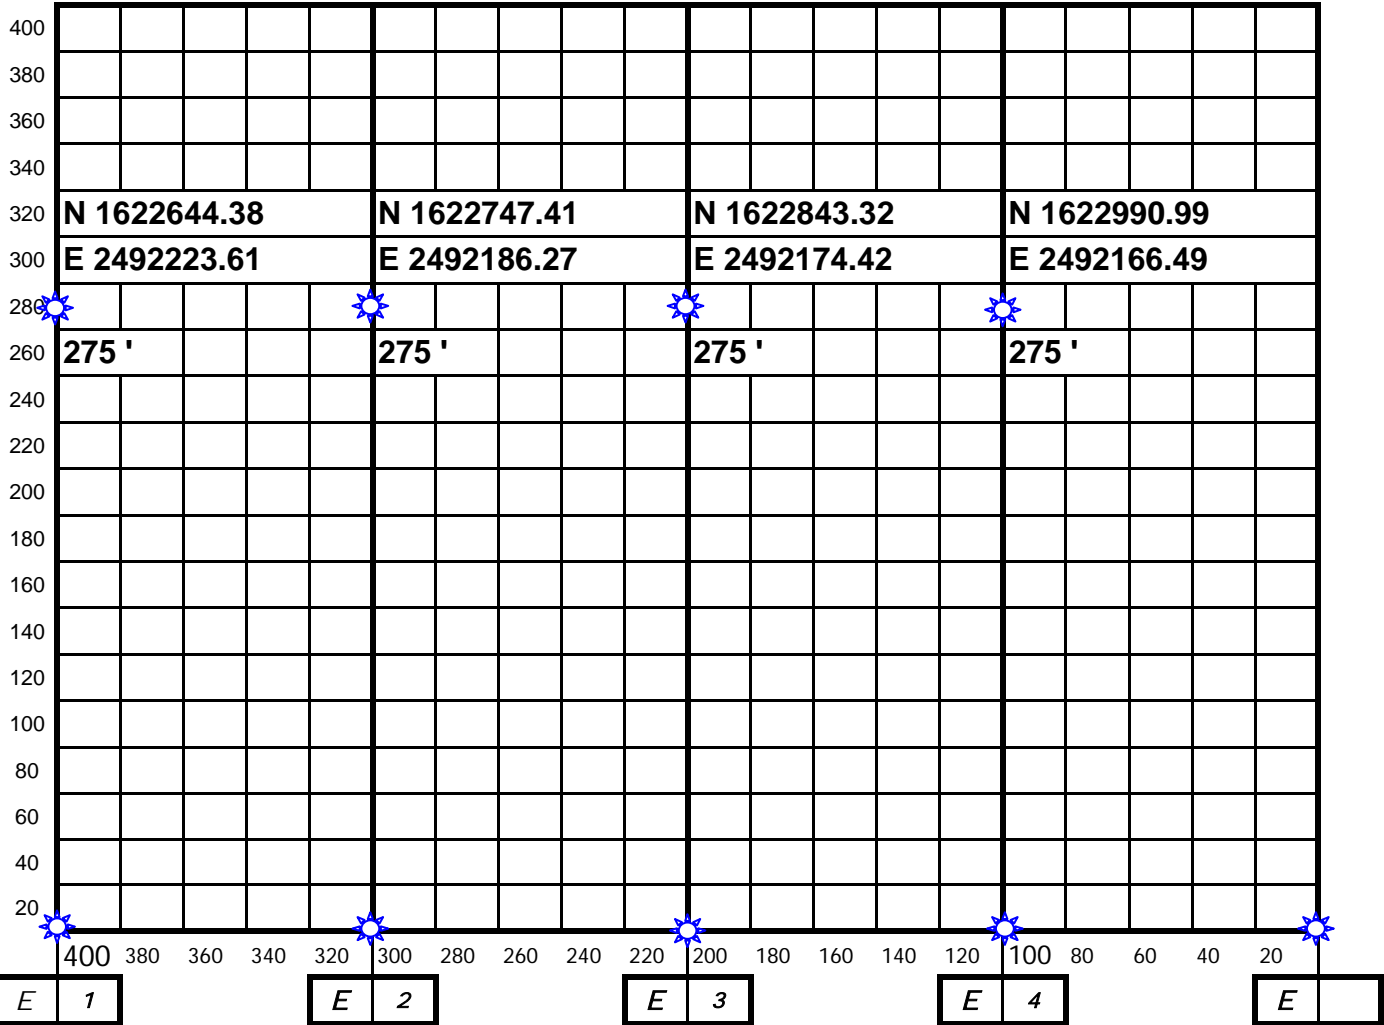


Start	Start	Start	Start	Start
8/14	8/14	8/14	8/14	
Finish	Finish	Finish	Finish	Finish
8/14	8/14	8/14	8/14	
MEC	MD	STAKE #		

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/14/2008	Completion Date:	8/14/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

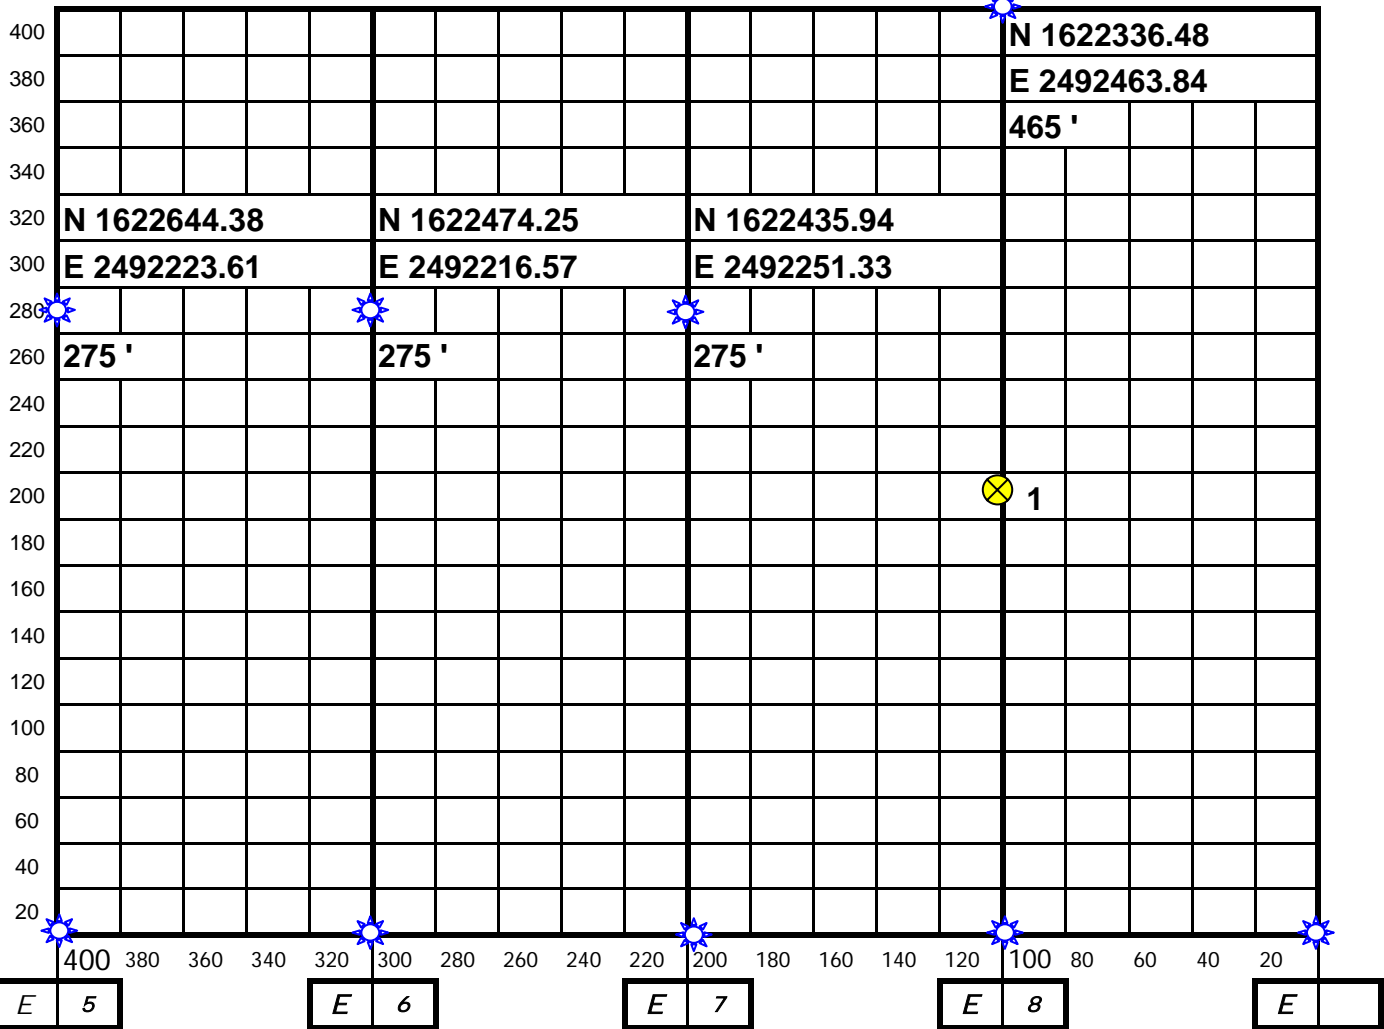

Start	Start	Start	Start	Start
8/14	8/14	8/14	8/14	
Finish	Finish	Finish	Finish	Finish
8/14	8/14	8/14	8/14	

MEC

MD

STAKE #


Comments/Notes:

Anomalies

#	ID	Northing	Easting	Comments
1	E 8A	1622365.25	2492191.7	MD Frag
2				
3				
4				
5				
6				
7				
8				
9				
10				
11				
12				
13				
14				
15				
16				
17				
18				
19				
20				
21				
22				
23				
24				
25				
26				
27				
28				
29				
30				
31				
32				
33				
34				
35				
36				
37				
38				
39				
40				
41				
42				
43				
44				

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/14/2008	Completion Date:	8/26/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

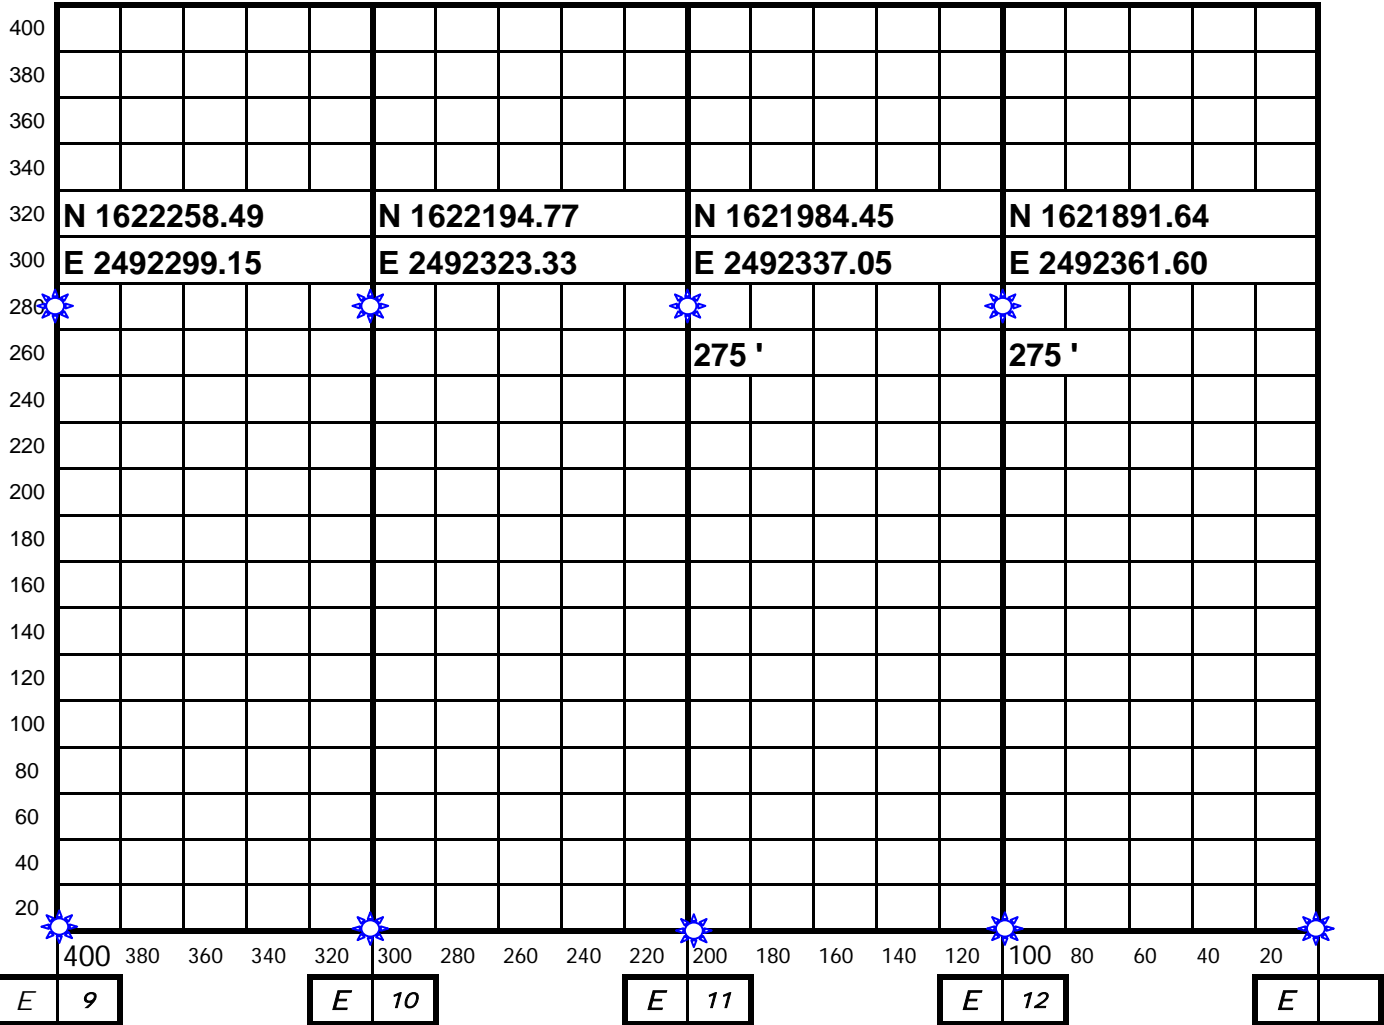


Start	Start	Start	Start	Start	
8/14	8/14	8/26	8/26		
Finish	Finish	Finish	Finish	Finish	
8/14	8/14	8/26	8/26		
	MEC		MD		STAKE #

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/26/2008	Completion Date:	9/9/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

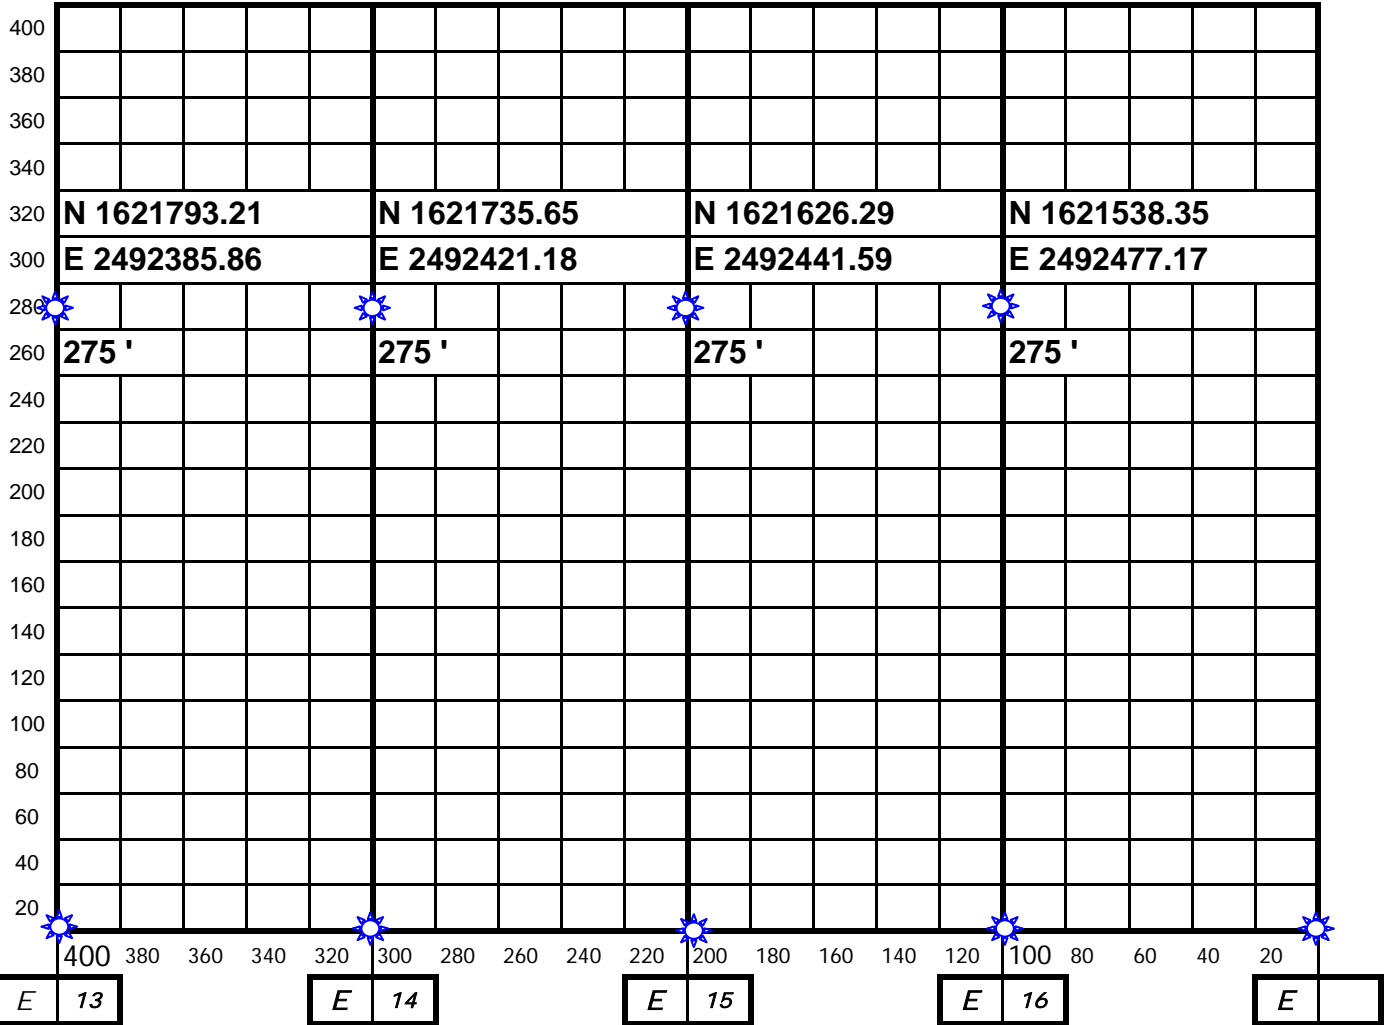


Start	Start	Start	Start	Start	
9/9	9/5	9/5	9/5		
Finish	Finish	Finish	Finish	Finish	
9/9	9/5	9/5	9/5		
	MEC		MD		STAKE #

Comments.Notes:

E-14 & E-17 possible EM-61 accessible

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	9/5/2008	Completion Date:	9/5/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

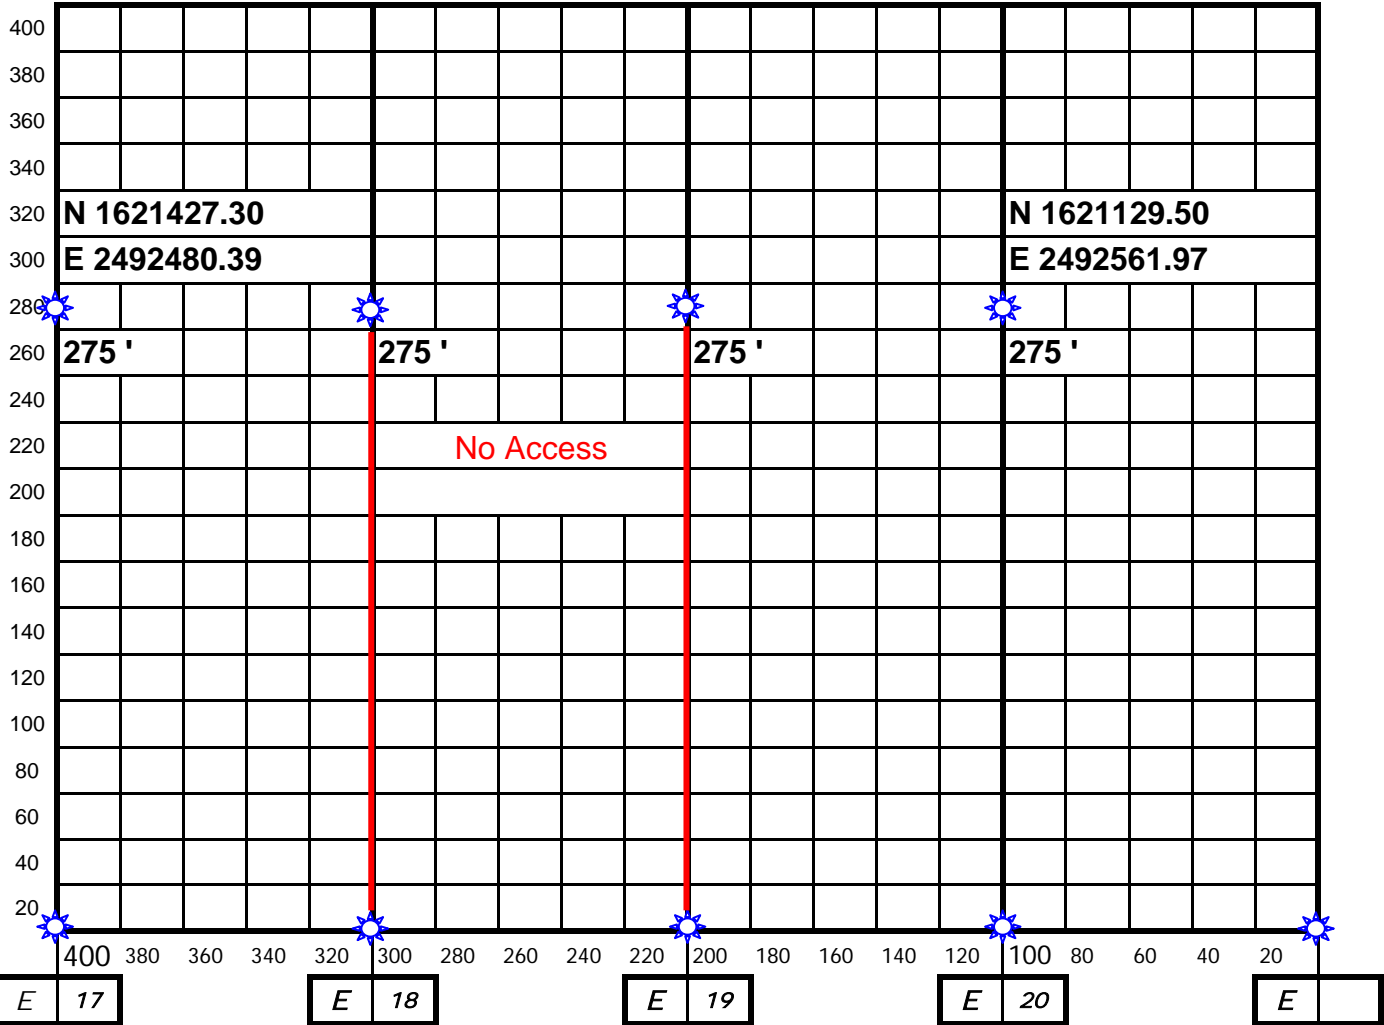

Start	Start	Start	Start	Start
<input type="text" value="9/5"/>	<input type="text" value="9/5"/>	<input type="text" value="9/5"/>	<input type="text" value="9/5"/>	<input type="text"/>
Finish	Finish	Finish	Finish	Finish
<input type="text" value="9/5"/>	<input type="text" value="9/5"/>	<input type="text" value="9/5"/>	<input type="text" value="9/5"/>	<input type="text"/>
MEC	MD	STAKE #		


Comments.Notes:

E-17: Possible EM-61 accessible

E-18 & E-19: Archeological sites, tribes asked us to avoid these areas

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	9/5/2008	Completion Date:	9/5/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

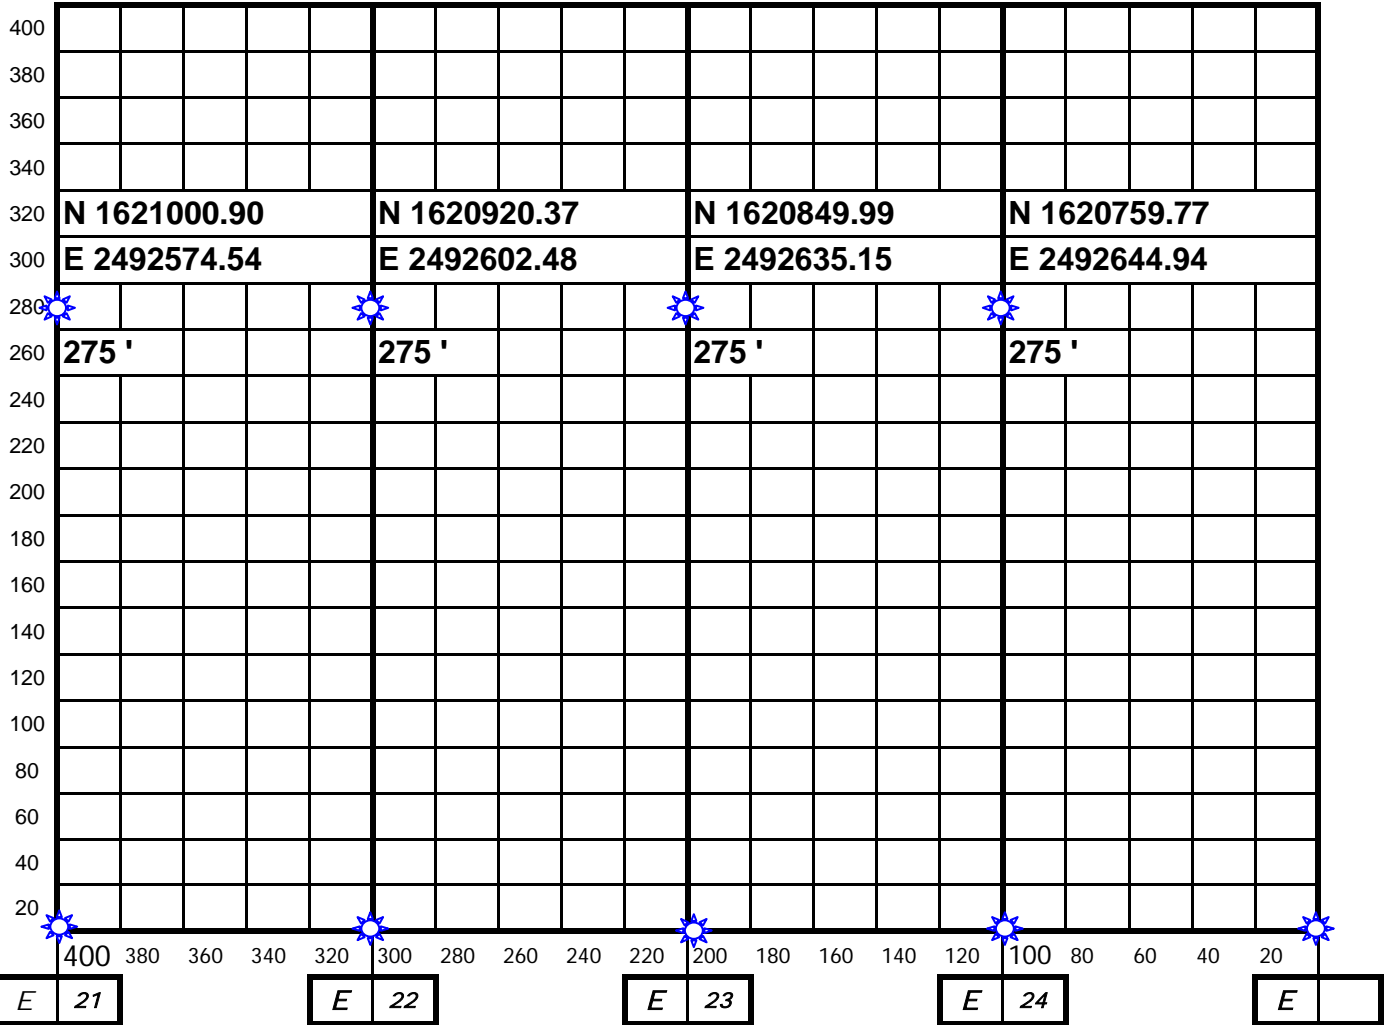


Start	Start	Start	Start	Start	
9/5	9/5	9/5	9/5		
Finish	Finish	Finish	Finish	Finish	
9/5	9/5	9/5	9/5		
	MEC		MD		STAKE #

Comments.Notes:

E-24: Offset 15' West because of arroyo

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	9/5/2008	Completion Date:	9/9/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

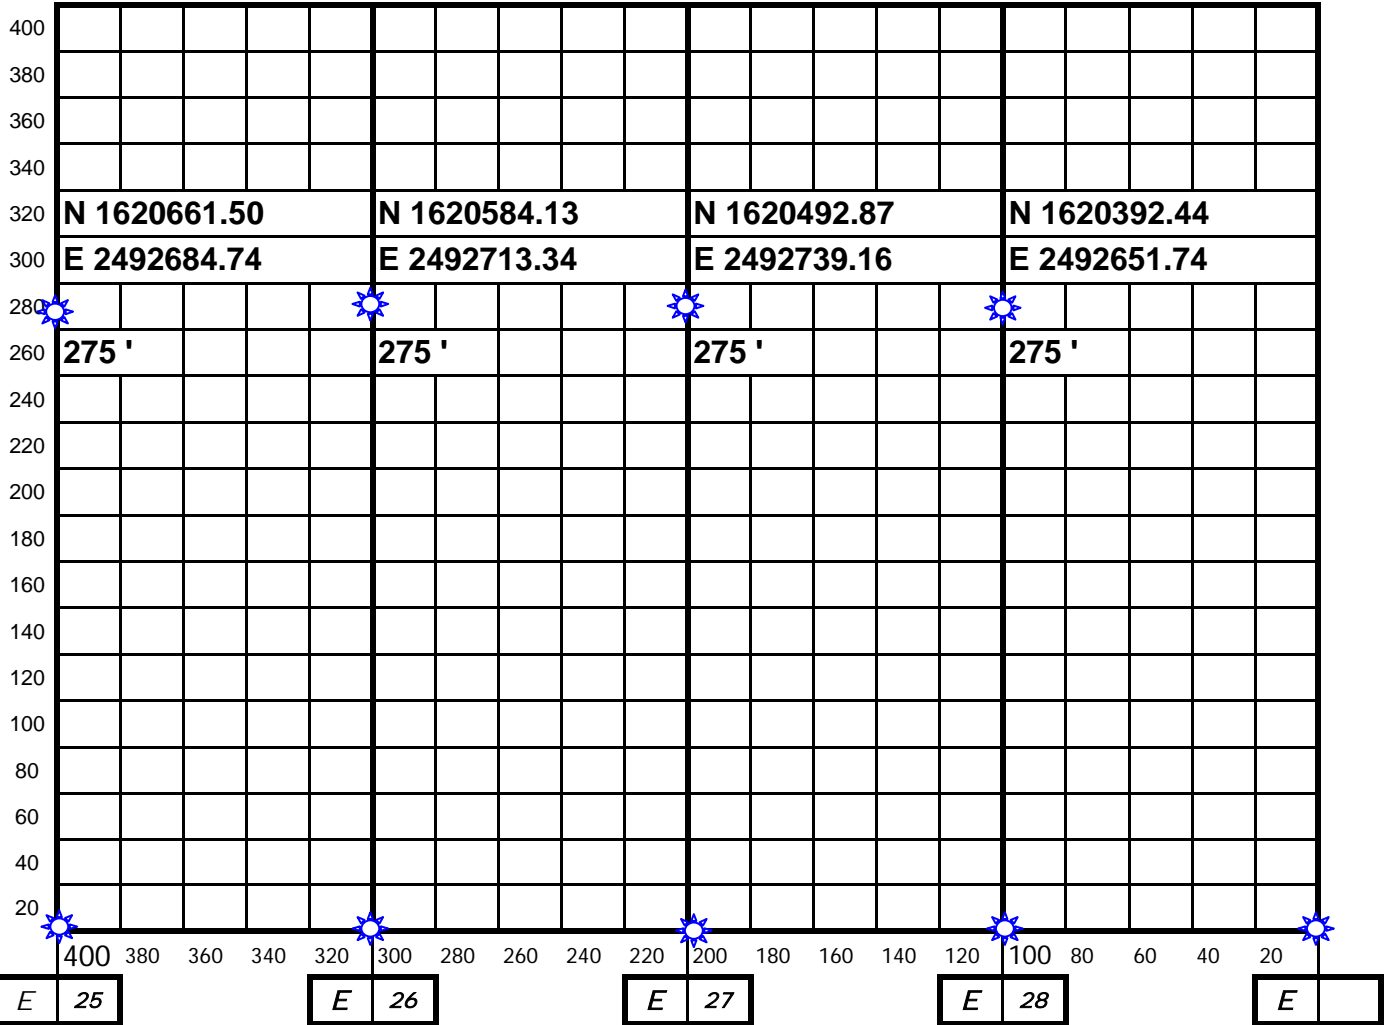


Start	Start	Start	Start	Start	
9/5	9/9	9/9	9/9		
Finish	Finish	Finish	Finish	Finish	
9/5	9/9	9/9	9/9		
	MEC		MD		STAKE #

Comments.Notes:

E-28: Offset 100' west of arroyo

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/25/2008	Completion Date:	8/25/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

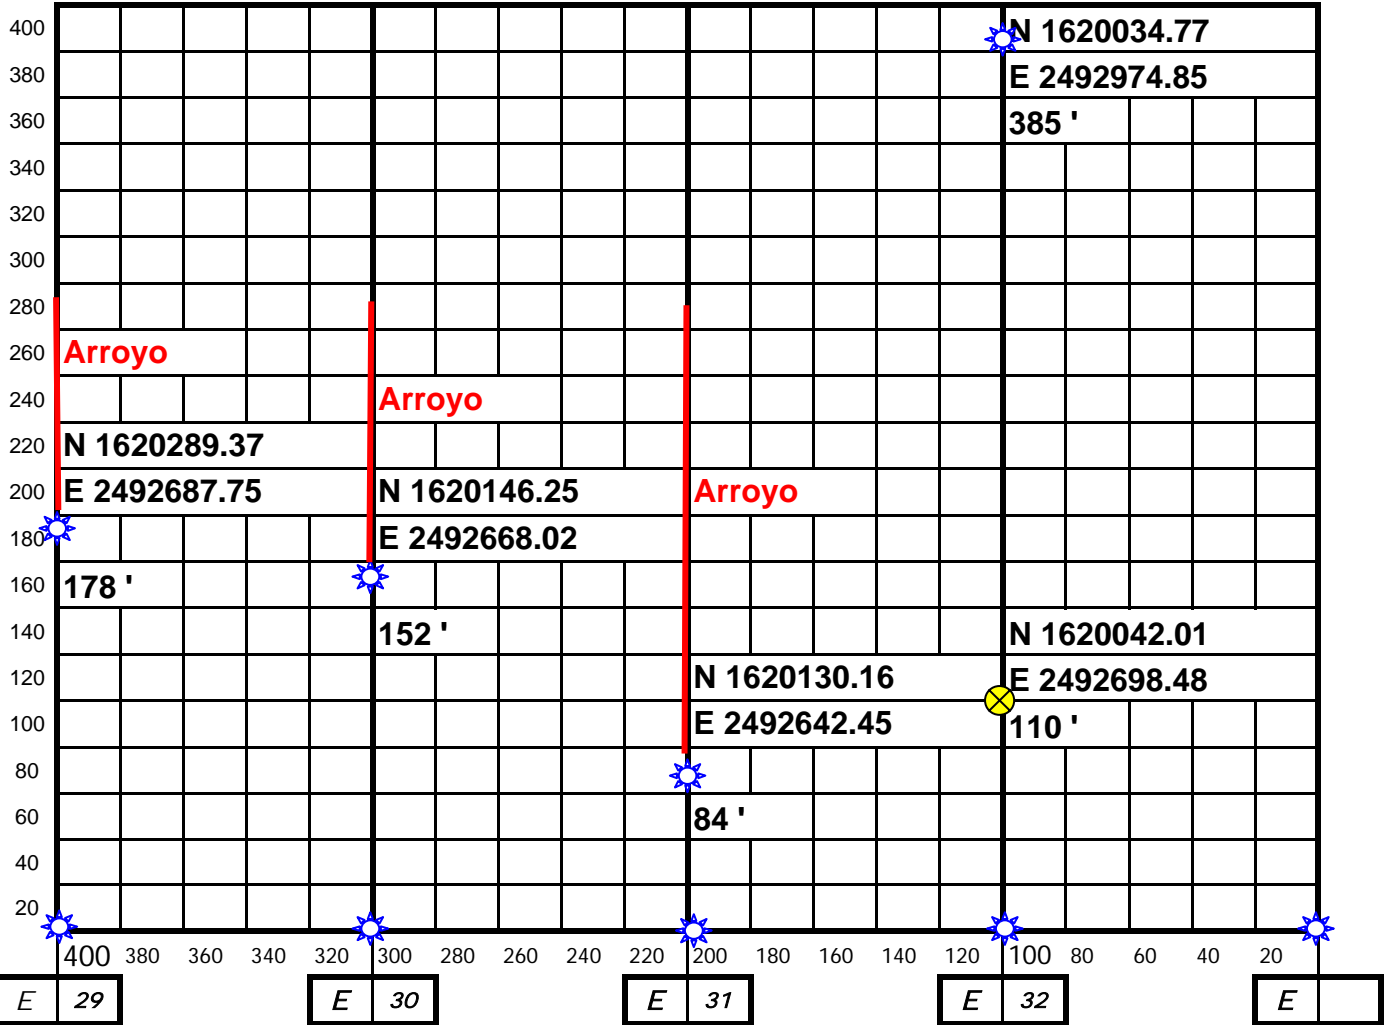

Start	Start	Start	Start	Start	
8/25	8/25	8/25	8/25	8/25	
Finish	Finish	Finish	Finish	Finish	
8/25	8/25	8/25	8/25	8/25	
	MEC		MD		STAKE #


Comments. Notes:

E-29: Offset 97' to West

E-30: Offset 103' to West

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/25/2008	Completion Date:	8/25/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

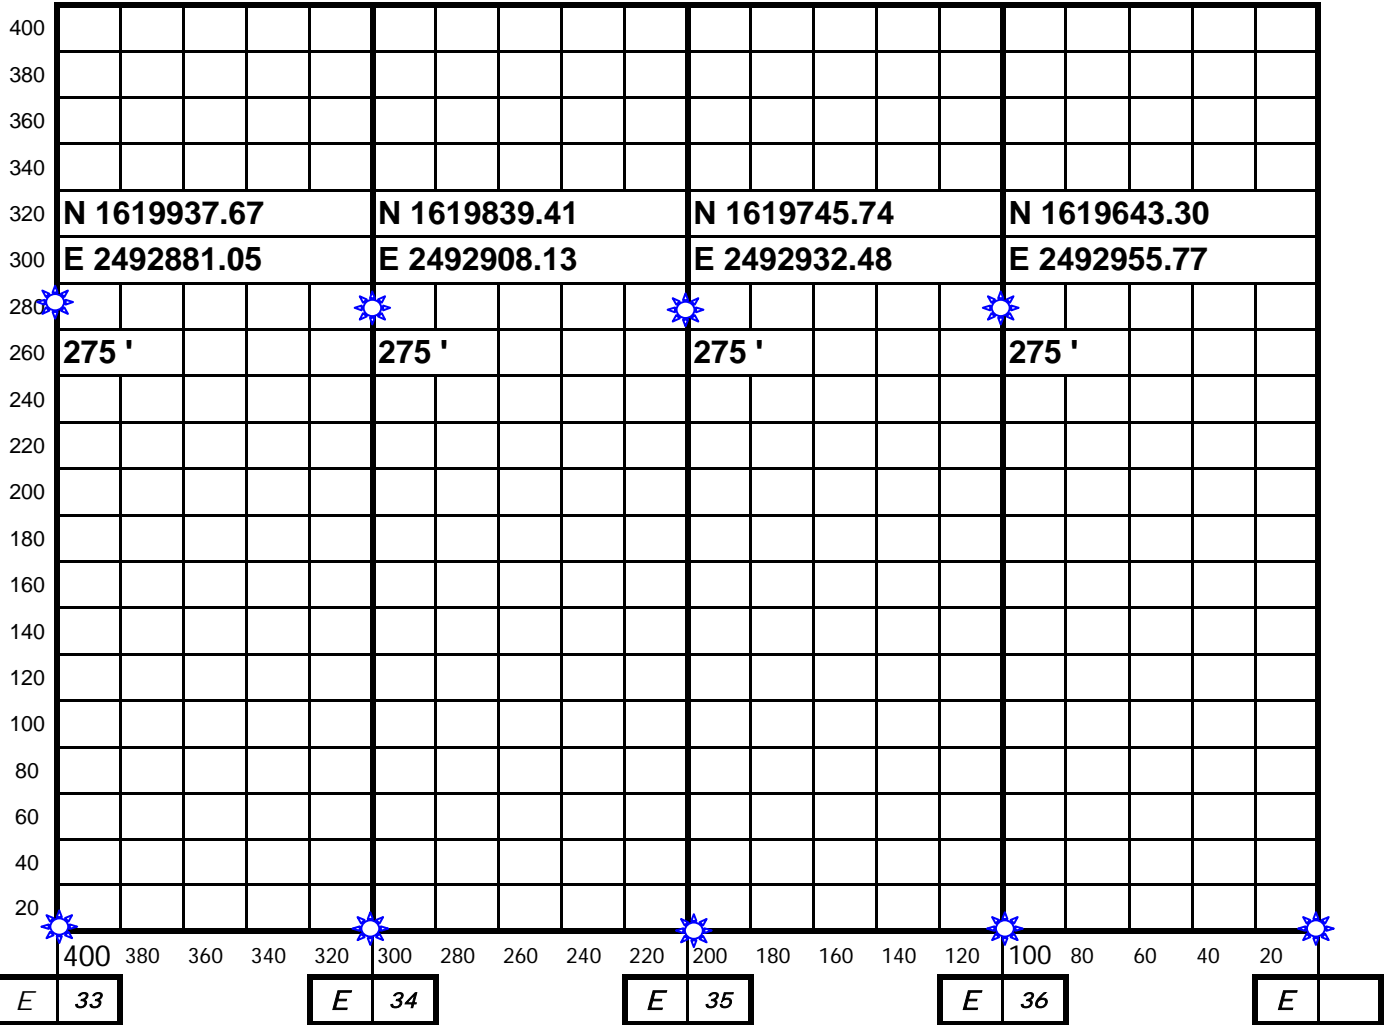


Start	Start	Start	Start	Start
<input type="text" value="8/25"/>	<input type="text" value="8/25"/>	<input type="text" value="8/25"/>	<input type="text" value="8/25"/>	<input type="text"/>
Finish	Finish	Finish	Finish	Finish
<input type="text" value="8/25"/>	<input type="text" value="8/25"/>	<input type="text" value="8/25"/>	<input type="text" value="8/25"/>	<input type="text"/>
MEC	MD	STAKE #		

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/25/2008	Completion Date:	8/25/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

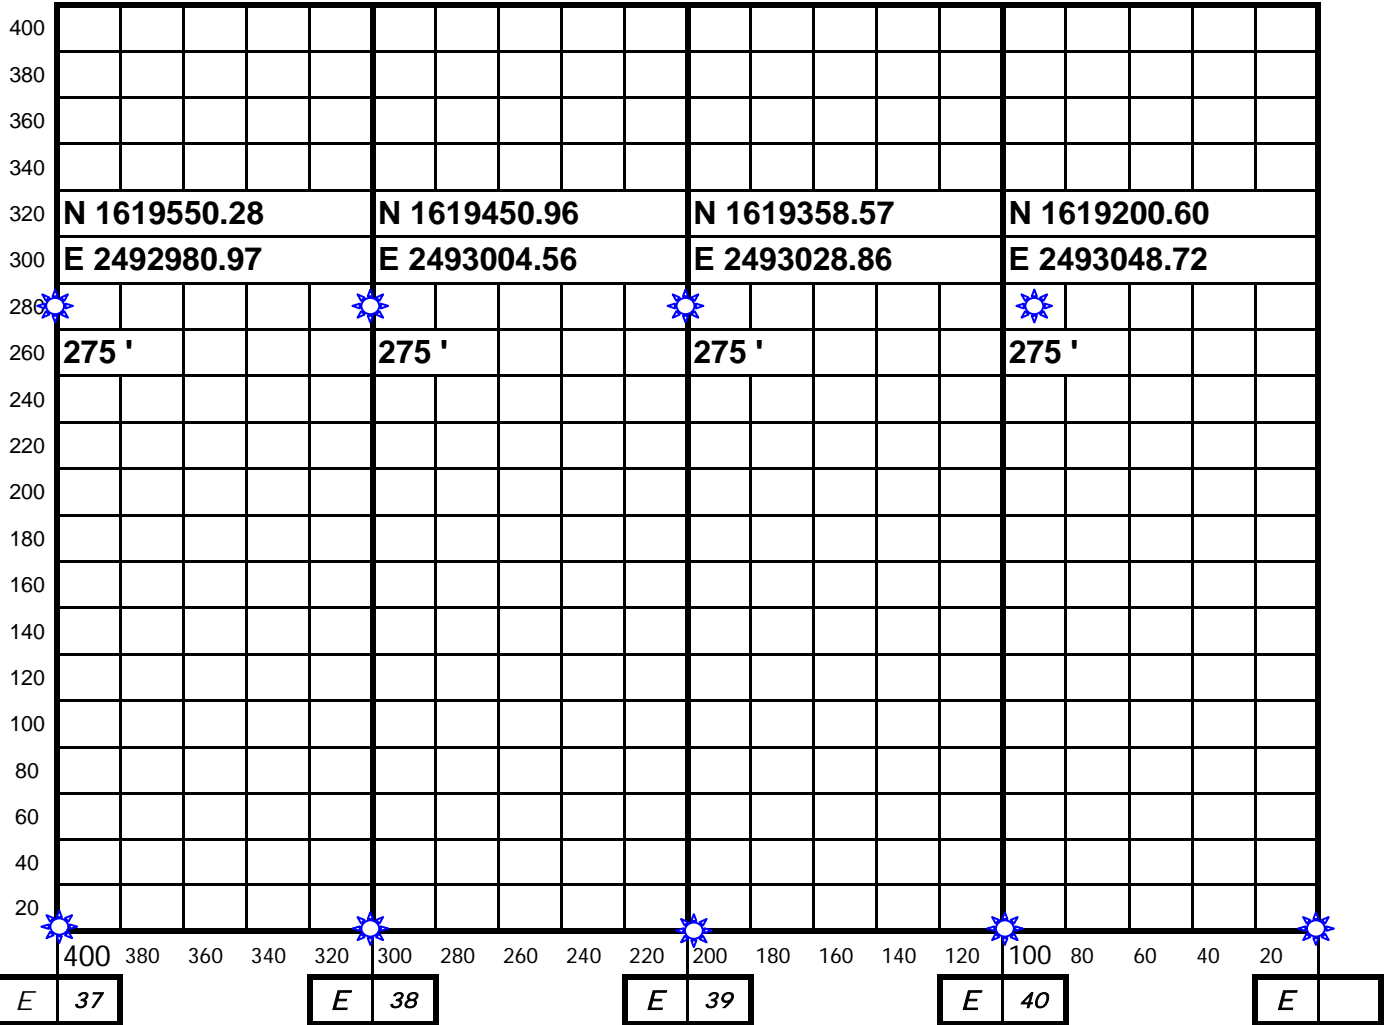


Start	Start	Start	Start	Start	
8/25	8/25	8/25	8/25		
Finish	Finish	Finish	Finish	Finish	
8/25	8/25	8/25	8/25		
	MEC		MD		STAKE #

Comments.Notes:

E-40 transect crosses buried cables

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/25/2008	Completion Date:	8/25/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

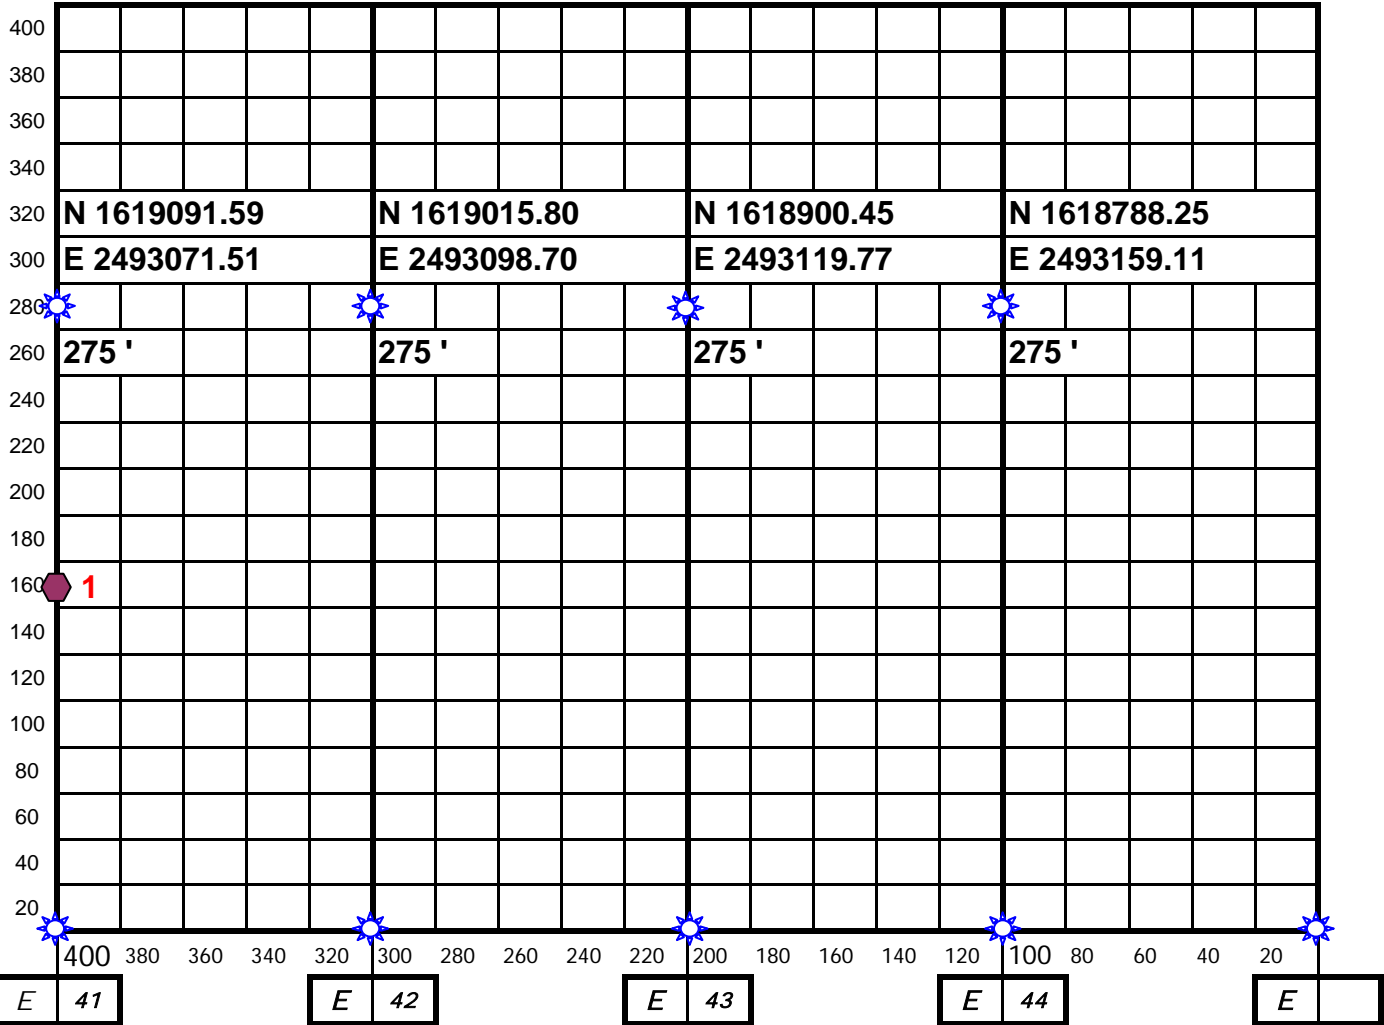

Start	Start	Start	Start	Start
<input type="text" value="8/25"/>	<input type="text" value="8/25"/>	<input type="text" value="8/25"/>	<input type="text" value="8/25"/>	<input type="text"/>
Finish	Finish	Finish	Finish	Finish
<input type="text" value="8/25"/>	<input type="text" value="8/25"/>	<input type="text" value="8/25"/>	<input type="text" value="8/25"/>	<input type="text"/>
	MEC		MD	
				STAKE #

Comments.Notes:

E 41 has buried comms cable


Anomalies

Base Line Data

#	ID	Northing	Easting	Comments
1	1	1619133.58	2492890.02	Buried rebar
2				
3				
4				
5				
6				
7				
8				
9				
10				
11				
12				
13				
14				
15				
16				
17				
18				
19				
20				
21				
22				
23				
24				
25				
26				
27				
28				
29				
30				
31				
32				
33				
34				
35				
36				
37				
38				
39				
40				
41				
42				
43				
44				

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/25/2008	Completion Date:	8/25/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

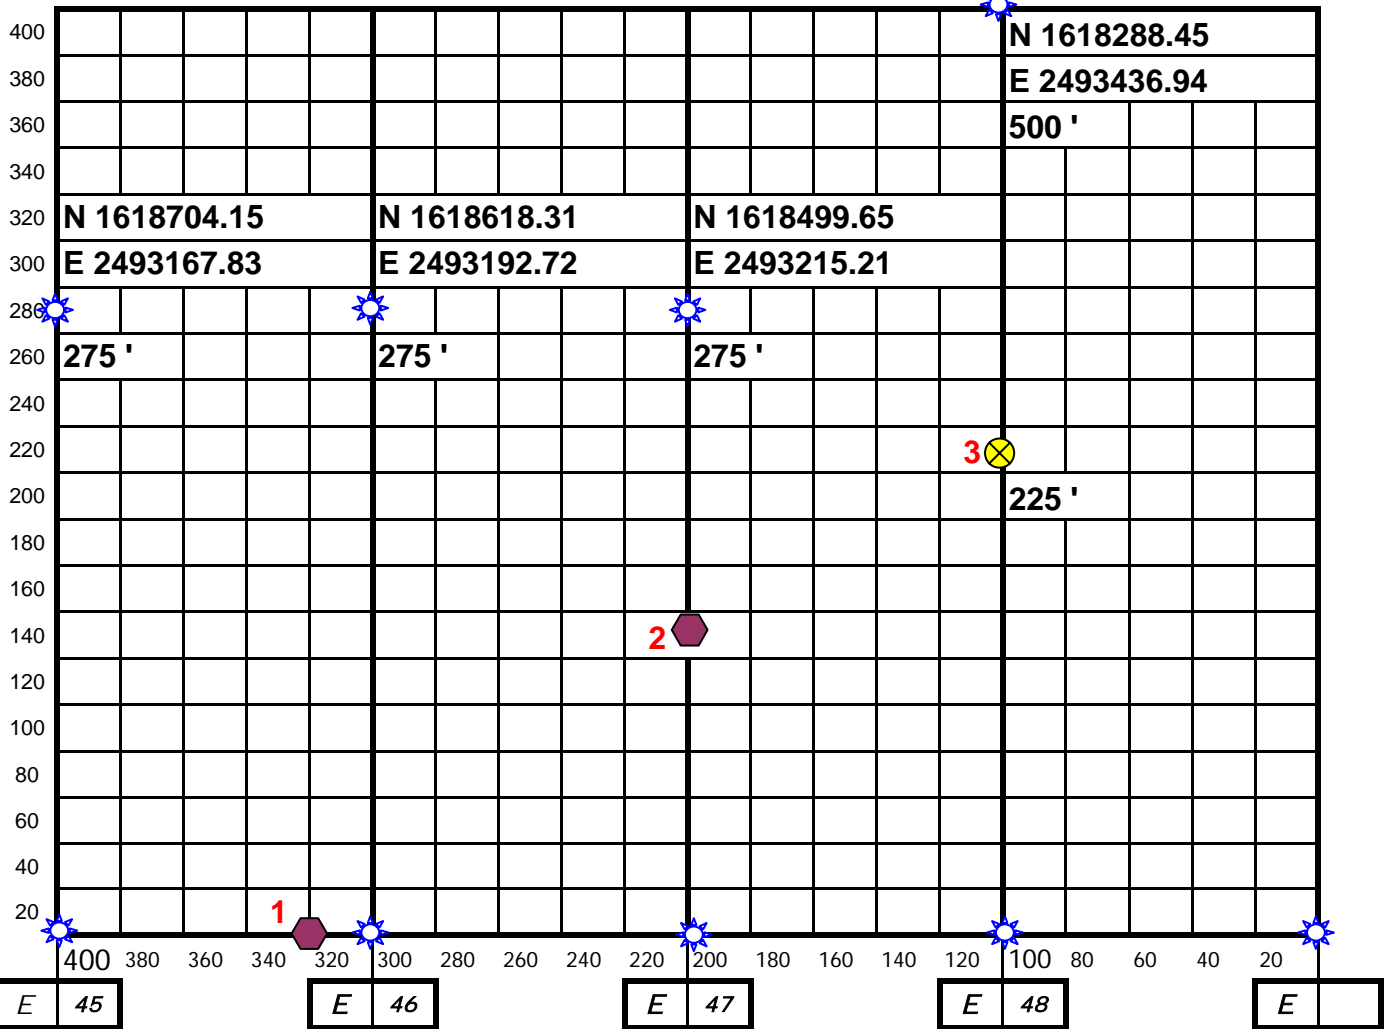

Start	Start	Start	Start	Start
8/25	8/25	8/25	8/25	
Finish	Finish	Finish	Finish	Finish
8/25	8/25	8/25	8/25	
	MEC		MD	
				STAKE #


Comments. Notes:

Anomalies

#	ID	Northing	Easting	Comments
1	1	1618686.72	2492910.98	Wire rope left in place
2	2	1618559.03	2493029.87	Chicken wire left in place
3	3	1618390.51	2493176.35	MD Frag
4				
5				
6				
7				
8				
9				
10				
11				
12				
13				
14				
15				
16				
17				
18				
19				
20				
21				
22				
23				
24				
25				
26				
27				
28				
29				
30				
31				
32				
33				
34				
35				
36				
37				
38				
39				
40				
41				
42				
43				

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/25/2008	Completion Date:	8/25/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

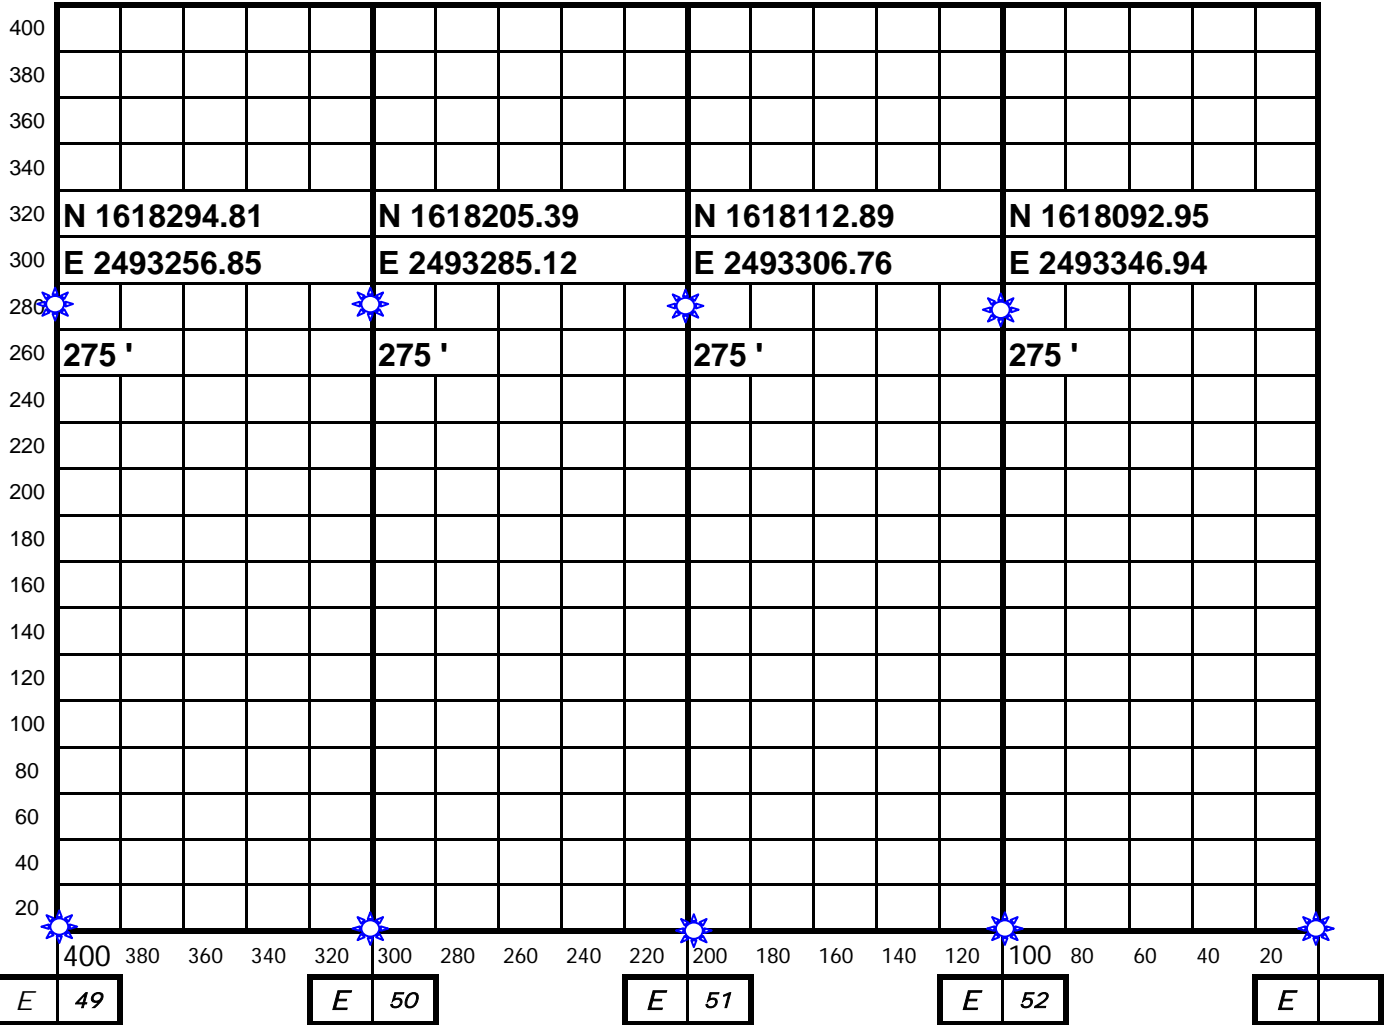


Start	Start	Start	Start	Start	
8/25	8/25	8/25	8/25		
Finish	Finish	Finish	Finish	Finish	
8/25	8/25	8/25	8/25		
	MEC		MD		STAKE #

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/25/2008	Completion Date:	8/26/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

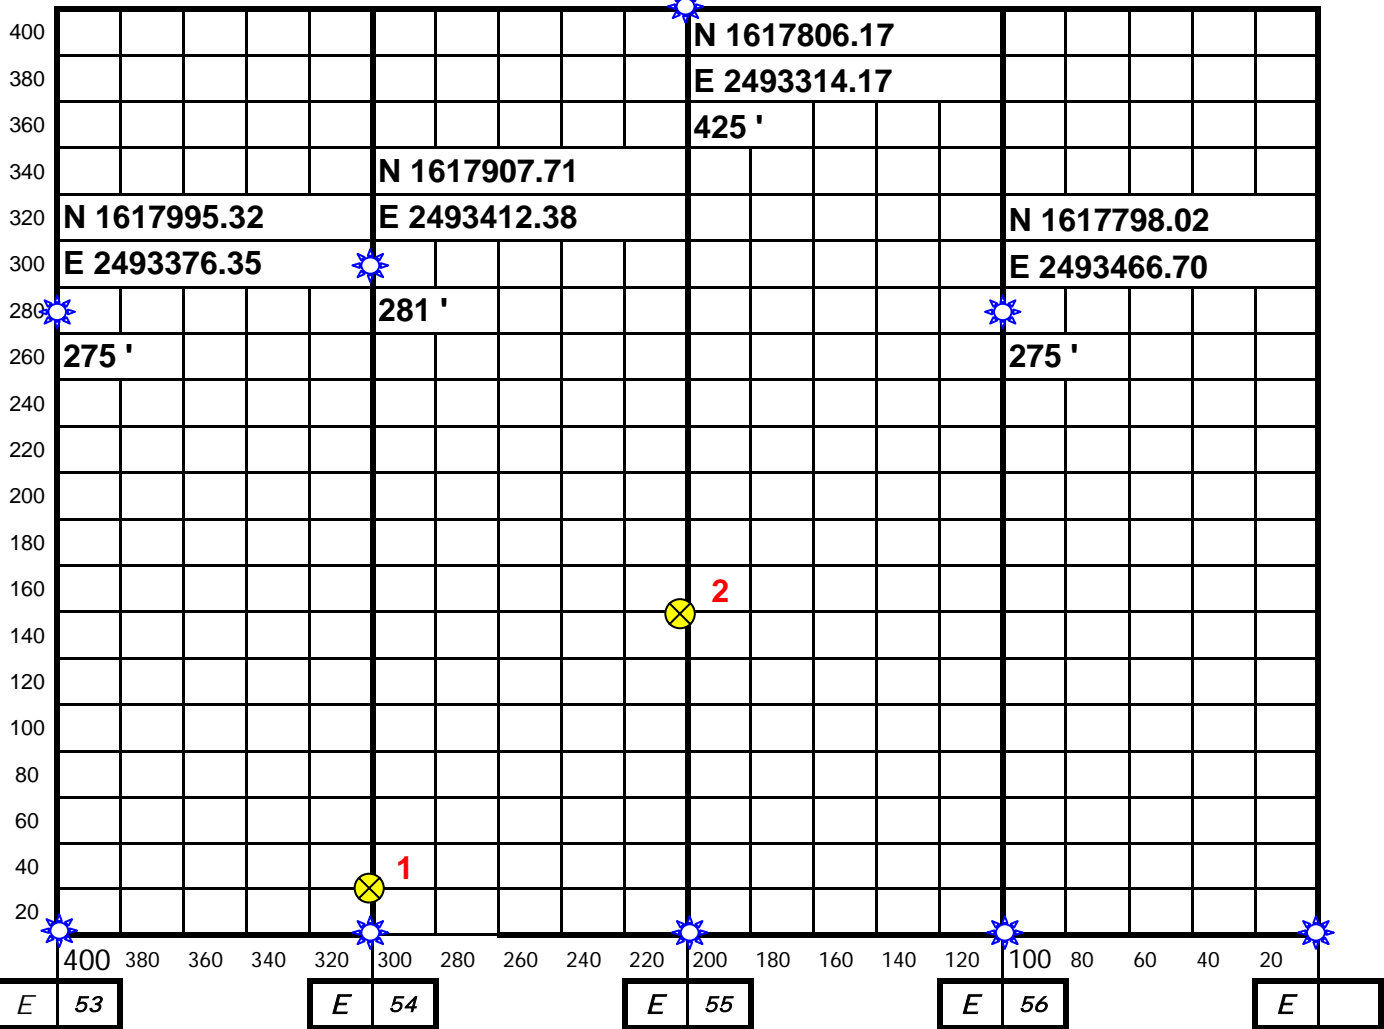

E	53	E	54	E	55	E	56	E	
---	----	---	----	---	----	---	----	---	--

Start	Start	Start	Start	Start
8/25	8/25	8/25	8/26	
Finish	Finish	Finish	Finish	Finish
8/25	8/25	8/25	8/26	
	MEC		MD	
				STAKE #


Comments/Notes:

Anomalies

#	ID	Northing	Easting	Comments
1	E 54A	1617902.05	2493137.01	25 lb frag bomb sleeve
2	E 55A	1617806.89	2493314.17	MD frag
3				
4				
5				
6				
7				
8				
9				
10				
11				
12				
13				
14				
15				
16				
17				
18				
19				
20				
21				
22				
23				
24				
25				
26				
27				
28				
29				
30				
31				
32				
33				
34				
35				
36				
37				
38				
39				
40				
41				
42				
43				
44				

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/26/2008	Completion Date:	8/26/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

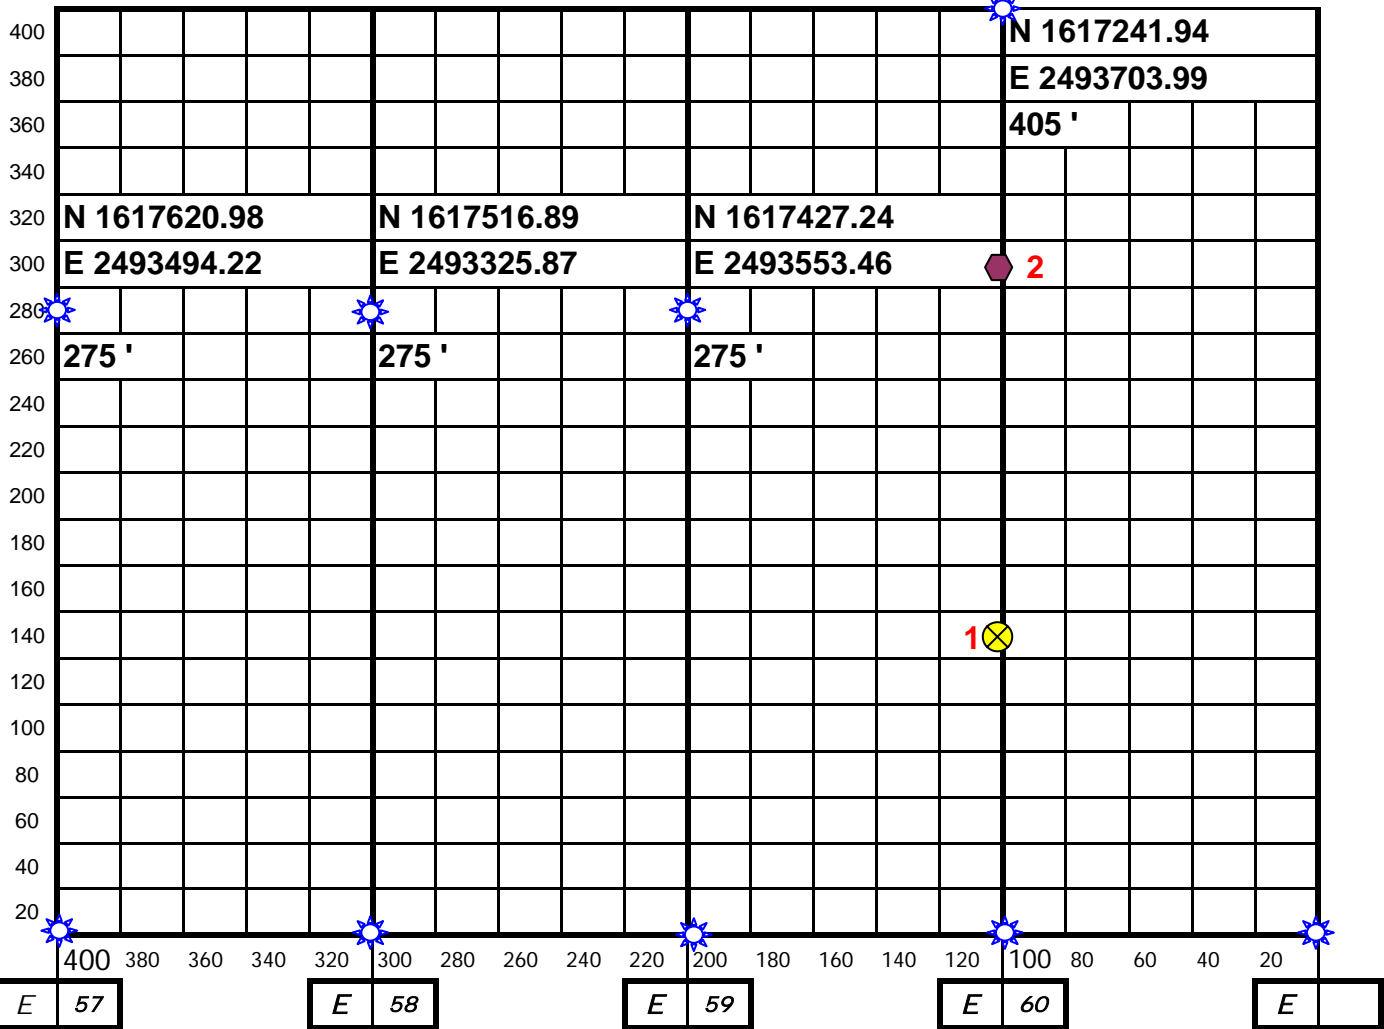

Start	Start	Start	Start	Start
<input type="text" value="8/26"/>	<input type="text" value="8/26"/>	<input type="text" value="8/26"/>	<input type="text" value="8/26"/>	<input type="text"/>
Finish	Finish	Finish	Finish	Finish
<input type="text" value="8/26"/>	<input type="text" value="8/26"/>	<input type="text" value="8/26"/>	<input type="text" value="8/26"/>	<input type="text"/>
MEC	MD	STAKE #		


Comments.Notes:

Anomalies

#	ID	Northing	Easting	Comments
1	1	1617312.18	2493434.33	MD Frag
2	2	1617323.12	2493401.16	Metal wire left in place
3				
4				
5				
6				
7				
8				
9				
10				
11				
12				
13				
14				
15				
16				
17				
18				
19				
20				
21				
22				
23				
24				
25				
26				
27				
28				
29				
30				
31				
32				
33				
34				
35				
36				
37				
38				
39				
40				
41				
42				
43				

PIKA Transect Sheets

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	8/26/2008	Completion Date:	8/26/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

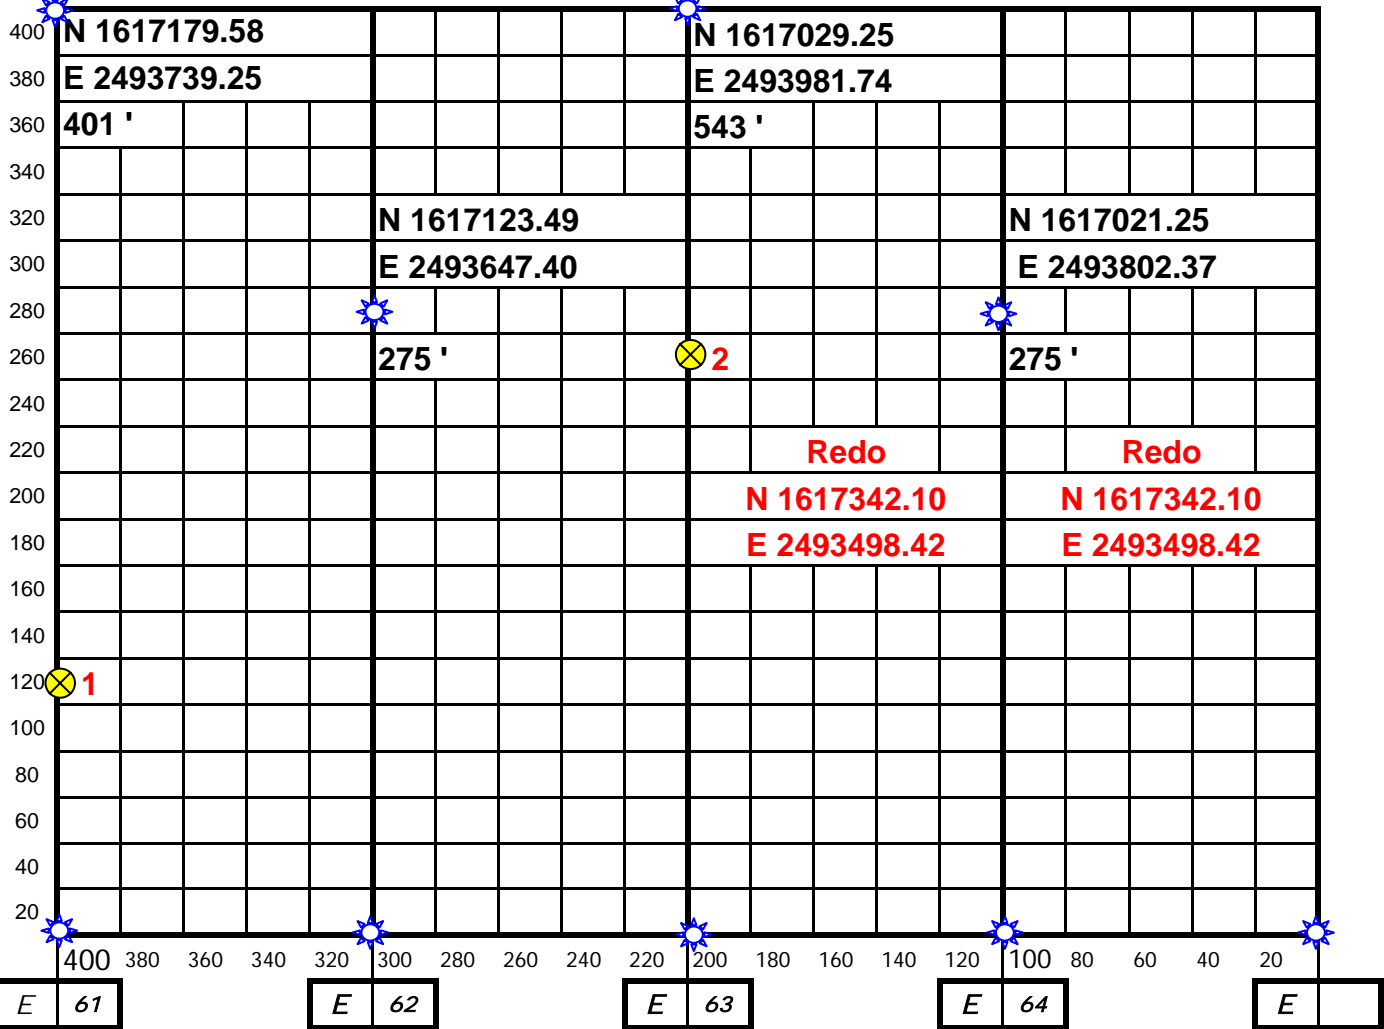

Start	Start	Start	Start	Start
<input type="text" value="8/26"/>	<input type="text" value="8/26"/>	<input type="text" value="8/26"/>	<input type="text" value="8/26"/>	<input type="text"/>
Finish	Finish	Finish	Finish	Finish
<input type="text" value="8/26"/>	<input type="text" value="8/26"/>	<input type="text" value="8/26"/>	<input type="text" value="8/26"/>	<input type="text"/>
MEC		MD	STAKE #	

Comments.Notes:


Transects redone to go out 90 degrees from base line

Anomalies

#	ID	Northing	Easting	Comments
1	63a	1617062.47	2493708.04	MD frag
2	63b	1617214.07	2493465.53	MD frag
3				
4				
5				
6				
7				
8				
9				
10				
11				
12				
13				
14				
15				
16				
17				
18				
19				
20				
21				
22				
23				
24				
25				
26				
27				
28				
29				
30				
31				
32				
33				
34				
35				
36				
37				
38				
39				
40				
42				
43				
44				

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/25/2008	Completion Date:	9/11/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

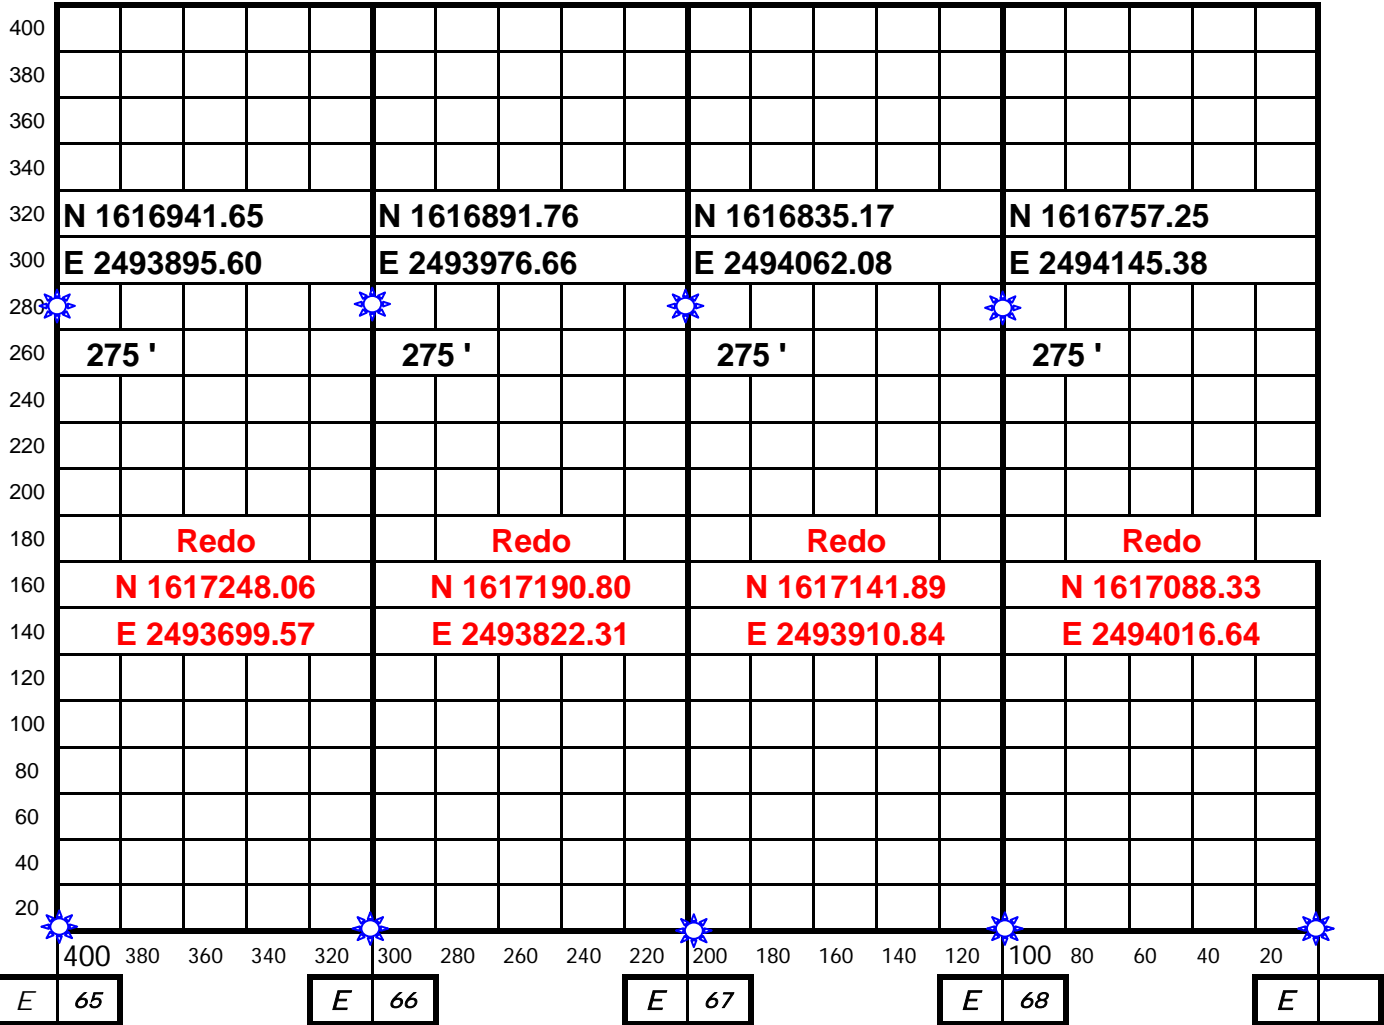

Start	Start	Start	Start	Start
8/25	9/11	9/11	9/11	
Finish	Finish	Finish	Finish	Finish
9/11	9/11	9/11	9/11	
	MEC		MD	STAKE #


Comments.Notes:

E-68: offset stake 10' SE

Transects redone to go out 90 degrees from baseline

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/13/2008	Completion Date:	8/13/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

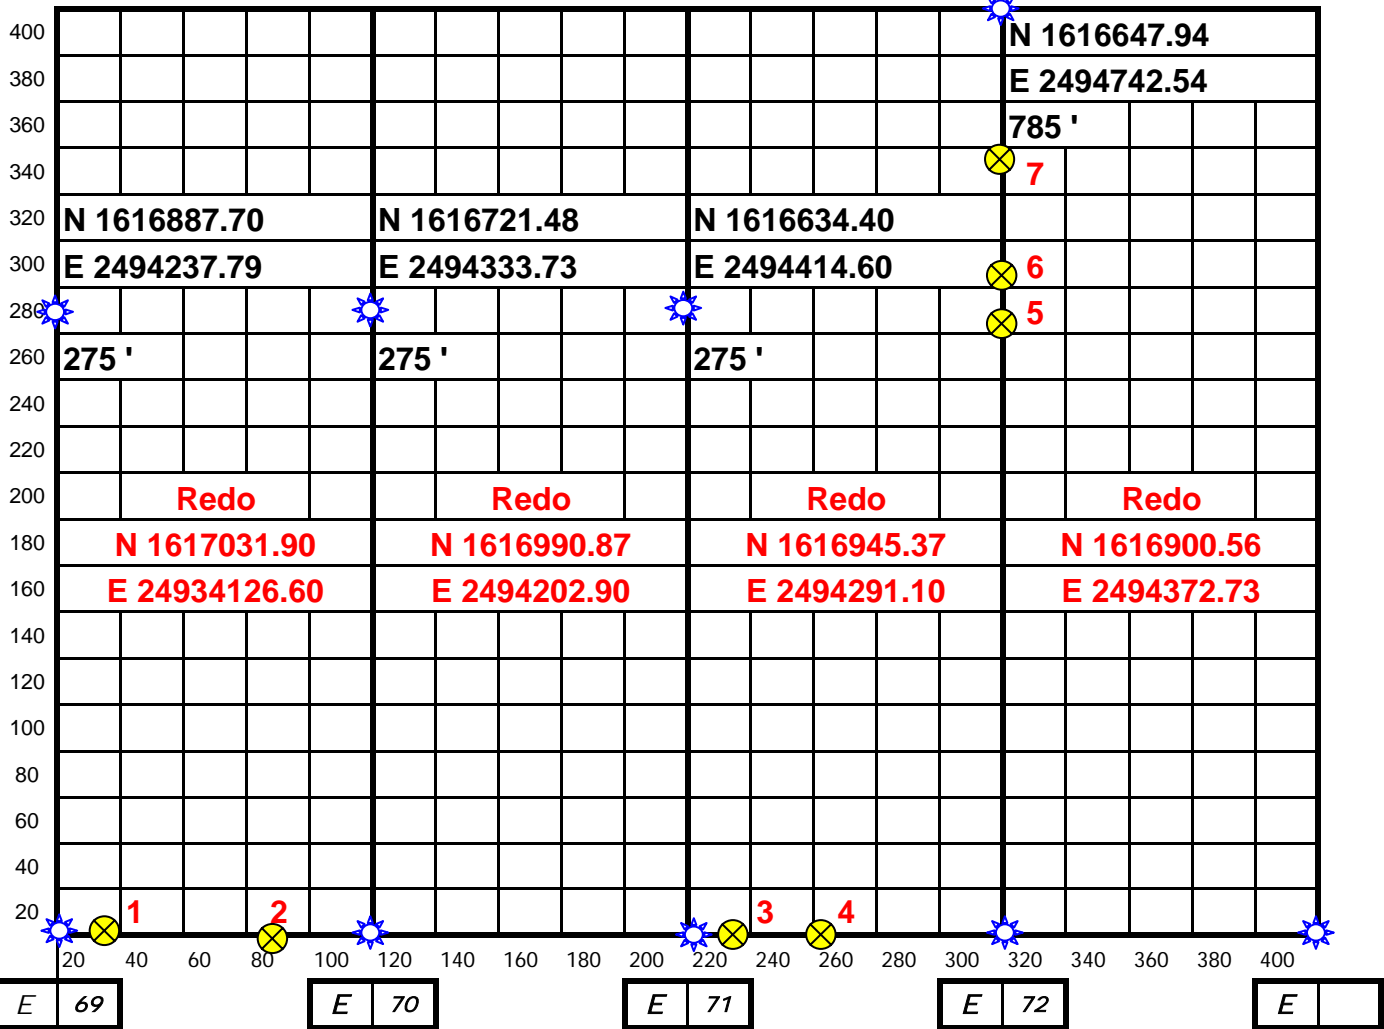

Start	Start	Start	Start	Start
8/13	8/13	8/13	8/13	
Finish	Finish	Finish	Finish	Finish
8/13	8/13	8/13	8/13	
MEC		MD		STAKE #

Comments.Notes:

Step - Out required for base line MD/frag fi


Transects redone to go out 90 degrees from base

Anomalies

#	ID	Northing	Easting	Comments
1	E 69.1	1616775.18	2493979.35	MD frag
2	E 69.2	1616779.26	2494012.7	MD frag
3	E 71.1	1616697.8	2494157.02	MD frag
4	E 71.2	1616695.5	2494170.27	MD frag
5	E 73 A	1616674.36	2494475.9	MD frag
6	E 73 B	1616684.11	2494510.59	MD frag
7	E 73 C	1616676.17	2494663.54	MD frag
8				
9				
10				
11				
12				
13				
14				
15				
16				
17				
18				
19				
20				
21				
22				
23				
24				
25				
26				
27				
28				
29				
30				
31				
32				
33				
34				
35				
36				
37				
38				
39				
40				
41				
42				
43				
44				

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/13/2008	Completion Date:	8/13/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

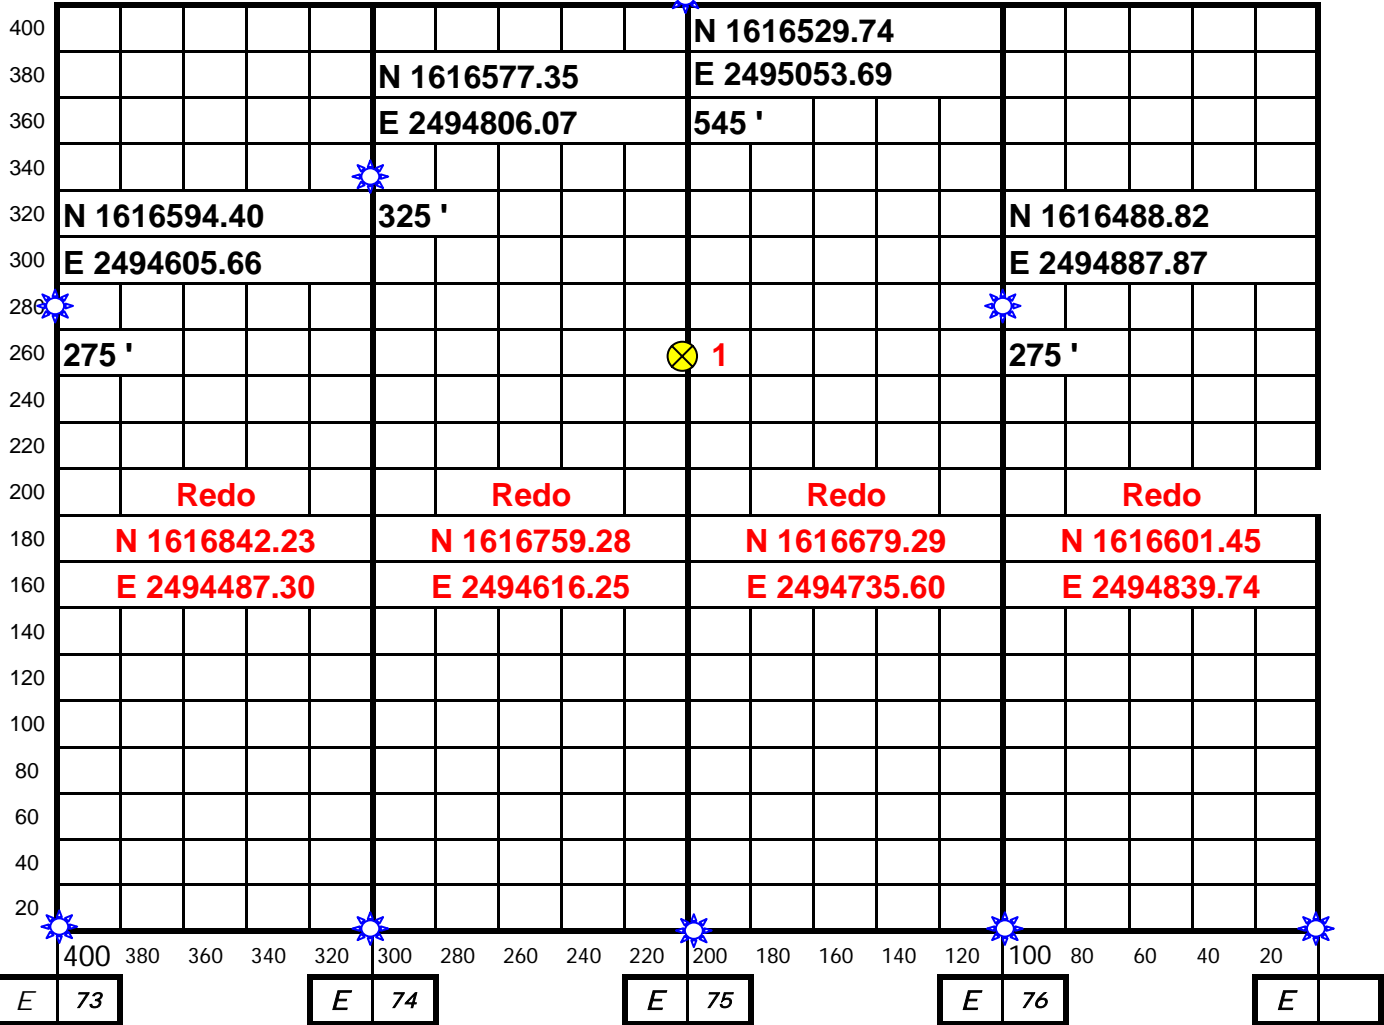

Start	Start	Start	Start	Start
8/13	8/13	8/13	8/13	
Finish	Finish	Finish	Finish	Finish
8/13	8/13	8/13	8/13	
MEC	MD	STAKE #		

Comments.Notes:


Transects redone to go out 90 degrees fro

Anomalies

#	ID	Northing	Easting	Comments
1	E 75A	1616521.63	2494774.42	MD frag
2				
3				
4				
5				
6				
7				
8				
9				
10				
11				
12				
13				
14				
15				
16				
17				
18				
19				
20				
21				
22				
23				
24				
25				
26				
27				
28				
29				
30				
31				
32				
33				
34				
35				
36				
37				
38				
39				
40				
41				
42				
43				
44				

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/13/2008	Completion Date:	8/13/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

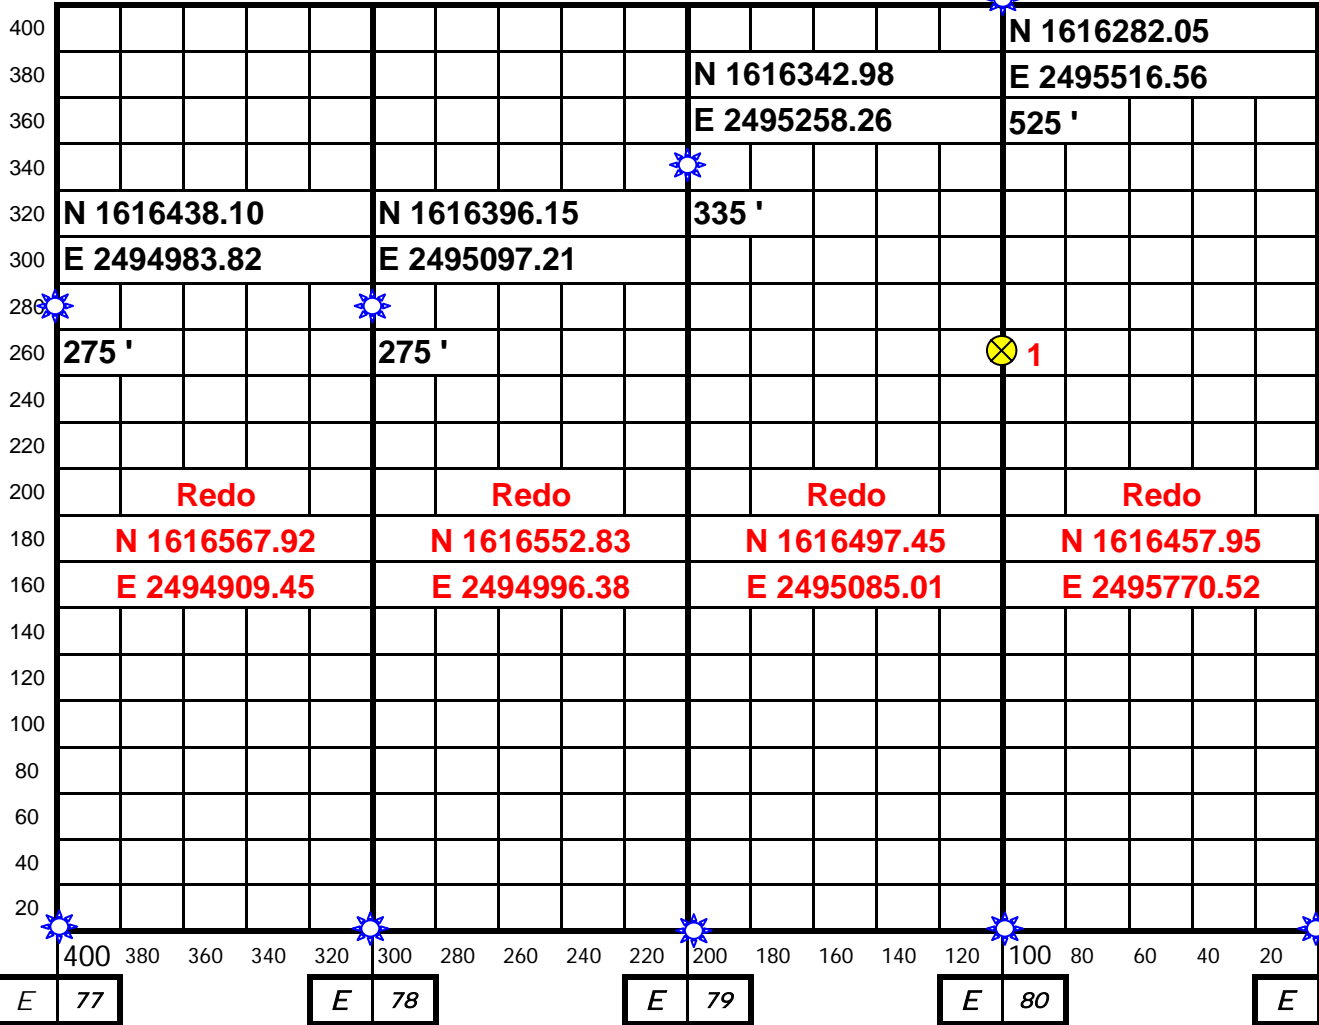

Start	Start	Start	Start	Start
<input type="text" value="8/13"/>	<input type="text" value="8/13"/>	<input type="text" value="8/13"/>	<input type="text" value="8/13"/>	<input type="text"/>
Finish	Finish	Finish	Finish	Finish
<input type="text" value="8/13"/>	<input type="text" value="8/13"/>	<input type="text" value="8/13"/>	<input type="text" value="8/13"/>	<input type="text"/>
MEC	MD	STAKE #		

Comments.Notes:


Transects redone to go out 90 degrees from baselone

Anomalies

#	ID	Northing	Easting	Comments
1	E 79A	1616296.41	2495195.29	Spent AP 57mm projectile case
2				
3				
4				
5				
6				
7				
8				
9				
10				
11				
12				
13				
14				
15				
16				
17				
18				
19				
20				
21				
22				
23				
24				
25				
26				
27				
28				
29				
30				
31				
32				
33				
34				
35				
36				
37				
38				
39				
40				
41				
42				
43				
44				

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/13/2008	Completion Date:	8/13/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

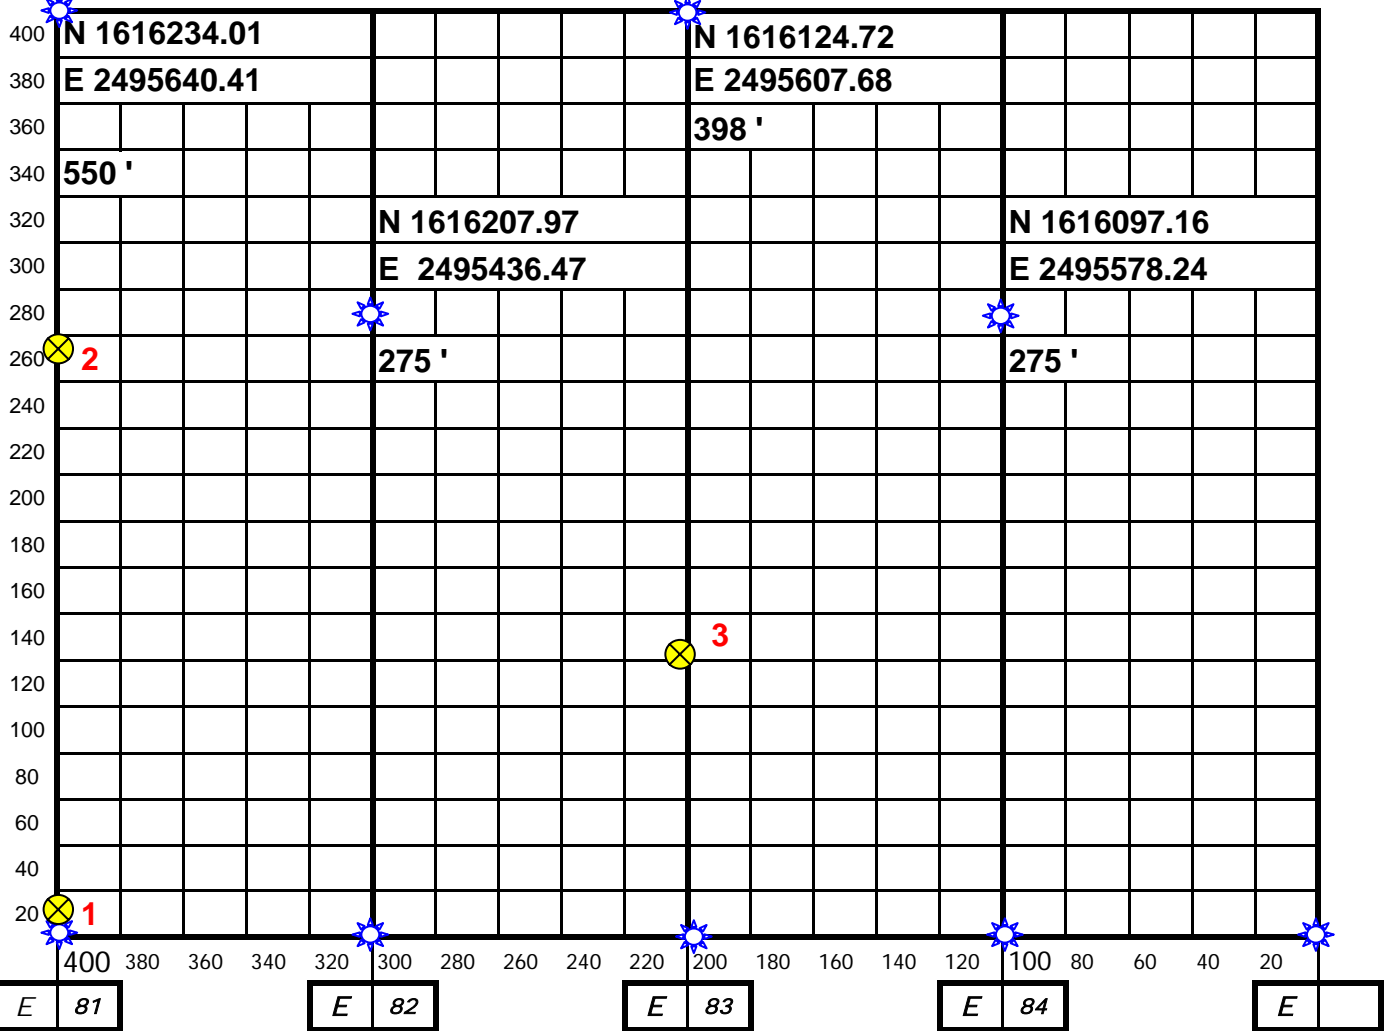

Start	Start	Start	Start	Start
8/13	8/13	8/13	8/13	
Finish	Finish	Finish	Finish	Finish
8/13	8/13	8/13	8/13	
	MEC		MD	
				STAKE #


Comments. Notes:

Anomalies

#	ID	Northing	Easting	Comments
1	E 81A	1616250.33	2495049.64	MD frag
2	E 81B	1616249.89	2495294.86	MD frag
3	E 83A	1616120.9	2495331.96	MD frag
4				
5				
6				
7				
8				
9				
10				
11				
12				
13				
14				
15				
16				
17				
18				
19				
20				
21				
22				
23				
24				
25				
26				
27				
28				
29				
30				
31				
32				
33				
34				
35				
36				
37				
38				
39				
40				
41				
42				
43				
44				

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/13/2008	Completion Date:	8/13/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

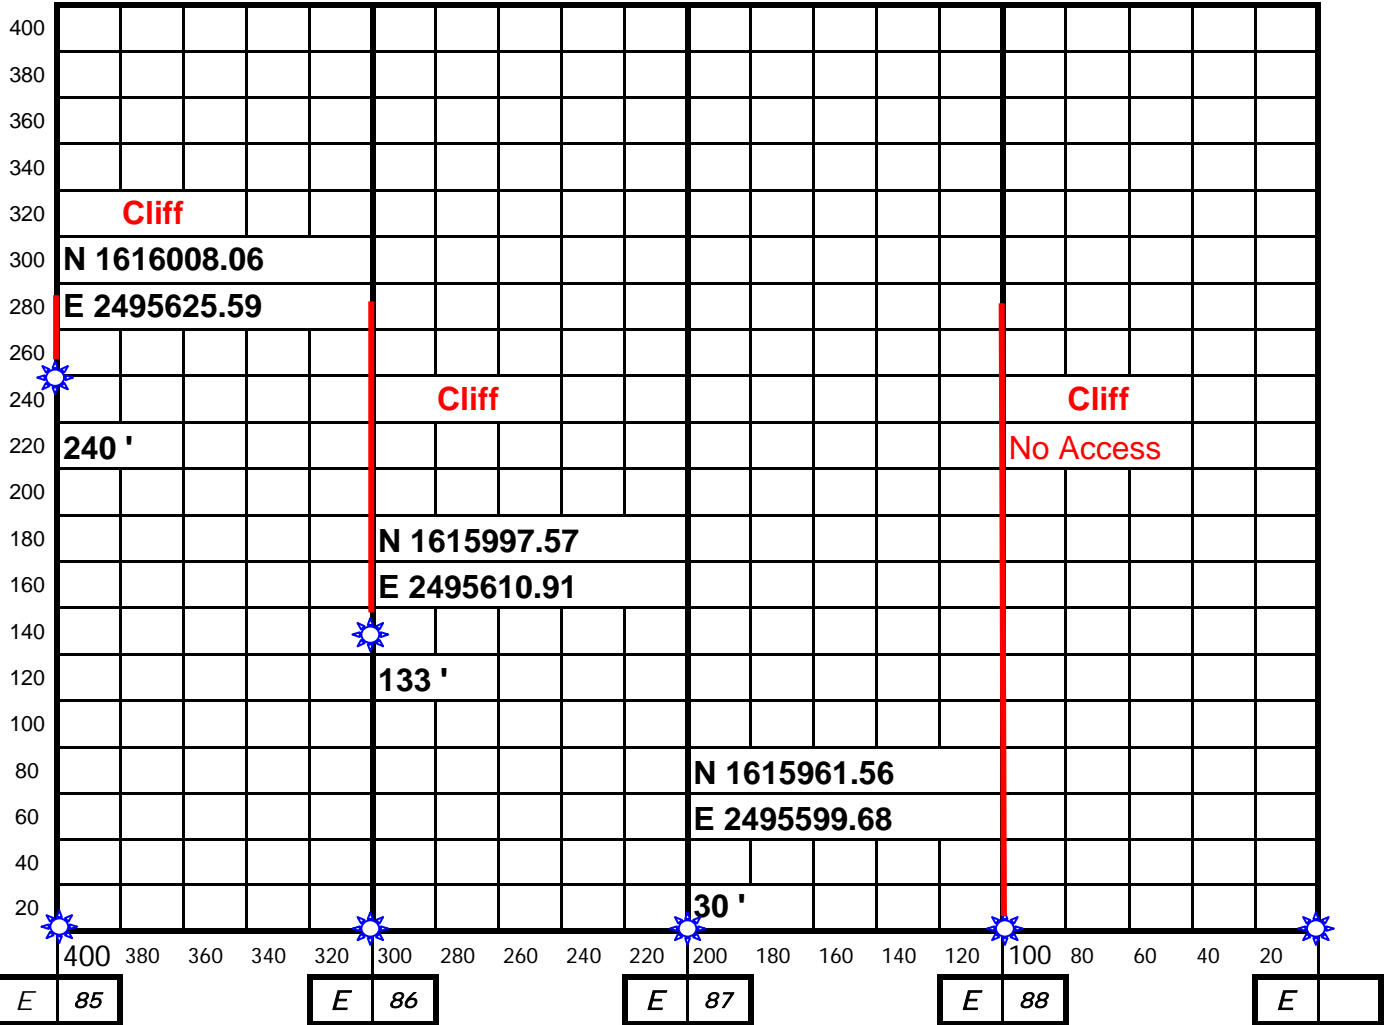


Start	Start	Start	Start	Start	
8/13	8/13	8/13	8/13		
Finish	Finish	Finish	Finish	Finish	
8/13	8/13	8/13	8/13		
	MEC		MD		STAKE #

Comments. Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/18/2008	Completion Date:	8/18/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

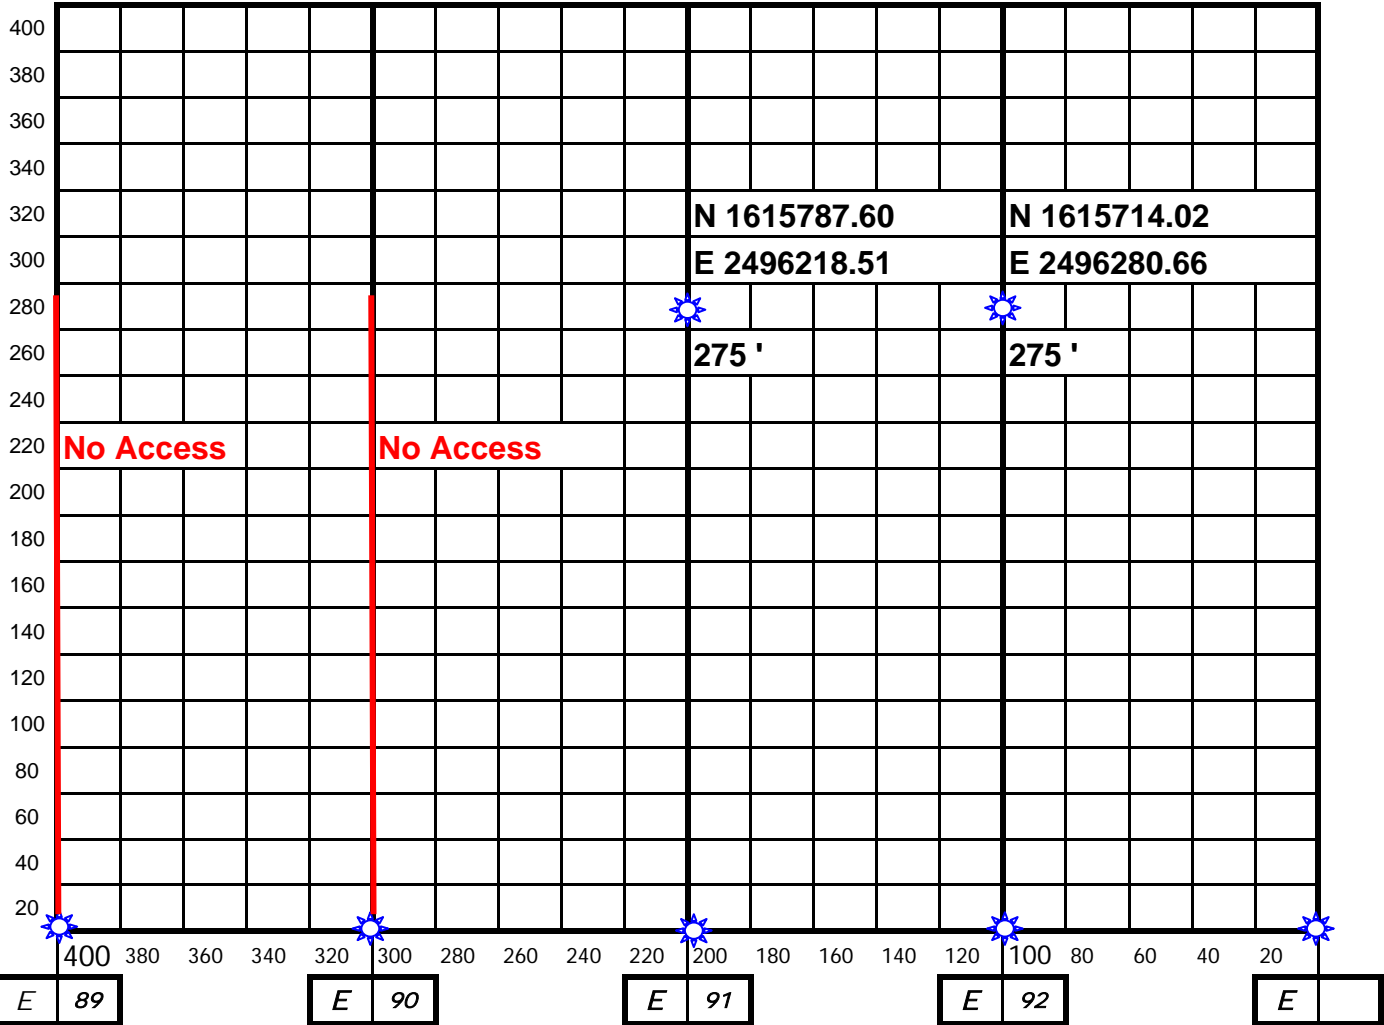


Start	Start	Start	Start	Start
		8/18	8/18	
Finish	Finish	Finish	Finish	Finish
		8/18	8/18	
MEC	MD	STAKE #		

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/18/2008	Completion Date:	8/18/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

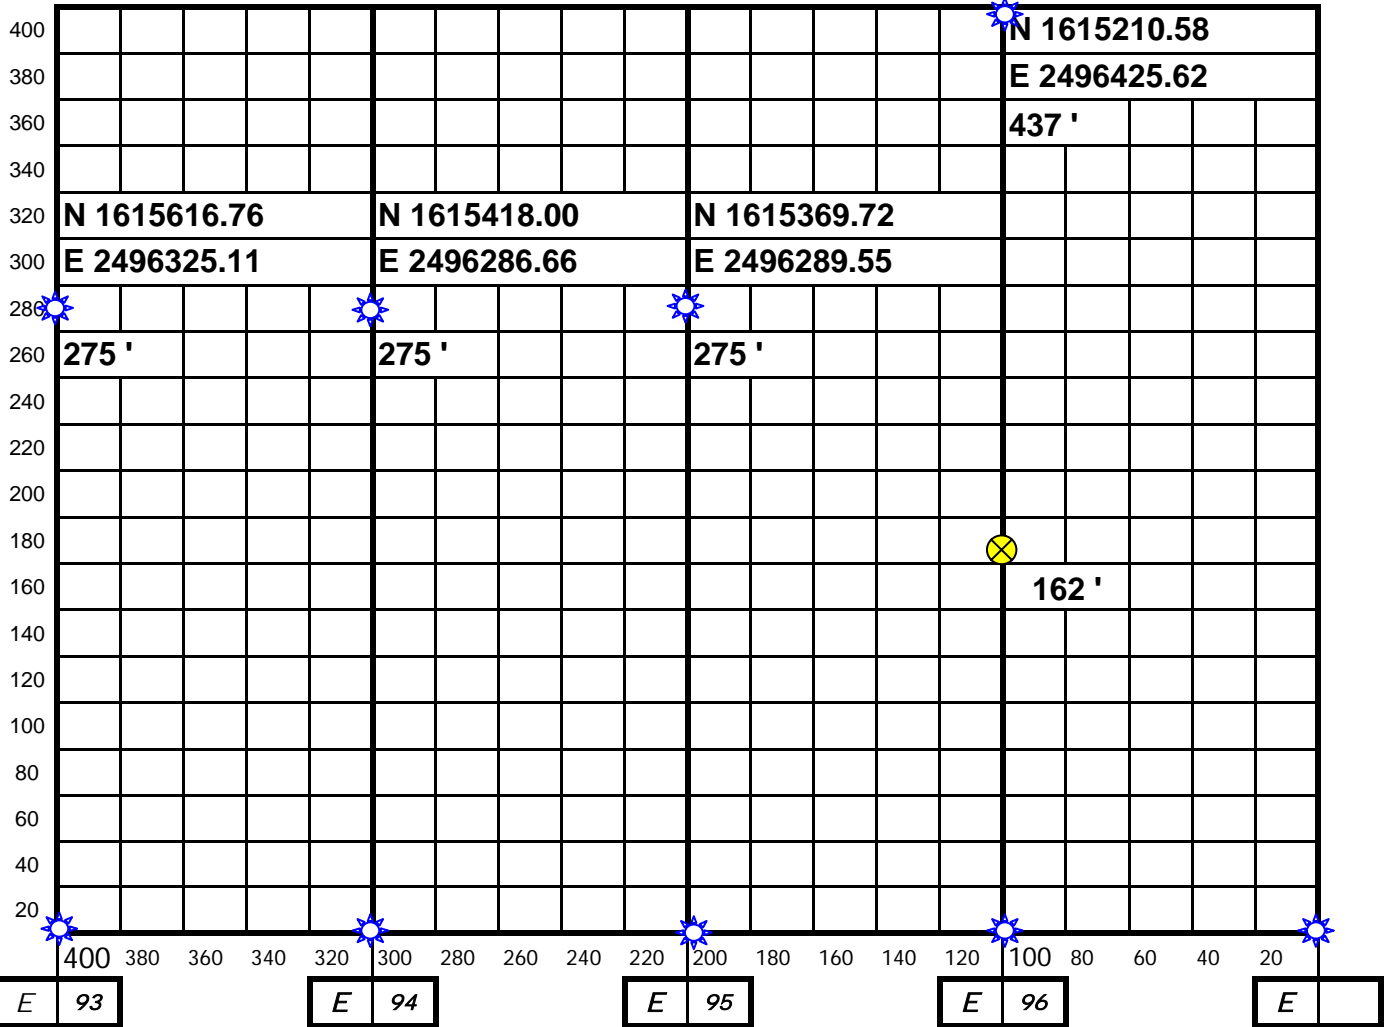

Start	Start	Start	Start	Start
<input type="text" value="8/18"/>	<input type="text" value="8/18"/>	<input type="text" value="8/18"/>	<input type="text" value="8/18"/>	<input type="text"/>
Finish	Finish	Finish	Finish	Finish
<input type="text" value="8/18"/>	<input type="text" value="8/18"/>	<input type="text" value="8/18"/>	<input type="text" value="8/18"/>	<input type="text"/>
MEC	MD	STAKE #		

Comments.Notes:


Flare body located

Anomalies

#	ID	Northing	Easting	Comments
1	E 96	1615210.58	2496425.62	Empty flare body
2				
3				
4				
5				
6				
7				
8				
9				
10				
11				
12				
13				
14				
15				
16				
17				
18				
19				
20				
21				
22				
23				
24				
25				
26				
27				
28				
29				
30				
31				
32				
33				
34				
35				
36				
37				
38				
39				
40				
41				
42				
43				
44				

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/18/2008	Completion Date:	8/18/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

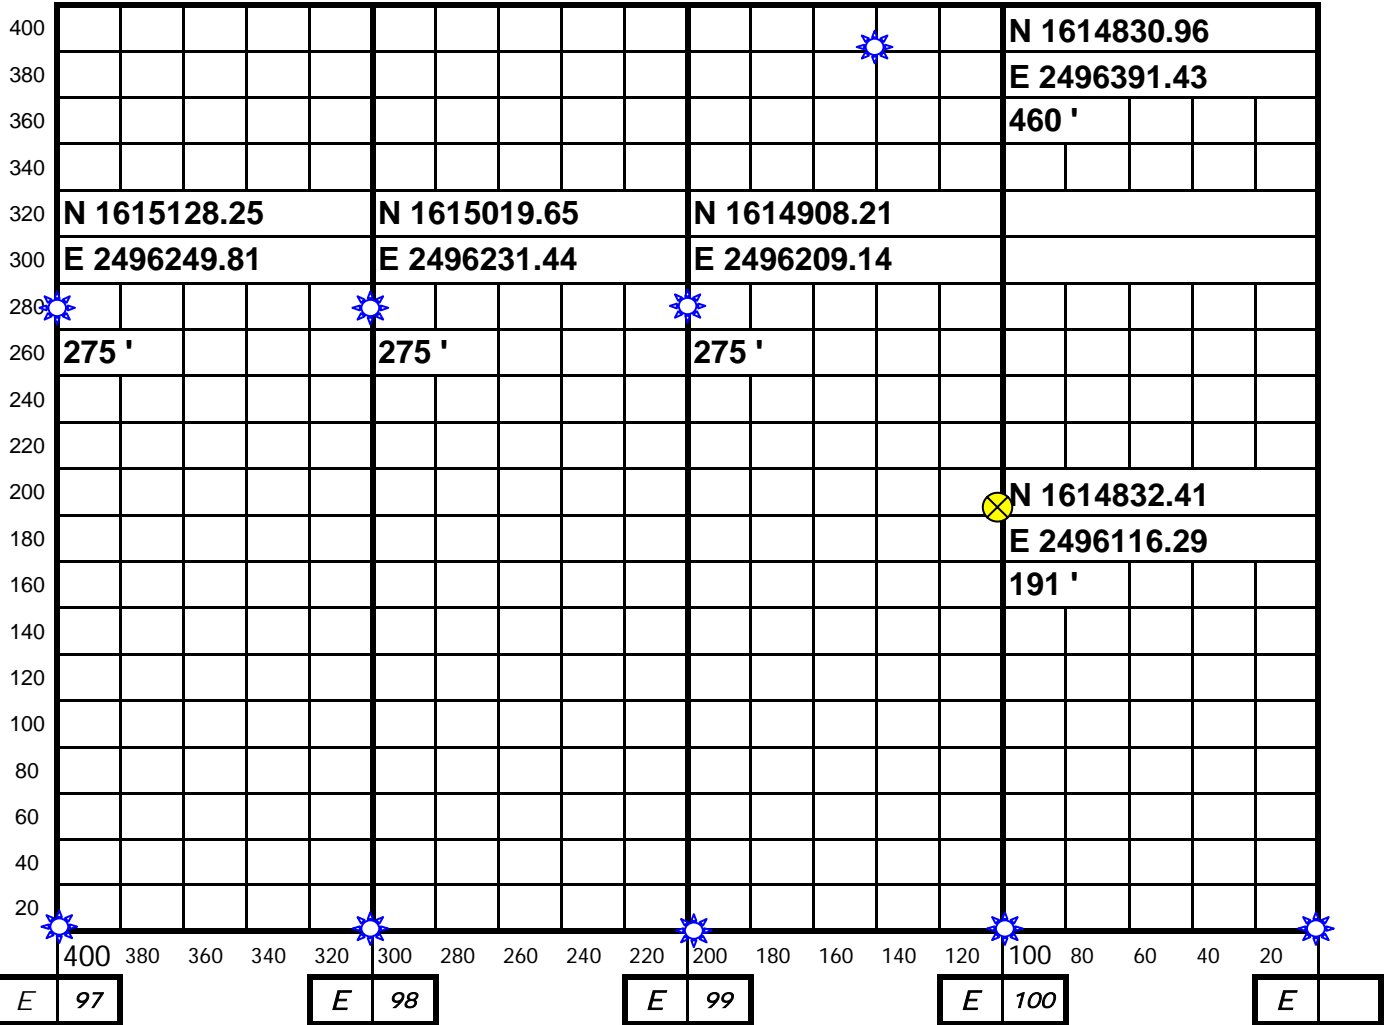

Start	Start	Start	Start	Start
<input type="text" value="8/18"/>	<input type="text" value="8/18"/>	<input type="text" value="8/18"/>	<input type="text" value="8/18"/>	<input type="text"/>
Finish	Finish	Finish	Finish	Finish
<input type="text" value="8/18"/>	<input type="text" value="8/18"/>	<input type="text" value="8/18"/>	<input type="text" value="8/18"/>	<input type="text"/>
	MEC		MD	
				STAKE #

Comments.Notes:


Frag located

Anomalies

#	ID	Northing	Easting	Comments
1	E 100	1614832.41	2496116.29	Fragmentation
2				
3				
4				
5				
6				
7				
8				
9				
10				
11				
12				
13				
14				
15				
16				
17				
18				
19				
20				
21				
22				
23				
24				
25				
26				
27				
28				
29				
30				
31				
32				
33				
34				
35				
36				
37				
38				
39				
41				
42				
43				
44				

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/18/2008	Completion Date:	8/18/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

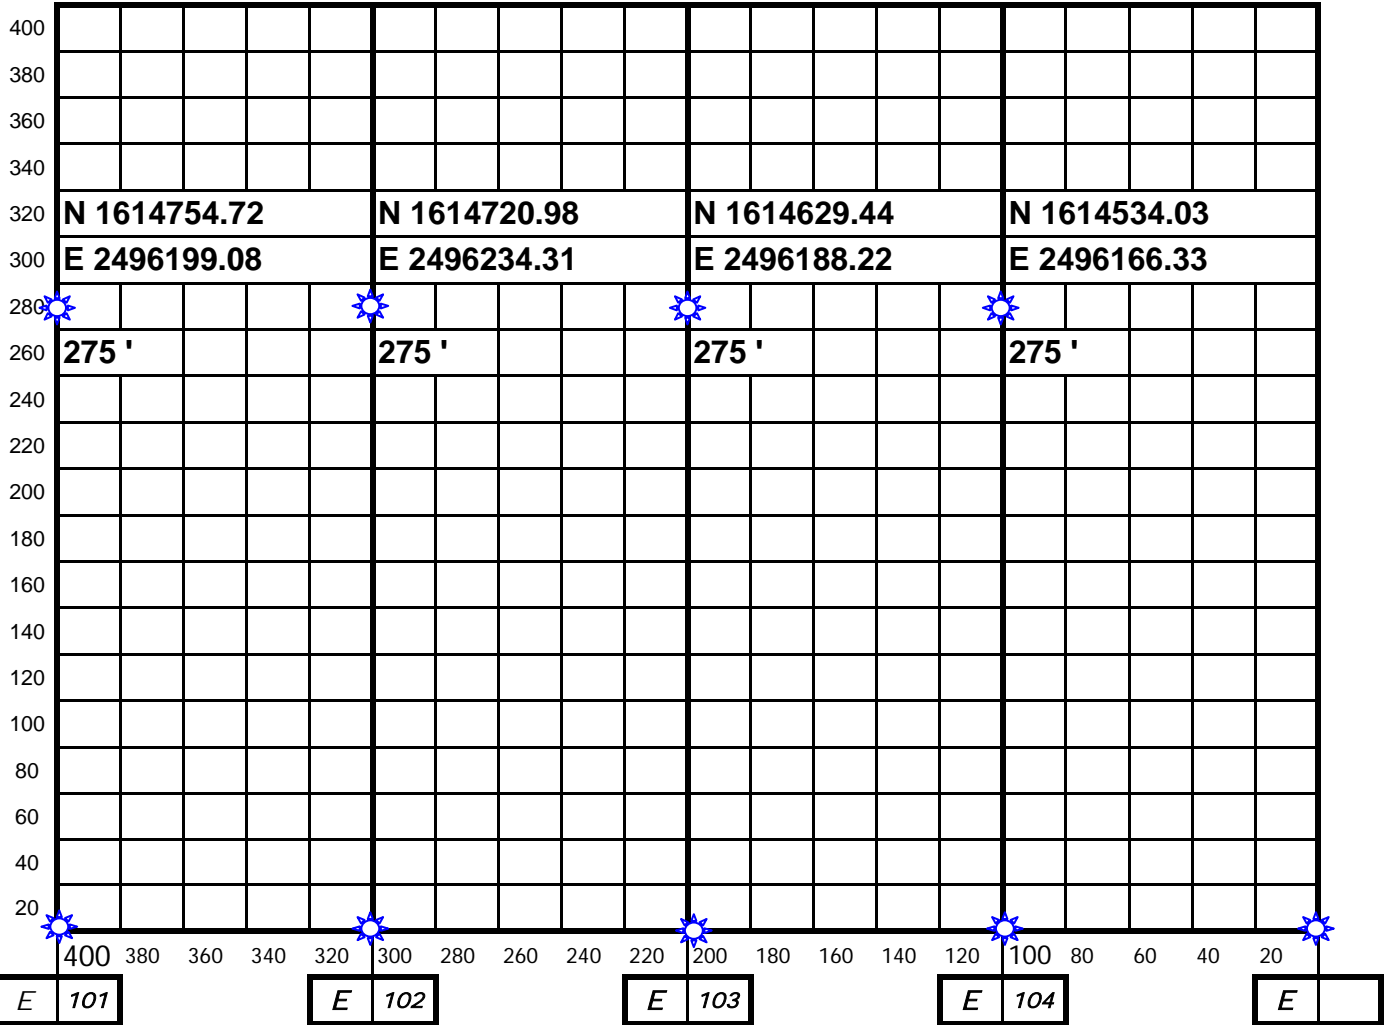


<i>E</i> 101	<i>E</i> 102	<i>E</i> 103	<i>E</i> 104	<i>E</i>
--------------	--------------	--------------	--------------	----------

Start	Start	Start	Start	Start
8/18	8/18	8/18	8/18	
Finish	Finish	Finish	Finish	Finish
8/18	8/18	8/18	8/18	
MEC	MD	STAKE #		

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/18/2008	Completion Date:	8/18/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

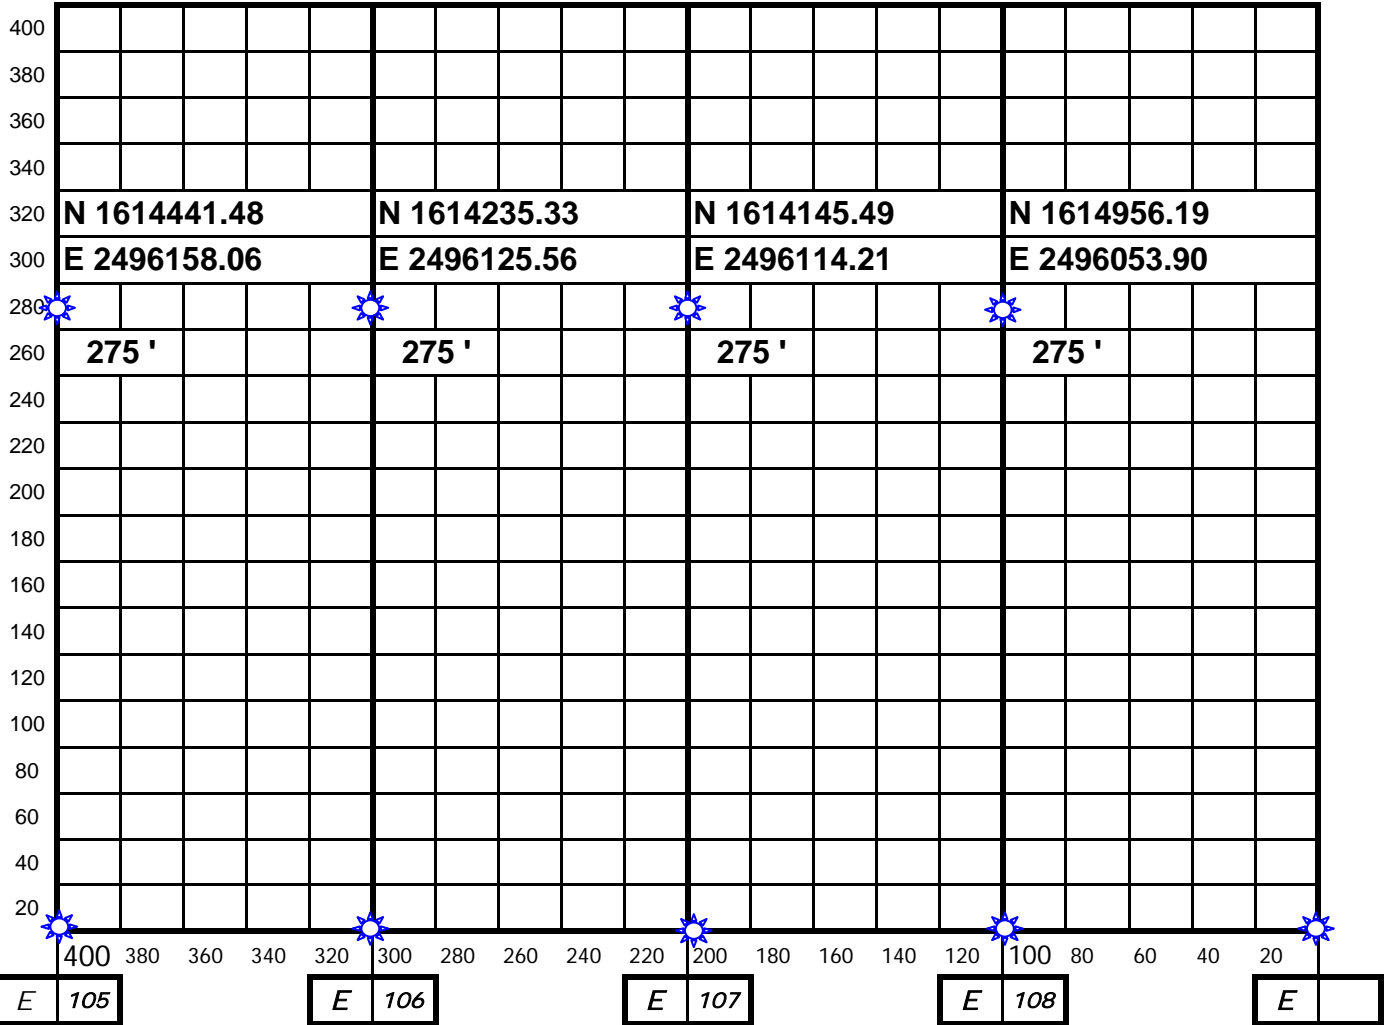


Start	Start	Start	Start	Start
<div style="border: 1px solid black; padding: 2px; width: 40px;">8/18</div>	<div style="border: 1px solid black; padding: 2px; width: 40px;">8/18</div>	<div style="border: 1px solid black; padding: 2px; width: 40px;">8/18</div>	<div style="border: 1px solid black; padding: 2px; width: 40px;">8/18</div>	<div style="border: 1px solid black; padding: 2px; width: 40px;"></div>
Finish	Finish	Finish	Finish	Finish
<div style="border: 1px solid black; padding: 2px; width: 40px;">8/18</div>	<div style="border: 1px solid black; padding: 2px; width: 40px;">8/18</div>	<div style="border: 1px solid black; padding: 2px; width: 40px;">8/18</div>	<div style="border: 1px solid black; padding: 2px; width: 40px;">8/18</div>	<div style="border: 1px solid black; padding: 2px; width: 40px;"></div>
<div style="border: 1px solid black; padding: 2px; width: 40px;"> MEC</div>	<div style="border: 1px solid black; padding: 2px; width: 40px;"> MD</div>	<div style="border: 1px solid black; padding: 2px; width: 40px;"> STAKE #</div>		

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/18/2008	Completion Date:	8/18/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

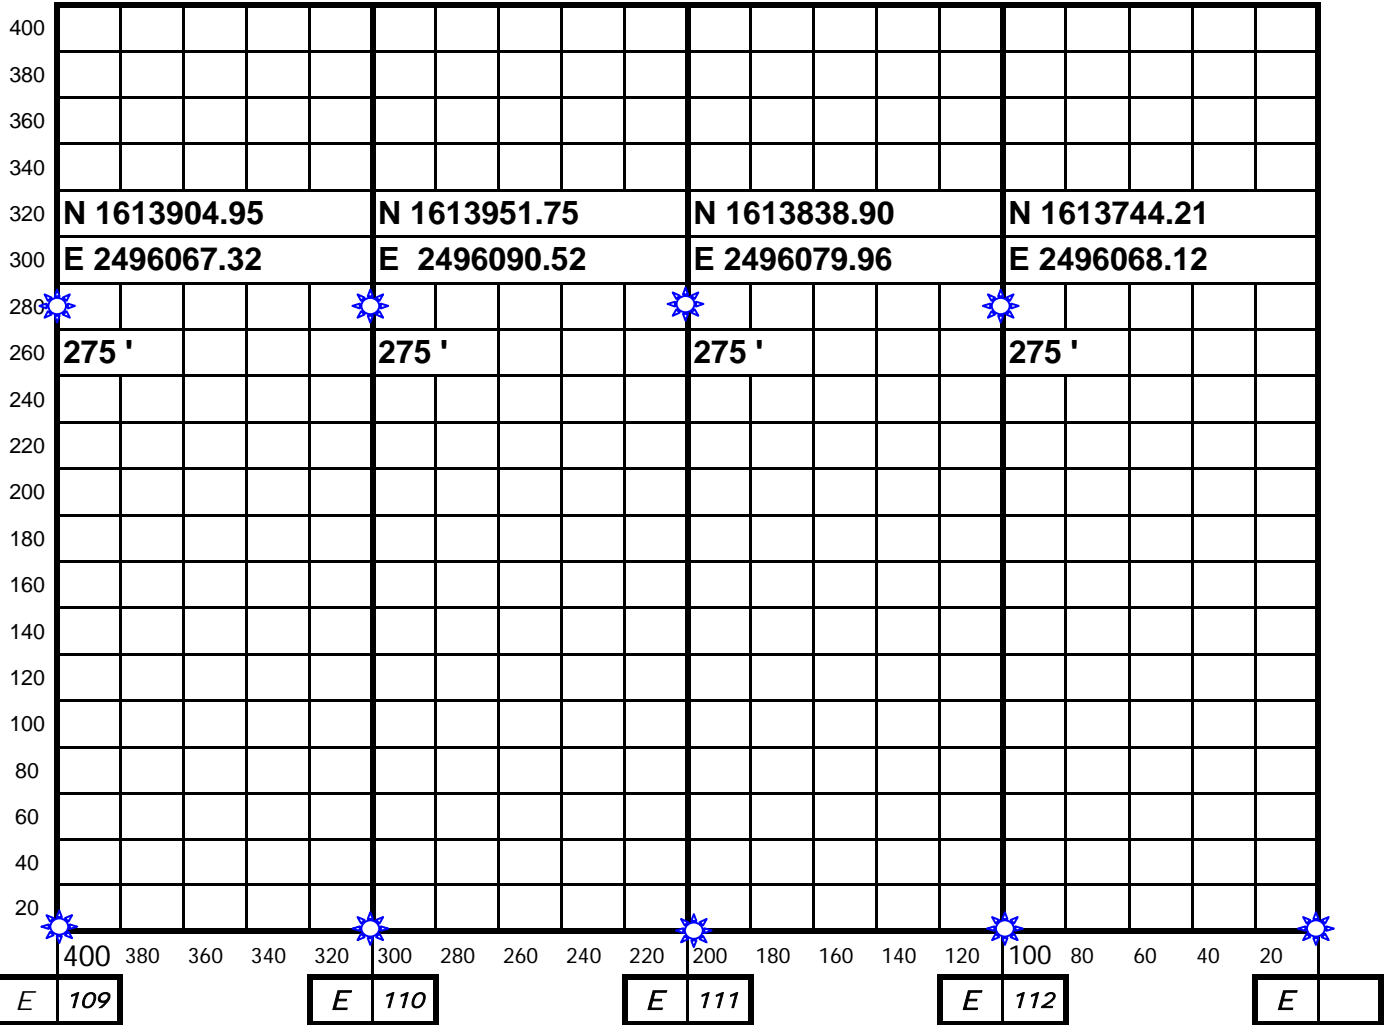


Start	Start	Start	Start	Start	
8/18	8/18	8/18	8/18		
Finish	Finish	Finish	Finish	Finish	
8/18	8/18	8/18	8/18		
	MEC		MD		STAKE #

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/19/2008	Completion Date:	8/19/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

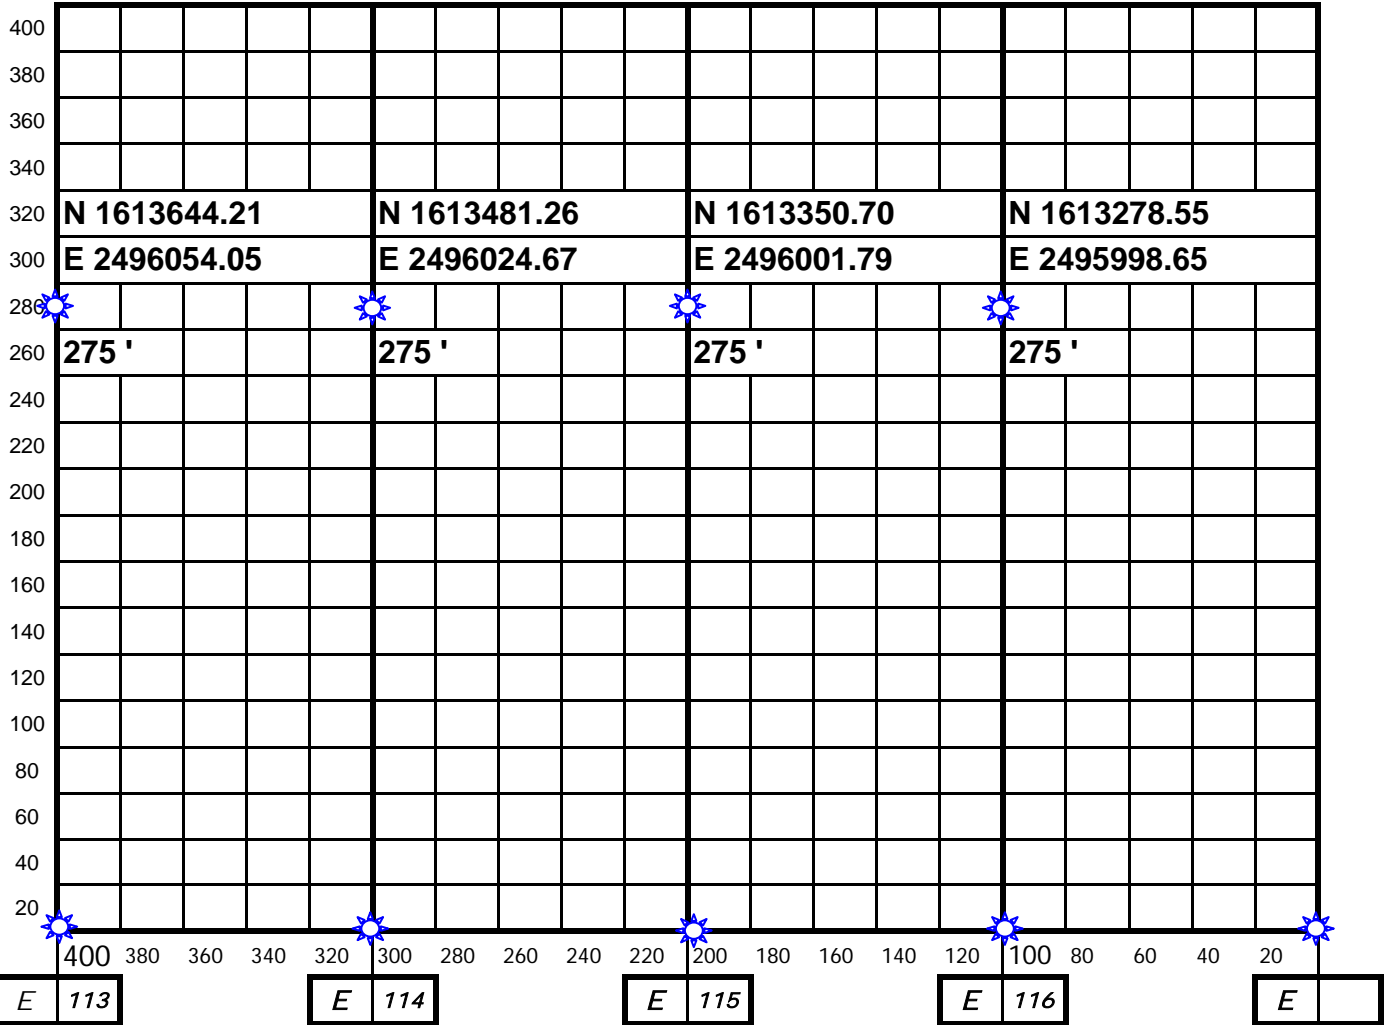


Start	Start	Start	Start	Start	
8/19	8/19	8/19	8/19		
Finish	Finish	Finish	Finish	Finish	
8/19	8/19	8/19	8/19		
	MEC		MD		STAKE #

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/19/2008	Completion Date:	8/19/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

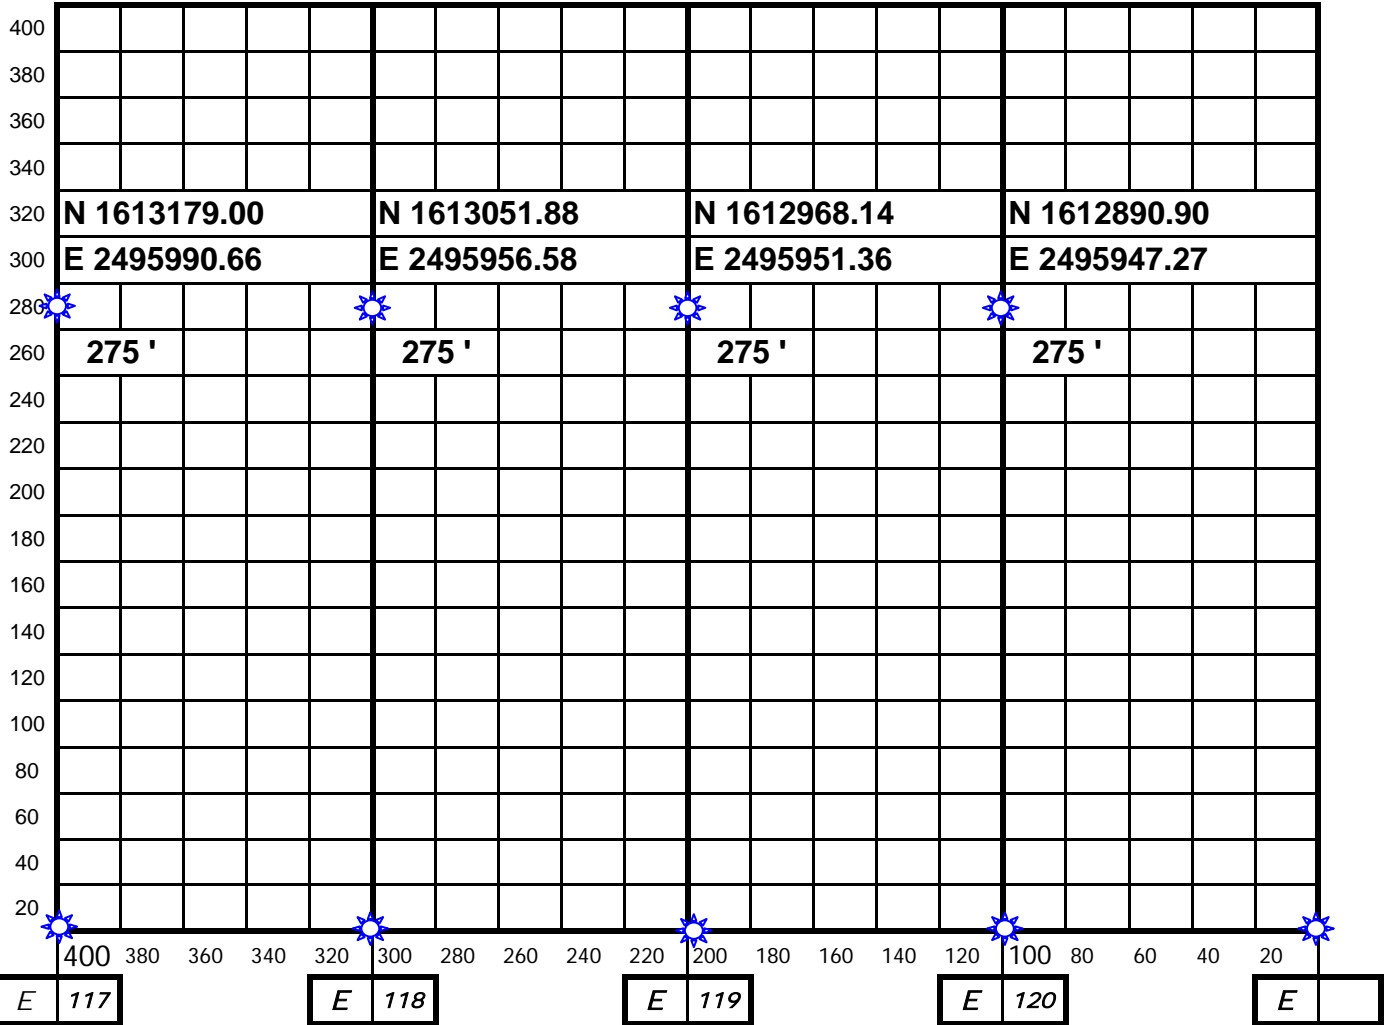


Start	Start	Start	Start	Start	
8/19	8/19	8/19	8/19		
Finish	Finish	Finish	Finish	Finish	
8/19	8/19	8/19	8/19		
	MEC		MD		STAKE #

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/20/2008	Completion Date:	8/20/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

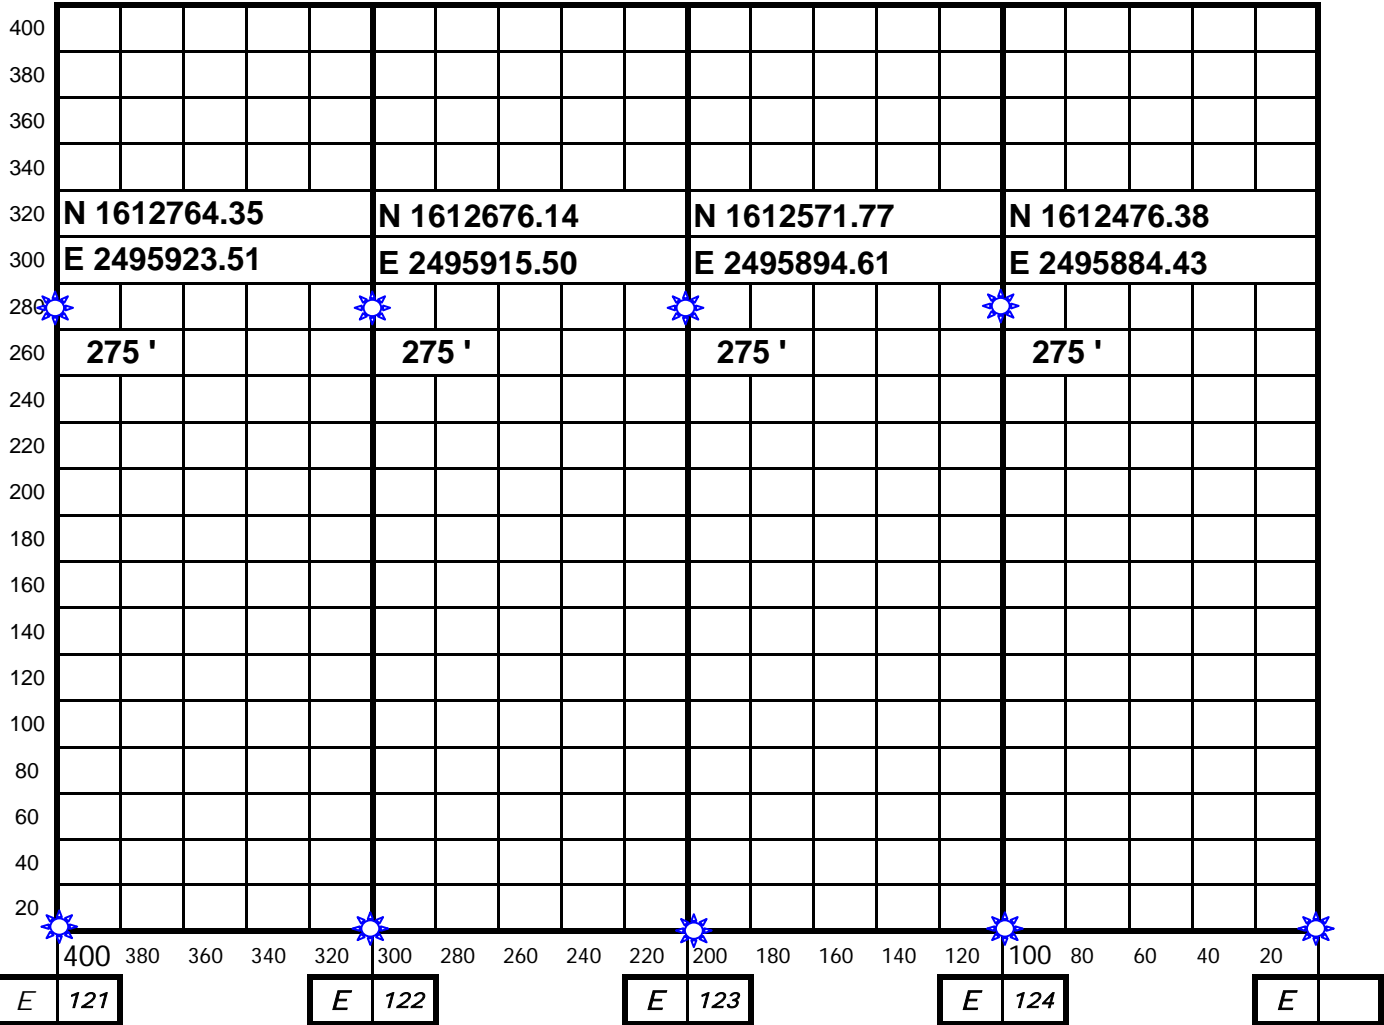


Start	Start	Start	Start	Start
<input type="text" value="8/20"/>	<input type="text" value="8/19"/>	<input type="text" value="8/19"/>	<input type="text" value="8/19"/>	<input type="text"/>
Finish	Finish	Finish	Finish	Finish
<input type="text" value="8/20"/>	<input type="text" value="8/19"/>	<input type="text" value="8/19"/>	<input type="text" value="8/19"/>	<input type="text"/>
MEC	MD	STAKE #		

Comments. Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/19/2008	Completion Date:	8/19/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

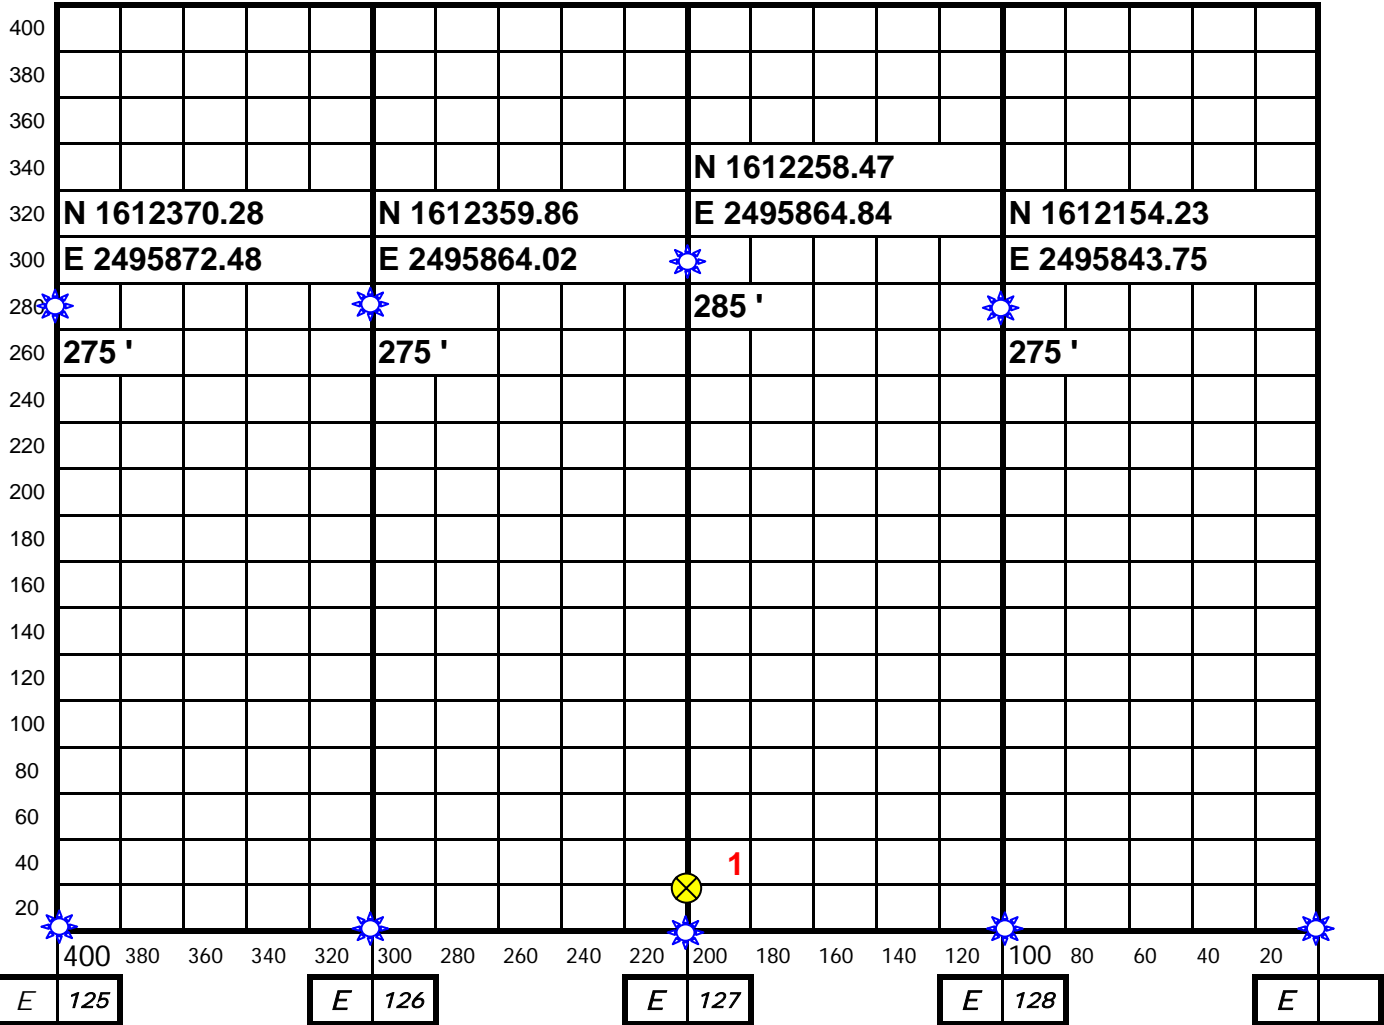

Start	Start	Start	Start	Start
<input type="text" value="8/19"/>	<input type="text" value="8/19"/>	<input type="text" value="8/19"/>	<input type="text" value="8/19"/>	<input type="text"/>
Finish	Finish	Finish	Finish	Finish
<input type="text" value="8/19"/>	<input type="text" value="8/19"/>	<input type="text" value="8/19"/>	<input type="text" value="8/19"/>	<input type="text"/>
MEC		MD		STAKE #

Comments.Notes:


75 mm shell casing

Anomalies

#	ID	Northing	Easting	Comments
1	E 127	1612258.47	2495864.84	Empty 75mm shell casing
2				
3				
4				
5				
6				
7				
8				
9				
10				
11				
12				
13				
14				
15				
16				
17				
18				
19				
20				
21				
22				
23				
24				
25				
26				
27				
28				
29				
30				
31				
32				
33				
34				
35				
36				
37				
38				
39				
40				
41				
42				
43				
44				

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/19/2008	Completion Date:	8/19/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

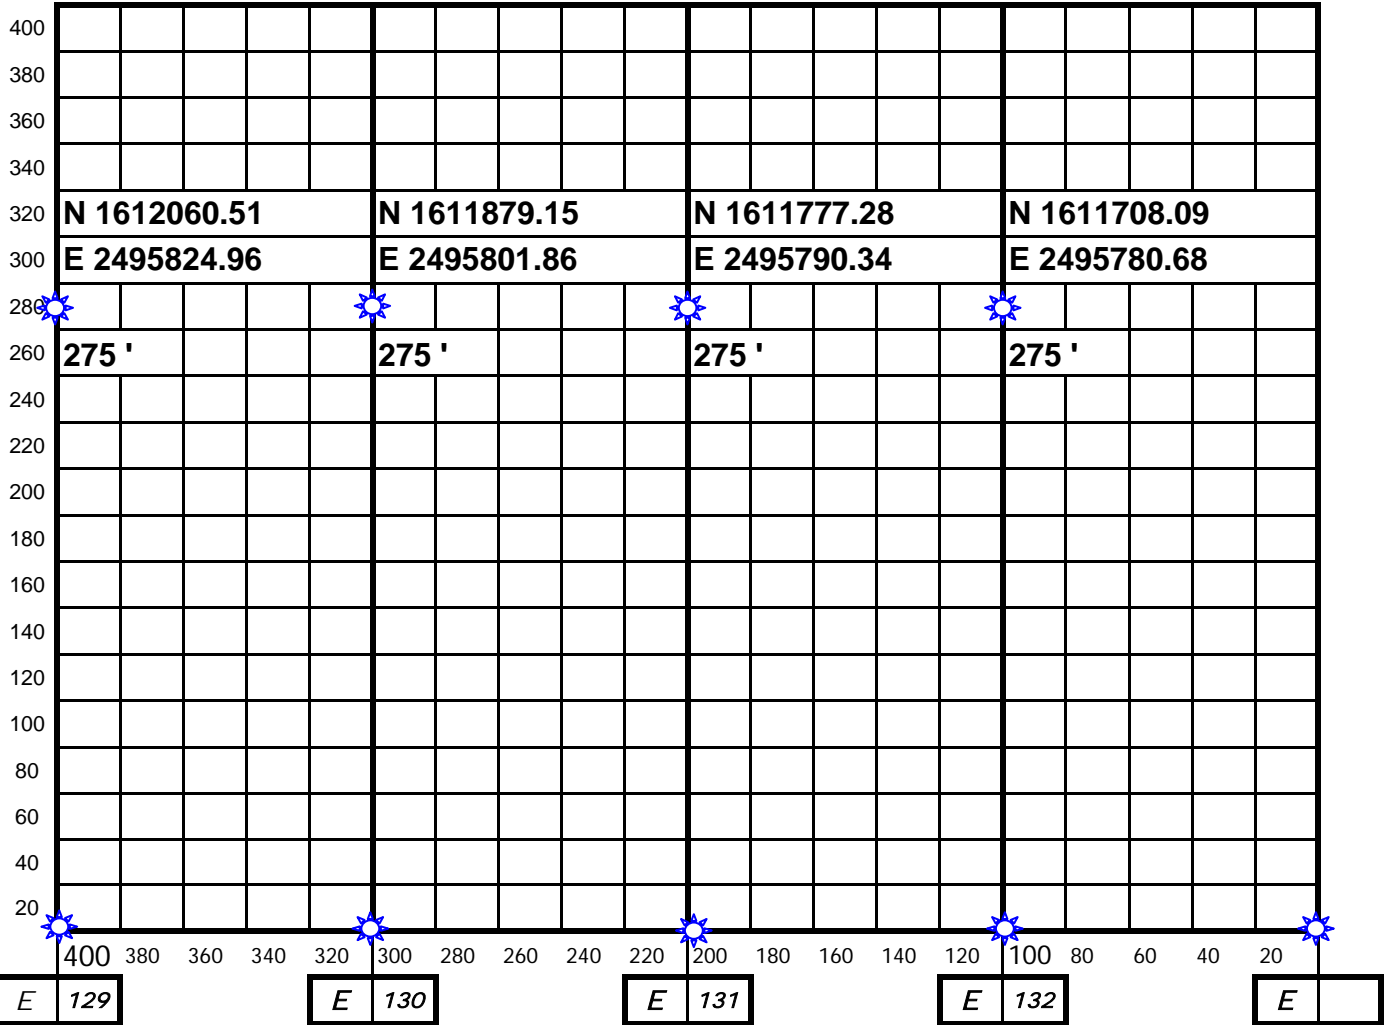


Start	Start	Start	Start	Start	
<input style="width: 80%;" type="text"/>	<input style="width: 80%;" type="text" value="8/19"/>	<input style="width: 80%;" type="text" value="8/19"/>	<input style="width: 80%;" type="text" value="8/19"/>	<input style="width: 80%;" type="text"/>	
Finish	Finish	Finish	Finish	Finish	
<input style="width: 80%;" type="text"/>	<input style="width: 80%;" type="text" value="8/19"/>	<input style="width: 80%;" type="text" value="8/19"/>	<input style="width: 80%;" type="text" value="8/19"/>	<input style="width: 80%;" type="text"/>	
	MEC		MD		STAKE #

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/19/2008	Completion Date:	8/19/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

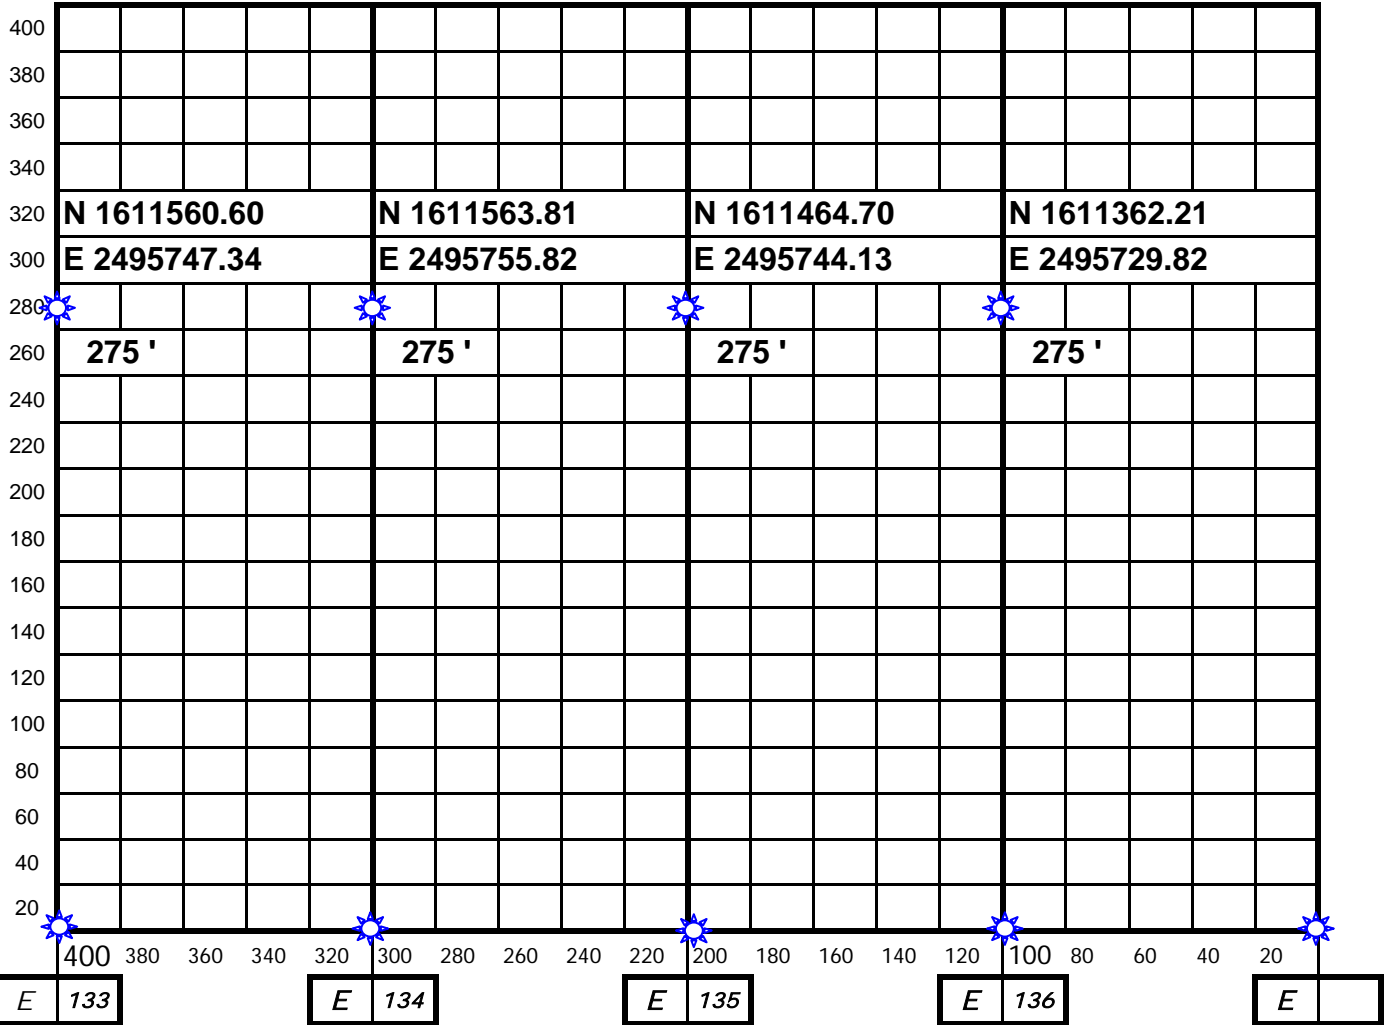


Start	Start	Start	Start	Start
8/19	8/19	8/19	8/19	
Finish	Finish	Finish	Finish	Finish
8/19	8/19	8/19	8/19	
MEC	MD	STAKE #		

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/20/2008	Completion Date:	8/20/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

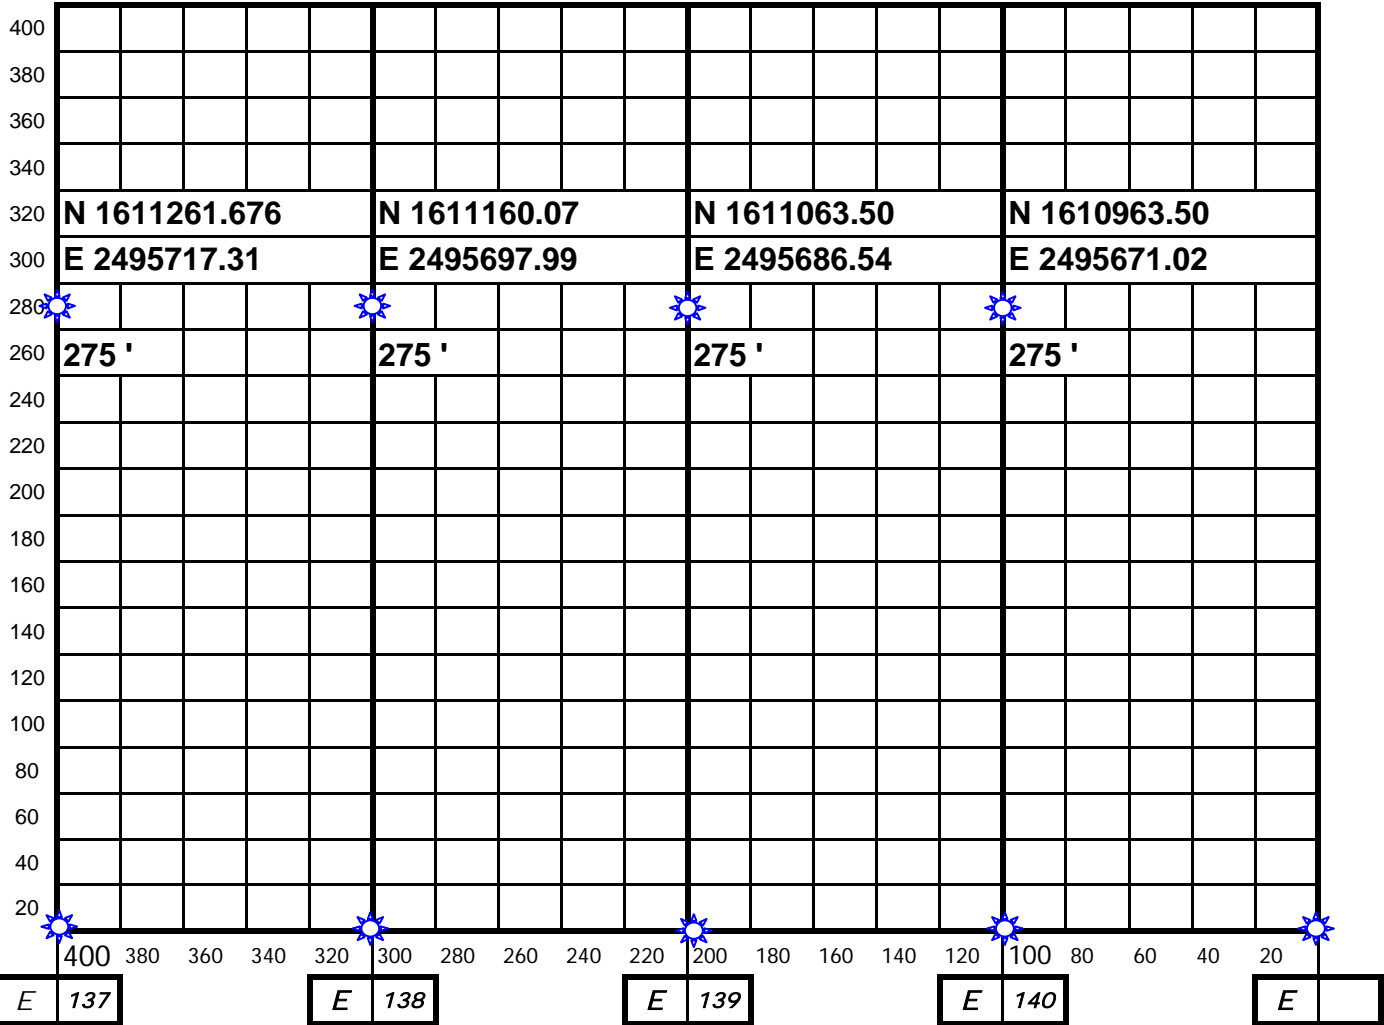


Start	Start	Start	Start	Start	
8/20	8/20	8/20	8/20		
Finish	Finish	Finish	Finish	Finish	
8/20	8/20	8/20	8/20		
	MEC		MD		STAKE #

Comments.Notes:

E-138 and E-139 possible EM-61 grids

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/20/2008	Completion Date:	8/20/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

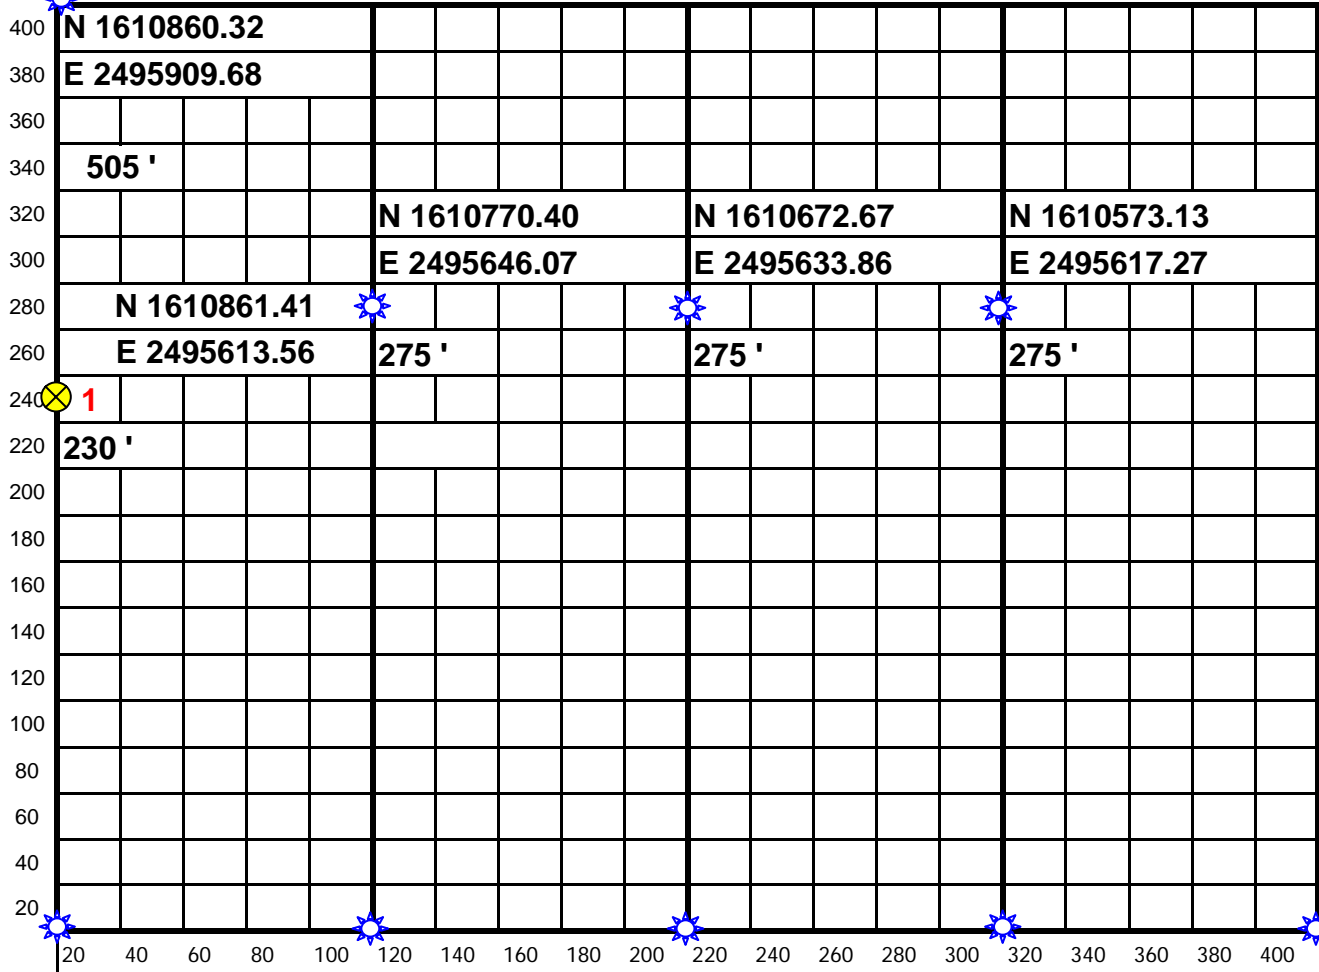

<i>E</i> 141	<i>E</i> 142	<i>E</i> 143	<i>E</i> 144	<i>E</i>
--------------	--------------	--------------	--------------	----------

Start	Start	Start	Start	Start
8/20	8/20	8/20	8/20	
Finish	Finish	Finish	Finish	Finish
8/20	8/20	8/20	8/20	
	MEC		MD	
				STAKE #


Comments.Notes:

Anomalies

#	ID	Northing	Easting	Comments
1	E-141	1620861.41	2495613.56	Frag
2				
3				
4				
5				
6				
7				
8				
9				
10				
11				
12				
13				
14				
15				
16				
17				
18				
19				
20				
21				
22				
23				
24				
25				
26				
27				
28				
29				
30				
31				
32				
33				
34				
35				
36				
37				
38				
39				
40				
41				
42				

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/20/2008	Completion Date:	8/20/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

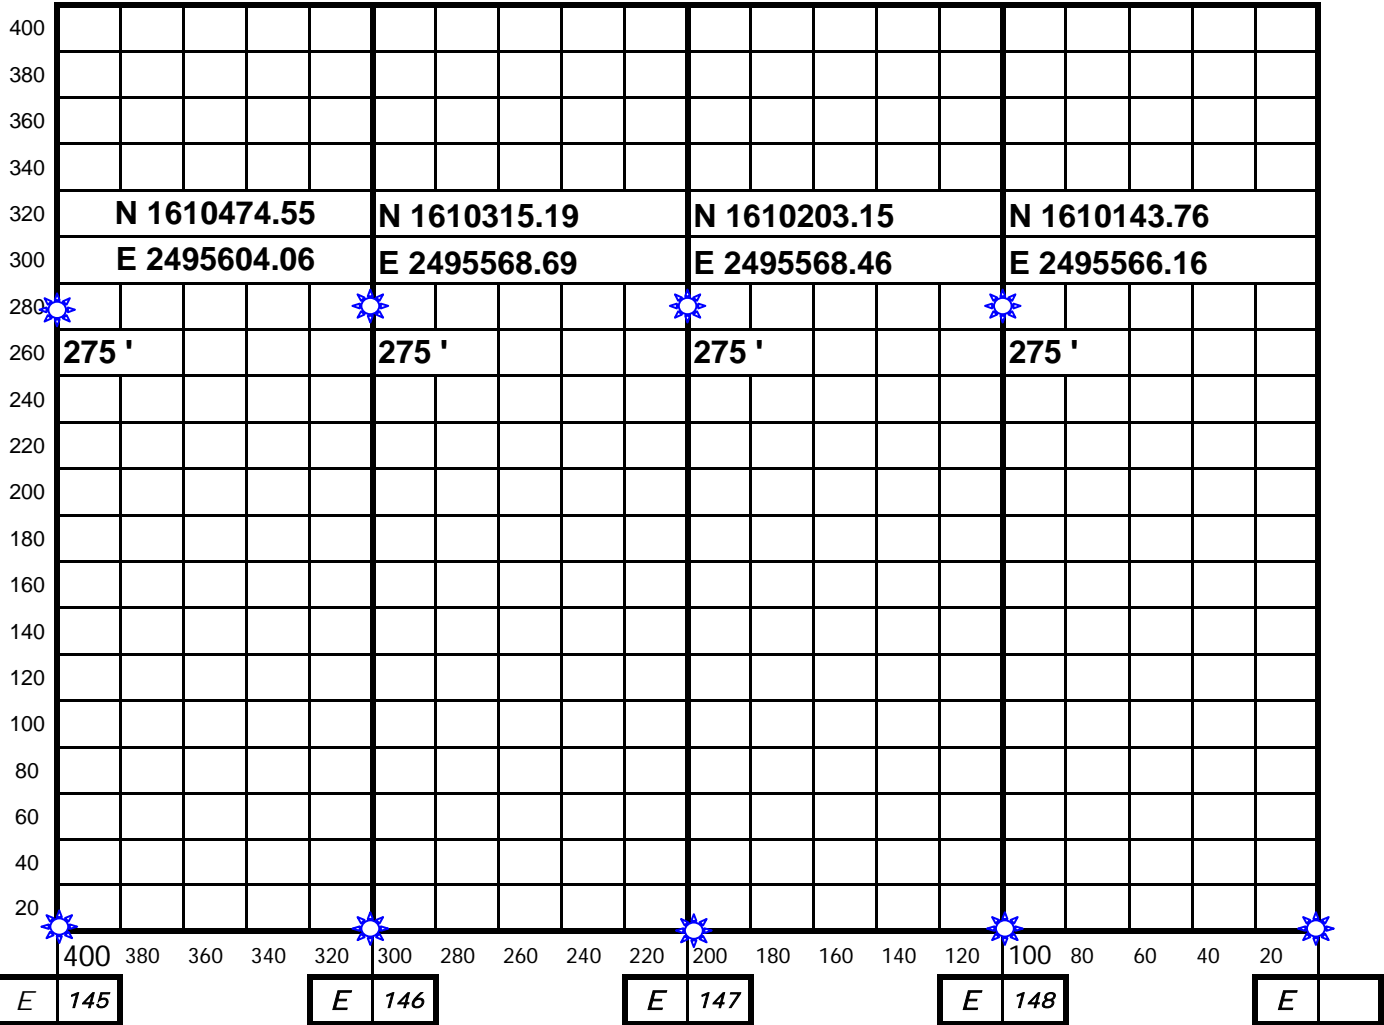


Start	Start	Start	Start	Start
<input type="text" value="8/20"/>	<input type="text" value="8/20"/>	<input type="text" value="8/20"/>	<input type="text" value="8/20"/>	<input type="text"/>
Finish	Finish	Finish	Finish	Finish
<input type="text" value="8/20"/>	<input type="text" value="8/20"/>	<input type="text" value="8/20"/>	<input type="text" value="8/20"/>	<input type="text"/>
MEC	MD	STAKE #		

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/20/2008	Completion Date:	8/20/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

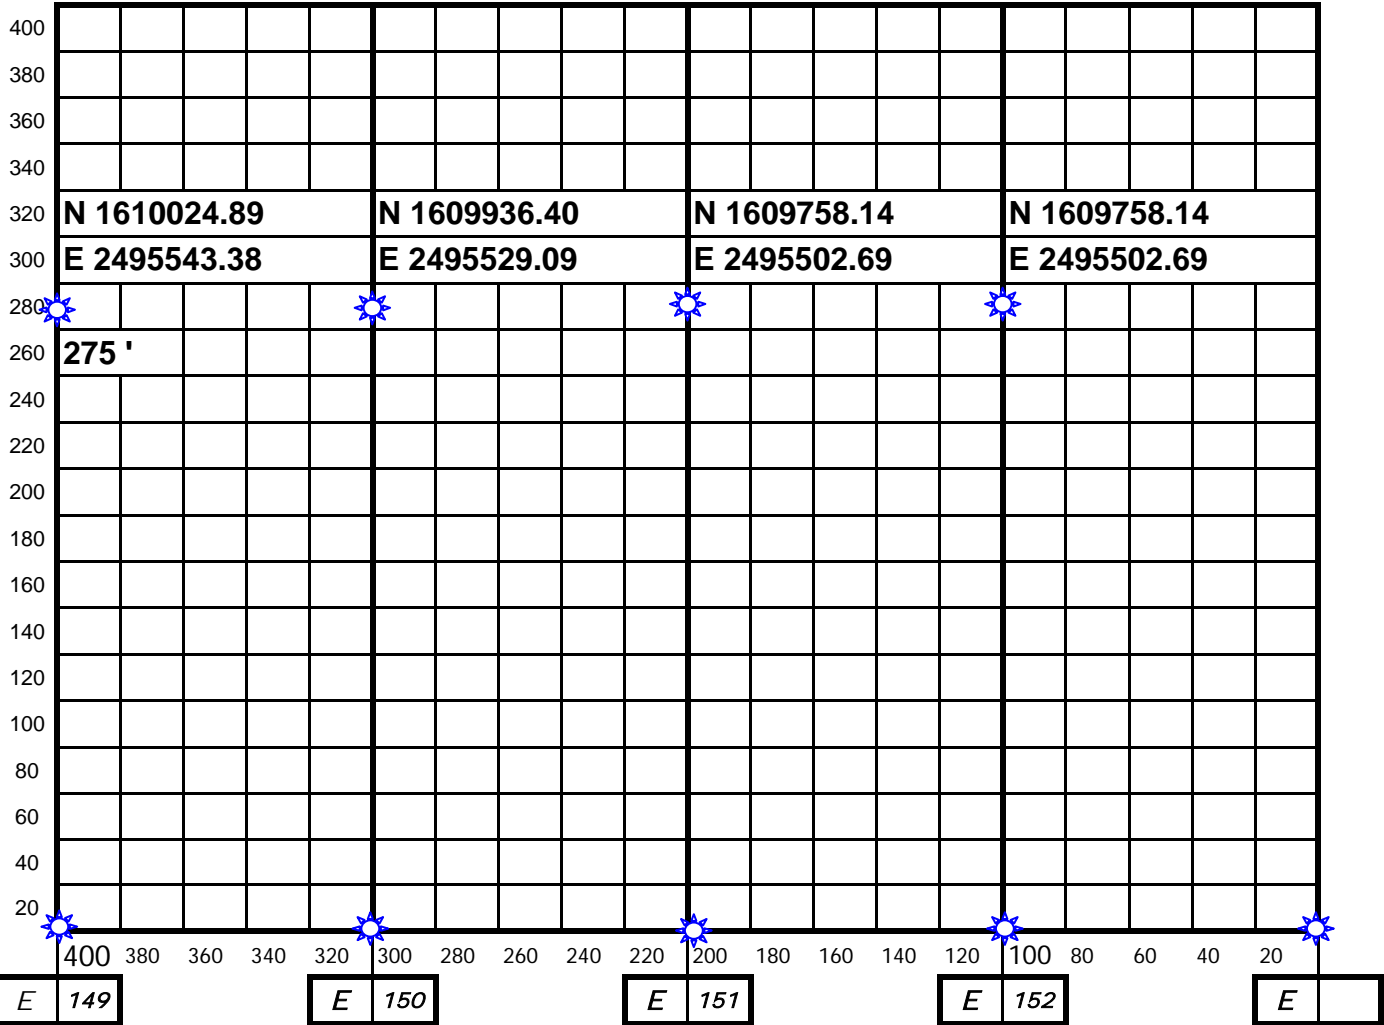


Start	Start	Start	Start	Start
<input type="text" value="8/20"/>	<input type="text" value="8/20"/>	<input type="text" value="8/20"/>	<input type="text" value="8/20"/>	<input type="text"/>
Finish	Finish	Finish	Finish	Finish
<input type="text" value="8/20"/>	<input type="text" value="8/20"/>	<input type="text" value="8/20"/>	<input type="text" value="8/20"/>	<input type="text"/>
MEC	MD	STAKE #		

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	9/11/2008	Completion Date:	9/11/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

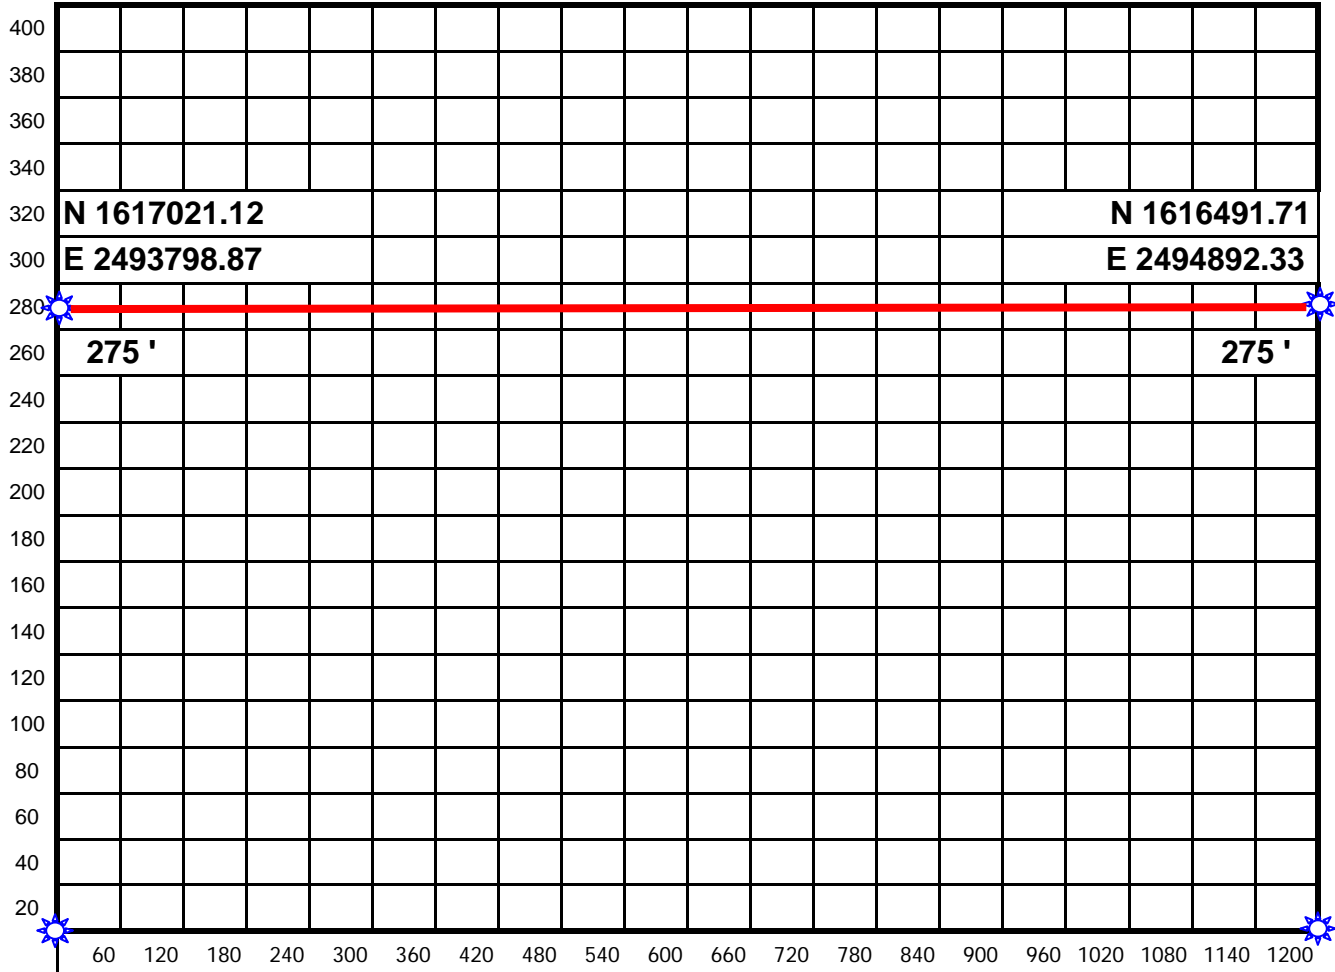

E 64

E 76

Start	Start
9/11	9/11
Finish	Finish
9/11	9/11

MEC

MD


STAKE #

Comments.Notes:

Step Out Transect Of 1200 feet per Work Plan

PIKA Transect Sheets

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	9/17/2008	Completion Date:	9/17/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

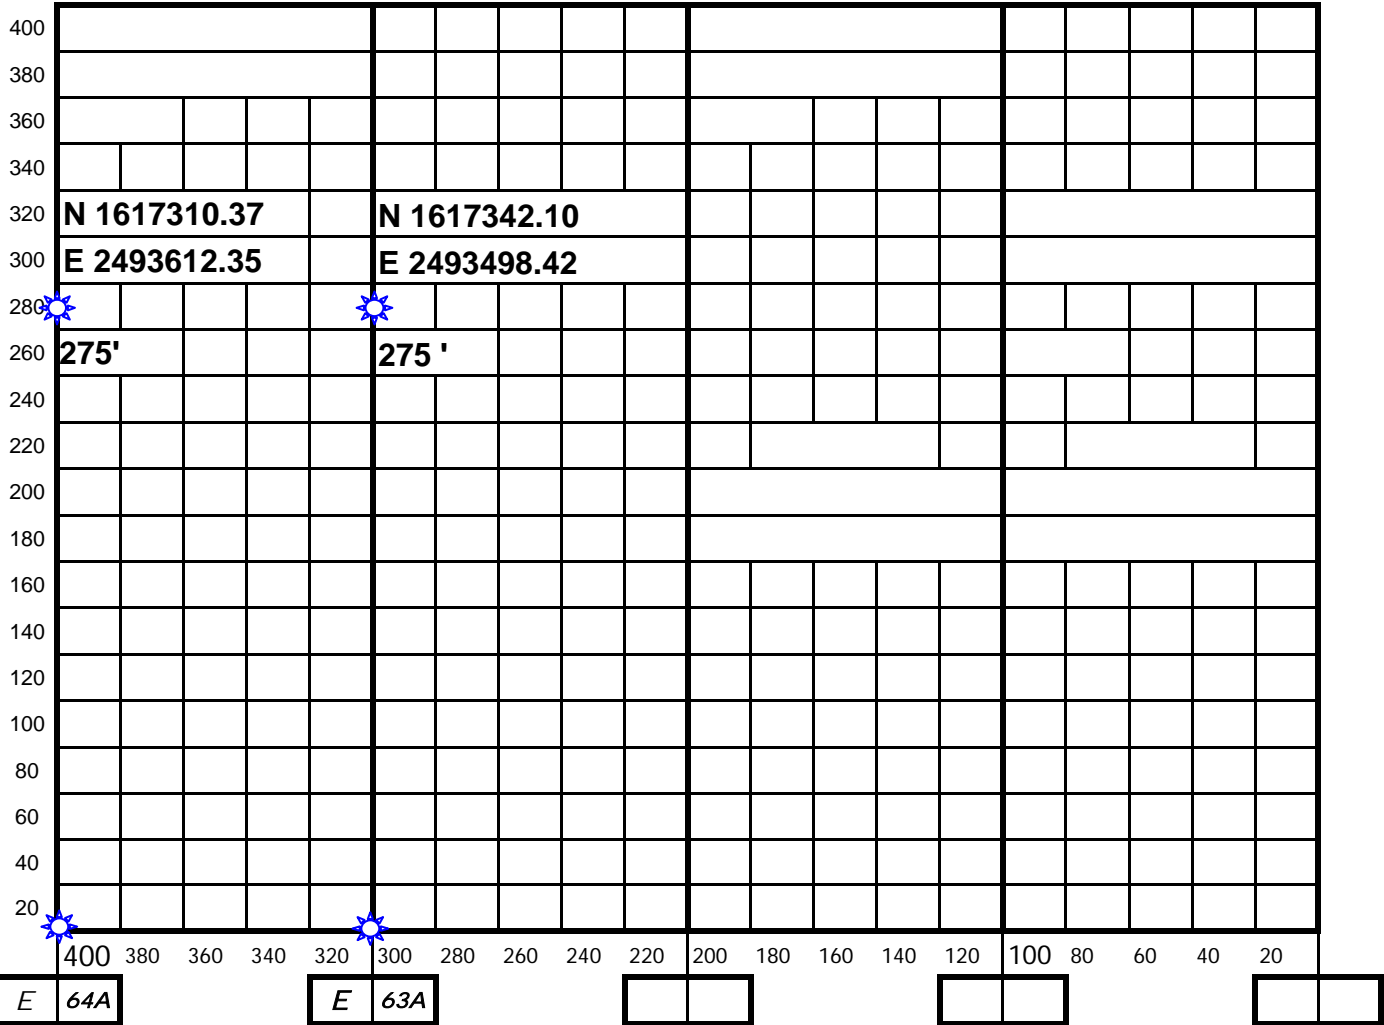


Start	Start	Start	Start	Start
9/17	9/17			
Finish	Finish	Finish	Finish	Finish
9/17	9/17			
MEC	MD	STAKE #		

Comments.Notes:

"A" denotes transect started 275' from original boundary to account for MD located along original boundary.

PIKA Transect Sheets

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	9/17/2008	Completion Date:	9/17/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

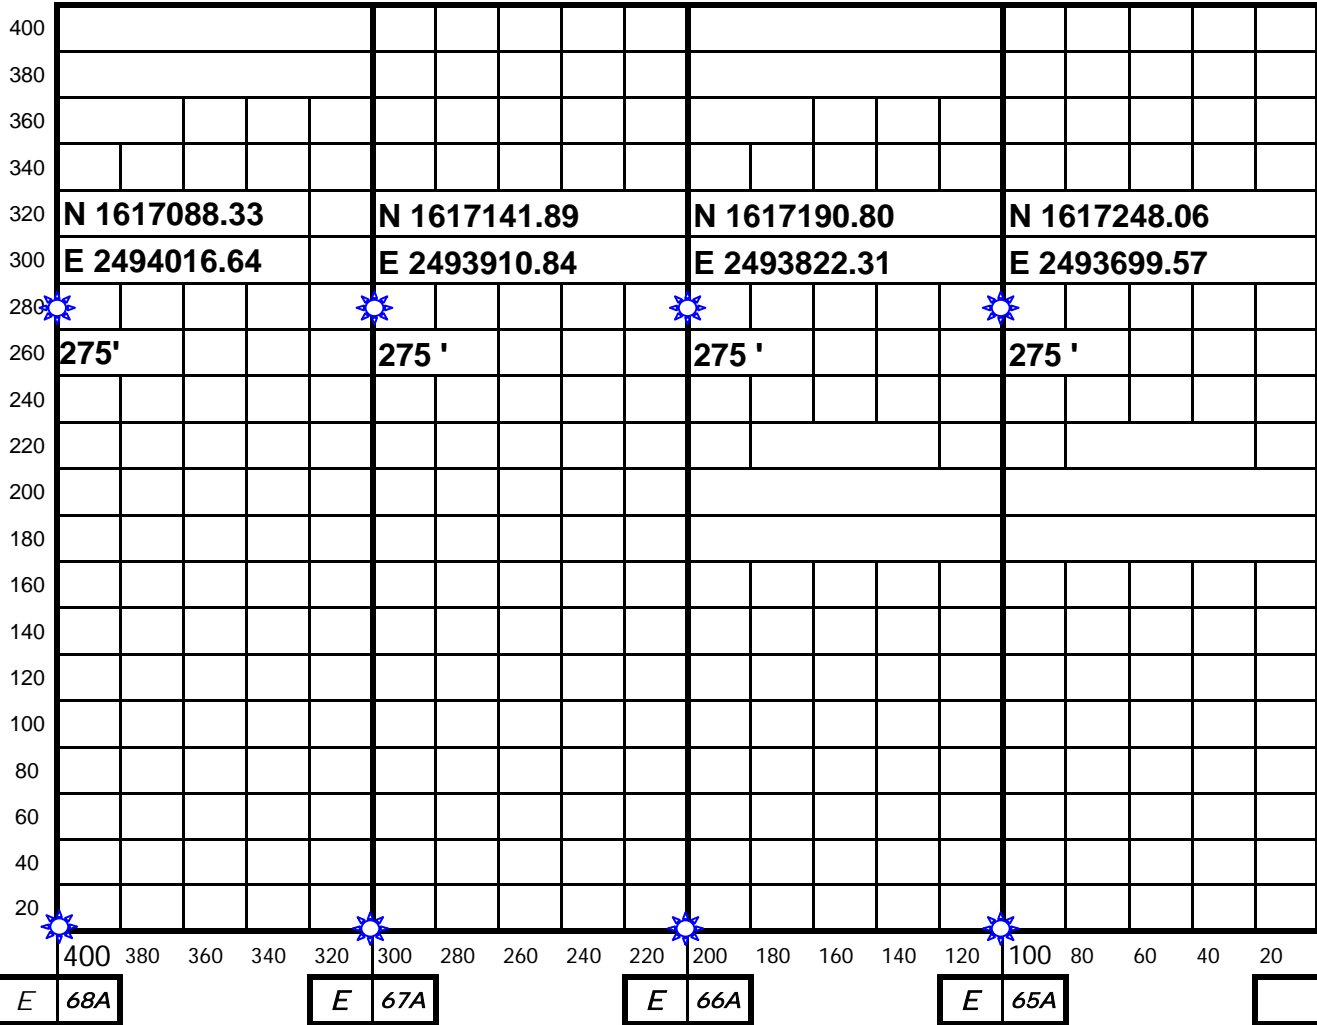


Start	Start	Start	Start	Start
<input type="text" value="9/17"/>	<input type="text" value="9/17"/>	<input type="text" value="9/17"/>	<input type="text" value="9/17"/>	<input type="text"/>
Finish	Finish	Finish	Finish	Finish
<input type="text" value="9/17"/>	<input type="text" value="9/17"/>	<input type="text" value="9/17"/>	<input type="text" value="9/17"/>	<input type="text"/>
MEC	MD	STAKE #		

Comments.Notes:

"A" denotes transect started 275' from original boundary to account for MD located along original boundary.

PIKA Transect Sheets

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	9/17/2008	Completion Date:	9/17/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

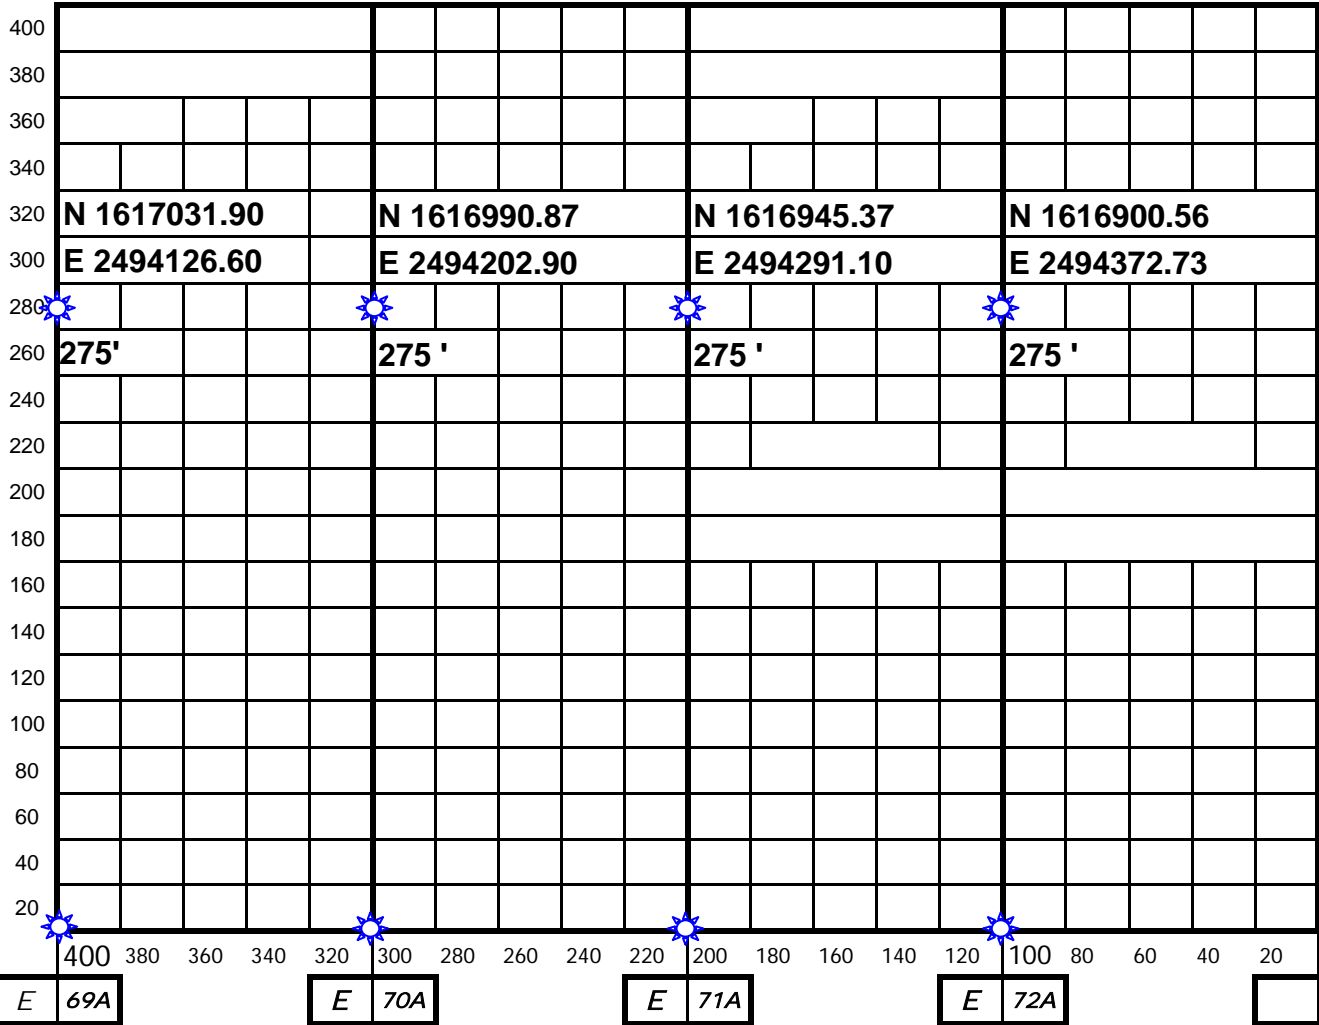


Comments.Notes:

"A" denotes transect started 275' from original boundary to account for MD located along original boundary.

PIKA Transect Sheets

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	9/17/2008	Completion Date:	9/17/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

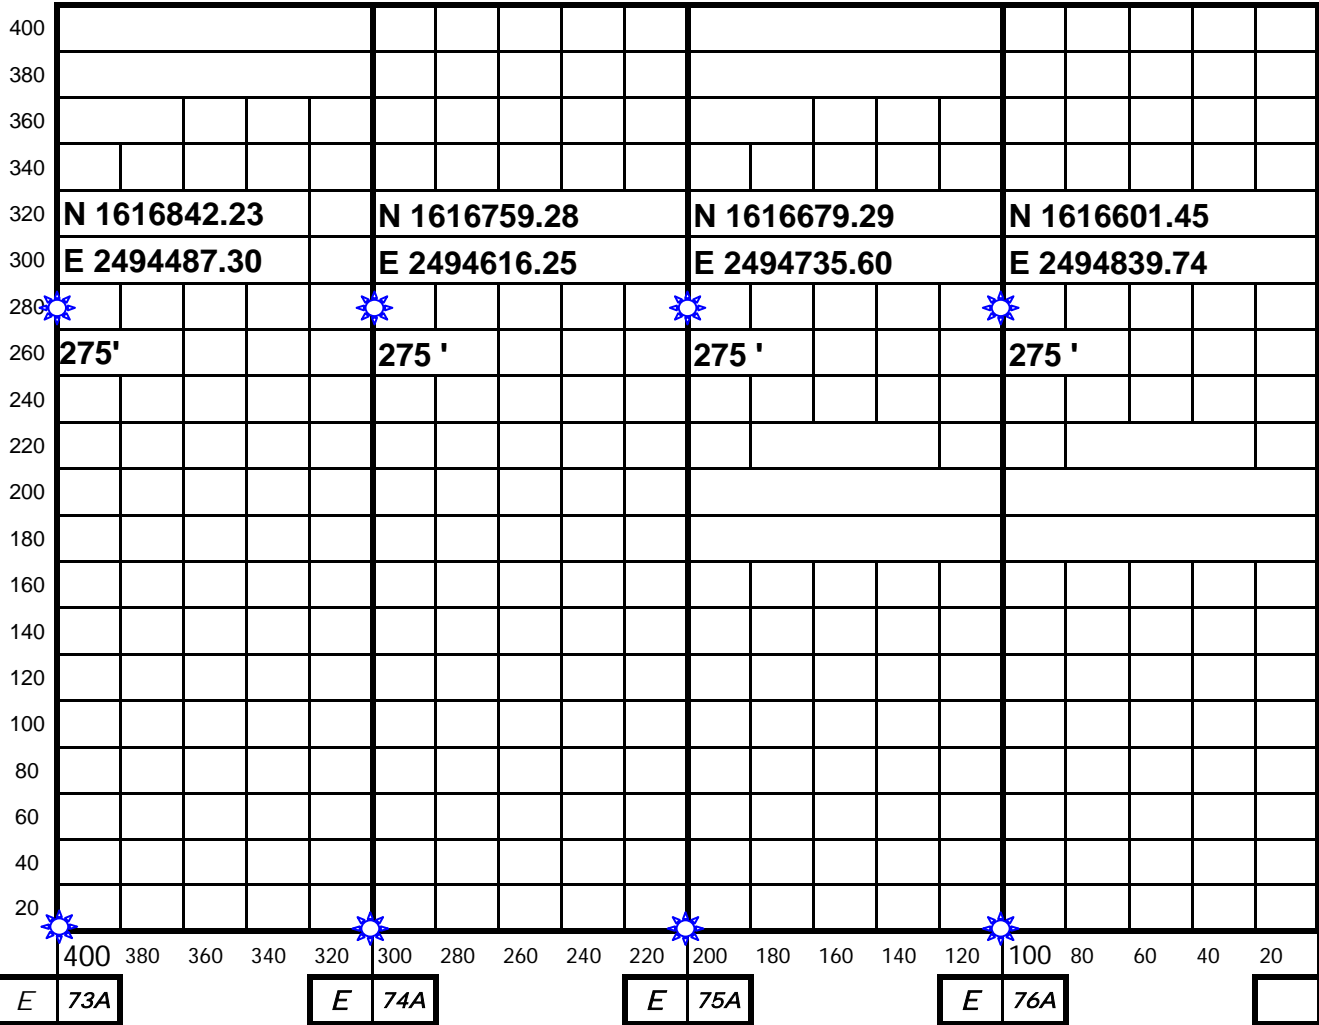


Start	Start	Start	Start	Start
<input type="text" value="9/17"/>	<input type="text" value="9/17"/>	<input type="text" value="9/17"/>	<input type="text" value="9/17"/>	<input type="text"/>
Finish	Finish	Finish	Finish	Finish
<input type="text" value="9/17"/>	<input type="text" value="9/17"/>	<input type="text" value="9/17"/>	<input type="text" value="9/17"/>	<input type="text"/>
MEC	MD	STAKE #		

Comments.Notes:

"A" denotes transect started 275' from original boundary to account for MD located along original boundary.

PIKA Transect Sheets

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	9/17/2008	Completion Date:	9/17/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

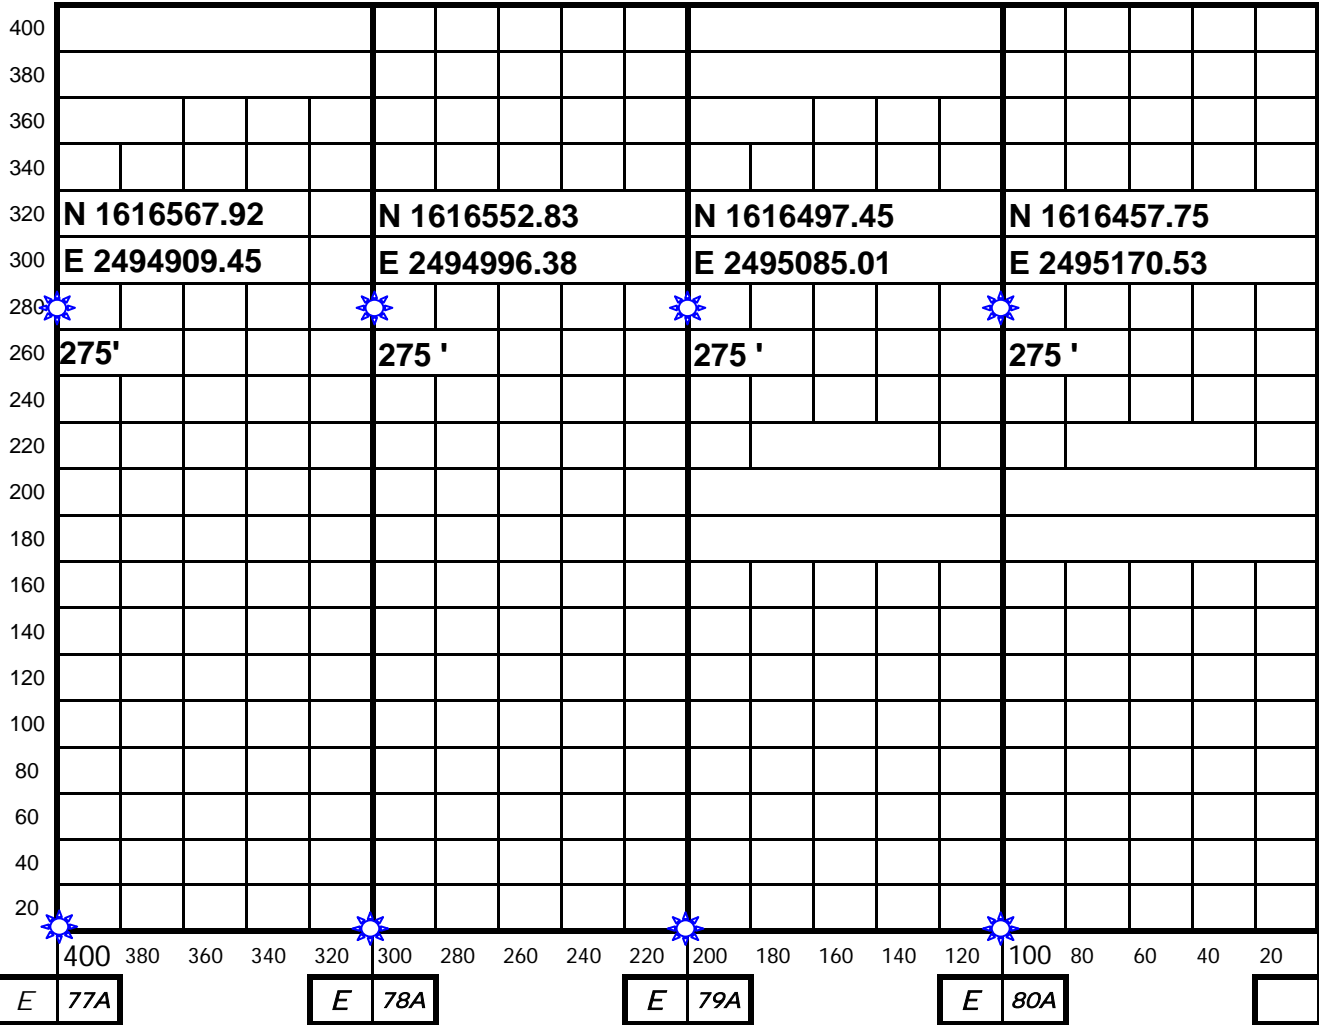


Start	Start	Start	Start	Start
<input type="text" value="9/17"/>	<input type="text" value="9/17"/>	<input type="text" value="9/17"/>	<input type="text" value="9/17"/>	<input type="text"/>
Finish	Finish	Finish	Finish	Finish
<input type="text" value="9/17"/>	<input type="text" value="9/17"/>	<input type="text" value="9/17"/>	<input type="text" value="9/17"/>	<input type="text"/>
MEC	MD	STAKE #		

Comments.Notes:

"A" denotes transect started 275' from original boundary to account for MD located along original boundary.

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/2/2009	Completion Date:	4/16/2009
QC Date:		QA Date	

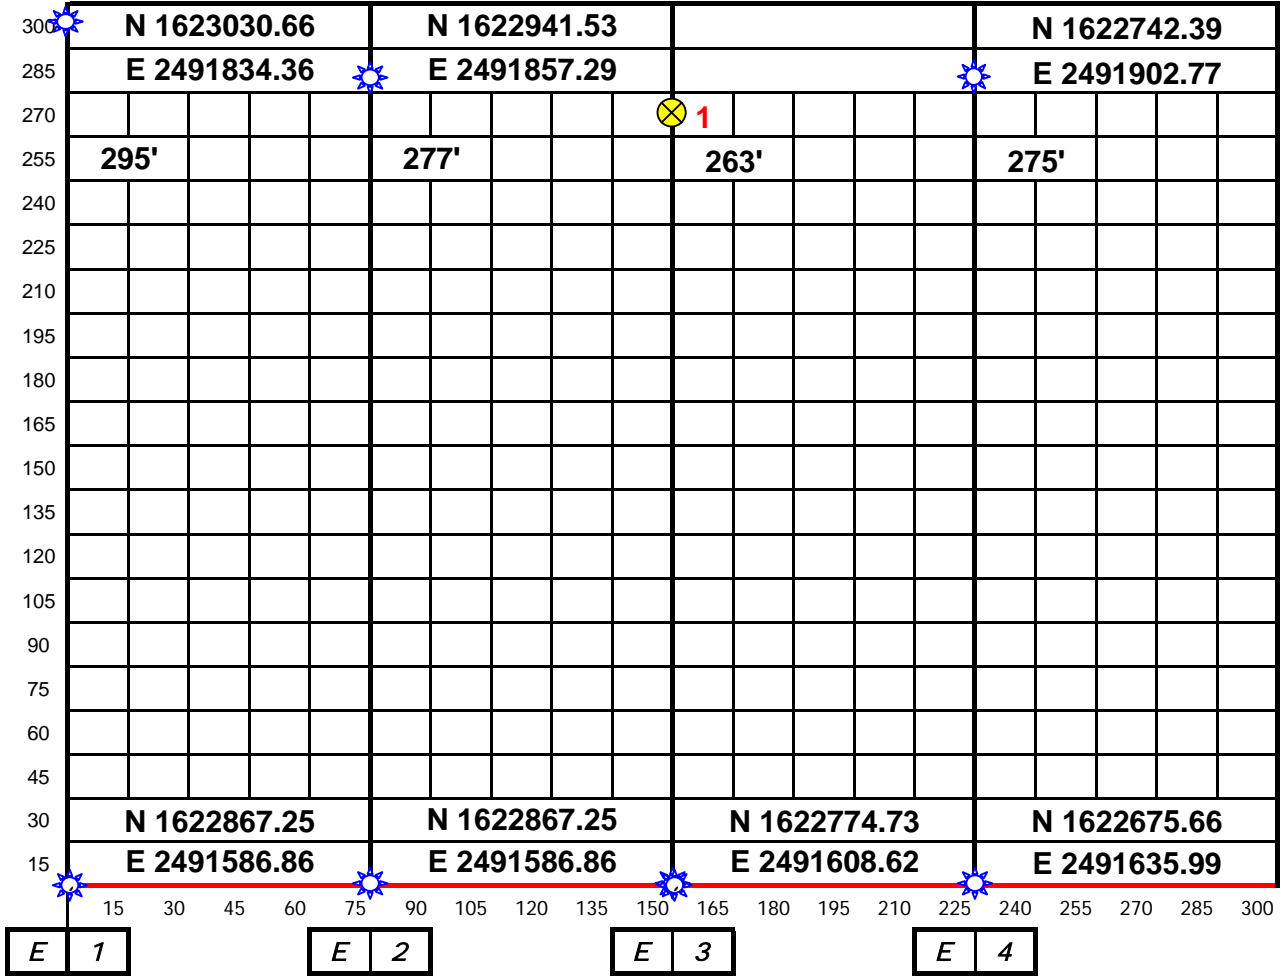


Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/2</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/2</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/2</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/16</div>
Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/2</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/2</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/2</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/16</div>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

1 Fragmentation located at 263 feet @ 30 degrees from E3

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/13/2009	Completion Date:	4/13/2009
QC Date:		QA Date	

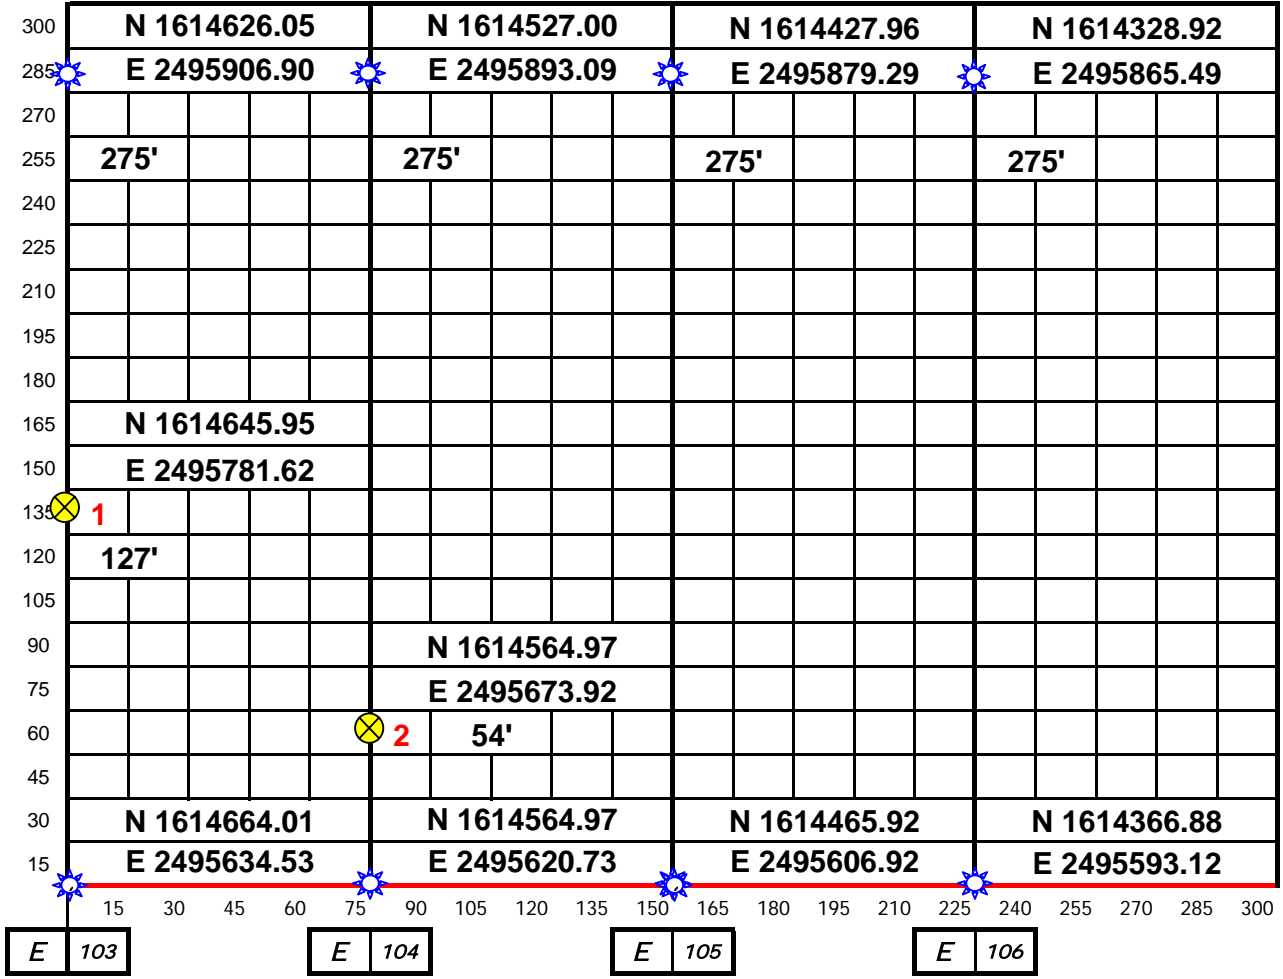


Start <input type="text" value="4/13"/>	Start <input type="text" value="4/13"/>	Start <input type="text" value="4/13"/>	Start <input type="text" value="4/13"/>
Finish <input type="text" value="4/13"/>	Finish <input type="text" value="4/13"/>	Finish <input type="text" value="4/13"/>	Finish <input type="text" value="4/13"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:
1,2 Fragmentation

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/13/2009	Completion Date:	4/13/2009
QC Date:		QA Date	

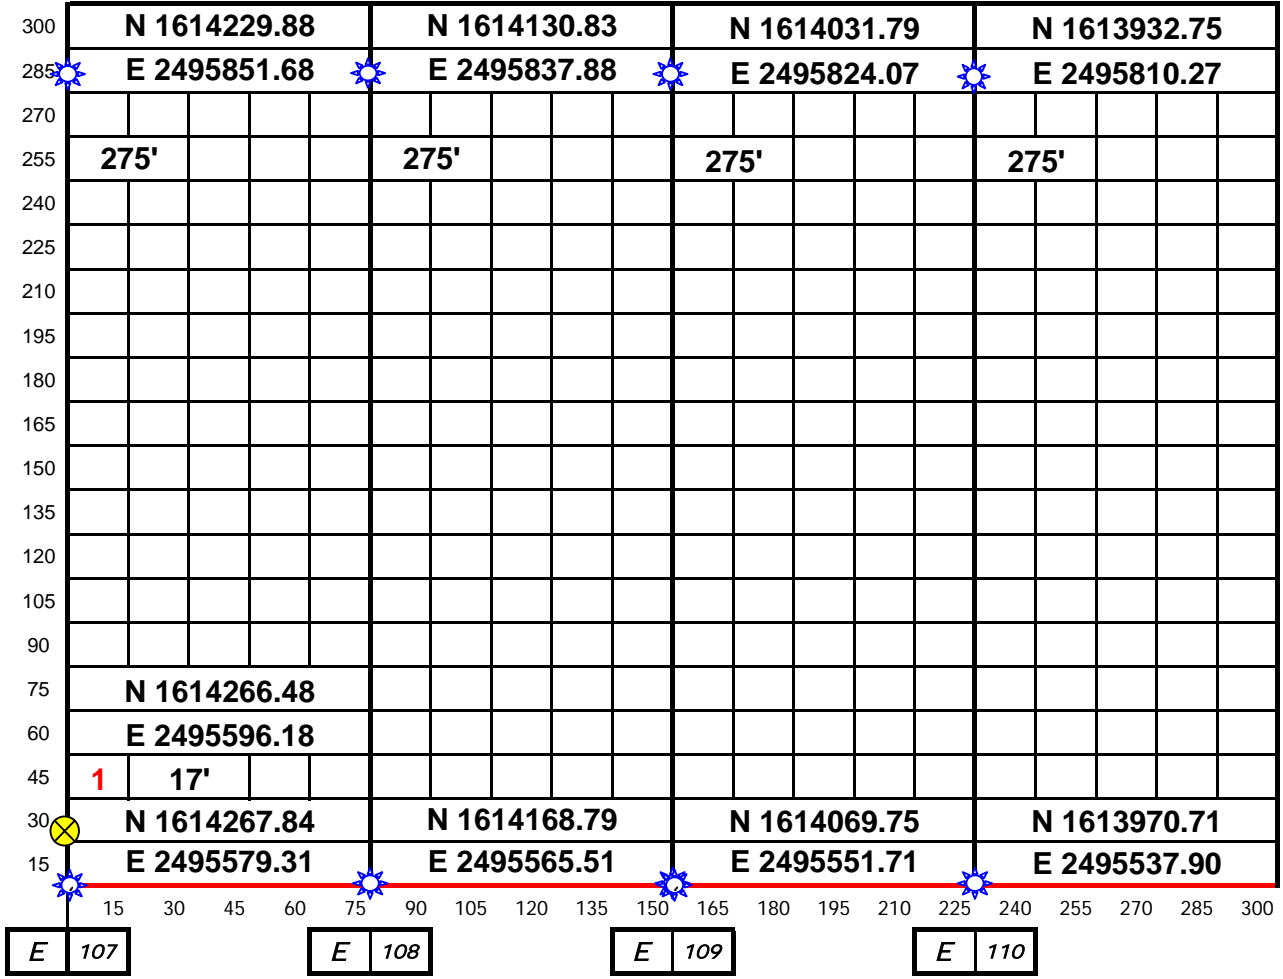


Start <input type="text" value="4/13"/>	Start <input type="text" value="4/13"/>	Start <input type="text" value="4/13"/>	Start <input type="text" value="4/13"/>
Finish <input type="text" value="4/13"/>	Finish <input type="text" value="4/13"/>	Finish <input type="text" value="4/13"/>	Finish <input type="text" value="4/13"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

1 Fragmentation

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/13/2009	Completion Date:	4/13/2009
QC Date:		QA Date	

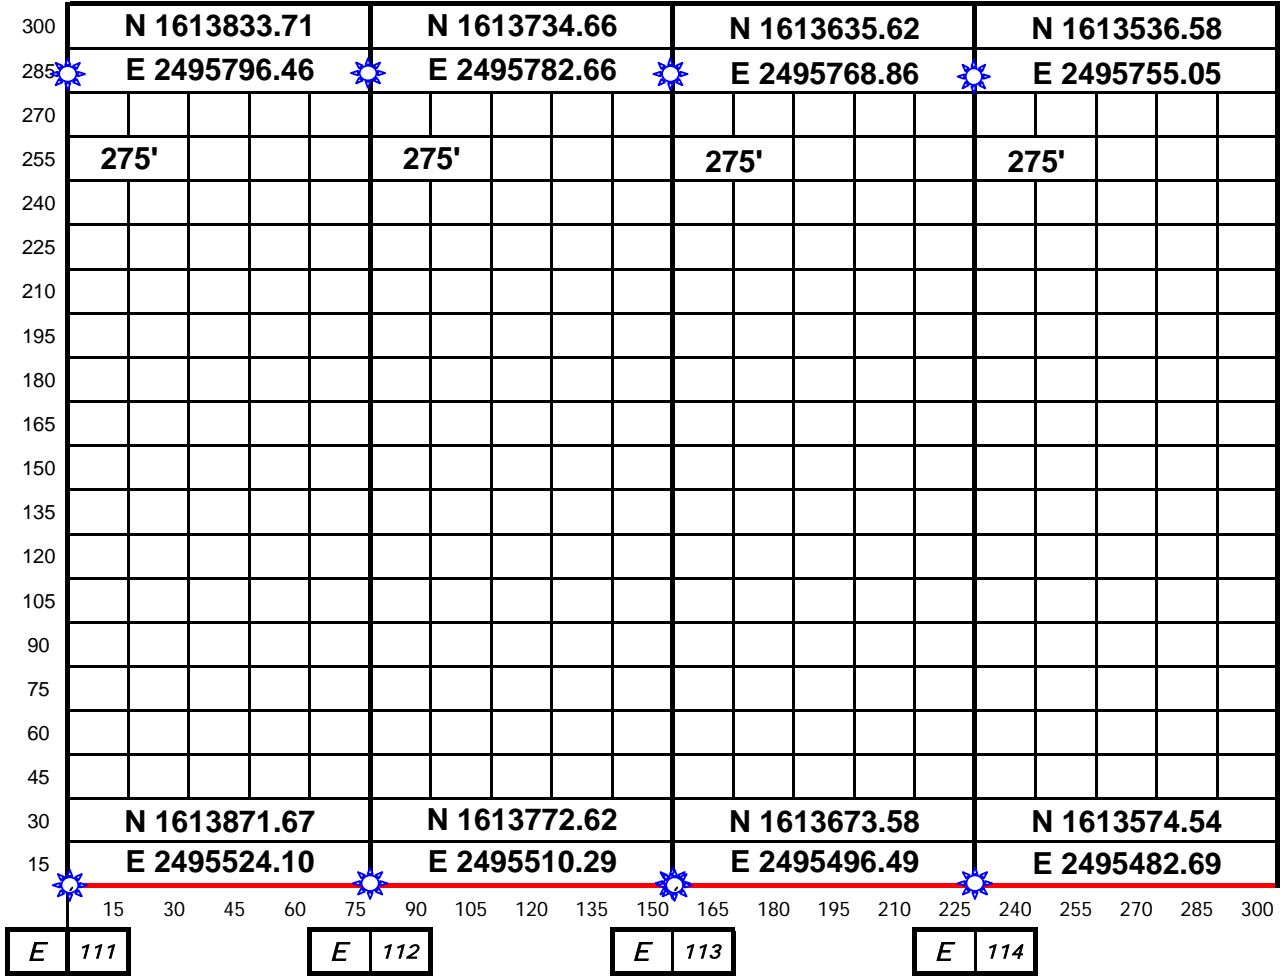


Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/13</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/13</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/13</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/13</div>
Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/13</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/13</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/13</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/13</div>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/14/2009	Completion Date:	4/14/2009
QC Date:		QA Date	

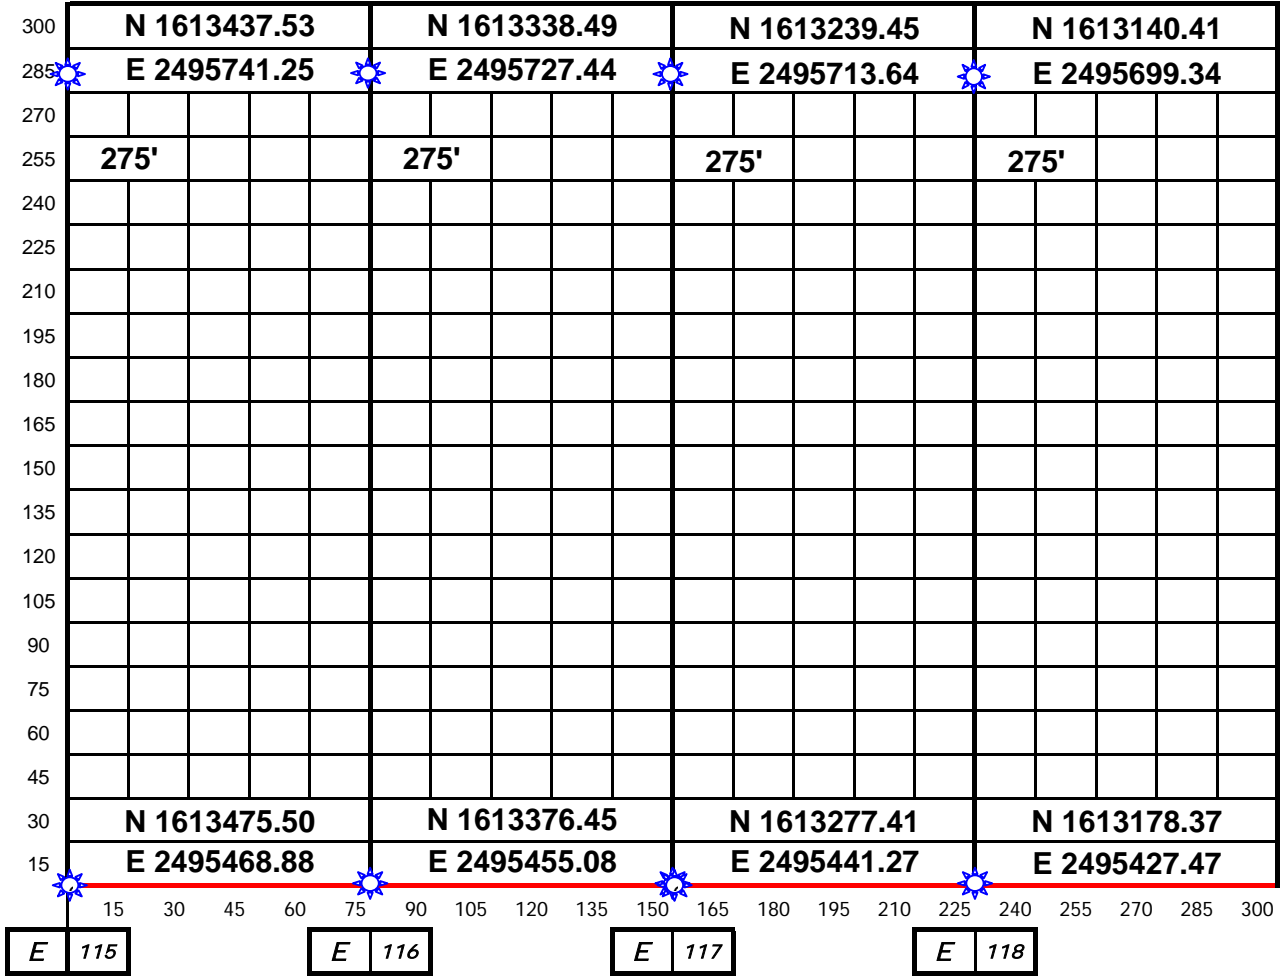


Start <input type="text" value="4/14"/>	Start <input type="text" value="4/14"/>	Start <input type="text" value="4/14"/>	Start <input type="text" value="4/14"/>
Finish <input type="text" value="4/14"/>	Finish <input type="text" value="4/14"/>	Finish <input type="text" value="4/14"/>	Finish <input type="text" value="4/14"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/14/2009	Completion Date:	4/14/2009
QC Date:		QA Date	

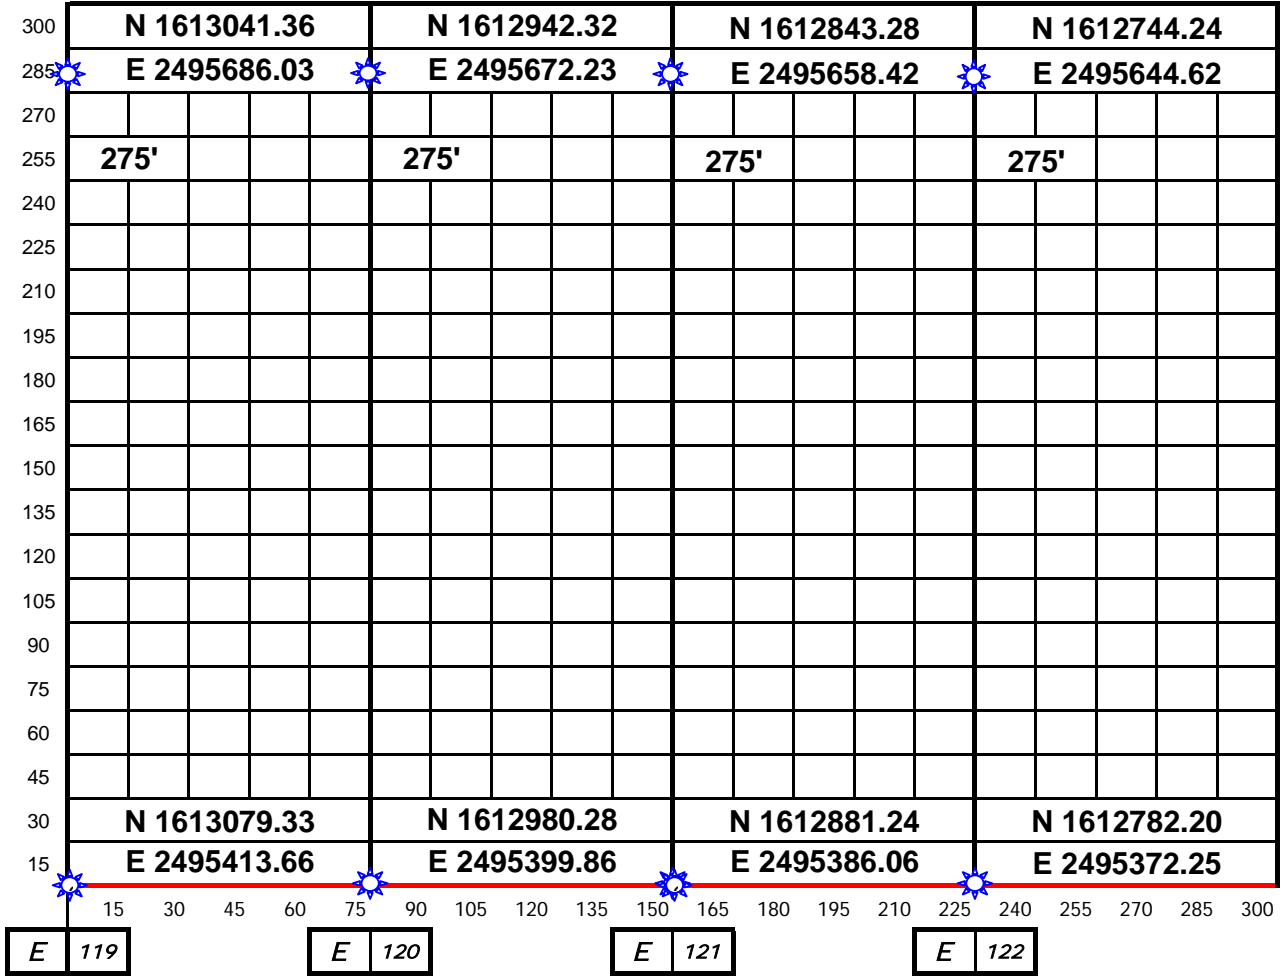


Start 4/14	Start 4/14	Start 4/14	Start 4/14
Finish 4/14	Finish 4/14	Finish 4/14	Finish 4/14
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/14/2009	Completion Date:	4/14/2009
QC Date:		QA Date	

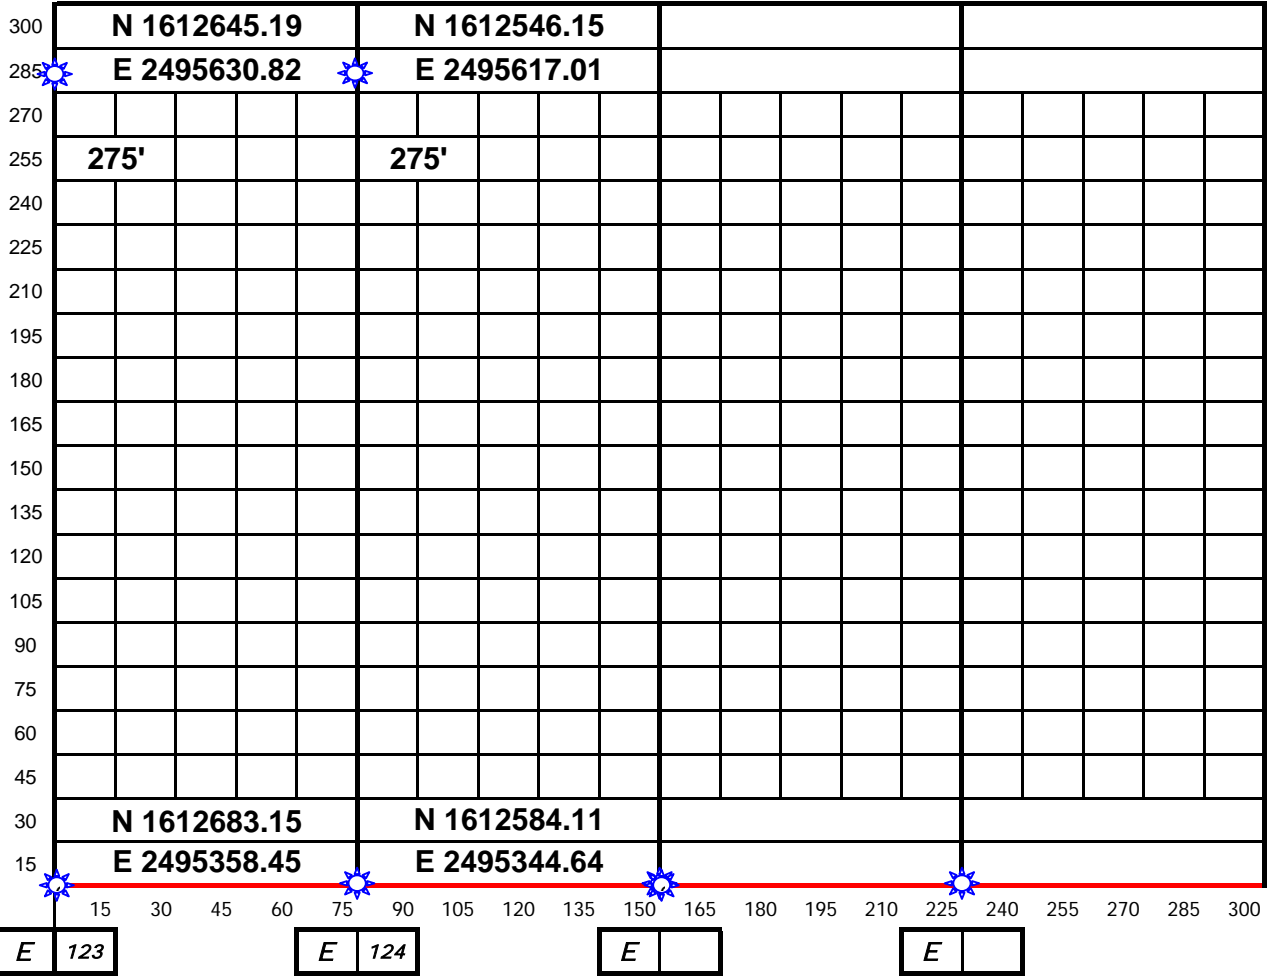


Start <input type="text" value="4/14"/>	Start <input type="text" value="4/14"/>	Start <input type="text"/>	Start <input type="text"/>
Finish <input type="text" value="4/14"/>	Finish <input type="text" value="4/14"/>	Finish <input type="text"/>	Finish <input type="text"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/14/2009	Completion Date:	4/14/2009
QC Date:		QA Date	

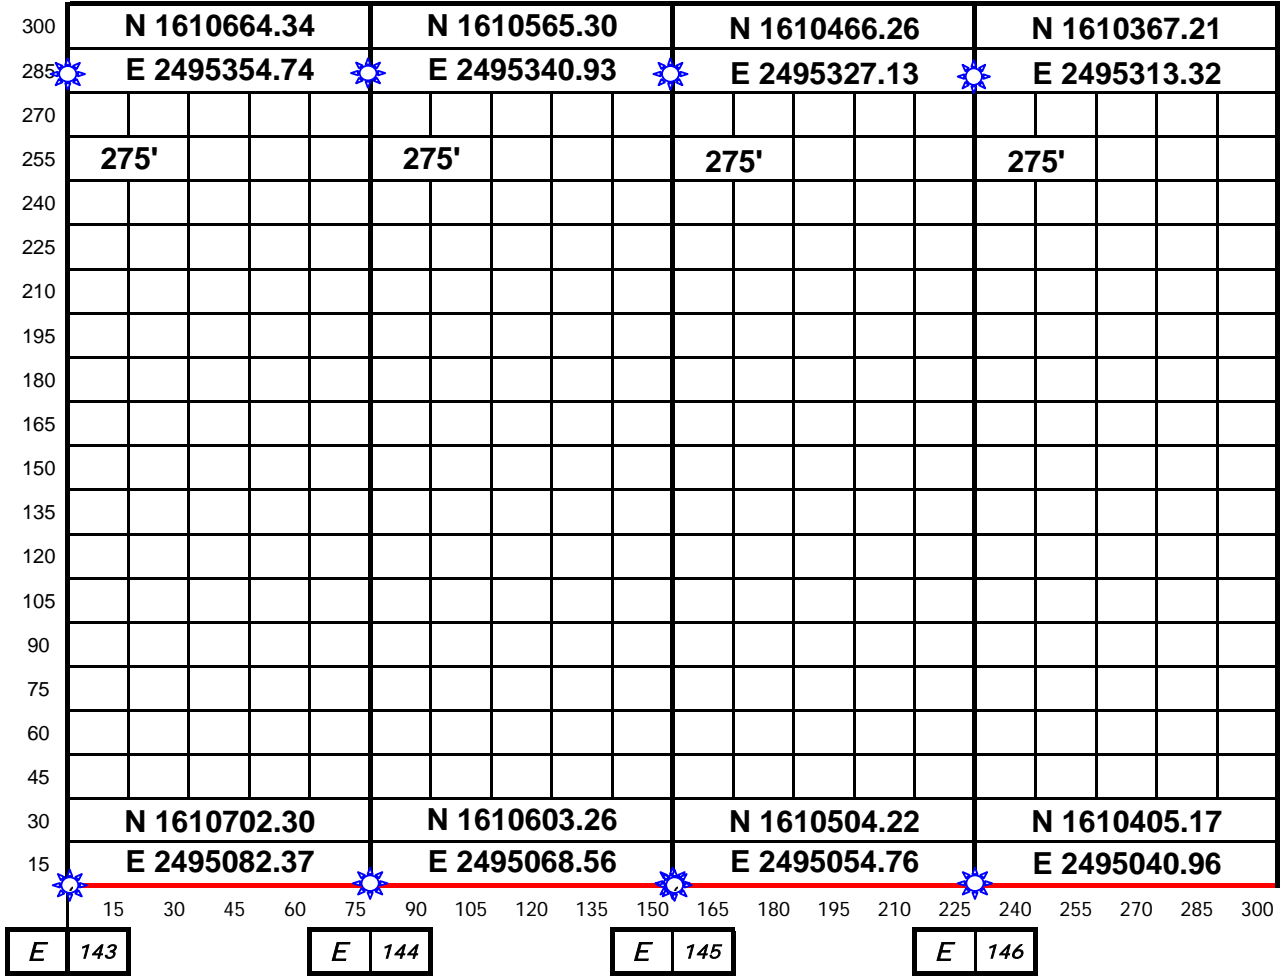


Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/14</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/14</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/14</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/14</div>
Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/14</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/14</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/14</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/14</div>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/14/2009	Completion Date:	4/15/2009
QC Date:		QA Date	

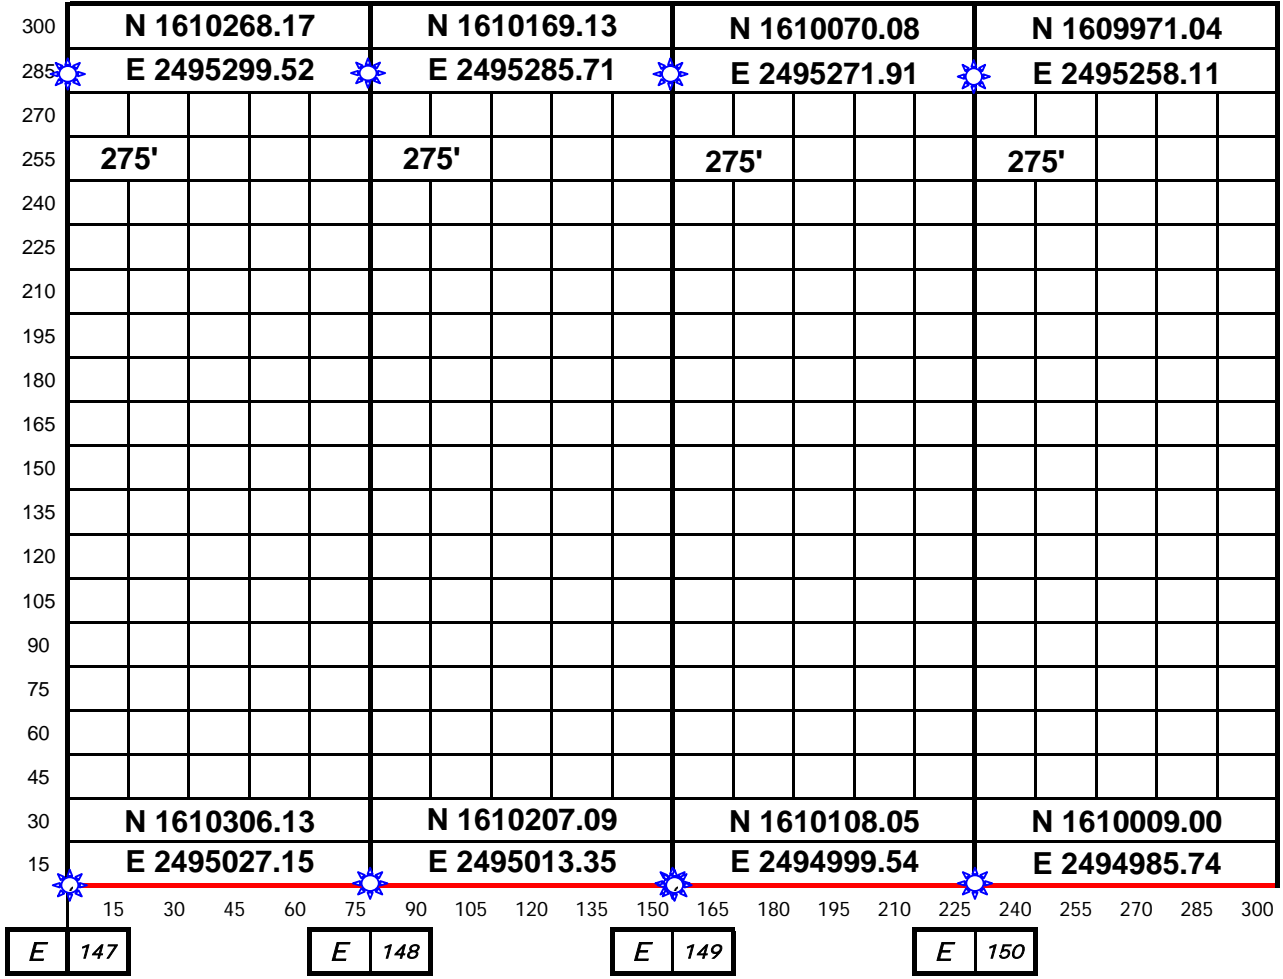


Start 4/14	Start 4/15	Start 4/15	Start 4/15
Finish 4/14	Finish 4/15	Finish 4/15	Finish 4/15
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/15/2009	Completion Date:	4/15/2009
QC Date:		QA Date	

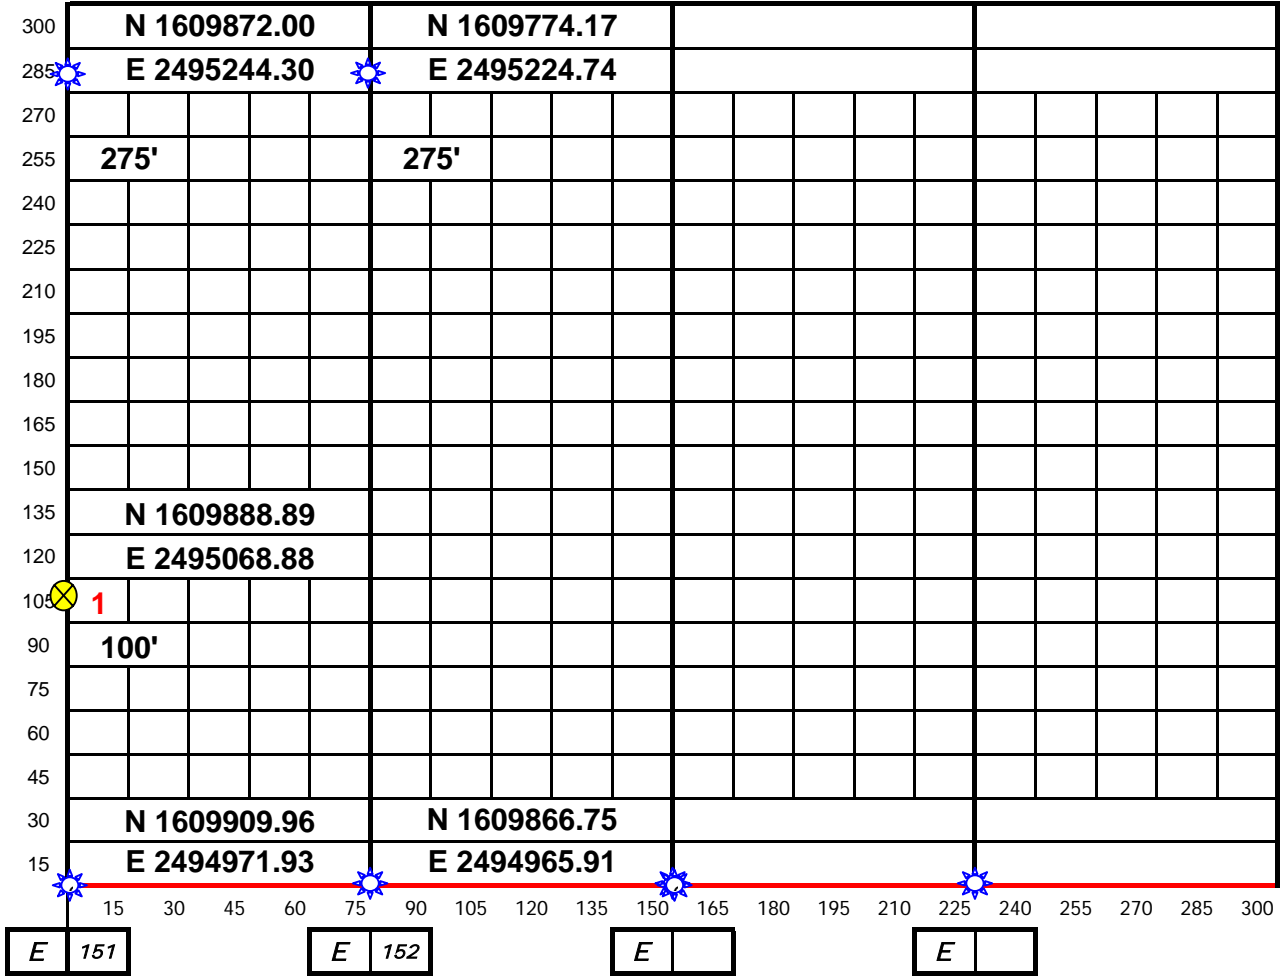


Start <input style="width: 50px; height: 20px;" type="text" value="4/14"/>	Start <input style="width: 50px; height: 20px;" type="text" value="4/15"/>	Start <input style="width: 50px; height: 20px;" type="text"/>	Start <input style="width: 50px; height: 20px;" type="text"/>
Finish <input style="width: 50px; height: 20px;" type="text" value="4/14"/>	Finish <input style="width: 50px; height: 20px;" type="text" value="4/15"/>	Finish <input style="width: 50px; height: 20px;" type="text"/>	Finish <input style="width: 50px; height: 20px;" type="text"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

1 Fragmentation

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	9/10/2008	Completion Date:	9/10/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

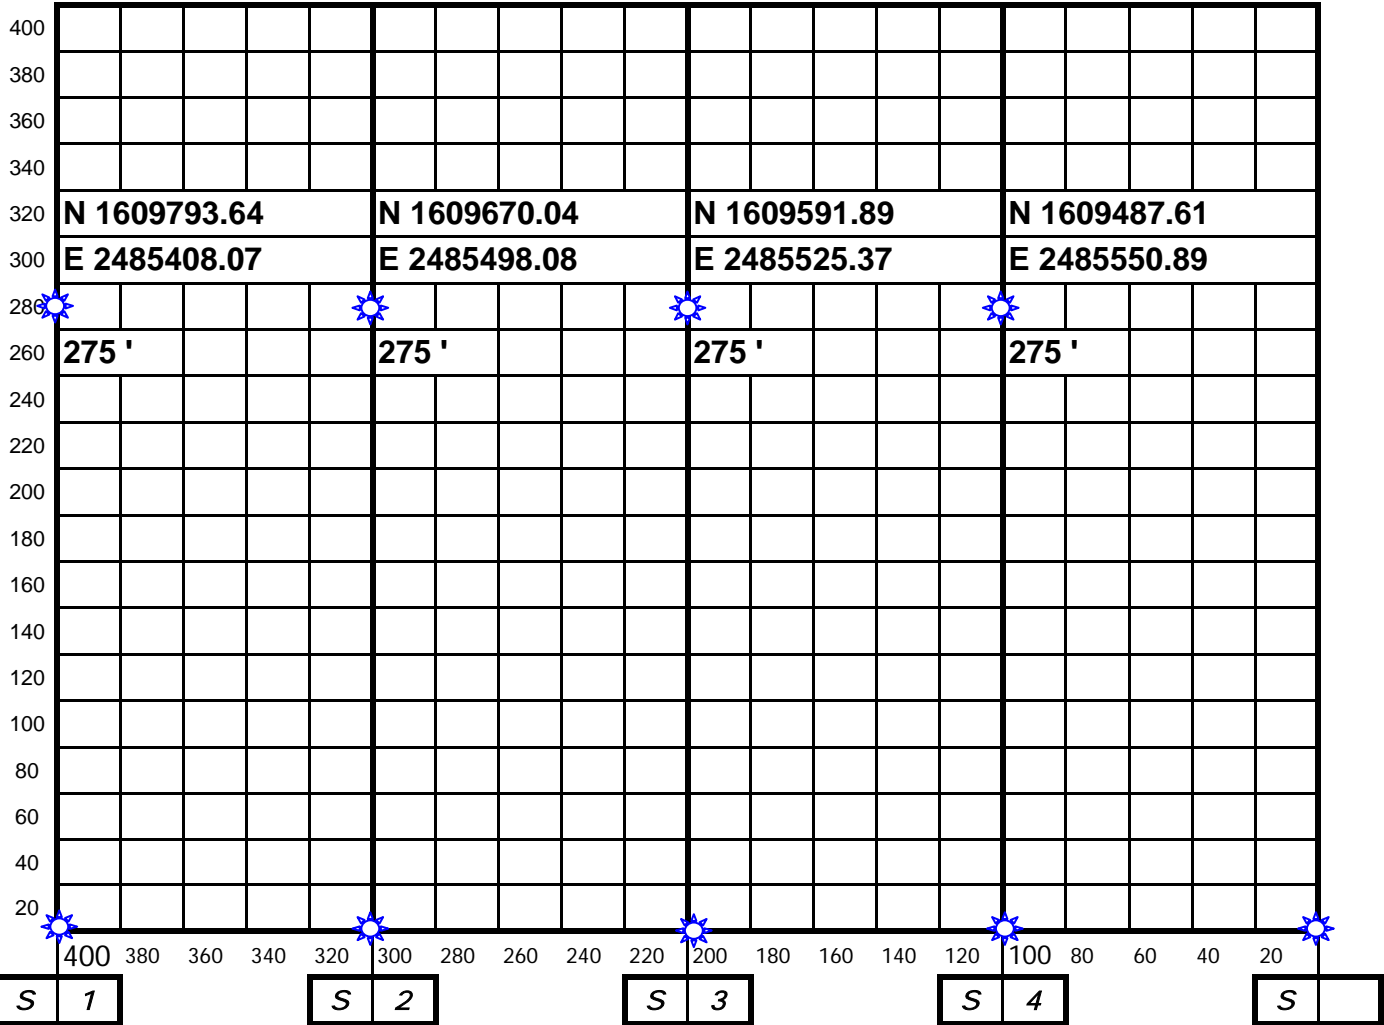


Start	Start	Start	Start	Start
9/10	9/10	9/10	9/10	
Finish	Finish	Finish	Finish	Finish
9/10	9/10	9/10	9/10	
	MEC		MD	STAKE #

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	9/10/2008	Completion Date:	9/10/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

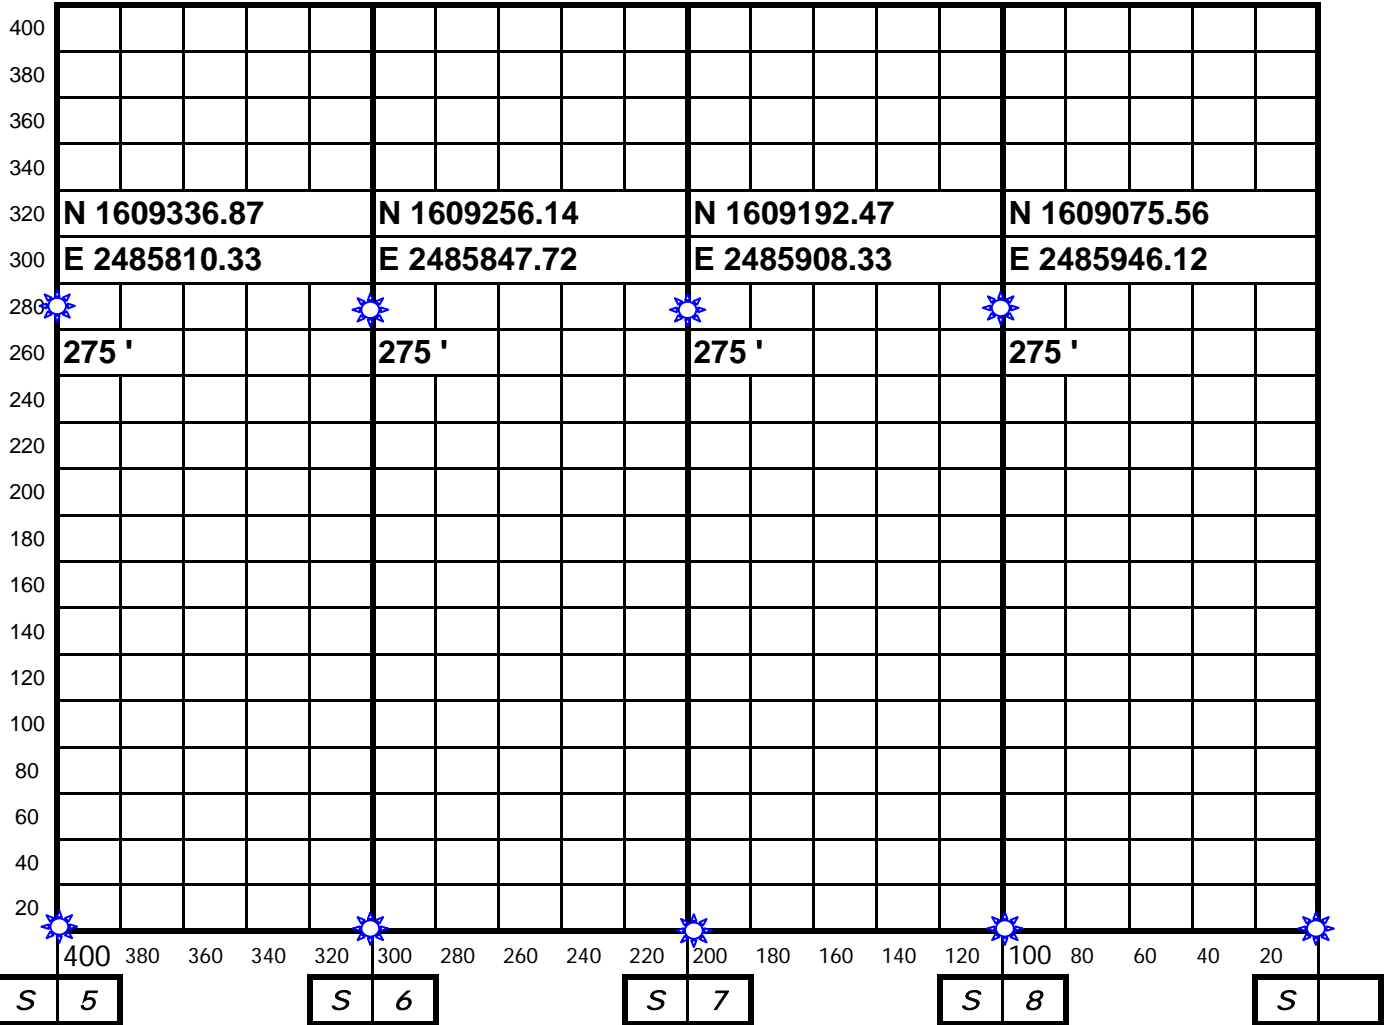


Start	Start	Start	Start	Start
<input type="text" value="9/10"/>	<input type="text" value="9/10"/>	<input type="text" value="9/10"/>	<input type="text" value="9/10"/>	<input type="text"/>
Finish	Finish	Finish	Finish	Finish
<input type="text" value="9/10"/>	<input type="text" value="9/10"/>	<input type="text" value="9/10"/>	<input type="text" value="9/10"/>	<input type="text"/>
MEC	MD	STAKE #		

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	9/10/2008	Completion Date:	9/10/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

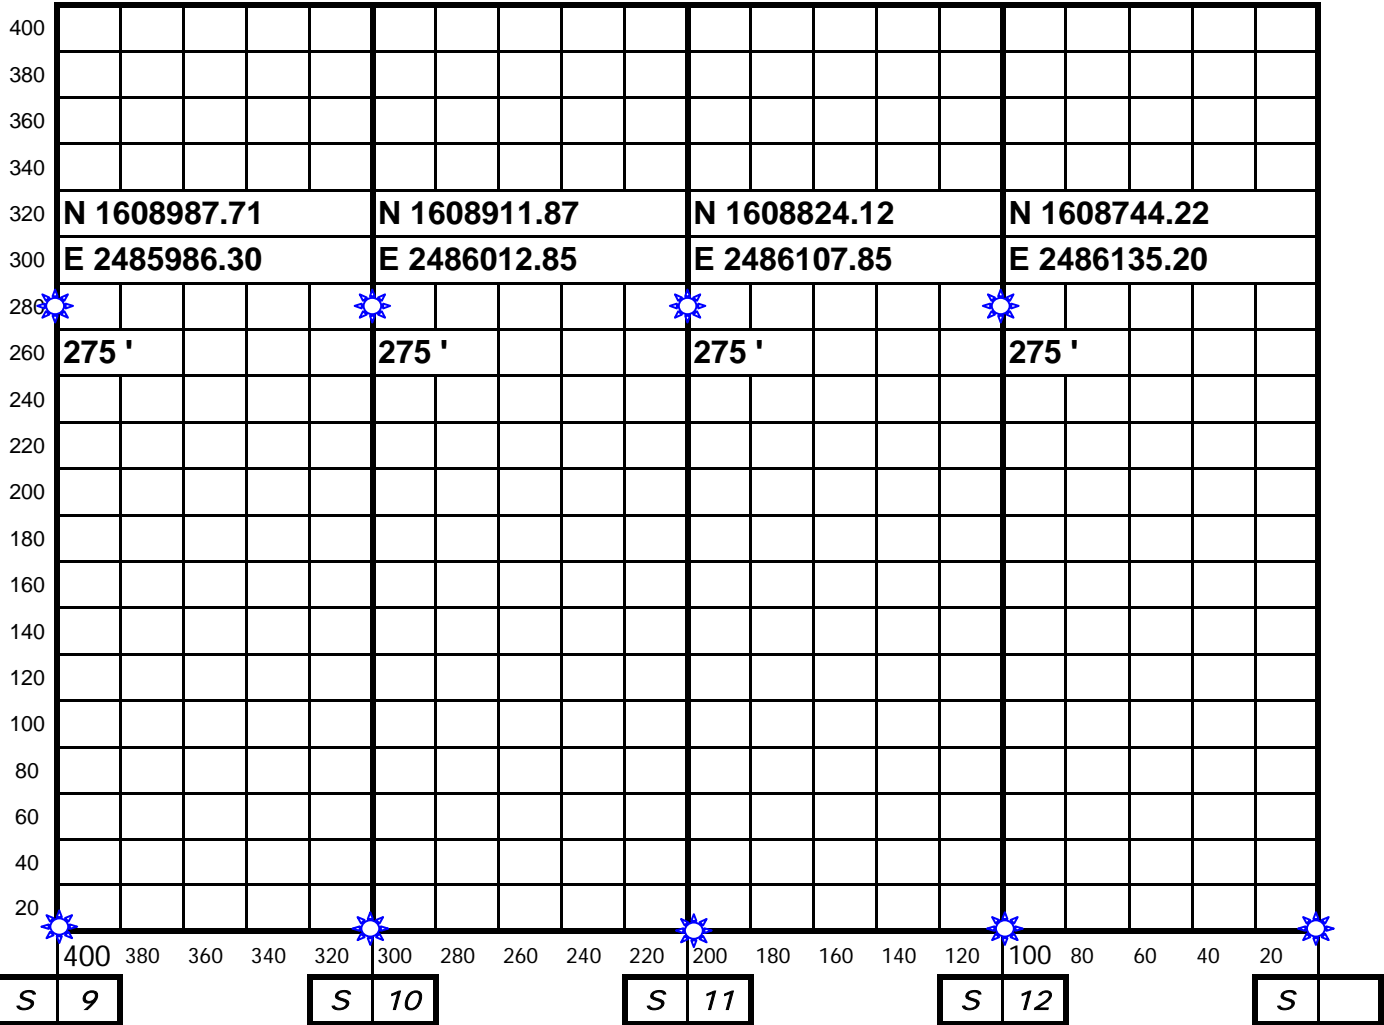


Start	Start	Start	Start	Start	
9/10	9/10	9/10	9/10		
Finish	Finish	Finish	Finish	Finish	
9/10	9/10	9/10	9/10		
	MEC		MD		STAKE #

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	9/10/2008	Completion Date:	9/10/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

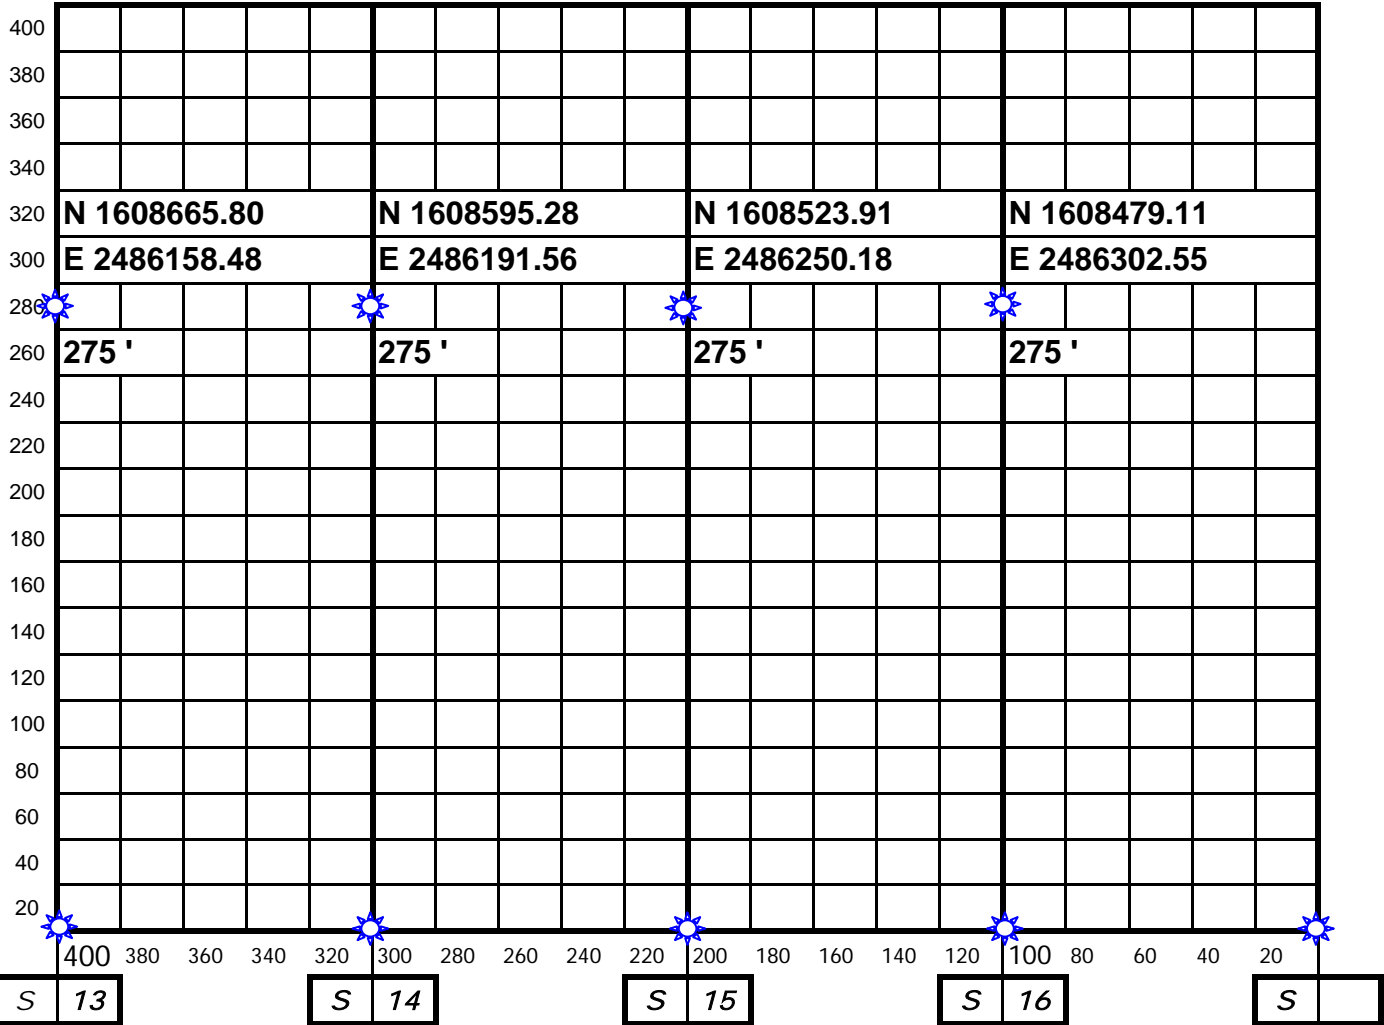


Start	Start	Start	Start	Start	
9/10	9/10	9/10	9/10		
Finish	Finish	Finish	Finish	Finish	
9/10	9/10	9/10	9/10		
	MEC		MD		STAKE #

Comments.Notes:

S-16: Offset 30' North due to cliff

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	9/11/2008	Completion Date:	9/11/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

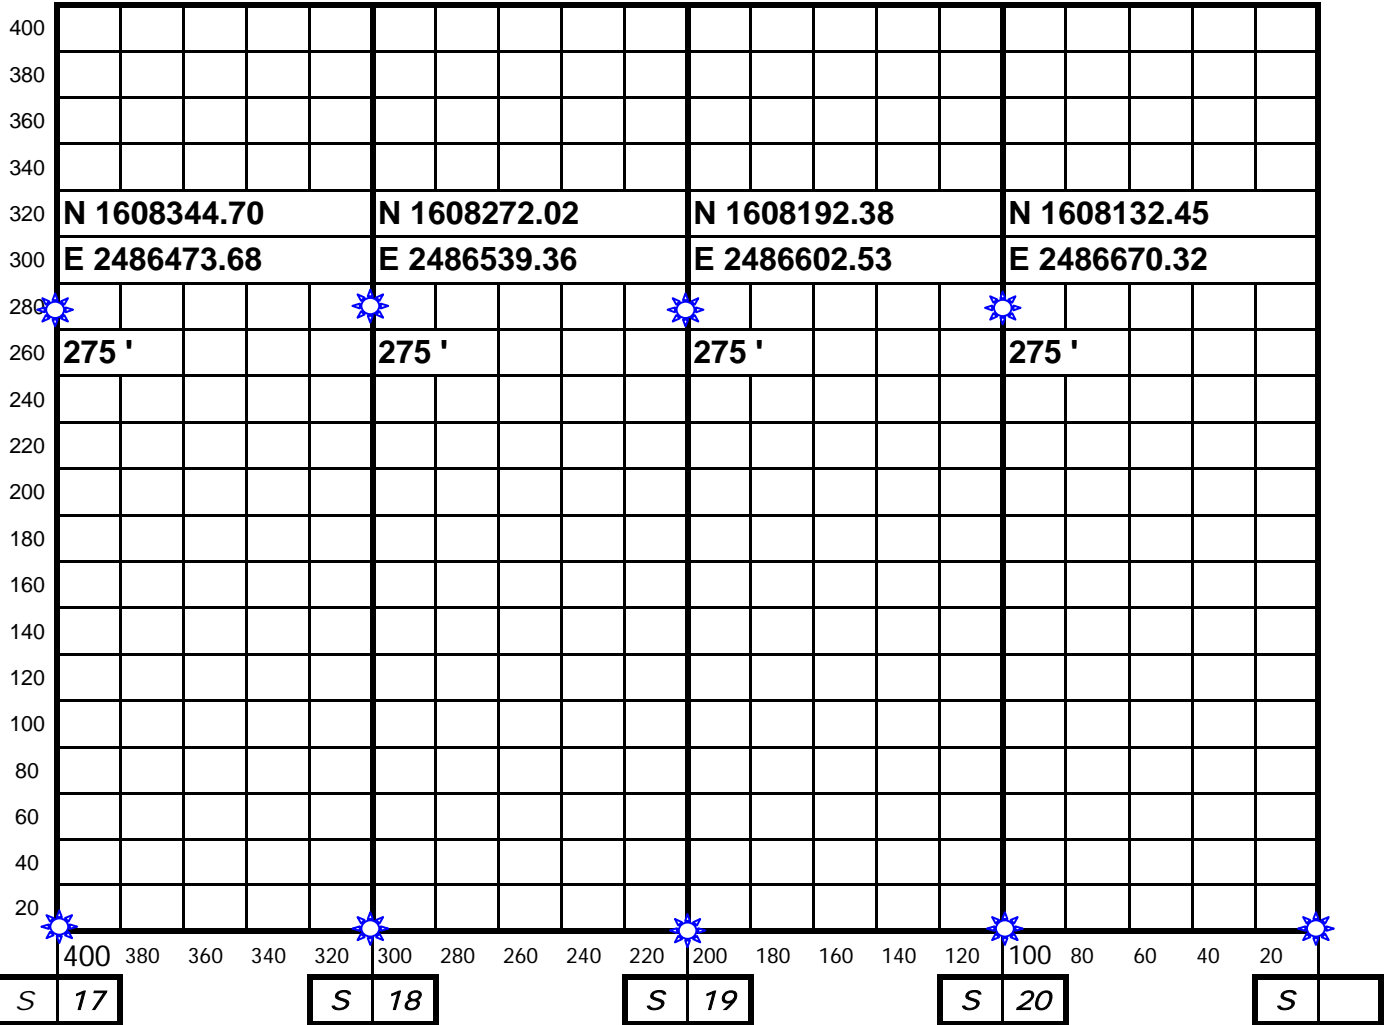


Start	Start	Start	Start	Start
9/11	9/11	9/11	9/11	
Finish	Finish	Finish	Finish	Finish
9/11	9/11	9/11	9/11	
MEC	MD	STAKE #		

Comments. Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	9/10/2008	Completion Date:	9/10/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

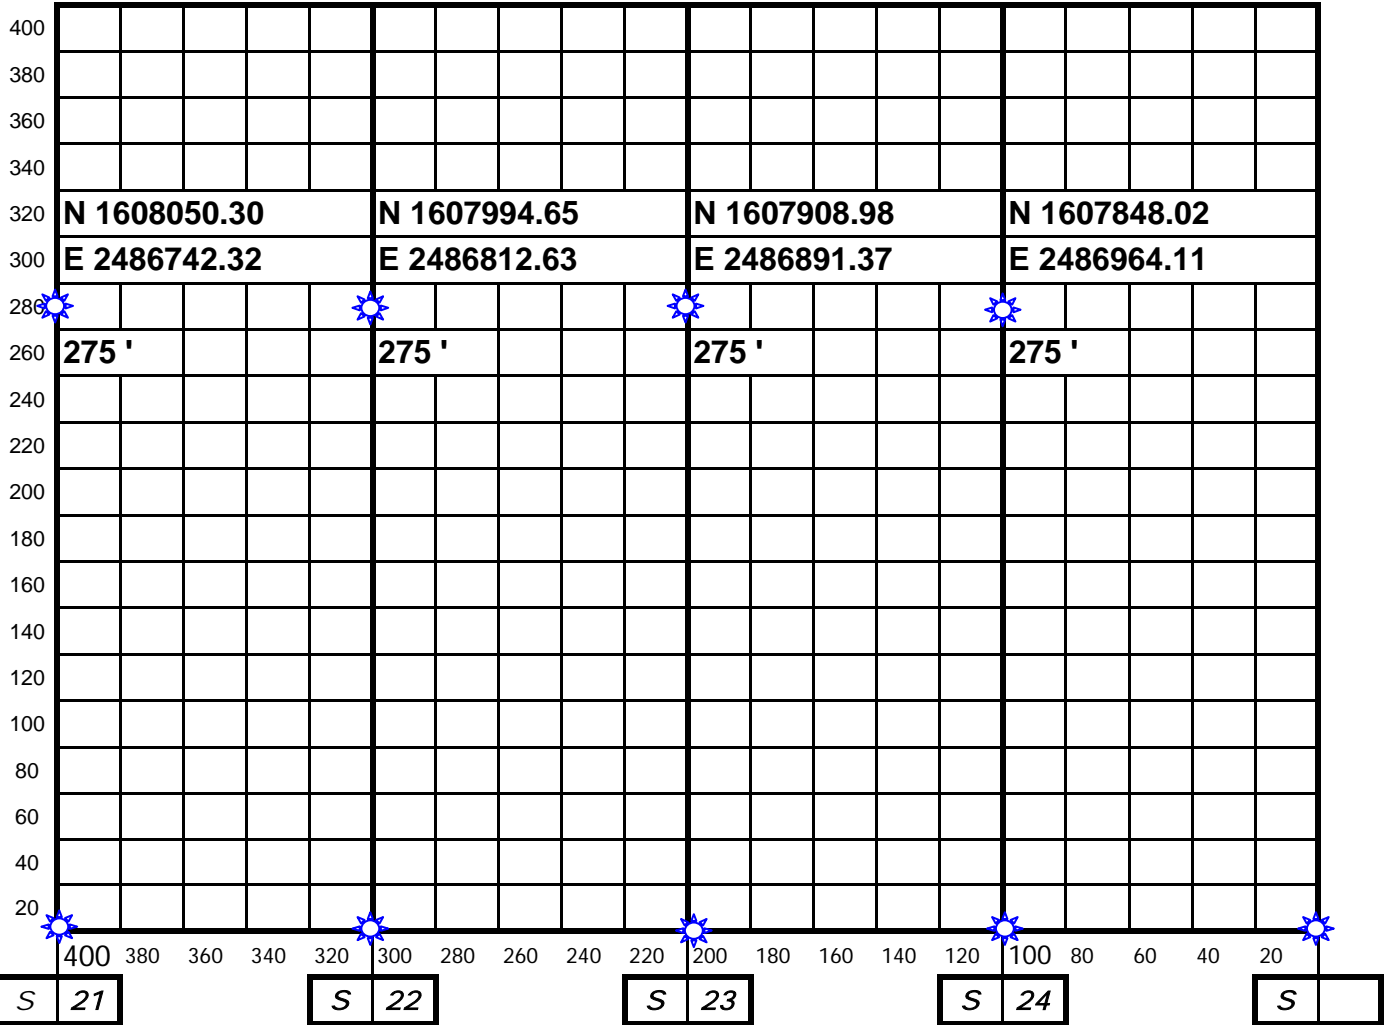


Start	Start	Start	Start	Start
9/11	9/11	9/11	9/11	
Finish	Finish	Finish	Finish	Finish
9/11	9/11	9/11	9/11	
	MEC		MD	
				STAKE #

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	9/16/2008	Completion Date:	9/16/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

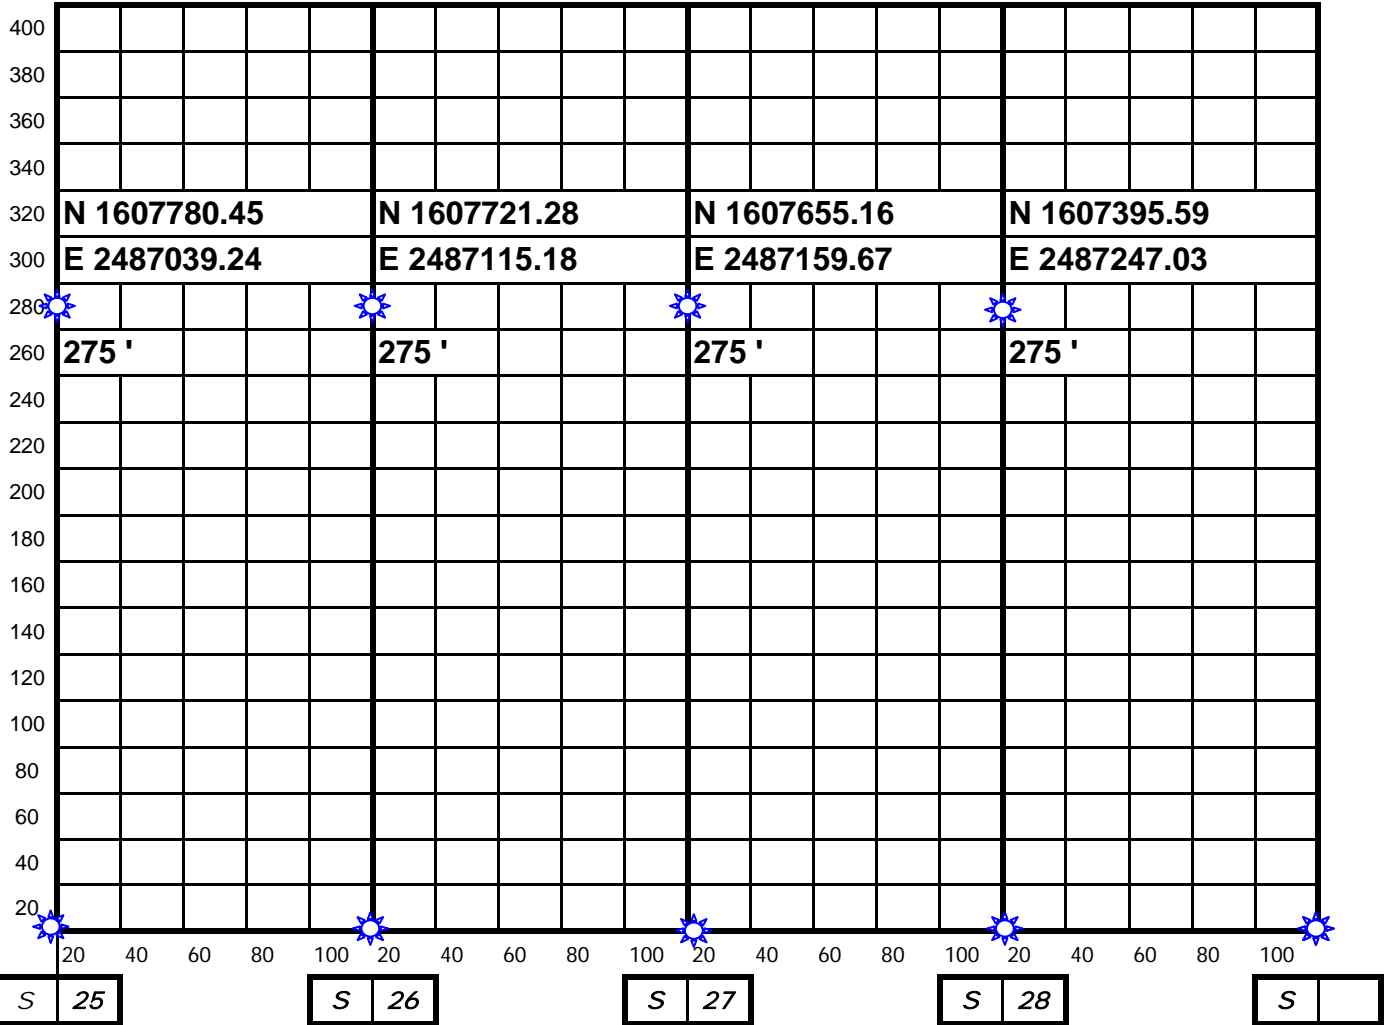


Start	Start	Start	Start	Start
<input type="text" value="9/16"/>	<input type="text" value="9/16"/>	<input type="text" value="9/16"/>	<input type="text" value="9/16"/>	<input type="text"/>
Finish	Finish	Finish	Finish	Finish
<input type="text" value="9/16"/>	<input type="text" value="9/16"/>	<input type="text" value="9/16"/>	<input type="text" value="9/16"/>	<input type="text"/>
MEC	MD	STAKE #		

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	9/16/2008	Completion Date:	9/16/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

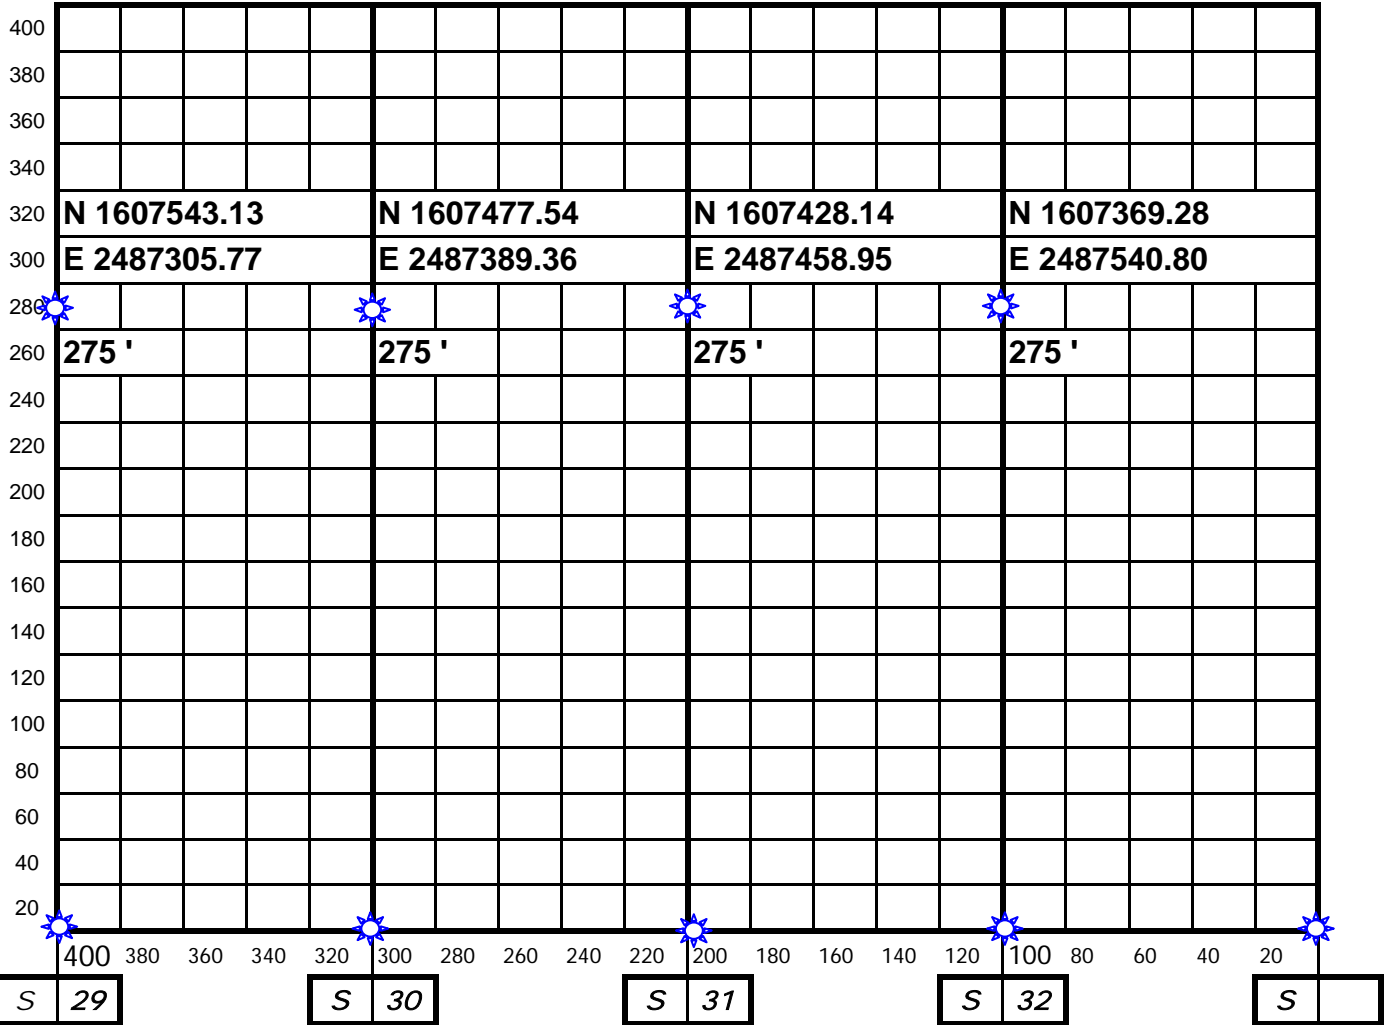


Start	Start	Start	Start	Start	
9/16	9/16	9/16	9/16		
Finish	Finish	Finish	Finish	Finish	
9/16	9/16	9/16	9/16		
	MEC		MD		STAKE #

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	9/16/2008	Completion Date:	9/16/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

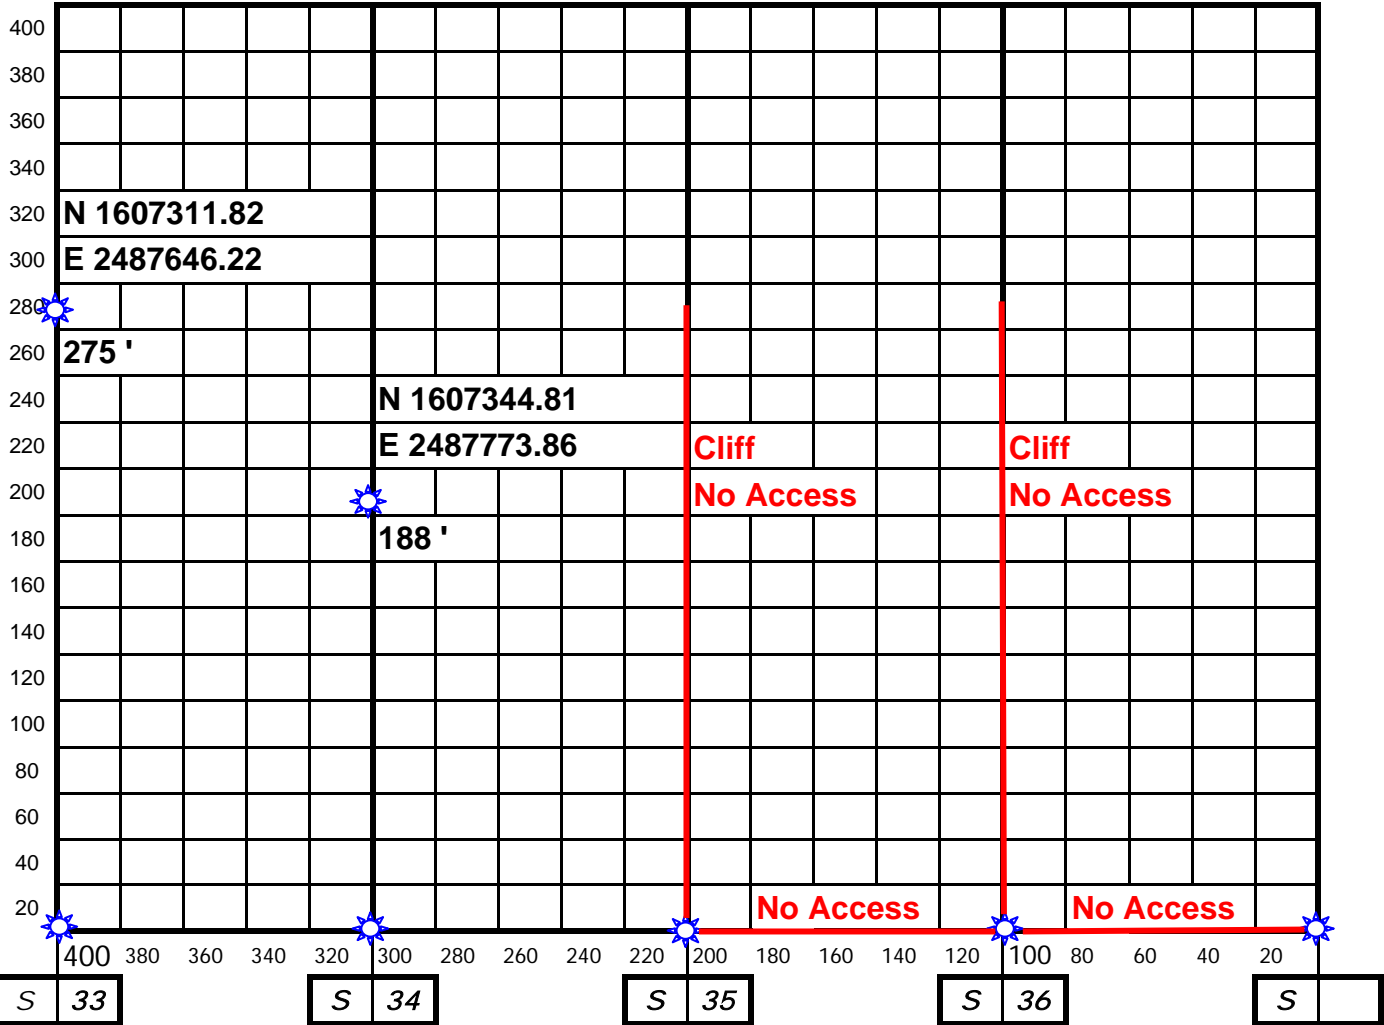


Start	Start	Start	Start	Start
<input type="text" value="9/16"/>	<input type="text" value="9/16"/>	<input type="text" value="9/16"/>	<input type="text" value="9/16"/>	<input type="text"/>
Finish	Finish	Finish	Finish	Finish
<input type="text" value="9/16"/>	<input type="text" value="9/16"/>	<input type="text" value="9/16"/>	<input type="text" value="9/16"/>	<input type="text"/>
MEC	MD	STAKE #		

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:		Completion Date:	
QC Date:		QC Signature:	
QA Date:		QA Signature:	

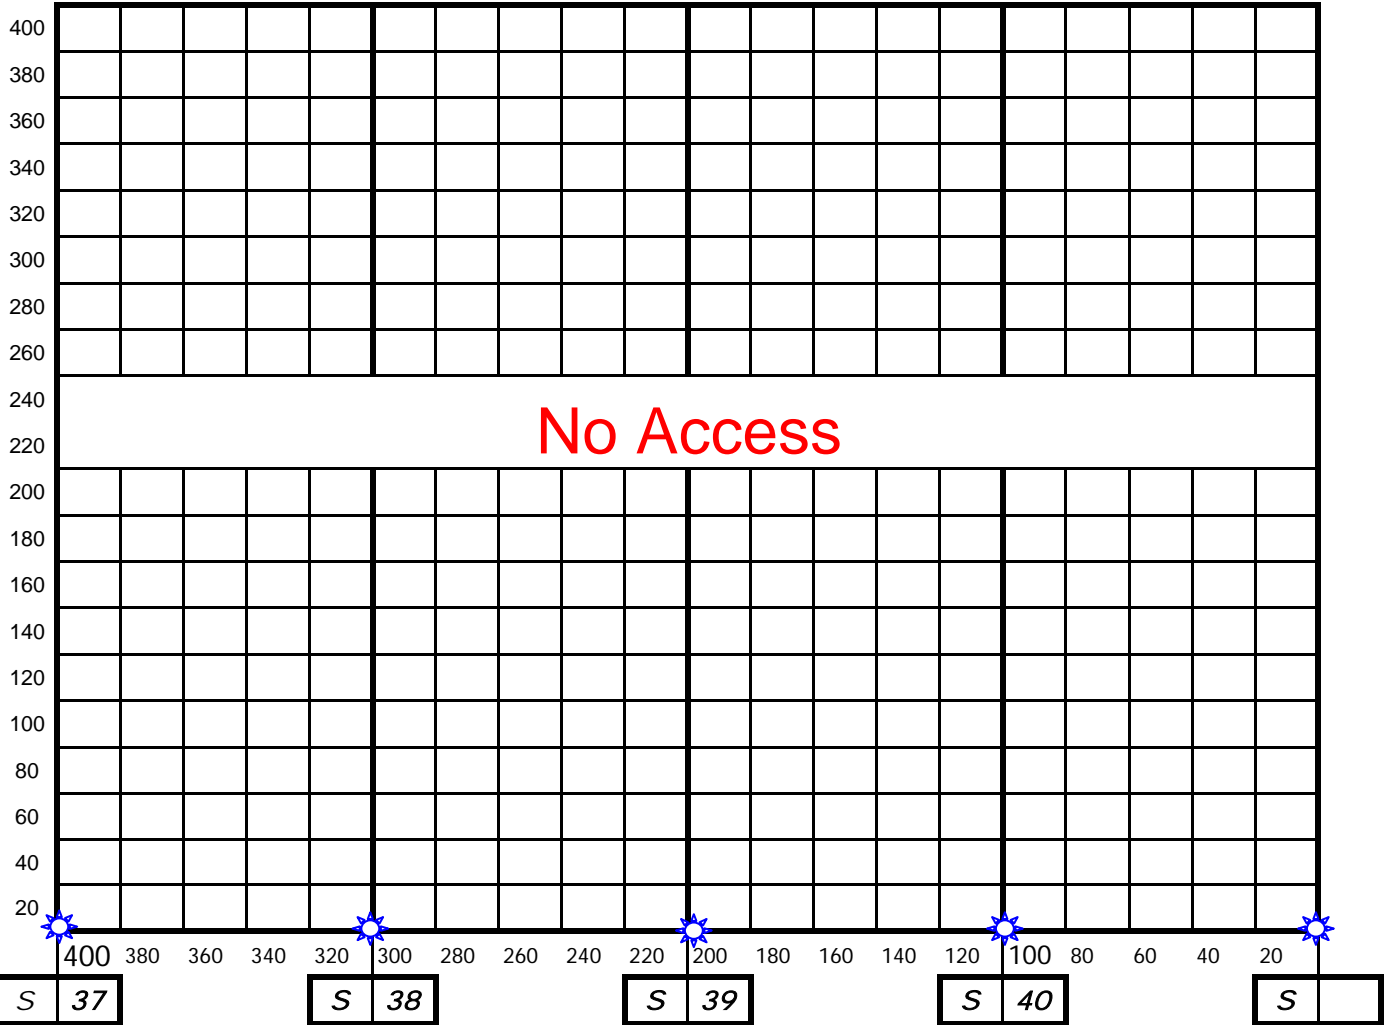


Start	Start	Start	Start	Start
Finish	Finish	Finish	Finish	Finish
MEC	MD	STAKE #		

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:		Completion Date:	
QC Date:		QC Signature:	
QA Date:		QA Signature:	

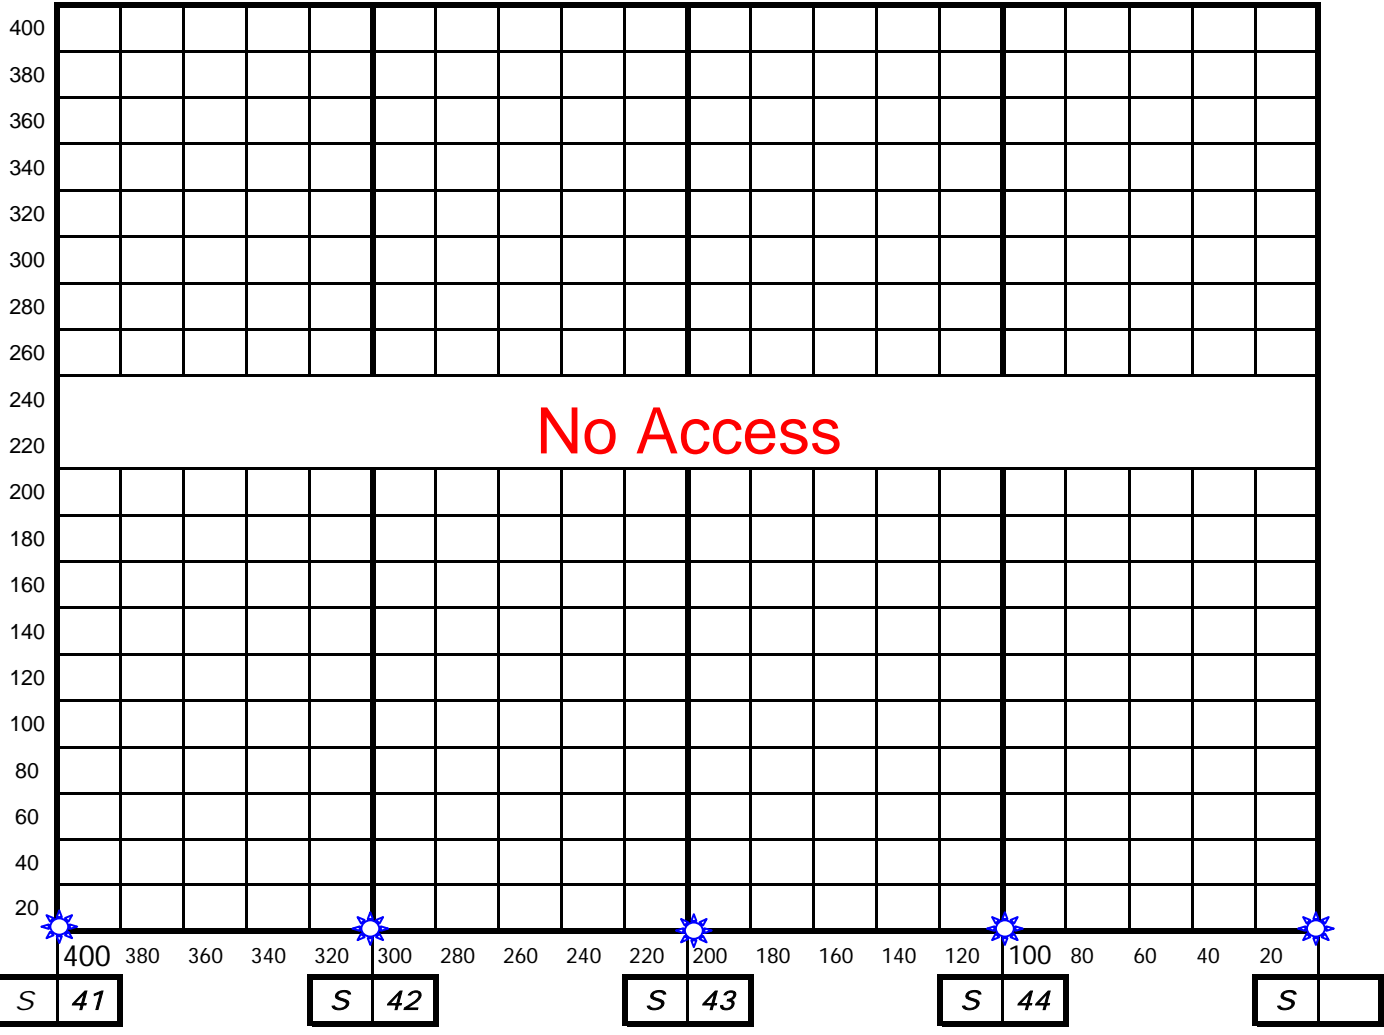


Start	Start	Start	Start	Start	
Finish	Finish	Finish	Finish	Finish	
	MEC		MD		STAKE #

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:		Completion Date:	
QC Date:		QC Signature:	
QA Date:		QA Signature:	

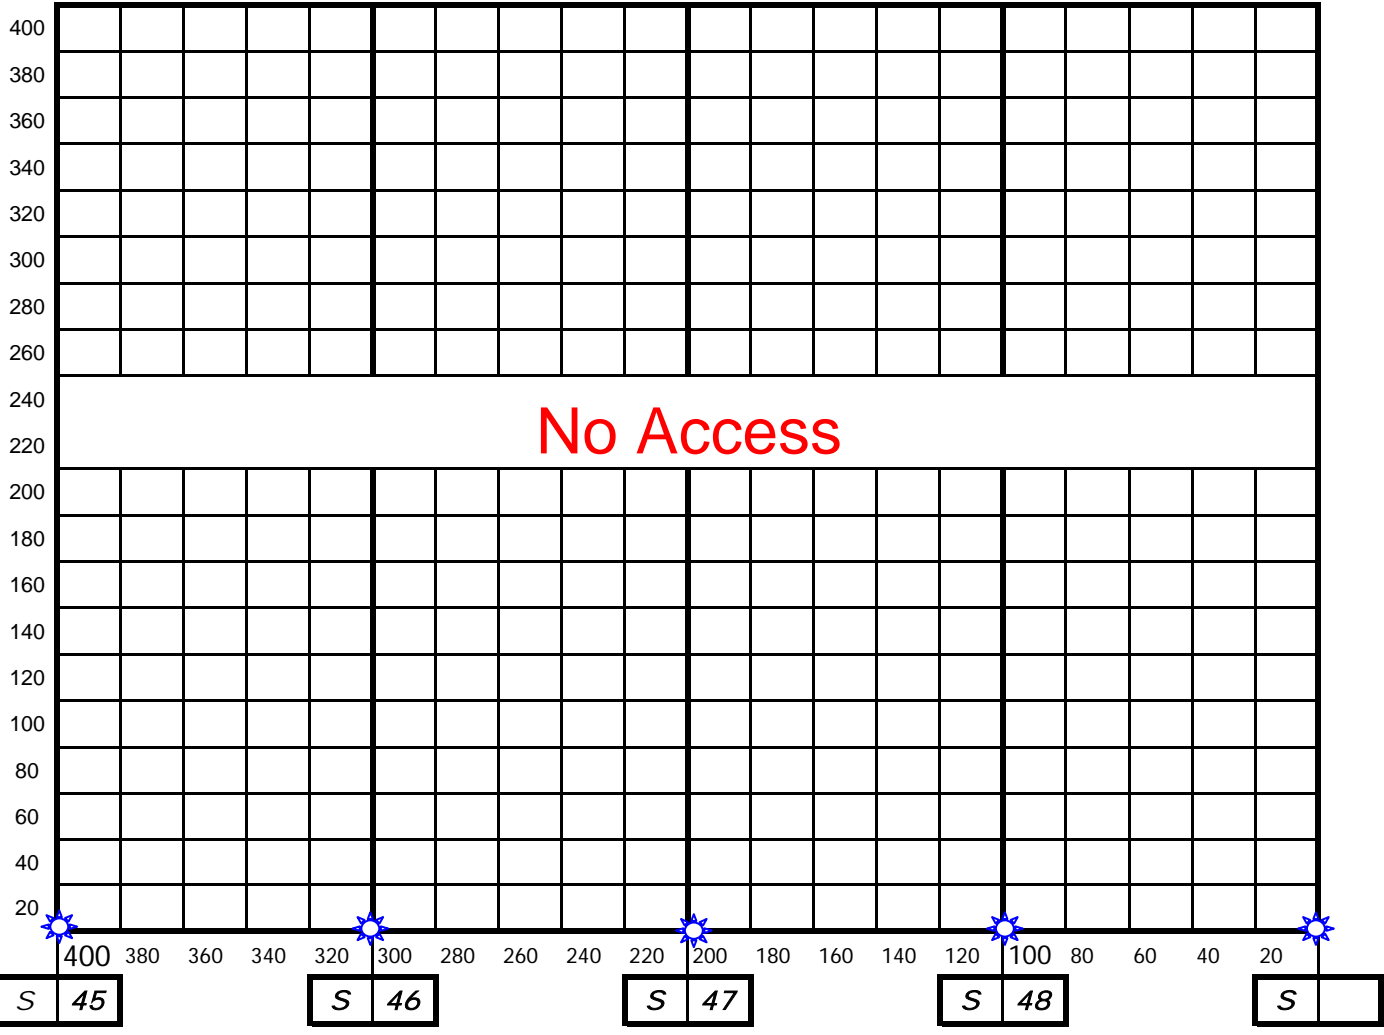


Start	Start	Start	Start	Start
Finish	Finish	Finish	Finish	Finish
MEC	MD	STAKE #		

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:		Completion Date:	
QC Date:		QC Signature:	
QA Date:		QA Signature:	

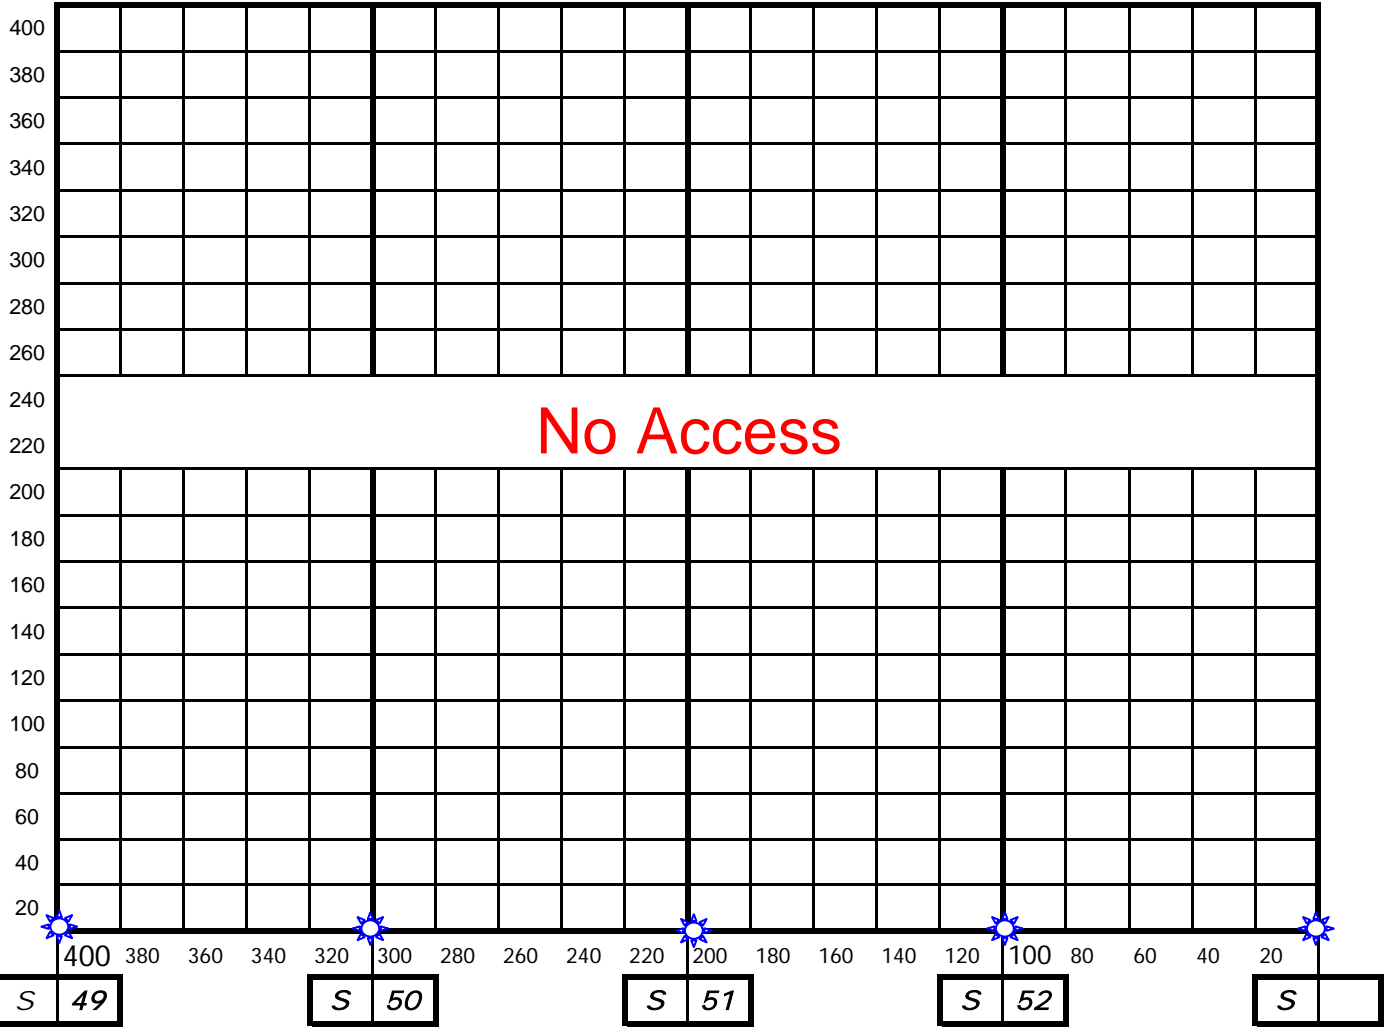


Start	Start	Start	Start	Start
Finish	Finish	Finish	Finish	Finish
MEC	MD	STAKE #		

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:		Completion Date:	
QC Date:		QC Signature:	
QA Date:		QA Signature:	

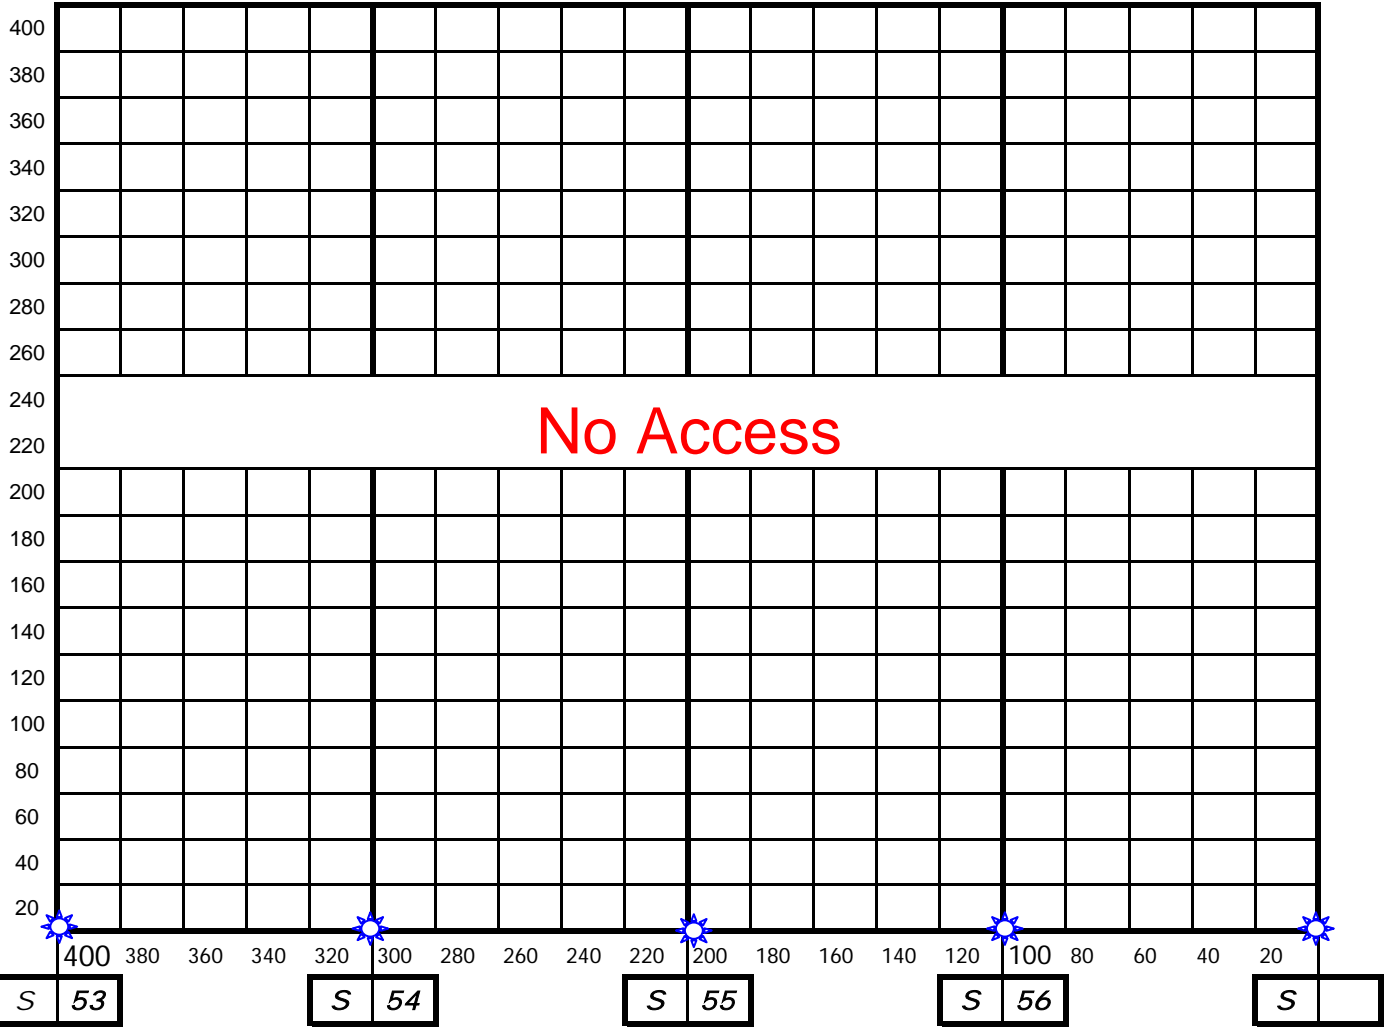


Start	Start	Start	Start	Start
Finish	Finish	Finish	Finish	Finish
MEC	MD	STAKE #		

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:		Completion Date:	
QC Date:		QC Signature:	
QA Date:		QA Signature:	

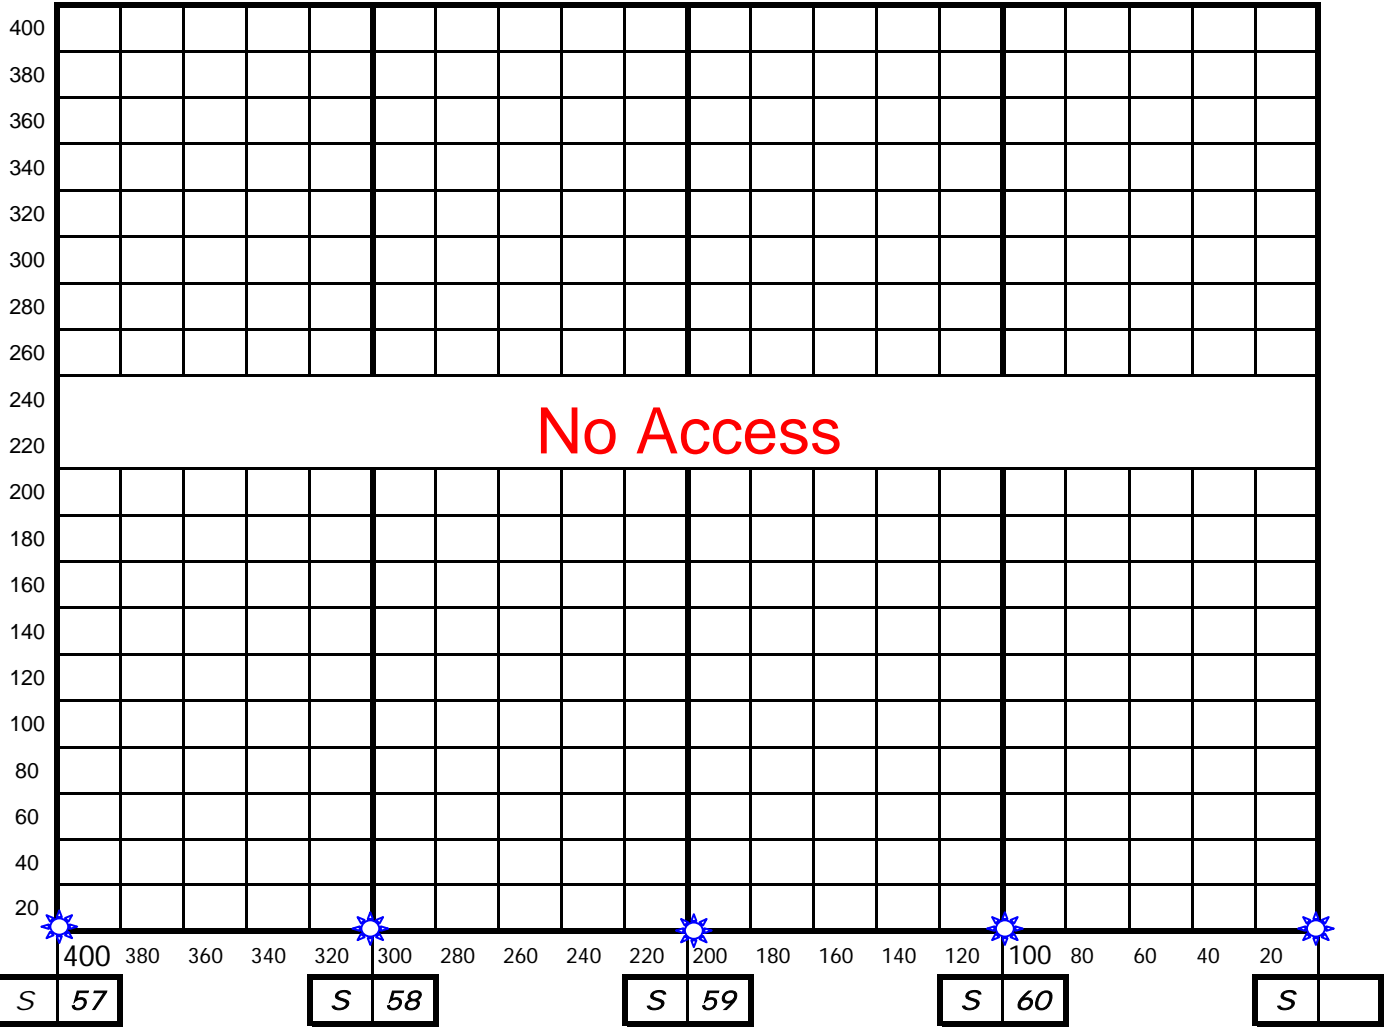


Start	Start	Start	Start	Start	
Finish	Finish	Finish	Finish	Finish	
	MEC		MD		STAKE #

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	9/8/2008	Completion Date:	9/8/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

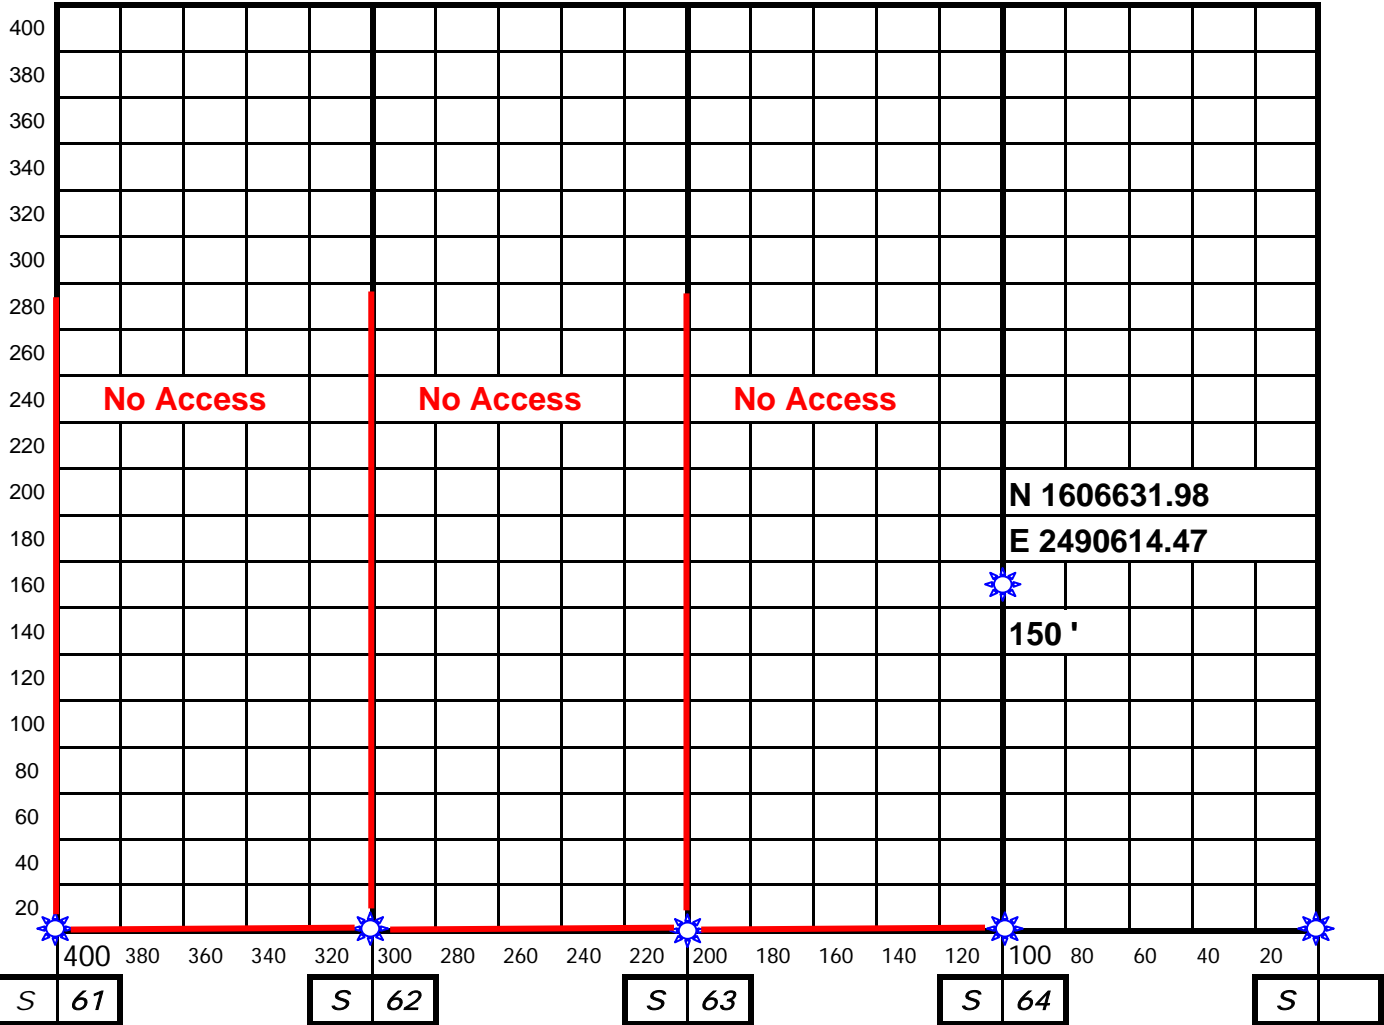


Start	Start	Start	Start	Start
			9/8	
Finish	Finish	Finish	Finish	Finish
			9/8	
MEC	MD	STAKE #		

Comments.Notes:

64: Partial due to terrain

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/28/2008	Completion Date:	8/28/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

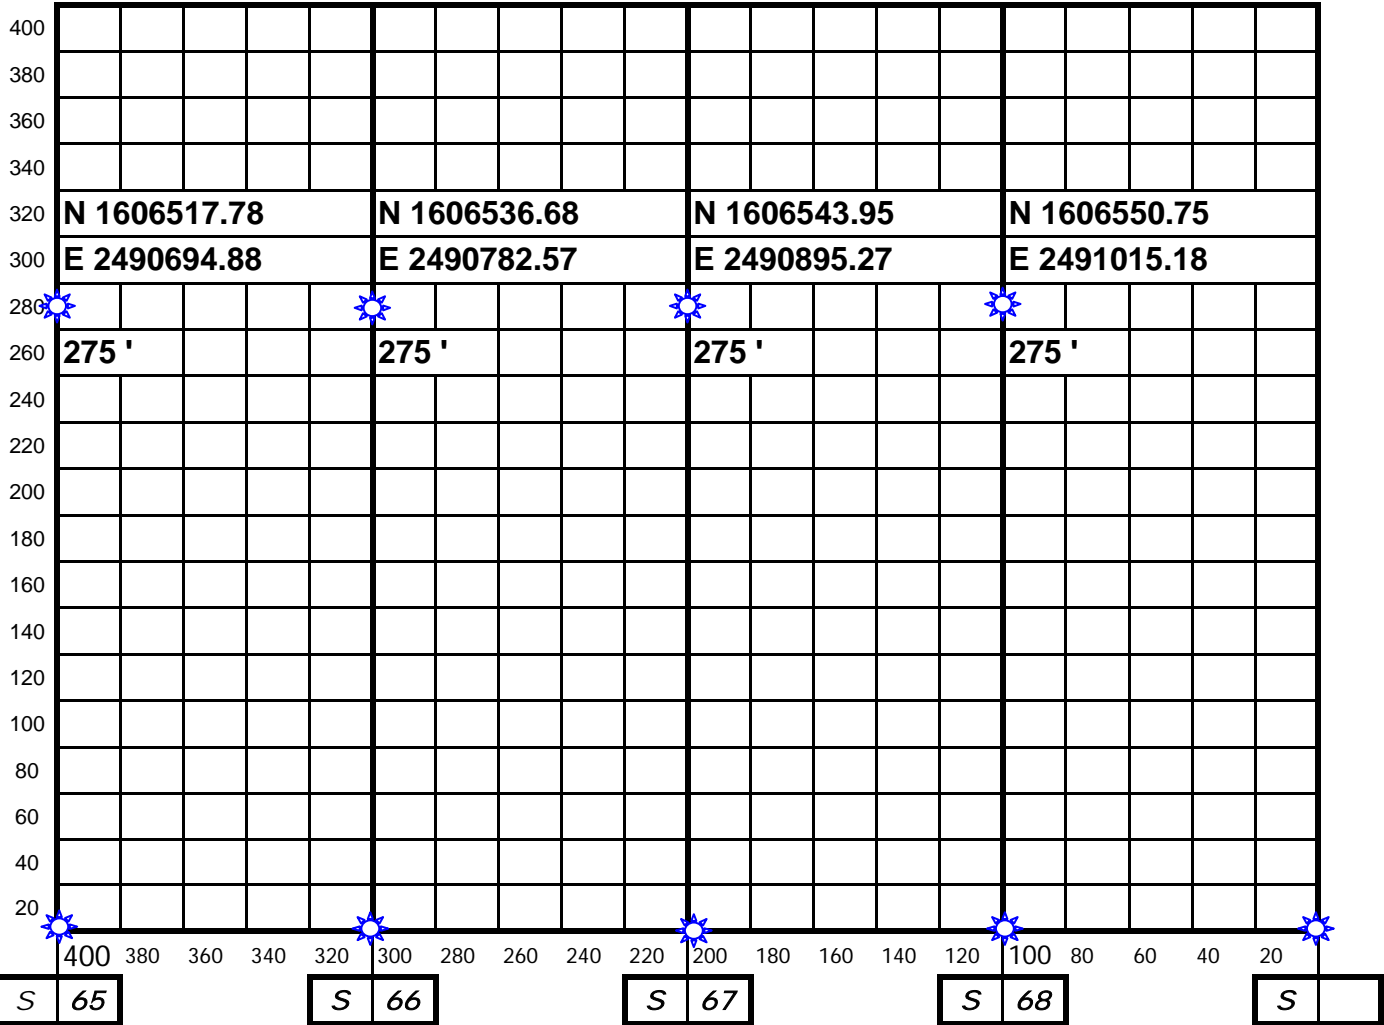


Start	Start	Start	Start	Start	
8/28	8/28	8/28	8/28		
Finish	Finish	Finish	Finish	Finish	
8/28	8/28	8/28	8/28		
	MEC		MD		STAKE #

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	9/8/2008	Completion Date:	9/8/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

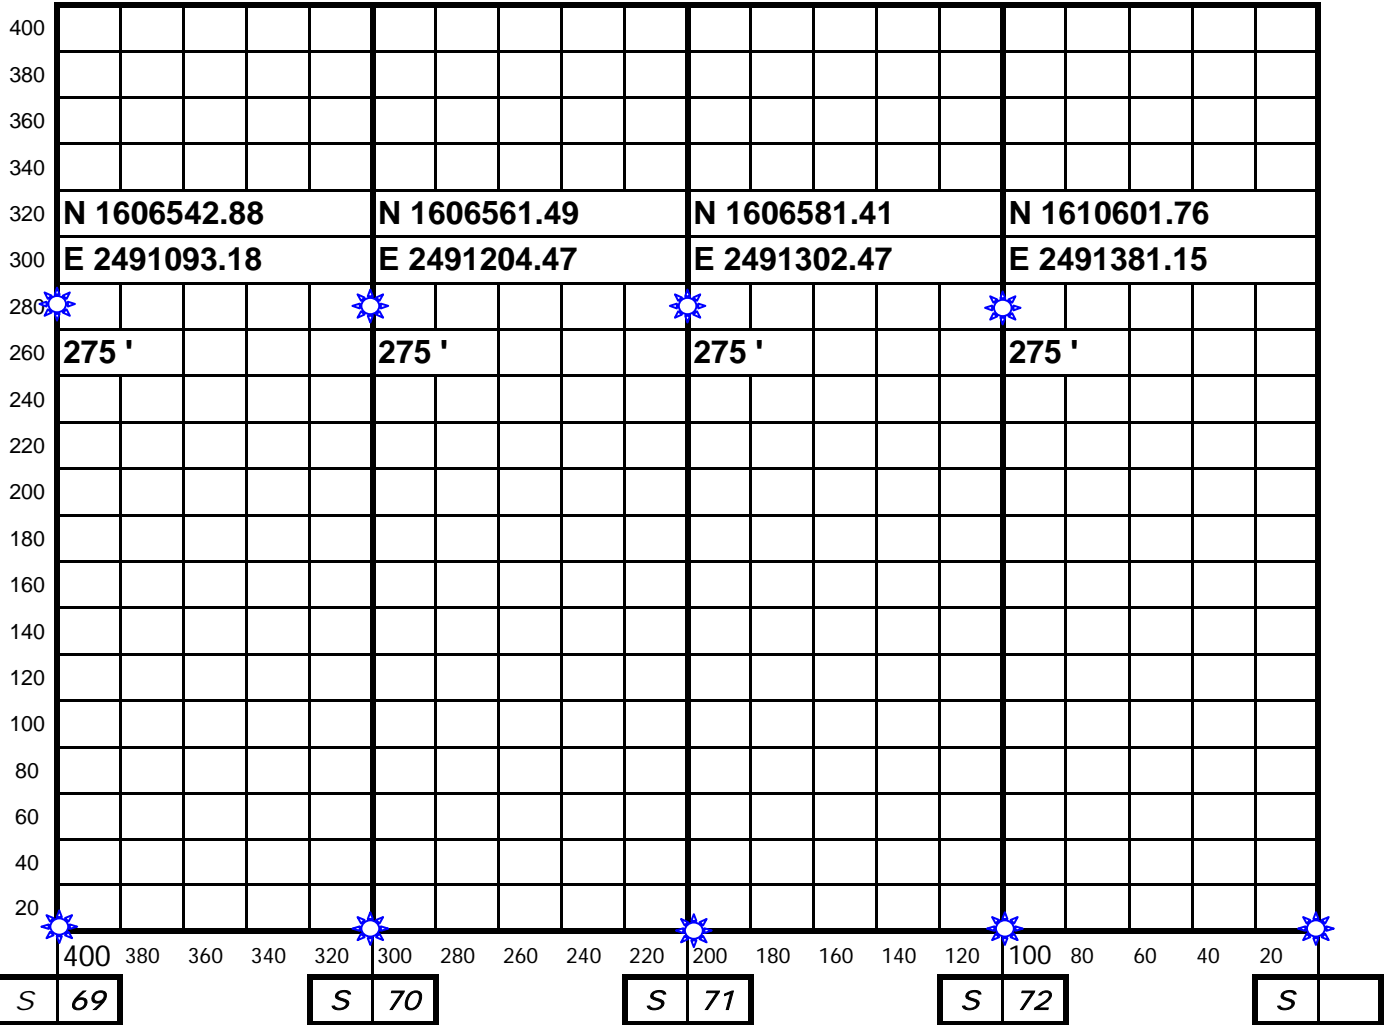


Start	Start	Start	Start	Start	
9/8	9/8	9/8	9/8		
Finish	Finish	Finish	Finish	Finish	
9/8	9/8	9/8	9/8		
	MEC		MD		STAKE #

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	9/8/2008	Completion Date:	9/8/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

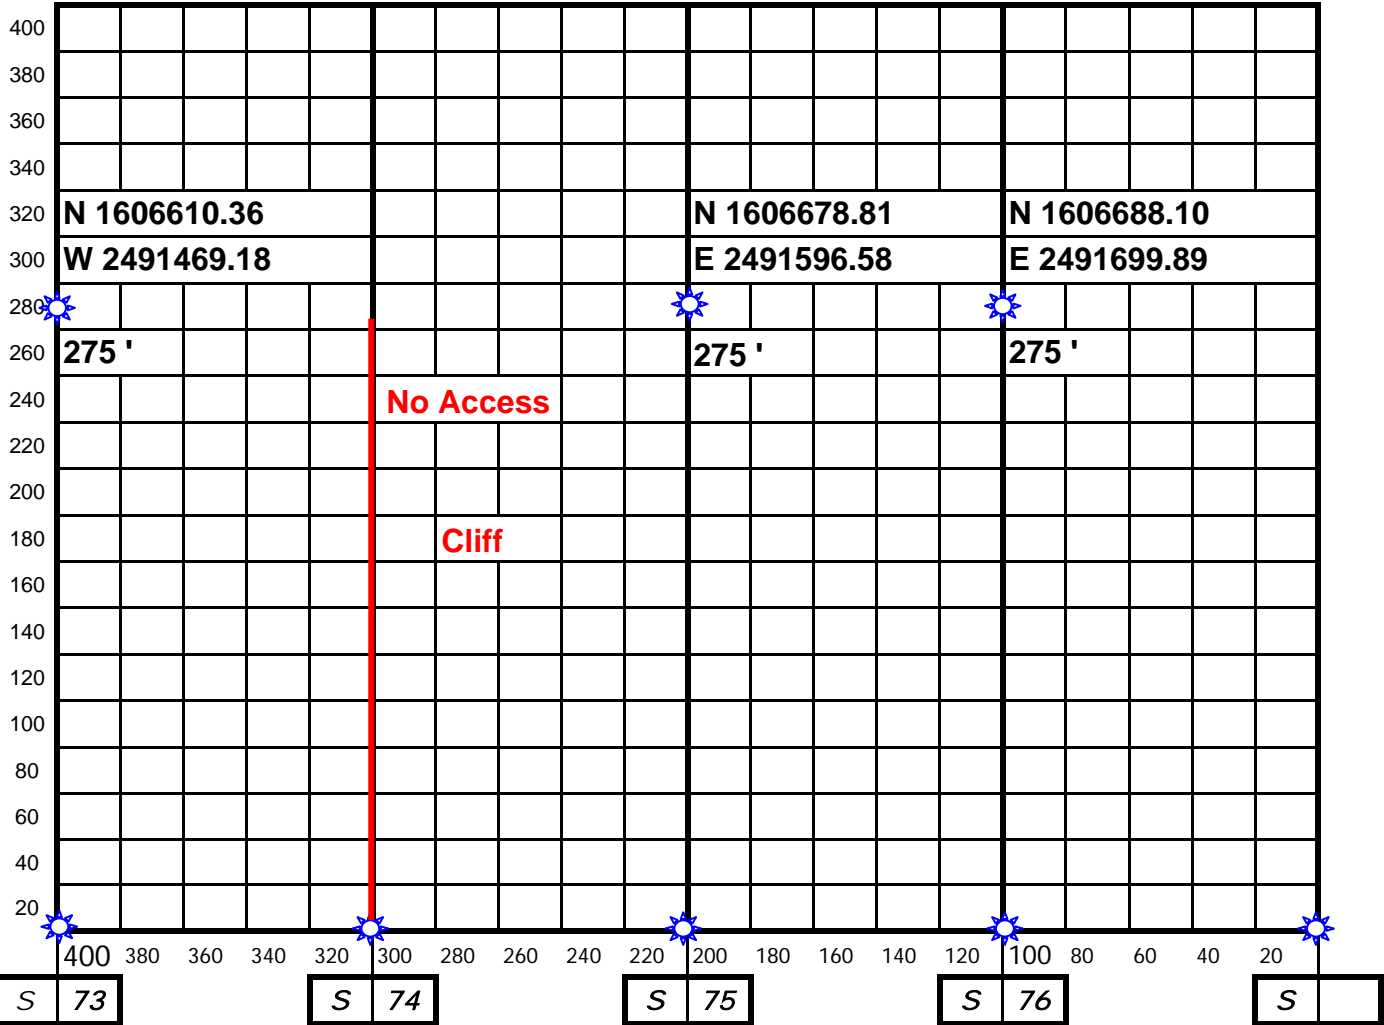


Start	Start	Start	Start	Start
9/8	9/8	9/8	9/8	
Finish	Finish	Finish	Finish	Finish
9/8	9/8	9/8	9/8	
MEC	MD	STAKE #		

Comments.Notes:

73-76 transects not accessible due to cliff:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/21/2008	Completion Date:	9/8/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

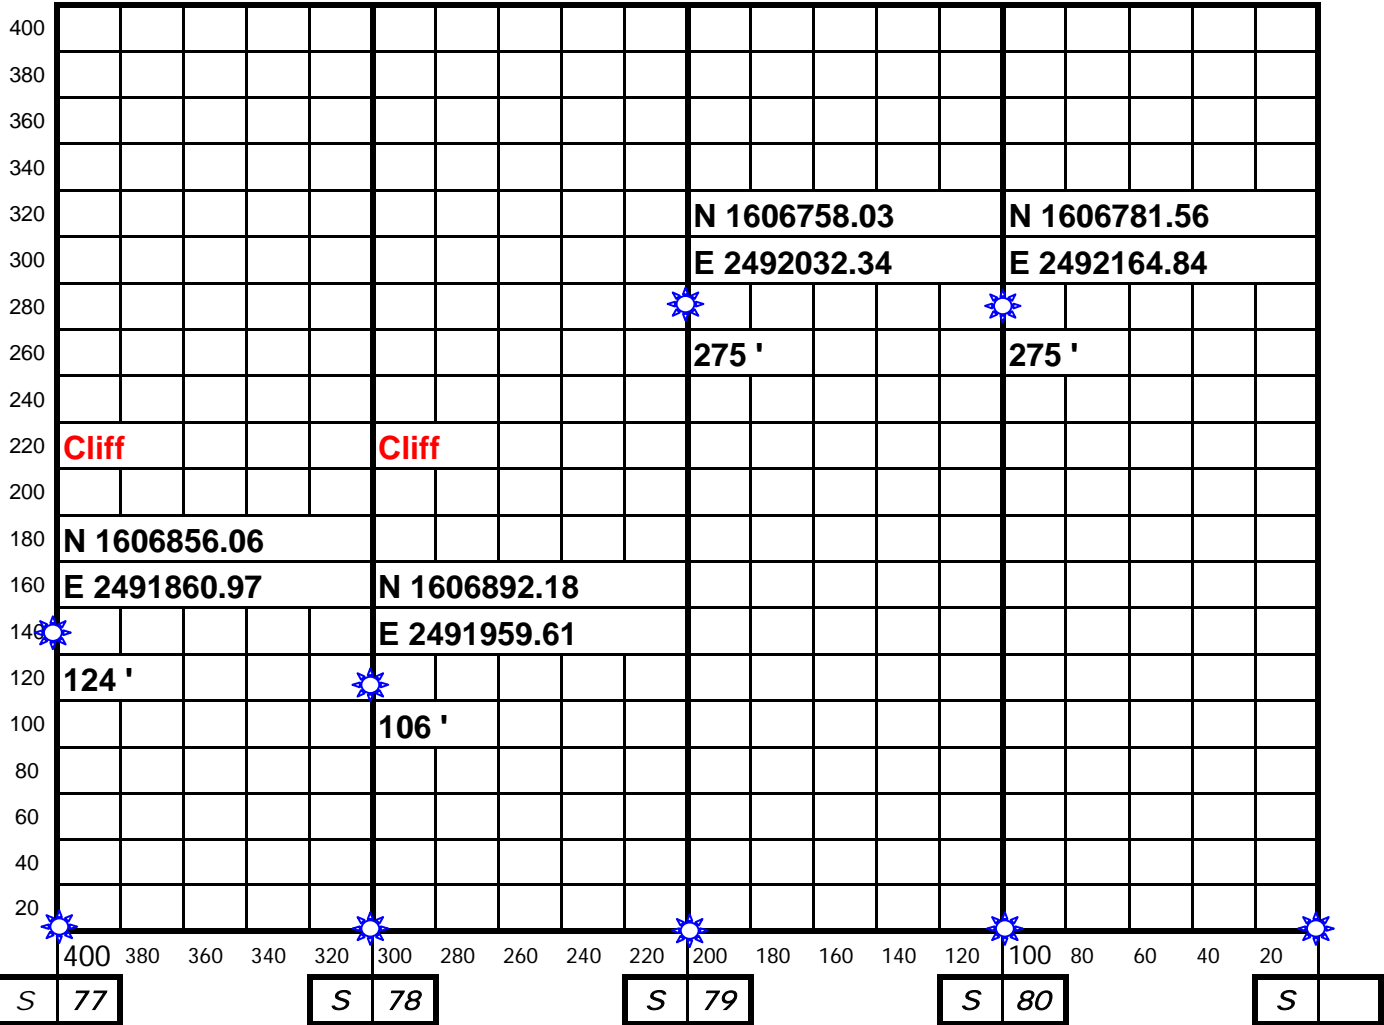


Start	Start	Start	Start	Start
9/8	9/8	9/8	21-Aug	
Finish	Finish	Finish	Finish	Finish
9/8	9/8	9/8	21-Aug	
MEC	MD	STAKE #		

Comments. Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/21/2008	Completion Date:	8/21/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

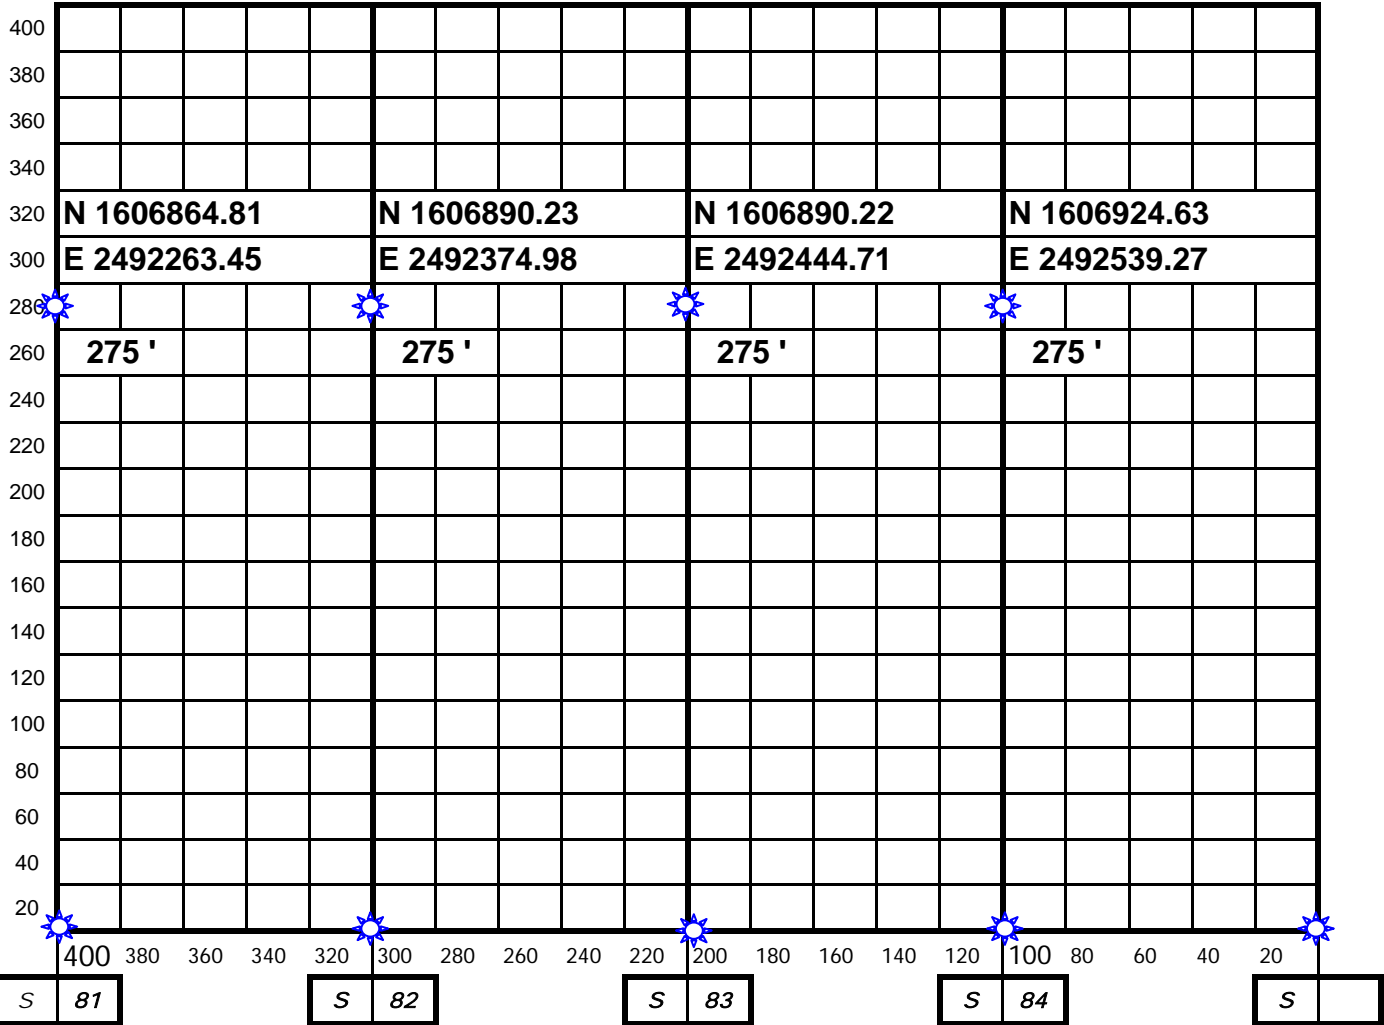


Start	Start	Start	Start	Start
<input type="text" value="8/21"/>	<input type="text" value="8/21"/>	<input type="text" value="8/21"/>	<input type="text" value="8/21"/>	<input type="text"/>
Finish	Finish	Finish	Finish	Finish
<input type="text" value="8/21"/>	<input type="text" value="8/21"/>	<input type="text" value="8/21"/>	<input type="text" value="8/21"/>	<input type="text"/>
MEC	MD	STAKE #		

Comments/Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/21/2008	Completion Date:	8/21/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

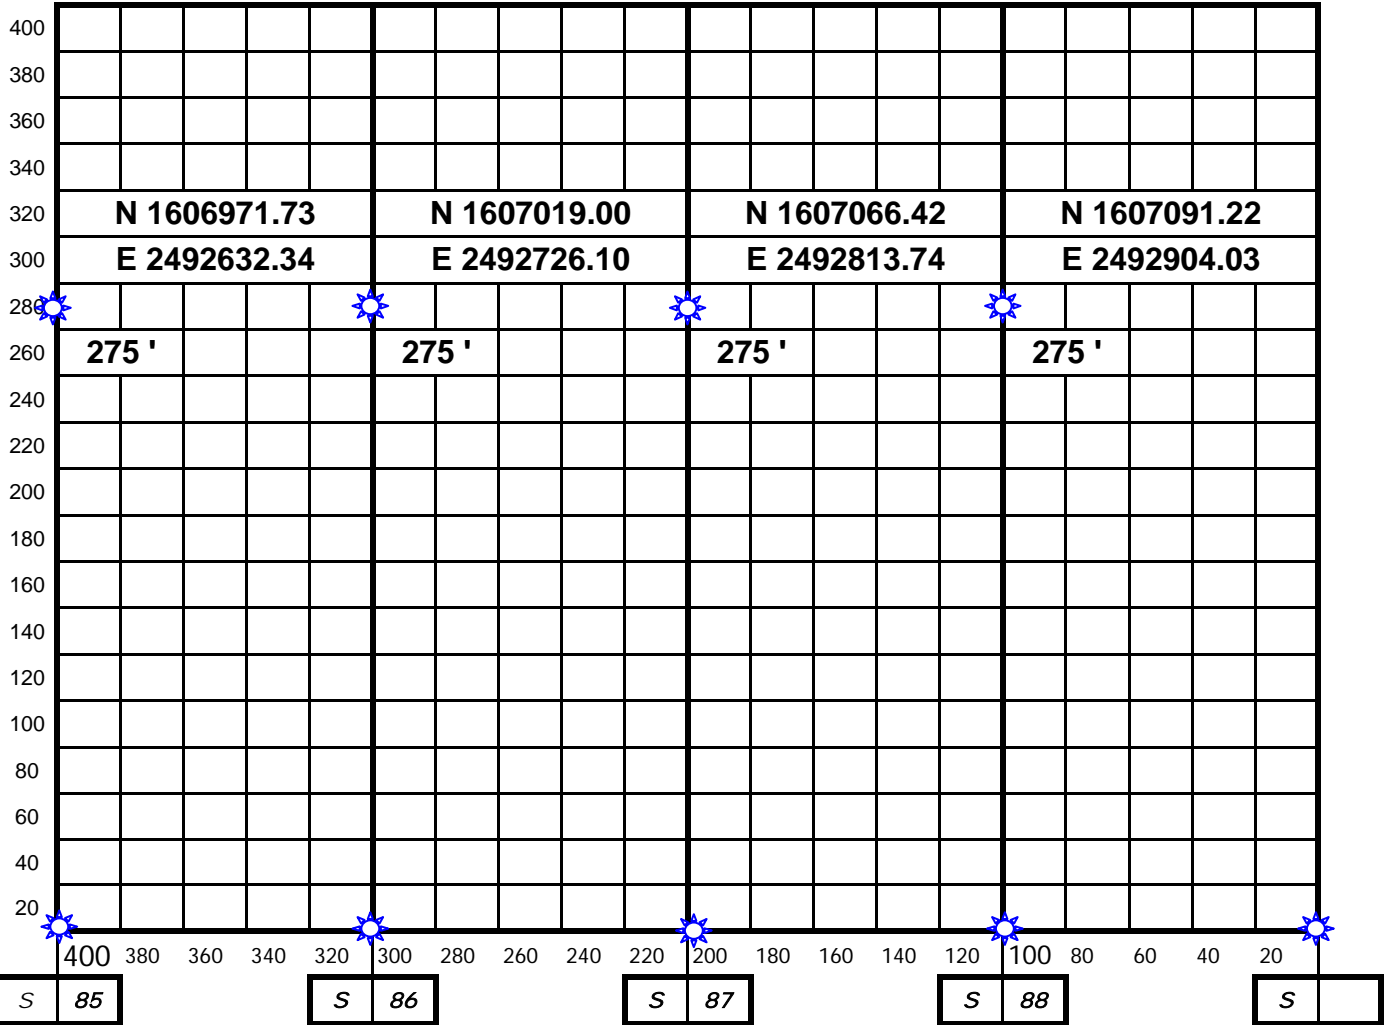


Start	Start	Start	Start	Start
8/21	8/21	8/21	8/21	
Finish	Finish	Finish	Finish	Finish
8/21	8/21	8/21	8/21	
MEC	MD	STAKE #		

Comments/Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/21/2008	Completion Date:	8/21/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

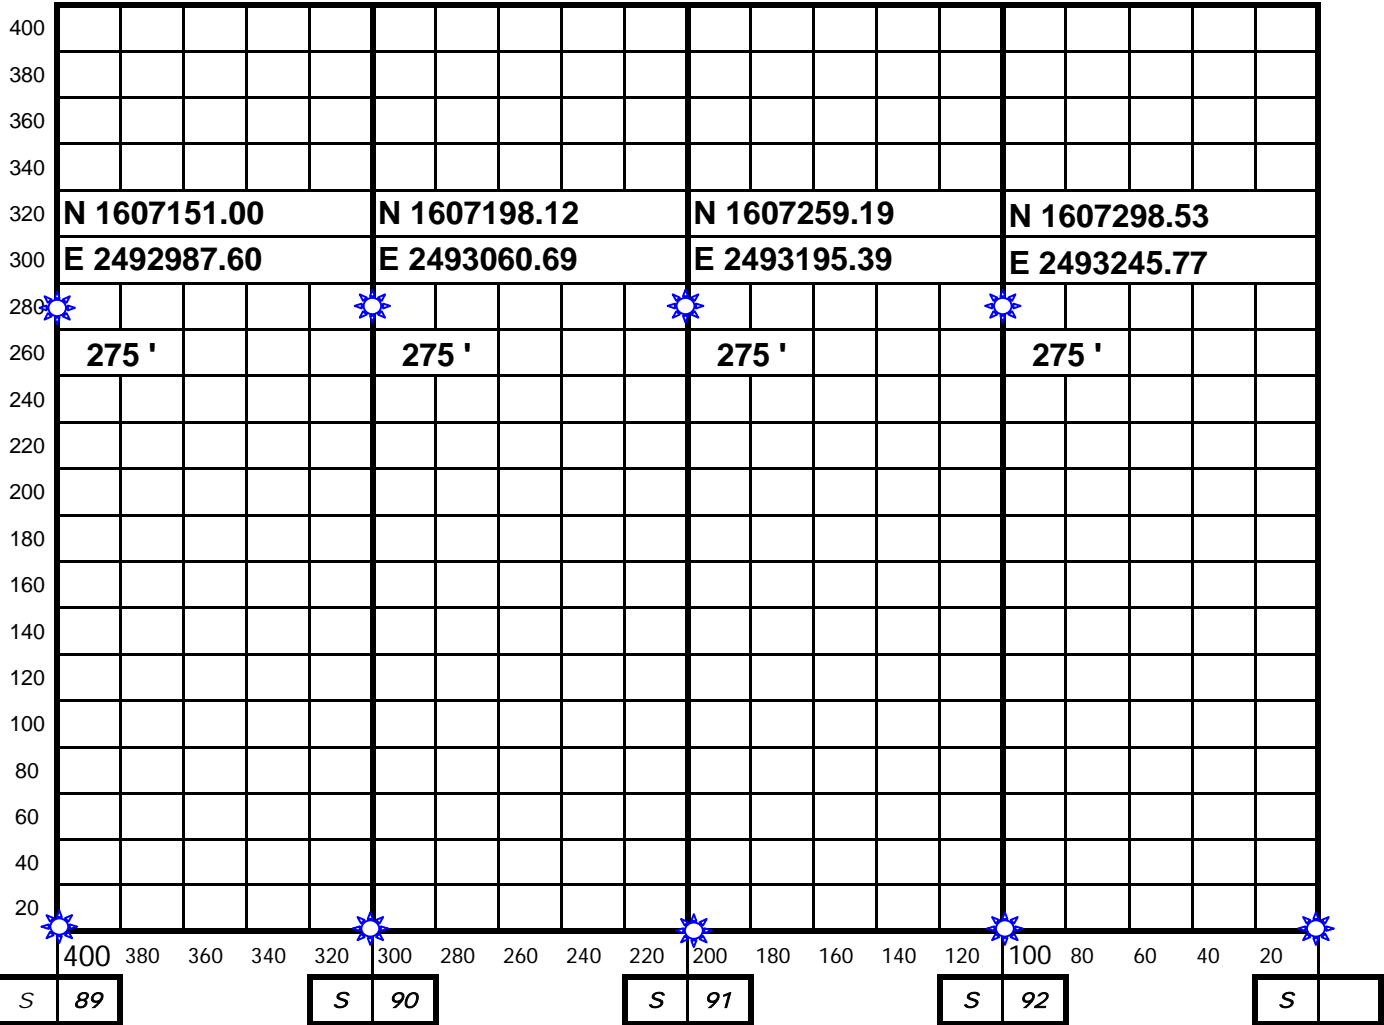


Start	Start	Start	Start	Start	
8/21	8/21	8/21	8/21		
Finish	Finish	Finish	Finish	Finish	
8/21	8/21	8/21	8/21		
	MEC		MD		STAKE #

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/21/2008	Completion Date:	8/21/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

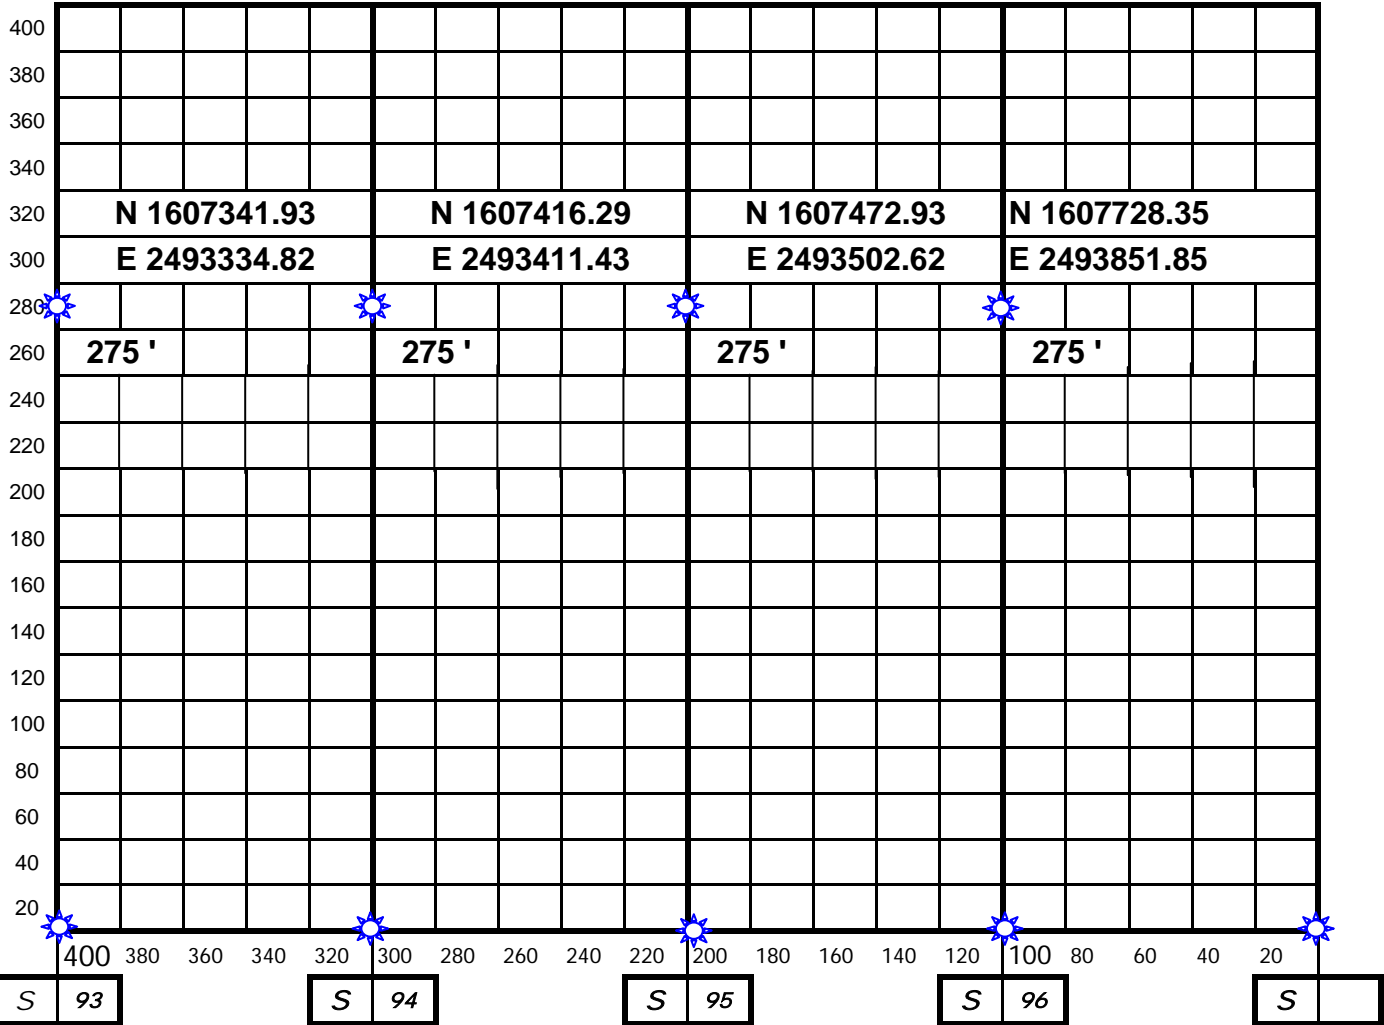


Start	Start	Start	Start	Start	
8/21	8/21	8/21	8/21		
Finish	Finish	Finish	Finish	Finish	
8/21	8/21	8/21	8/21		
	MEC		MD		STAKE #

Comments. Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/21/2008	Completion Date:	8/21/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

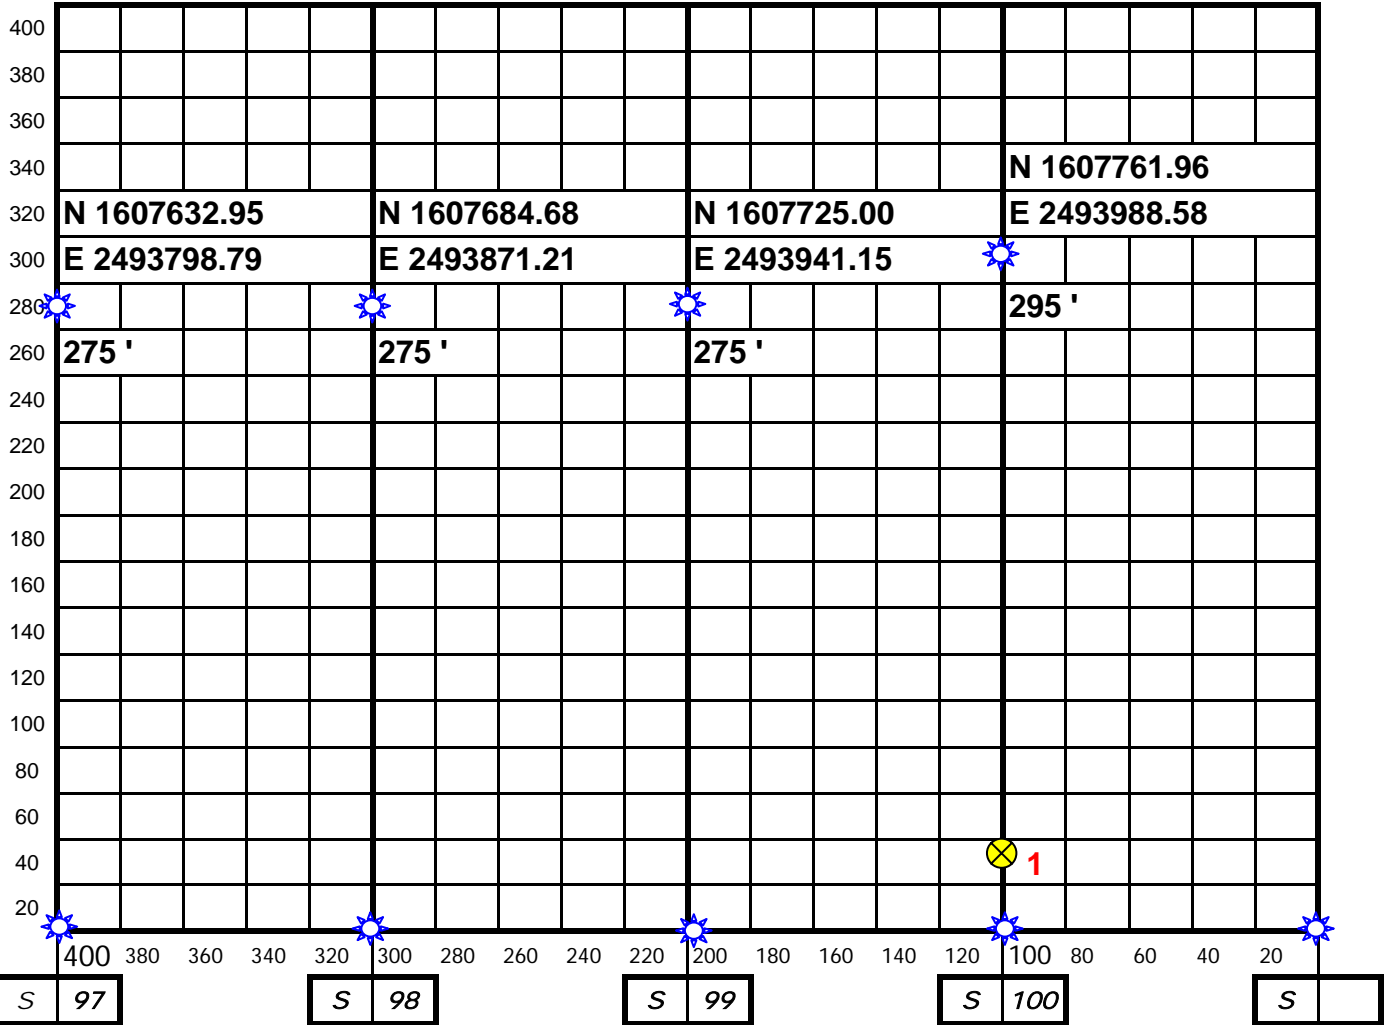

Start	Start	Start	Start	Start
<input type="text" value="8/21"/>	<input type="text" value="8/21"/>	<input type="text" value="8/21"/>	<input type="text" value="8/21"/>	<input type="text"/>
Finish	Finish	Finish	Finish	Finish
<input type="text" value="8/21"/>	<input type="text" value="8/21"/>	<input type="text" value="8/21"/>	<input type="text" value="8/21"/>	<input type="text"/>
MEC	MD	STAKE #		


Comments.Notes:

Anomalies

#	ID	Northing	Easting	Comments
1	S100-A	1608026.56	2493893.07	Base plate
2				
3				
4				
5				
6				
7				
8				
9				
10				
11				
12				
13				
14				
15				
16				
17				
18				
19				
20				
21				
22				
23				
24				
25				
26				
27				
28				
29				
30				
31				
32				
33				
34				
35				
36				
37				
38				
39				
40				
41				
42				
43				
44				

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/21/2008	Completion Date:	8/21/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

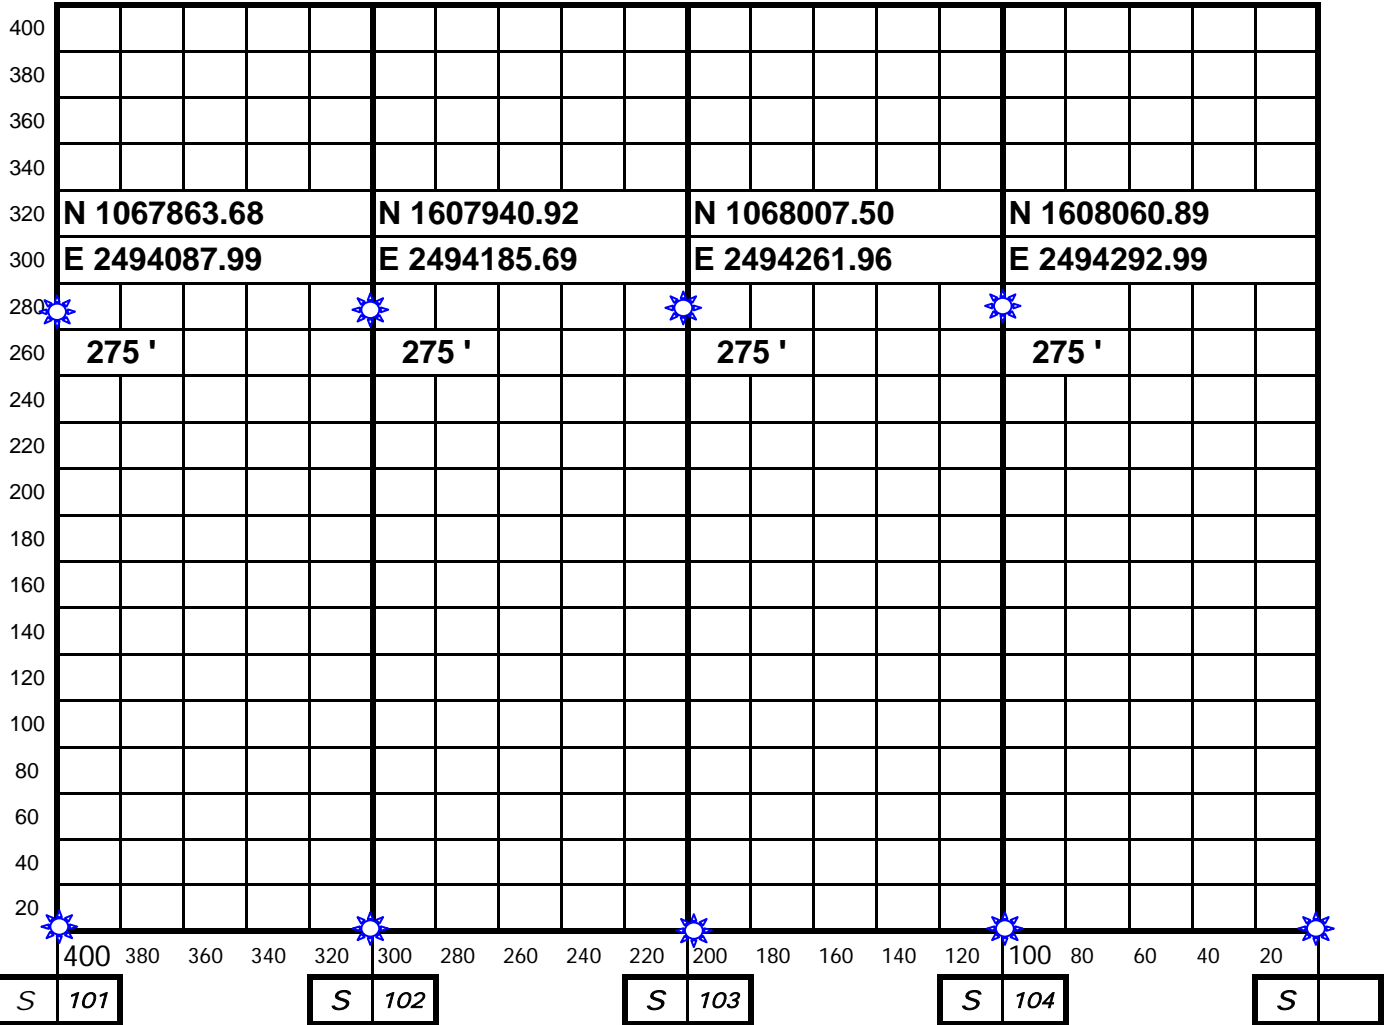


Start	Start	Start	Start	Start
8/21	8/21	8/21	8/21	
Finish	Finish	Finish	Finish	Finish
8/21	8/21	8/21	8/21	
	MEC		MD	
				STAKE #

Comments.Notes:

S-102 through S-106 are EM-61 accessible

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/21/2008	Completion Date:	8/21/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

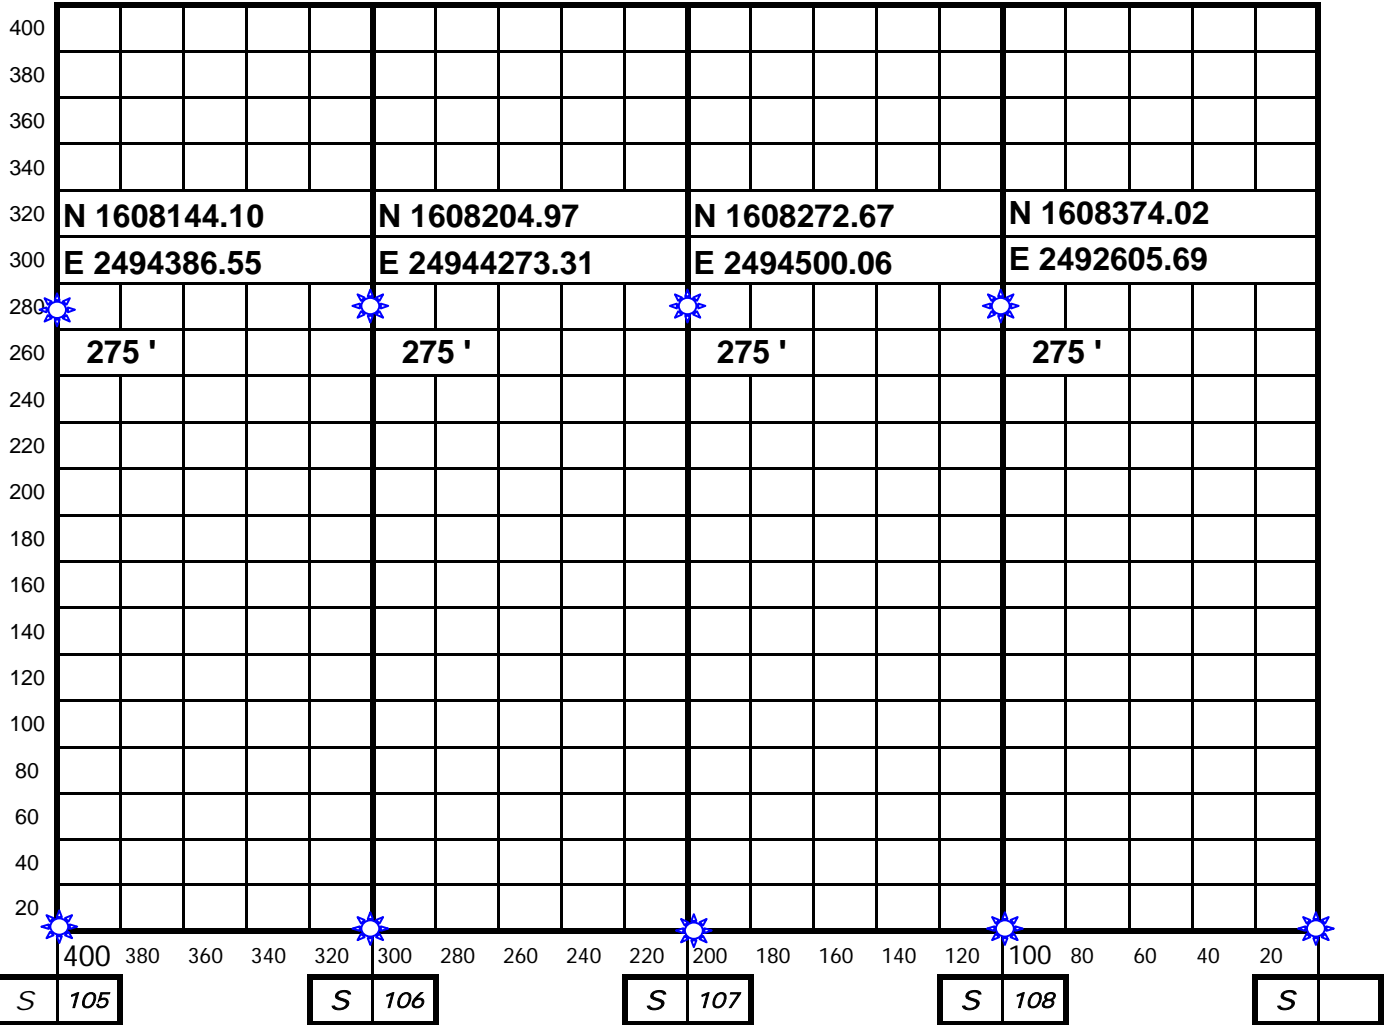


Start	Start	Start	Start	Start	
8/21	8/21	8/21	8/21		
Finish	Finish	Finish	Finish	Finish	
8/21	8/21	8/21	8/21		
	MEC		MD		STAKE #

Comments. Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:		Completion Date:	
QC Date:		QC Signature:	
QA Date:		QA Signature:	

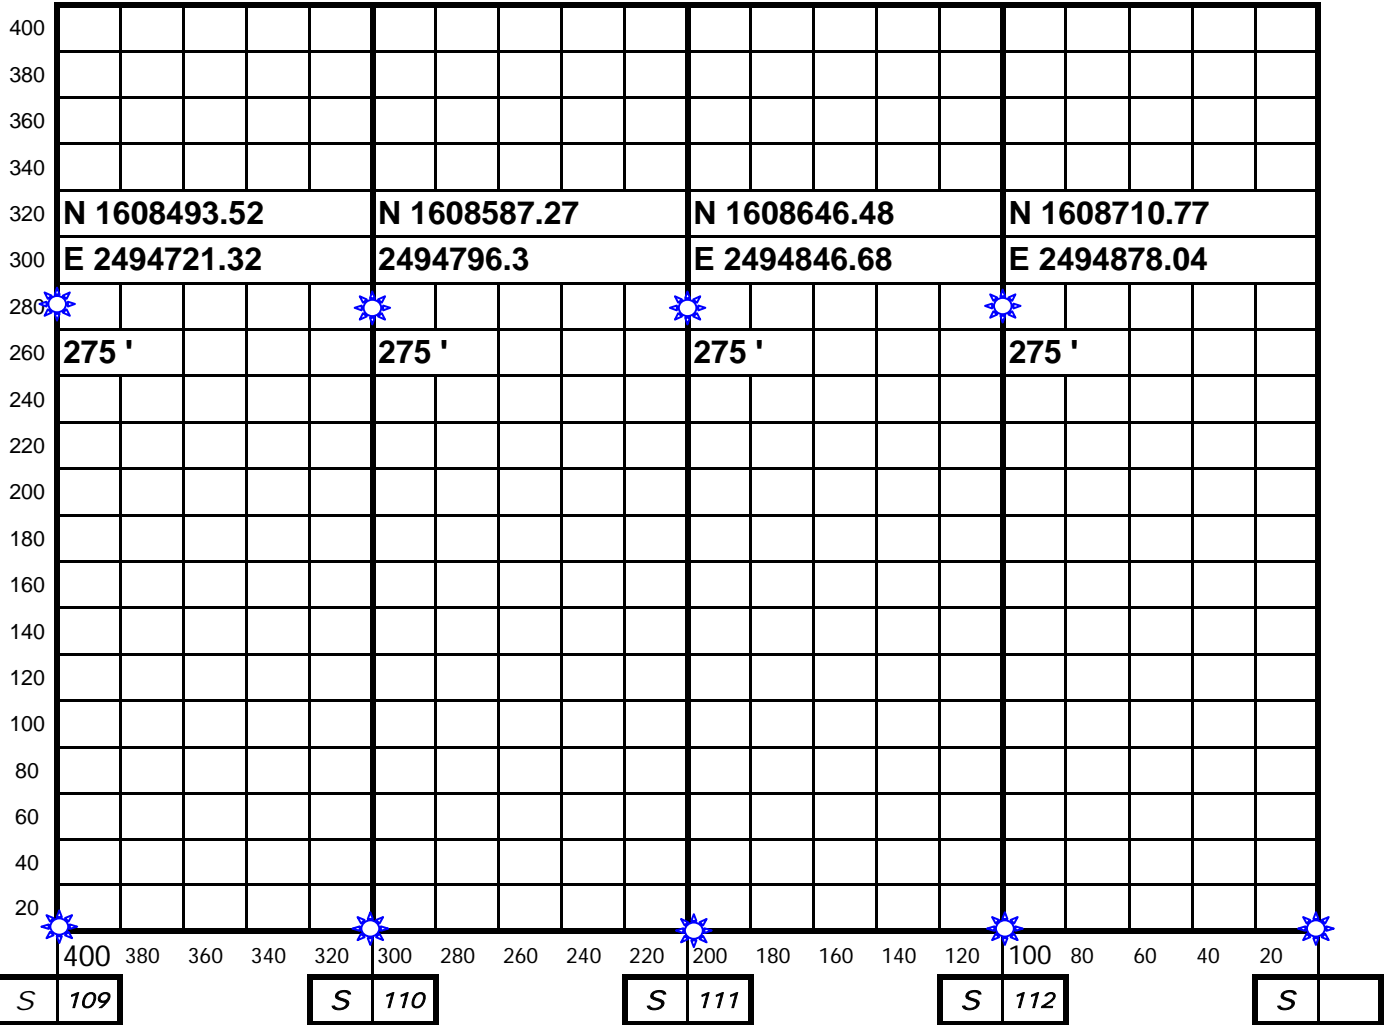


Start	Start	Start	Start	Start	
8/20	8/20	8/20	8/20		
Finish	Finish	Finish	Finish	Finish	
8/20	8/20	8/20	8/20		
	MEC		MD		STAKE #

Comments. Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/20/2008	Completion Date:	8/20/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

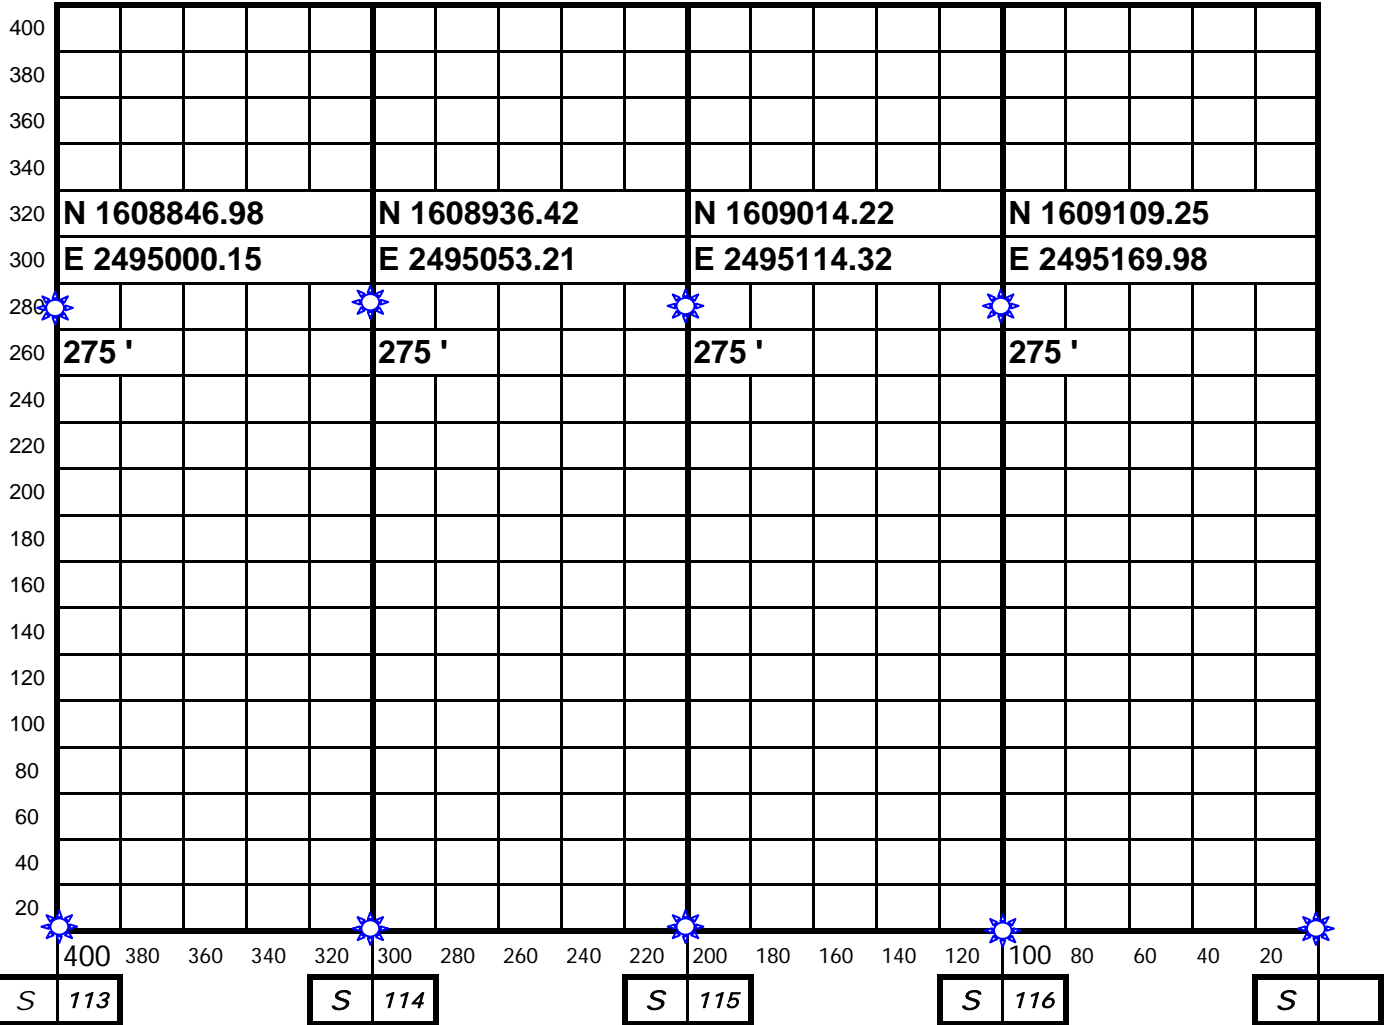


Start	Start	Start	Start	Start	
8/20	8/20	8/20	8/20		
Finish	Finish	Finish	Finish	Finish	
8/20	8/20	8/20	8/20		
	MEC		MD		STAKE #

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/20/2008	Completion Date:	8/20/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

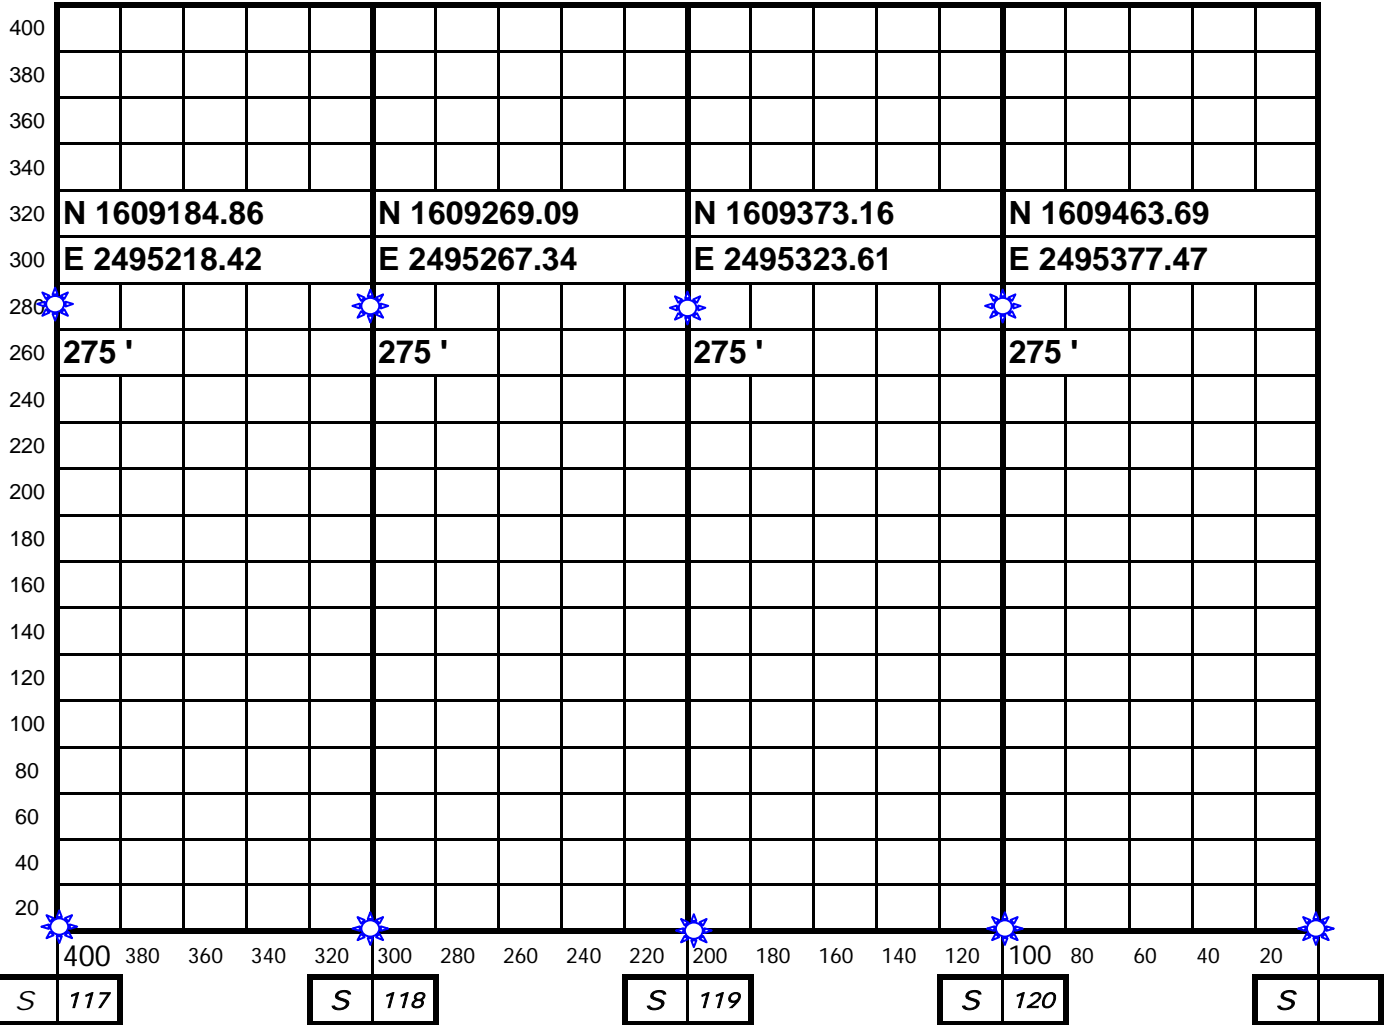


Start	Start	Start	Start	Start	
8/20	8/20	8/20	8/20		
Finish	Finish	Finish	Finish	Finish	
8/20	8/20	8/20	8/20		
	MEC		MD		STAKE #

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/20/2008	Completion Date:	8/20/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

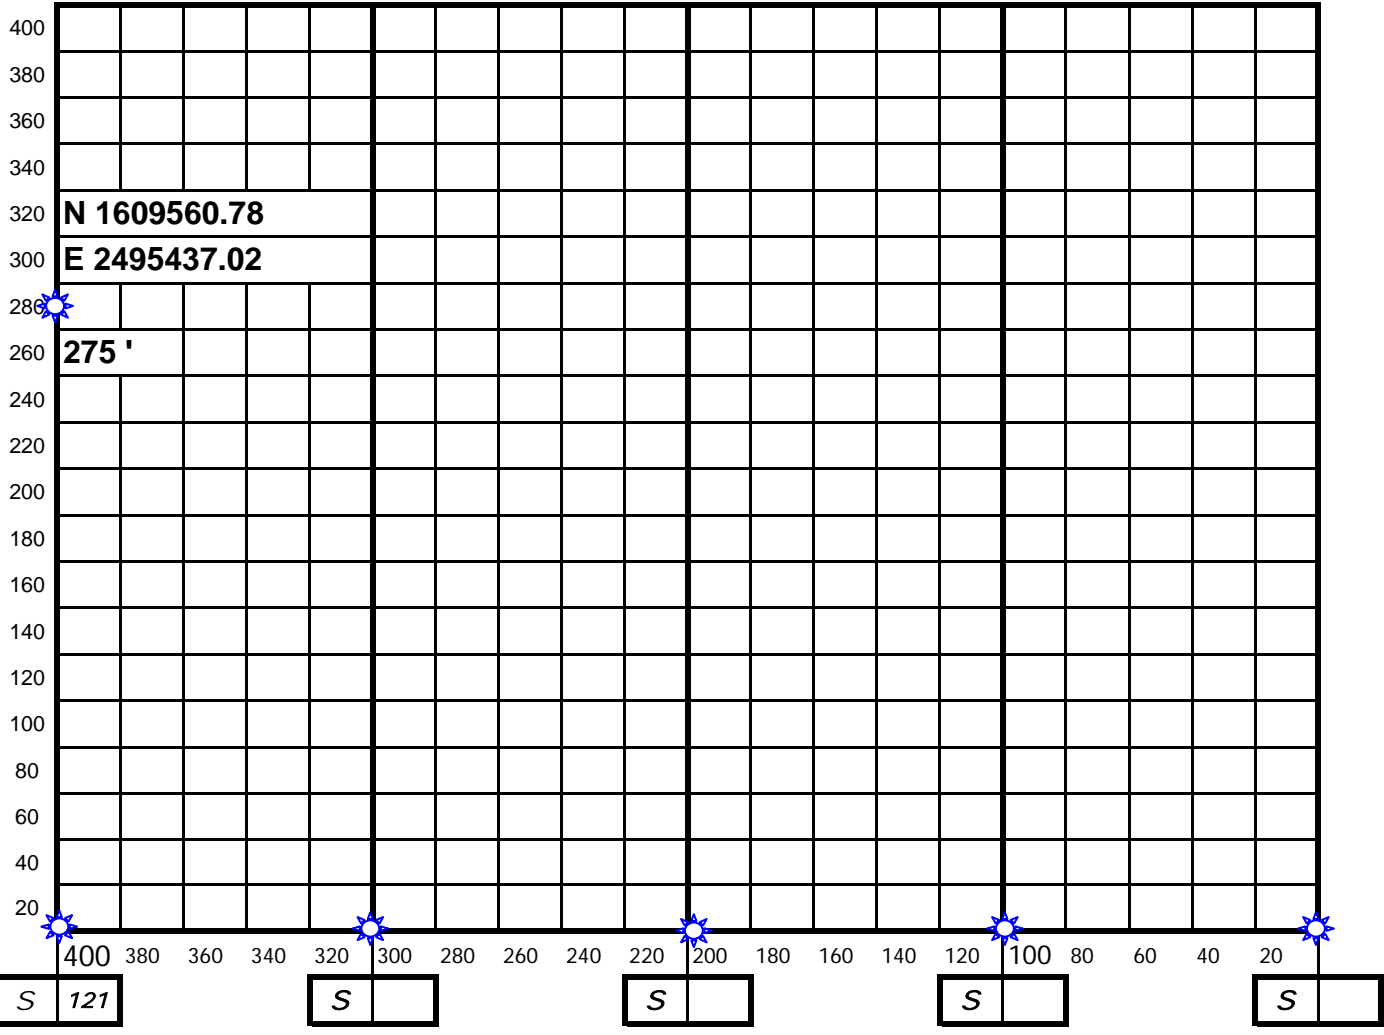


Start	Start	Start	Start	Start
8/20				
Finish	Finish	Finish	Finish	Finish
8/20				
MEC	MD	STAKE #		

Comments.Notes:

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/7/2009	Completion Date:	4/7/2009
QC Date:		QA Date	

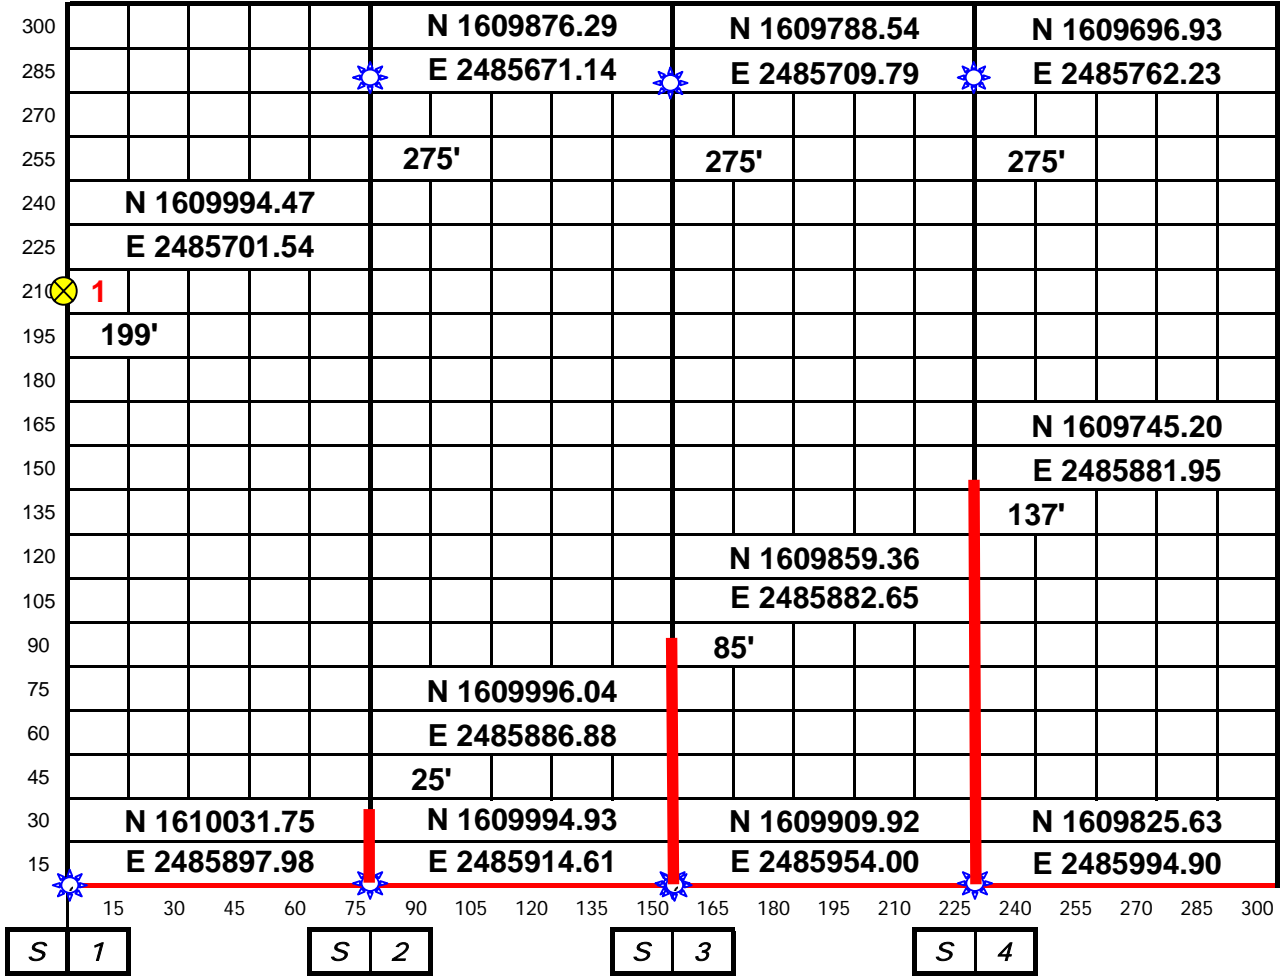

Start 4/7	Start 4/7	Start 4/7	Start 4/7
Finish 4/7	Finish 4/7	Finish 4/7	Finish 4/7
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

S2 No Access/Safety first 25 feet (Fence/Road)


S3 No Access/Safety first 85 feet (Fence)

S4 No Access/Safety first 137 feet (Fence)

1 Fragmentation

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/7/2009	Completion Date:	4/8/2009
QC Date:		QA Date	

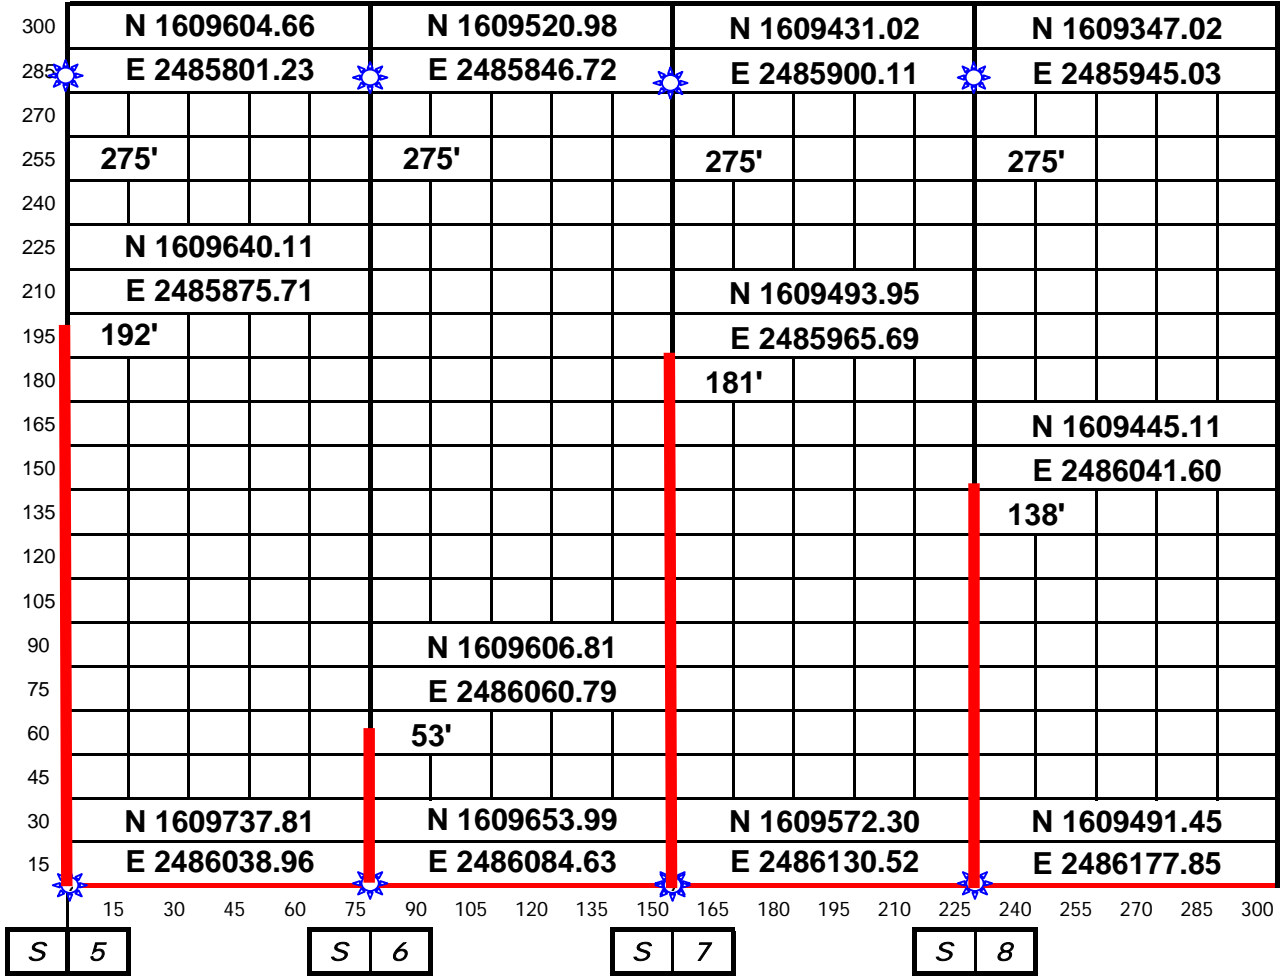

Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/7</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/7</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/8</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/8</div>
Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/7</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/7</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/8</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/8</div>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

S5 No Access/Safety first 192 feet (Fence)


S6 No Access/Safety first 53 feet

S7 No Access/Safety first 181 feet (Straight Down)

S8 No Access/Safety first 138 feet (Straight Down)

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/8/2009	Completion Date:	4/8/2009
QC Date:		QA Date	

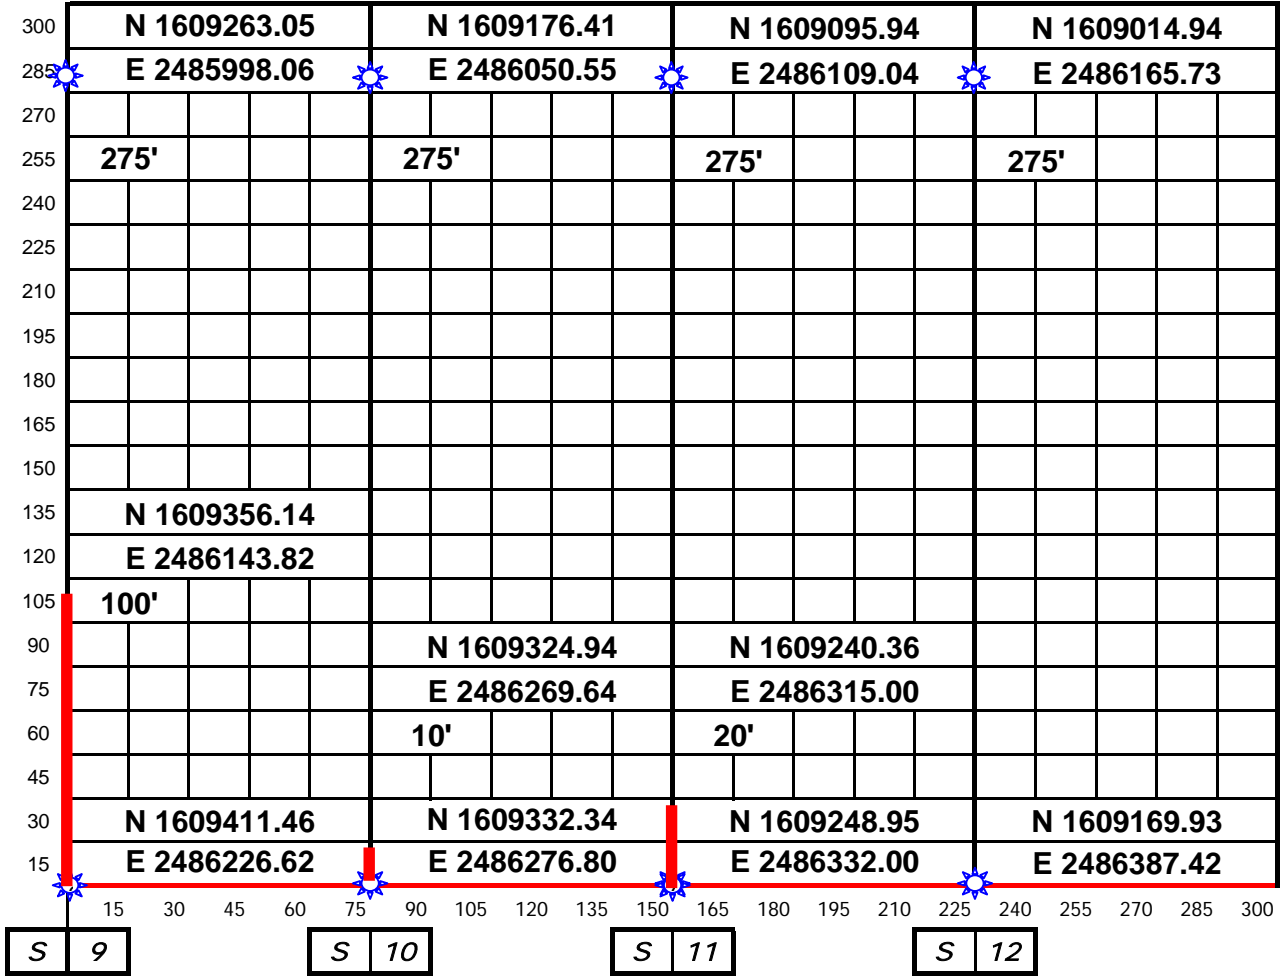

Start <input type="text" value="4/8"/>	Start <input type="text" value="4/8"/>	Start <input type="text" value="4/8"/>	Start <input type="text" value="4/8"/>
Finish <input type="text" value="4/8"/>	Finish <input type="text" value="4/8"/>	Finish <input type="text" value="4/8"/>	Finish <input type="text" value="4/8"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:


S9 No Access/Safety first 100 feet (Straight Down)

S10 End point offset 10 feet west for safety

S11 No Access/Safety first 20 feet

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/8/2009	Completion Date:	4/8/2009
QC Date:		QA Date	

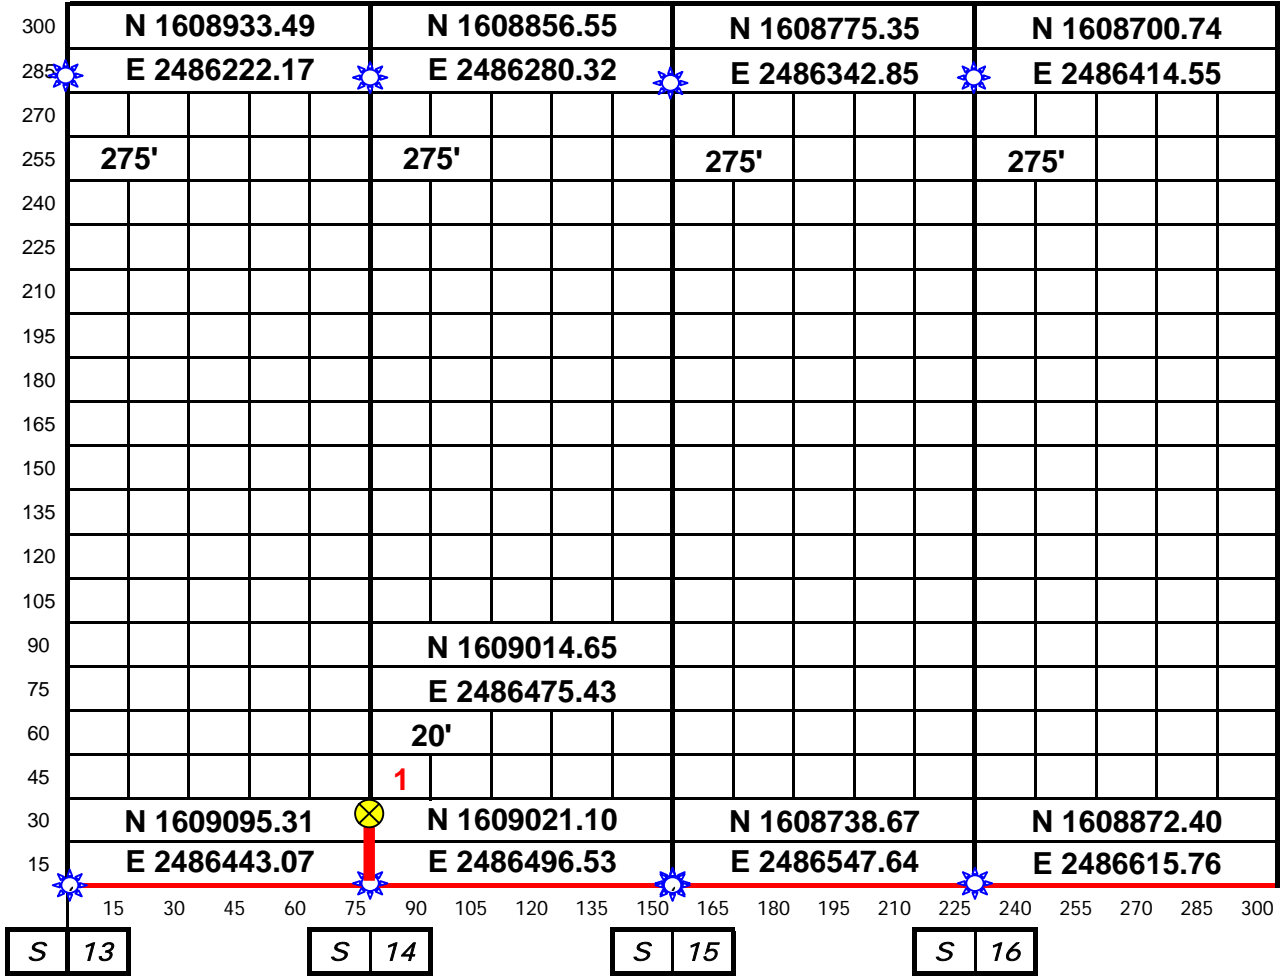

Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/8</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/8</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/8</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/8</div>
Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/8</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/8</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/8</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/8</div>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	


Comments:

S14 No Access/Safety first 20 feet

1 Fragmentation

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/8/2009	Completion Date:	4/9/2009
QC Date:		QA Date	

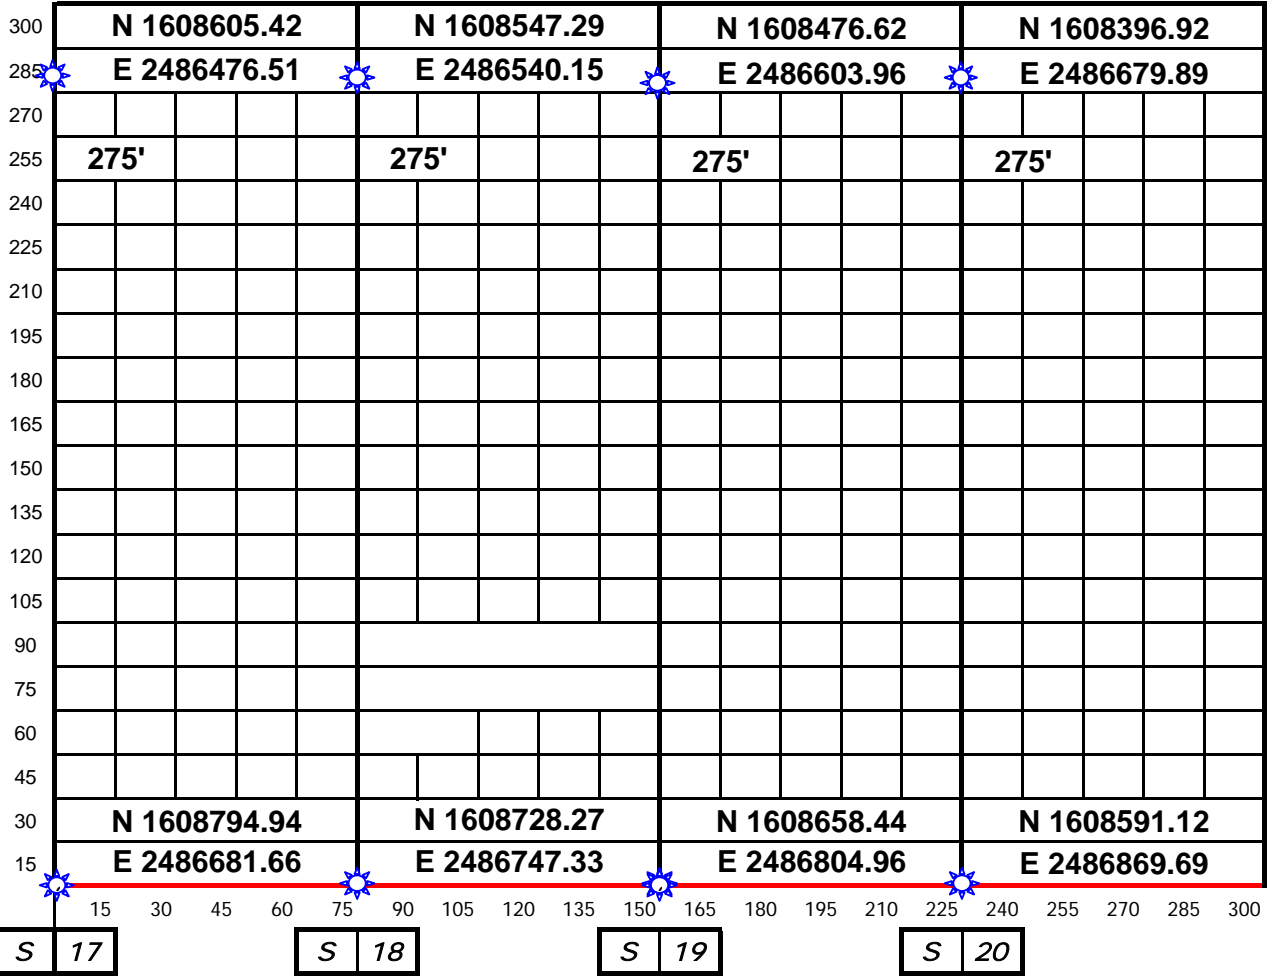


Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/8</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/8</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/9</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/9</div>
Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/8</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/8</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/9</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/9</div>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/9/2009	Completion Date:	4/16/2009
QC Date:		QA Date	

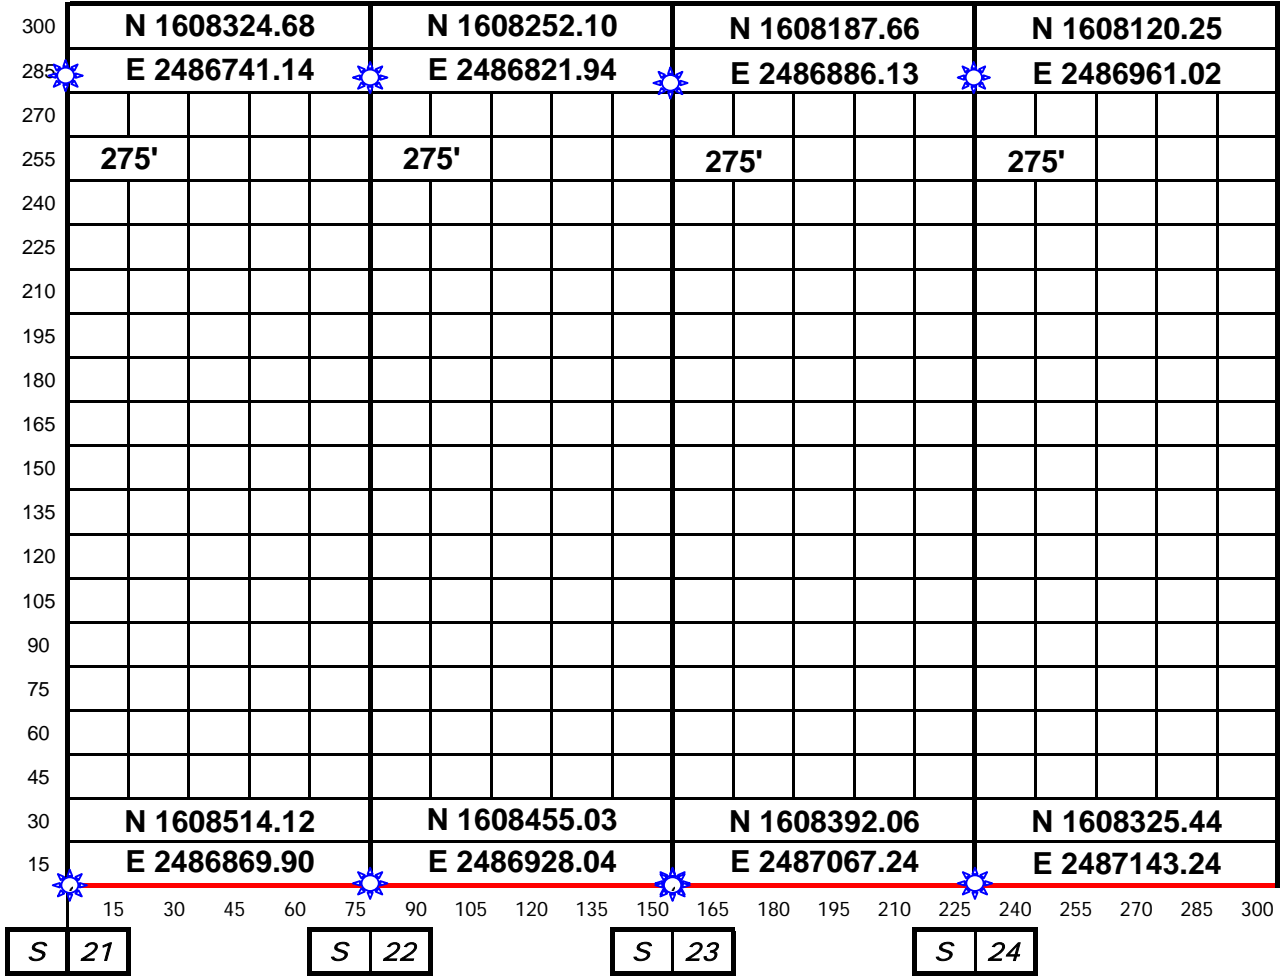


Start <input type="text" value="4/16"/>	Start <input type="text" value="4/16"/>	Start <input type="text" value="4/9"/>	Start <input type="text" value="4/9"/>
Finish <input type="text" value="4/16"/>	Finish <input type="text" value="4/16"/>	Finish <input type="text" value="4/9"/>	Finish <input type="text" value="4/9"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/9/2009	Completion Date:	4/9/2009
QC Date:		QA Date	

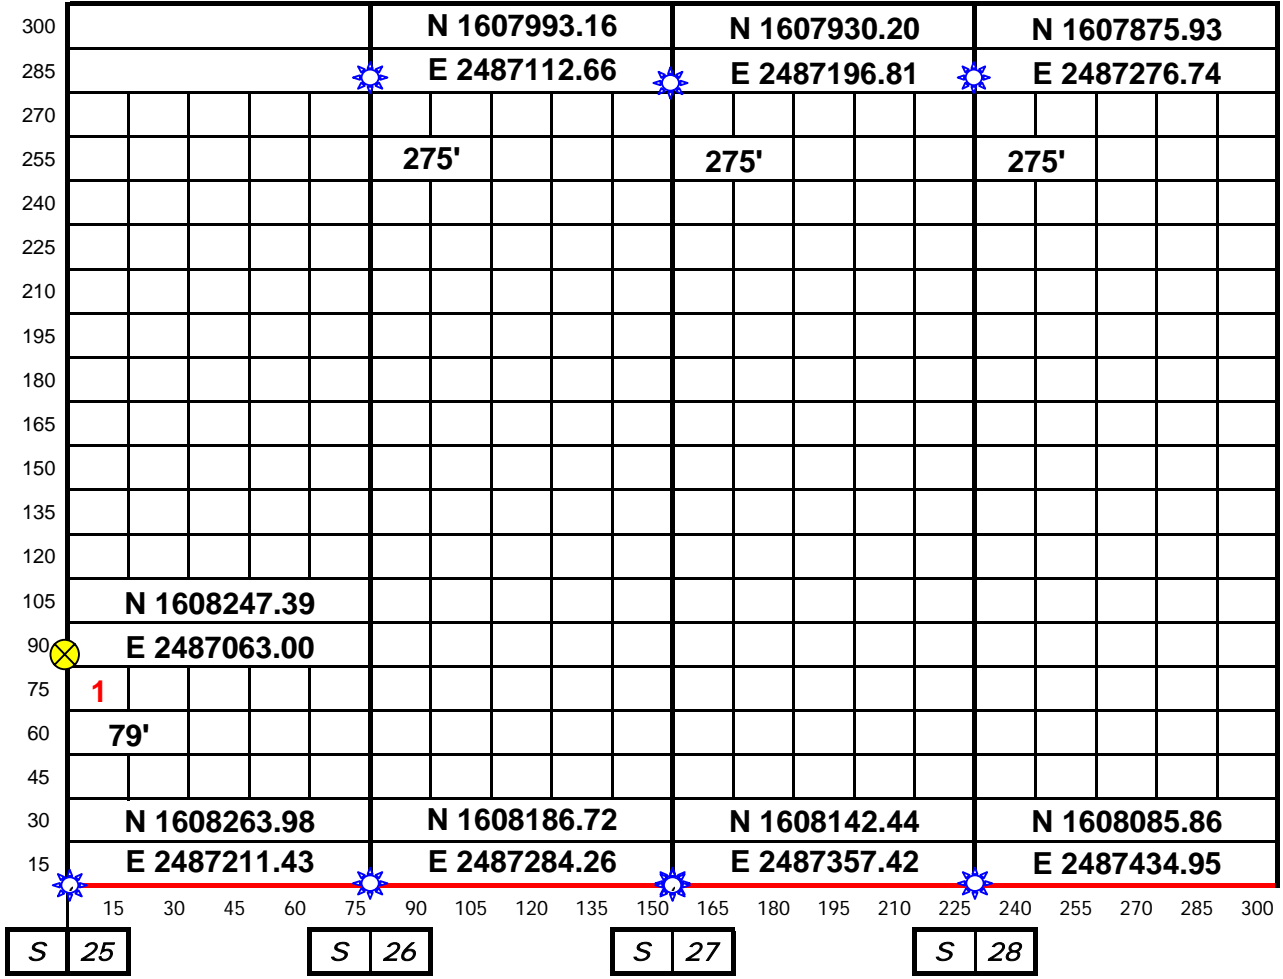


Start <input type="text" value="4/9"/>	Start <input type="text" value="4/9"/>	Start <input type="text" value="4/9"/>	Start <input type="text" value="4/9"/>
Finish <input type="text" value="4/9"/>	Finish <input type="text" value="4/9"/>	Finish <input type="text" value="4/9"/>	Finish <input type="text" value="4/9"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

1 Fragmentation

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/9/2009	Completion Date:	4/16/2009
QC Date:		QA Date	

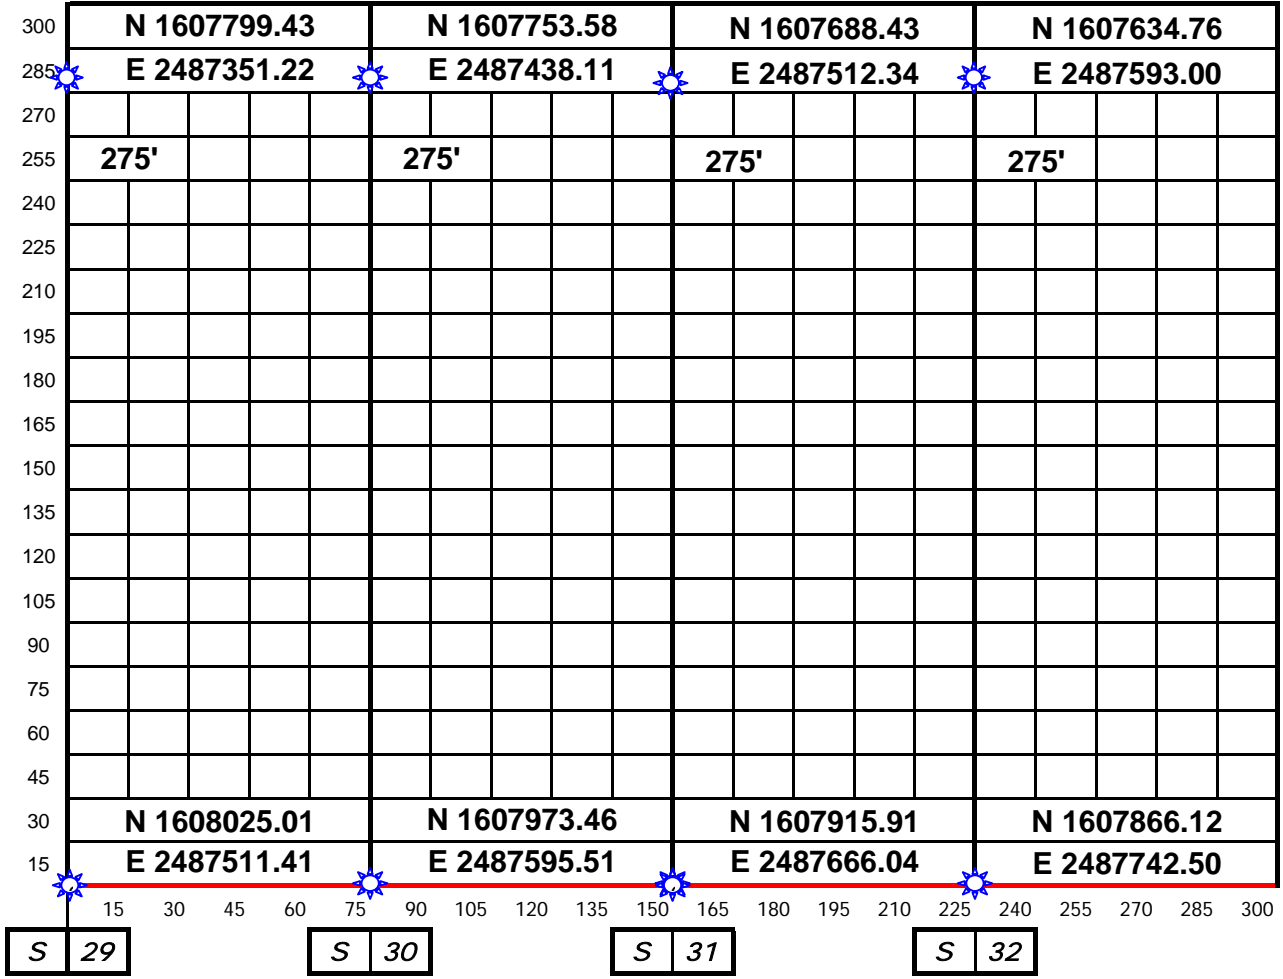


Start <input type="text" value="4/9"/>	Start <input type="text" value="4/9"/>	Start <input type="text" value="4/16"/>	Start <input type="text" value="4/16"/>
Finish <input type="text" value="4/9"/>	Finish <input type="text" value="4/9"/>	Finish <input type="text" value="4/16"/>	Finish <input type="text" value="4/16"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/16/2009	Completion Date:	
QC Date:		QA Date	

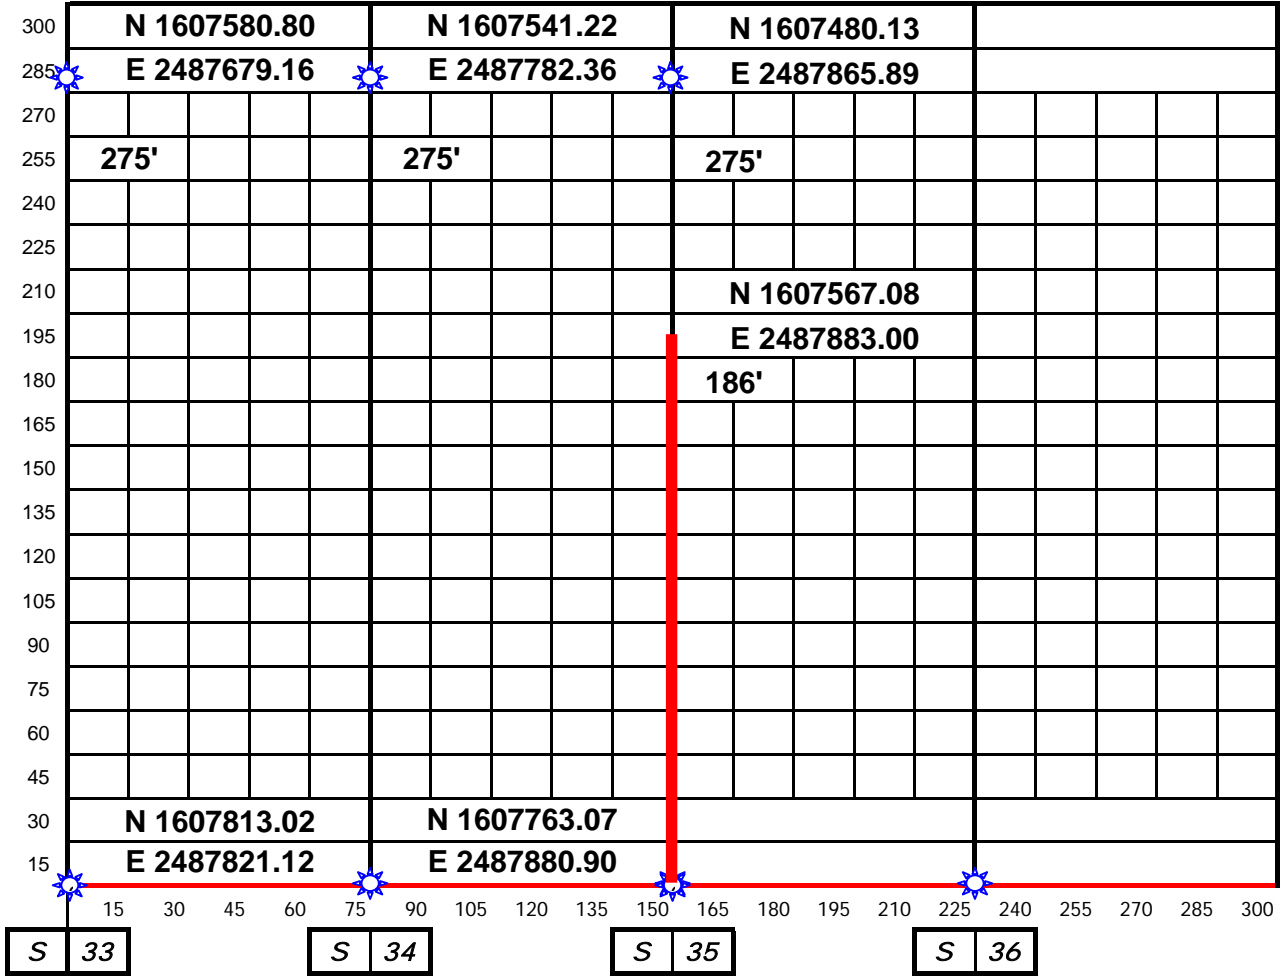


Start <input type="text" value="4/16"/>	Start <input type="text" value="4/16"/>	Start <input type="text" value="4/16"/>	Start <input type="text" value="4/16"/>
Finish <input type="text" value="4/16"/>	Finish <input type="text" value="4/16"/>	Finish <input type="text" value="4/16"/>	Finish <input type="text" value="4/16"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

W35 No Access/Safety first 186' from red line

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/14/2009	Completion Date:	
QC Date:		QA Date	

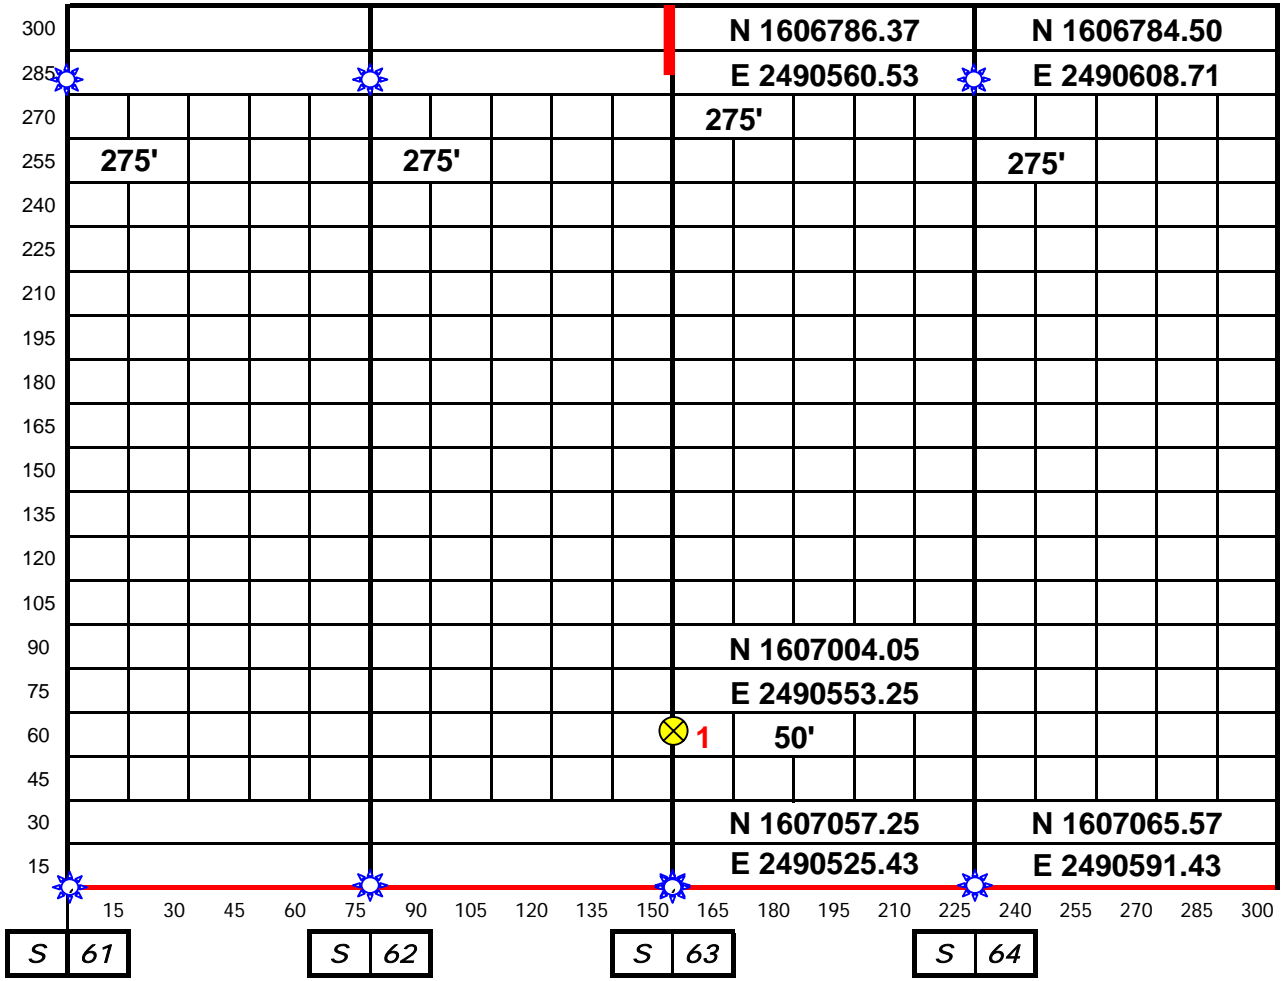

Start <input type="text"/>	Start <input type="text"/>	Start <input type="text" value="4/14"/>	Start <input type="text" value="4/14"/>
Finish <input type="text"/>	Finish <input type="text"/>	Finish <input type="text" value="4/14"/>	Finish <input type="text" value="4/14"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	


Comments:

1 Fragmentation

W63 No Access/Safety beyond 275 feet

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/14/2009	Completion Date:	4/15/2009
QC Date:		QA Date	

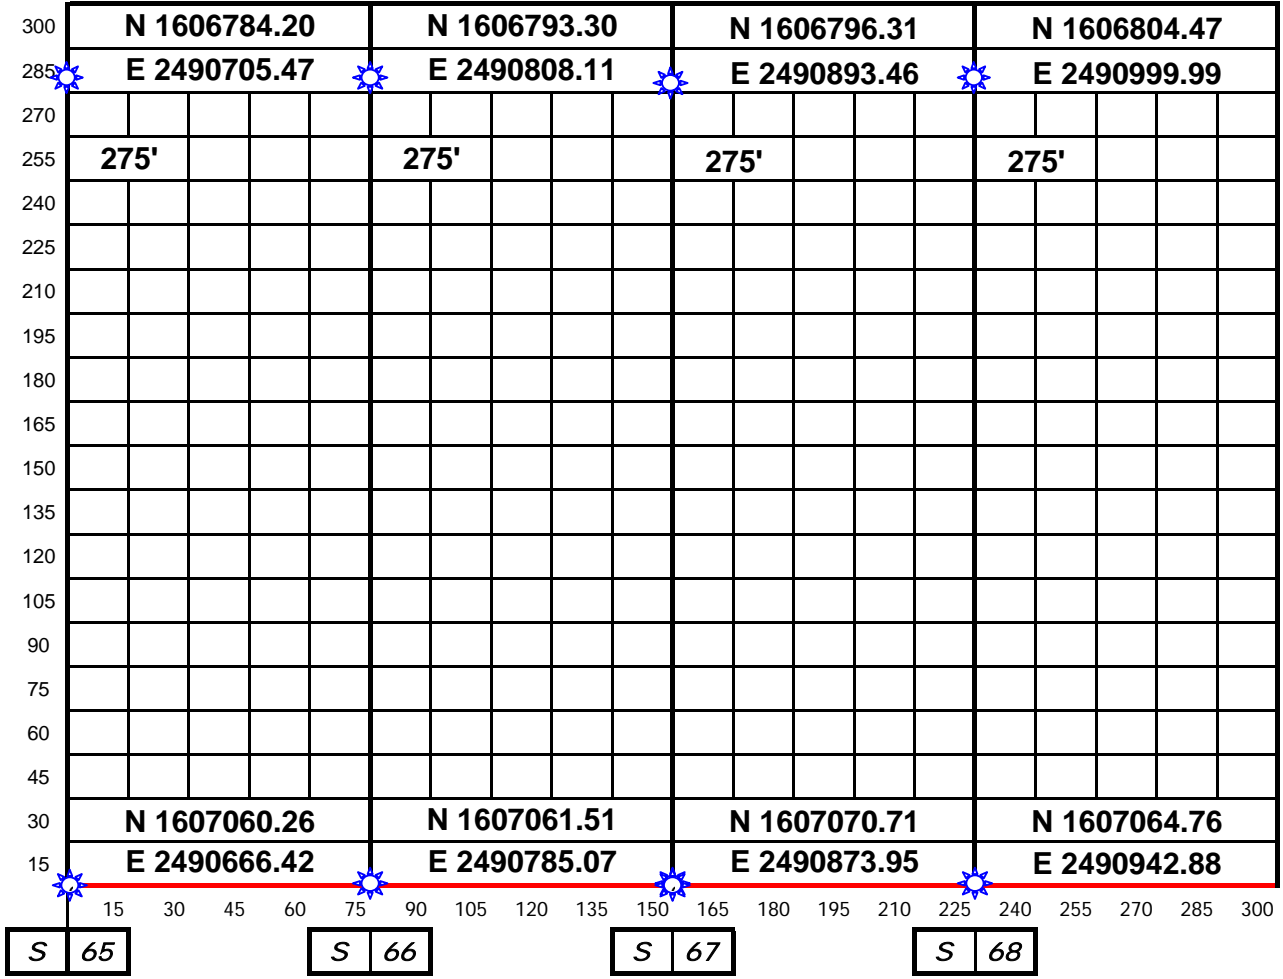


Start <input type="text" value="4/14"/>	Start <input type="text" value="4/14"/>	Start <input type="text" value="4/15"/>	Start <input type="text" value="4/15"/>
Finish <input type="text" value="4/14"/>	Finish <input type="text" value="4/14"/>	Finish <input type="text" value="4/15"/>	Finish <input type="text" value="4/15"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/15/2009	Completion Date:	4/15/2009
QC Date:		QA Date	

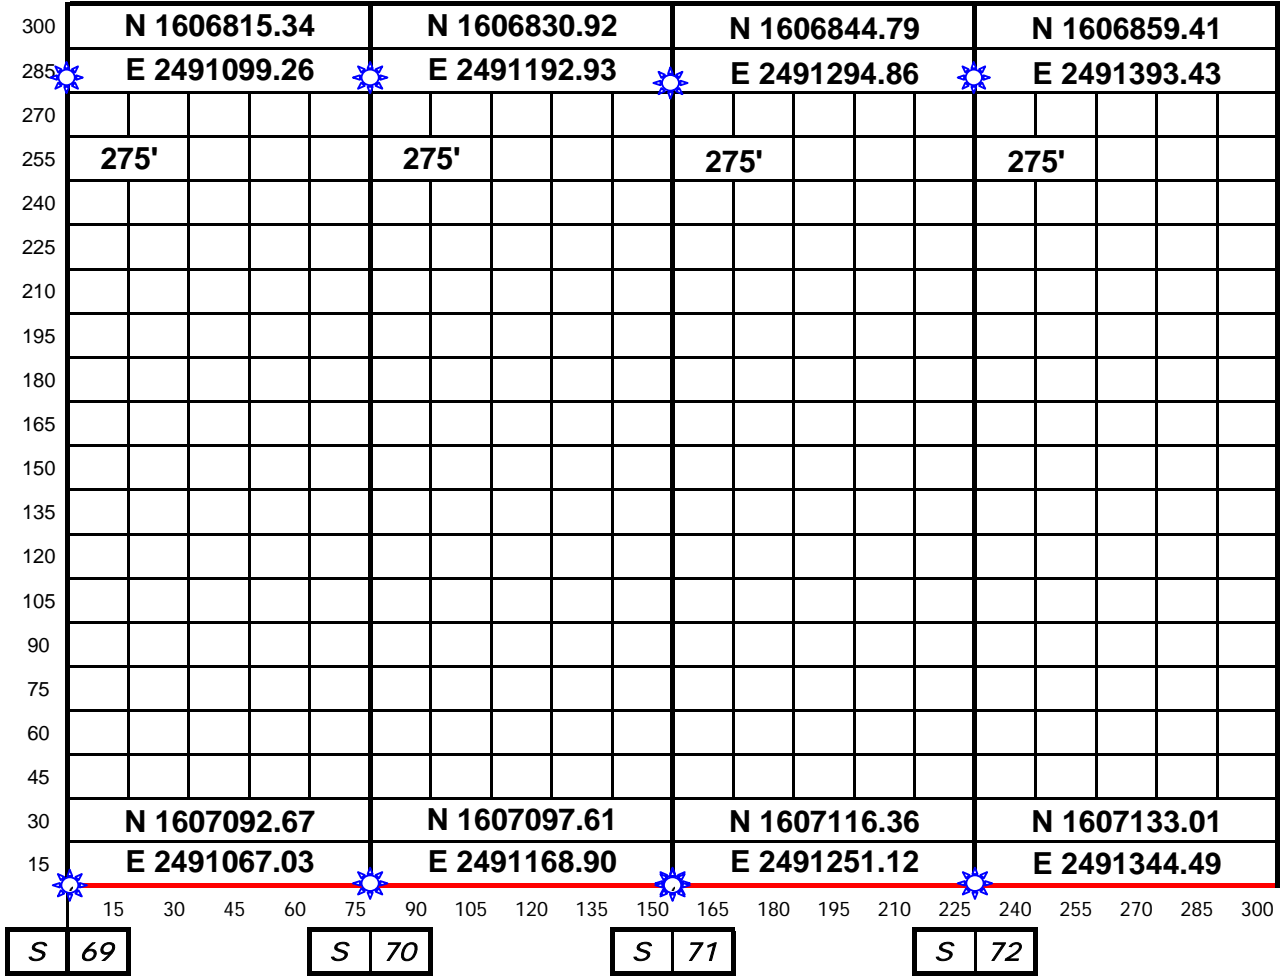


Start <input type="text" value="4/15"/>	Start <input type="text" value="4/15"/>	Start <input type="text" value="4/15"/>	Start <input type="text" value="4/15"/>
Finish <input type="text" value="4/15"/>	Finish <input type="text" value="4/15"/>	Finish <input type="text" value="4/15"/>	Finish <input type="text" value="4/15"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/15/2009	Completion Date:	4/15/2009
QC Date:		QA Date	

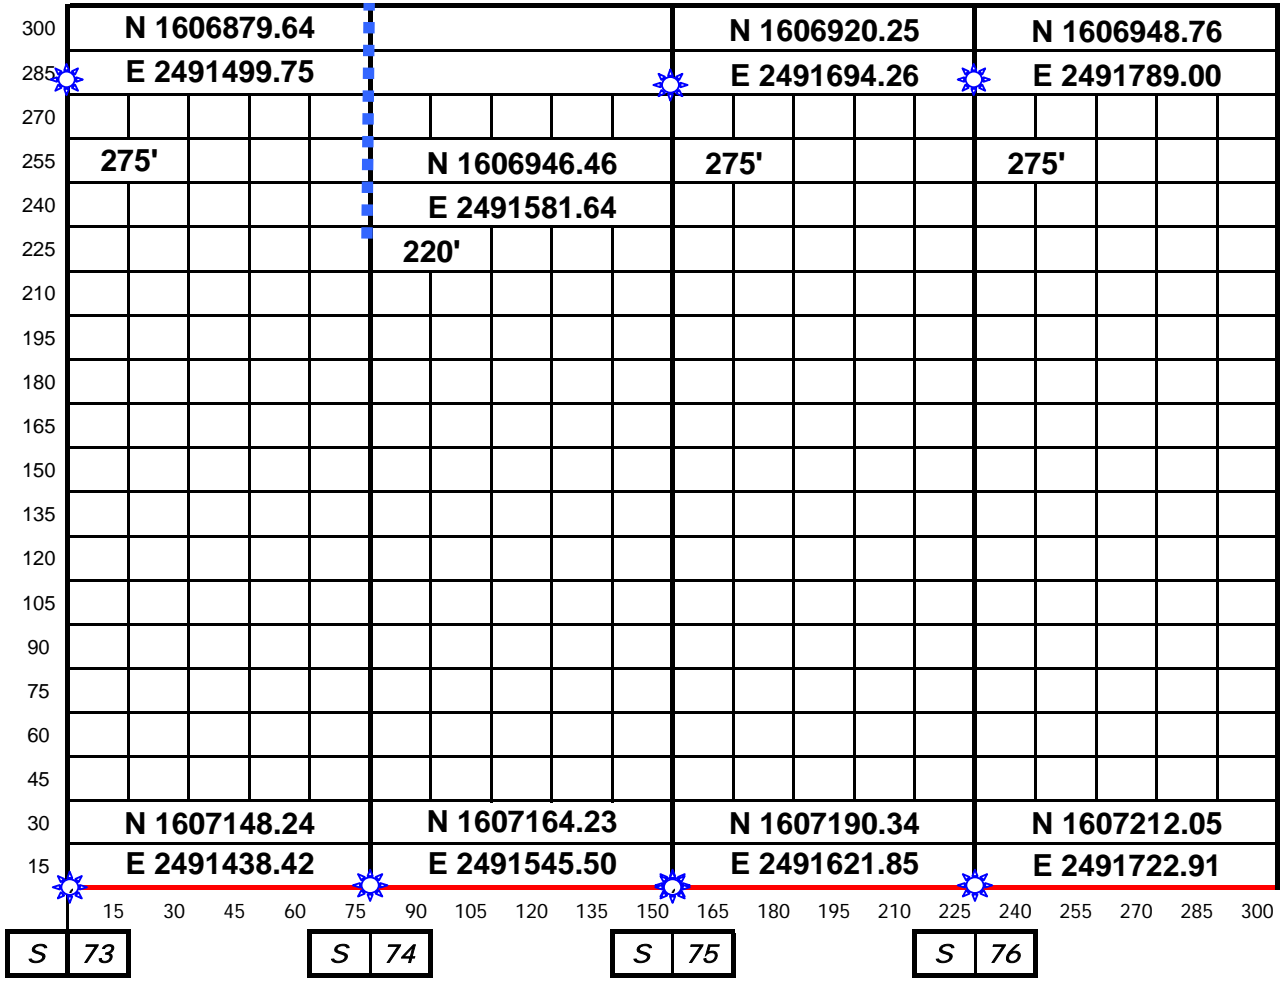


Start <input type="text" value="4/15"/>	Start <input type="text" value="4/15"/>	Start <input type="text" value="4/15"/>	Start <input type="text" value="4/15"/>
Finish <input type="text" value="4/15"/>	Finish <input type="text" value="4/15"/>	Finish <input type="text" value="4/15"/>	Finish <input type="text" value="4/15"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

S74 No Access/Cultural beyond 220'

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/15/2009	Completion Date:	4/15/2009
QC Date:		QA Date	

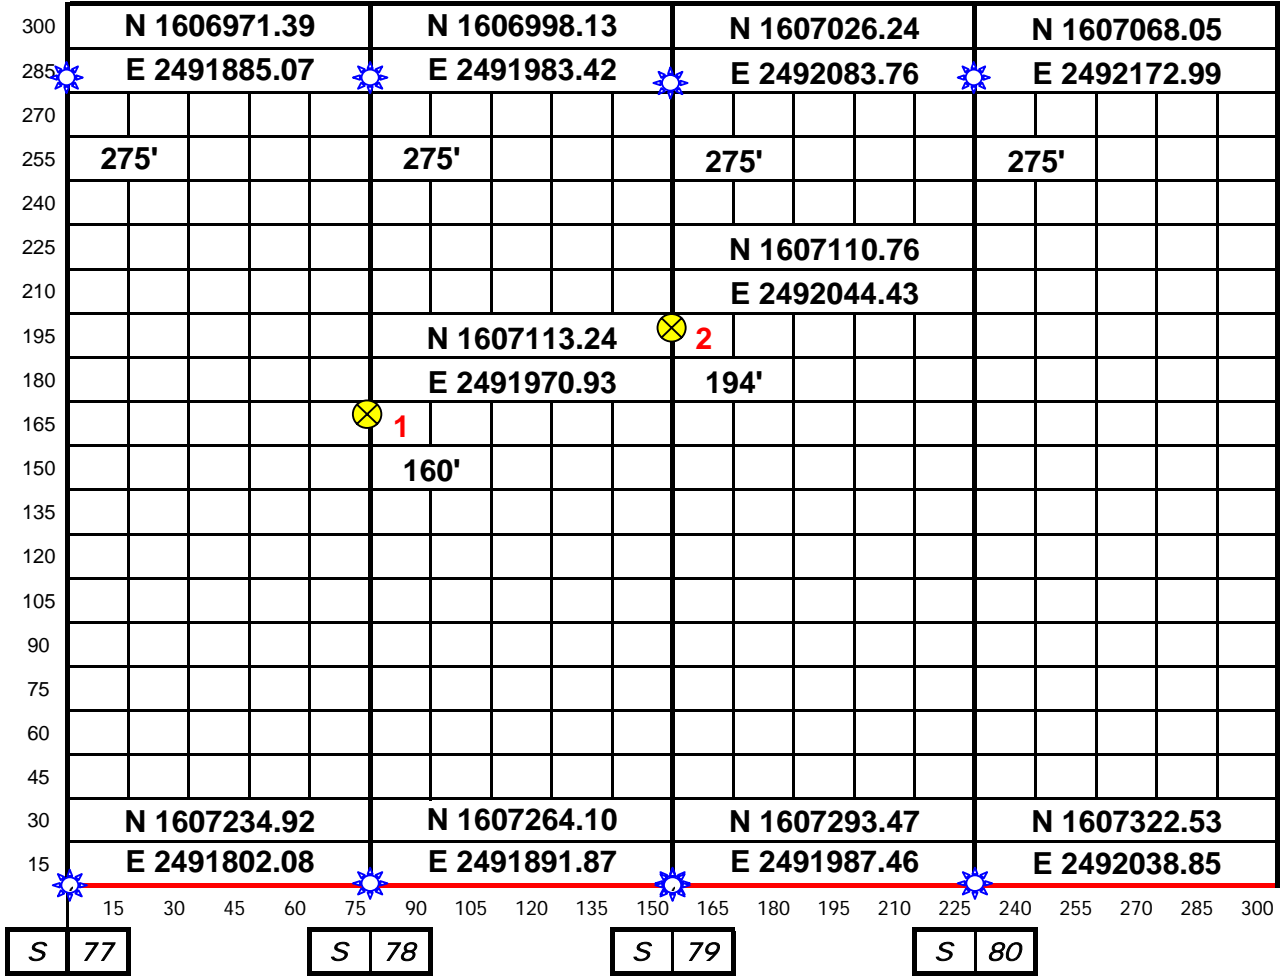


Start 4/15	Start 4/15	Start 4/15	Start 4/15
Finish 4/15	Finish 4/15	Finish 4/15	Finish 4/15
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:
1,2 Fragmentation

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/13/2009	Completion Date:	4/13/2009
QC Date:		QA Date	

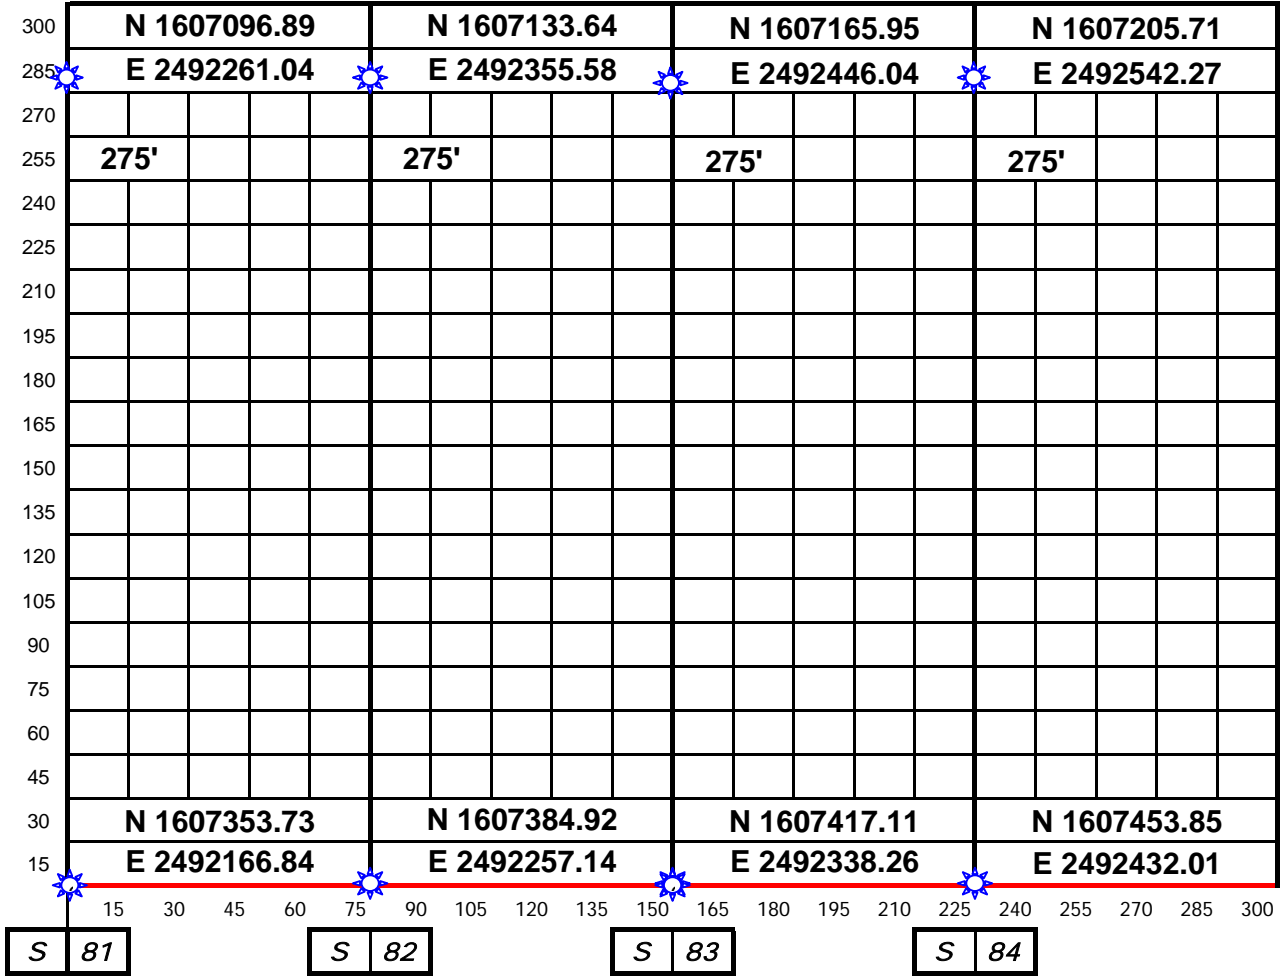


Start <input type="text" value="4/13"/>	Start <input type="text" value="4/13"/>	Start <input type="text" value="4/13"/>	Start <input type="text" value="4/13"/>
Finish <input type="text" value="4/13"/>	Finish <input type="text" value="4/13"/>	Finish <input type="text" value="4/13"/>	Finish <input type="text" value="4/13"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/13/2009	Completion Date:	4/13/2009
QC Date:		QA Date	

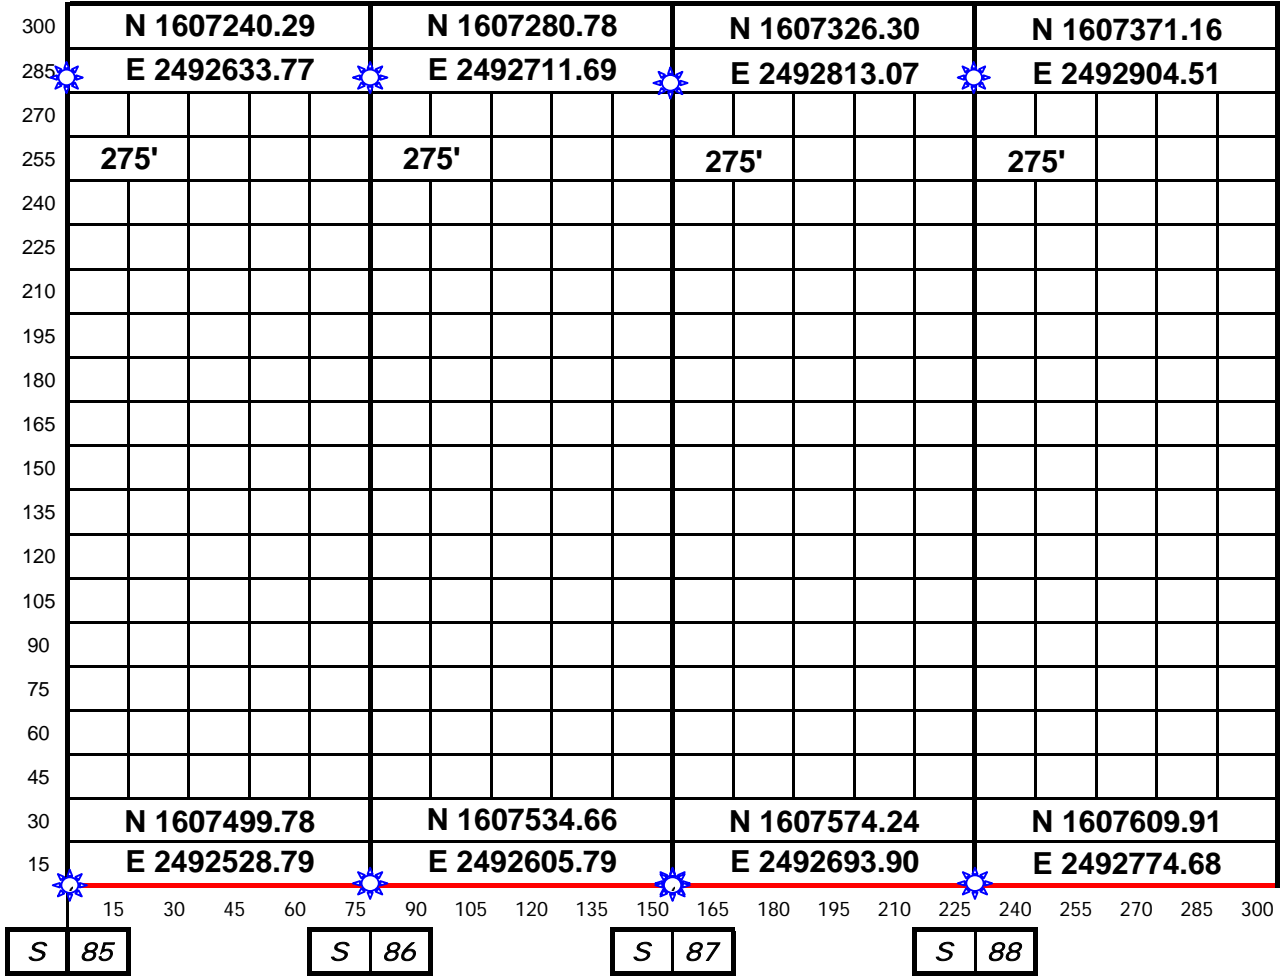


Start <input type="text" value="4/13"/>	Start <input type="text" value="4/13"/>	Start <input type="text" value="4/13"/>	Start <input type="text" value="4/13"/>
Finish <input type="text" value="4/13"/>	Finish <input type="text" value="4/13"/>	Finish <input type="text" value="4/13"/>	Finish <input type="text" value="4/13"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/13/2009	Completion Date:	4/13/2009
QC Date:		QA Date	

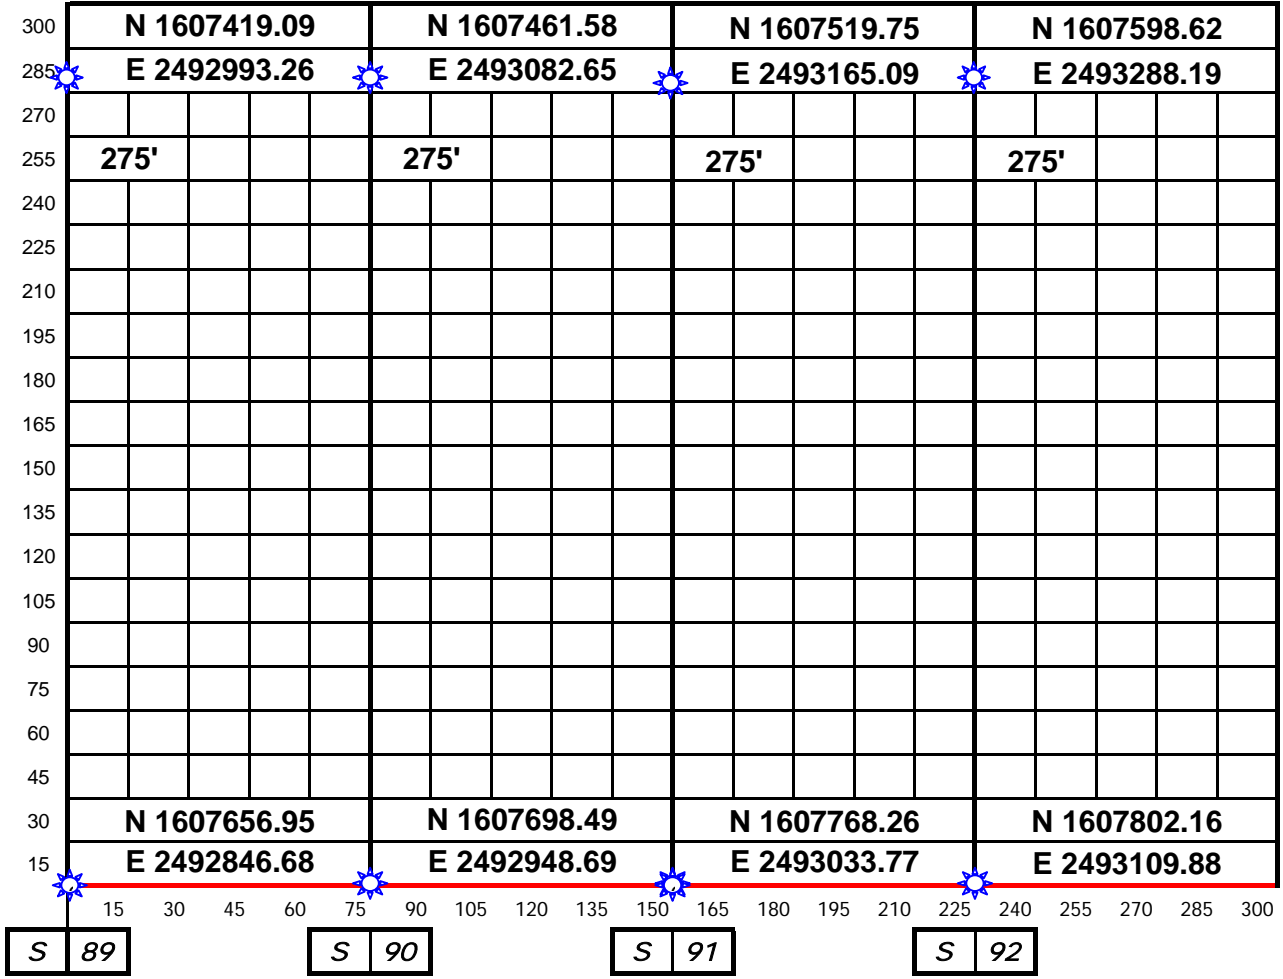

Start <input type="text" value="4/13"/>	Start <input type="text" value="4/13"/>	Start <input type="text" value="4/13"/>	Start <input type="text" value="4/13"/>
Finish <input type="text" value="4/13"/>	Finish <input type="text" value="4/13"/>	Finish <input type="text" value="4/13"/>	Finish <input type="text" value="4/13"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	


Comments:

S91 Offset 13' East (Scrub Oak)

S92 Offset 50' East (Arch Site)

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/13/2009	Completion Date:	4/13/2009
QC Date:		QA Date	

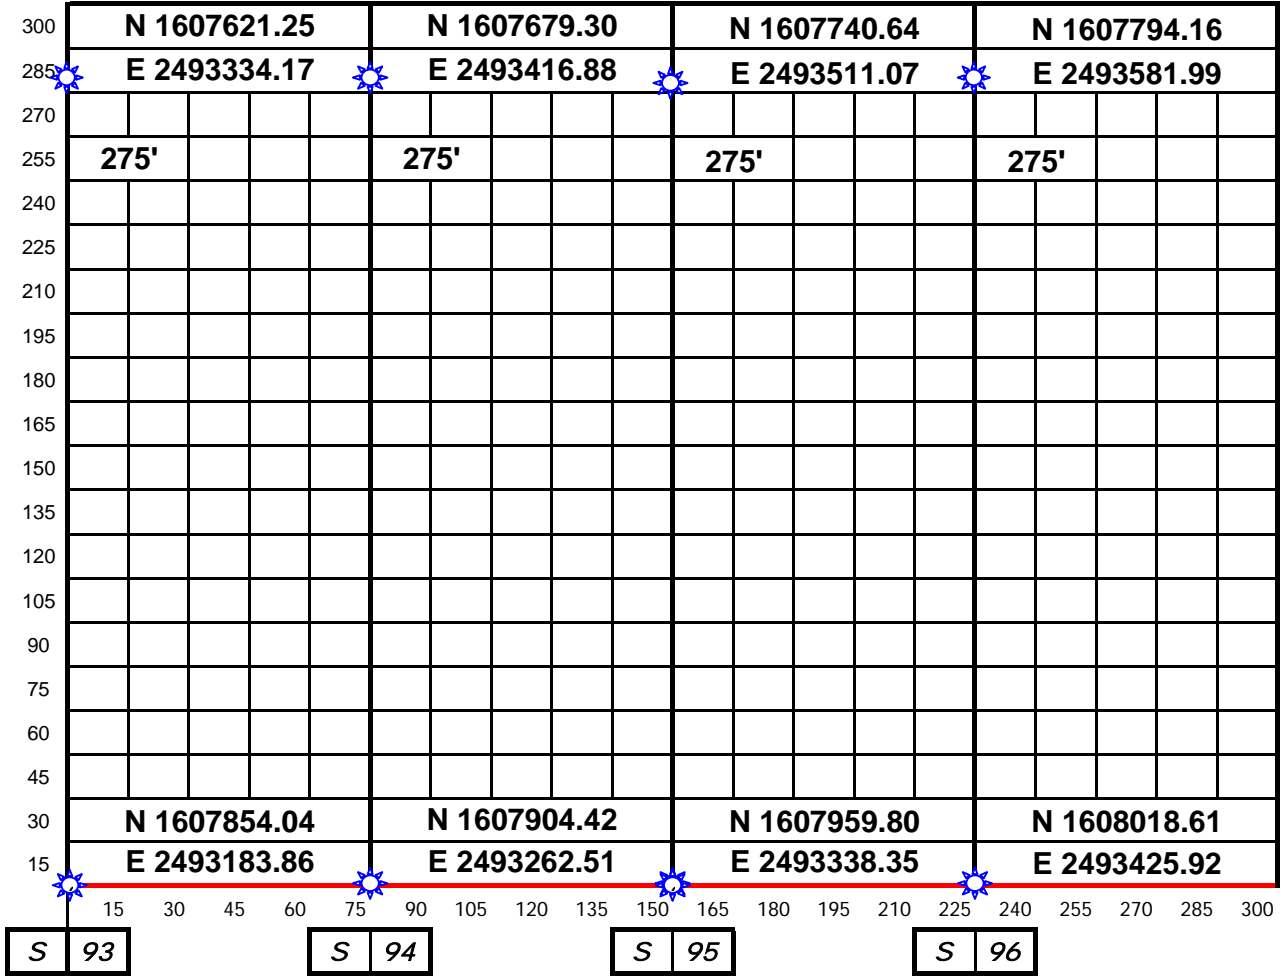


Start <input type="text" value="4/13"/>	Start <input type="text" value="4/13"/>	Start <input type="text" value="4/13"/>	Start <input type="text" value="4/13"/>
Finish <input type="text" value="4/13"/>	Finish <input type="text" value="4/13"/>	Finish <input type="text" value="4/13"/>	Finish <input type="text" value="4/13"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/16/2009	Completion Date:	4/16/2009
QC Date:		QA Date	

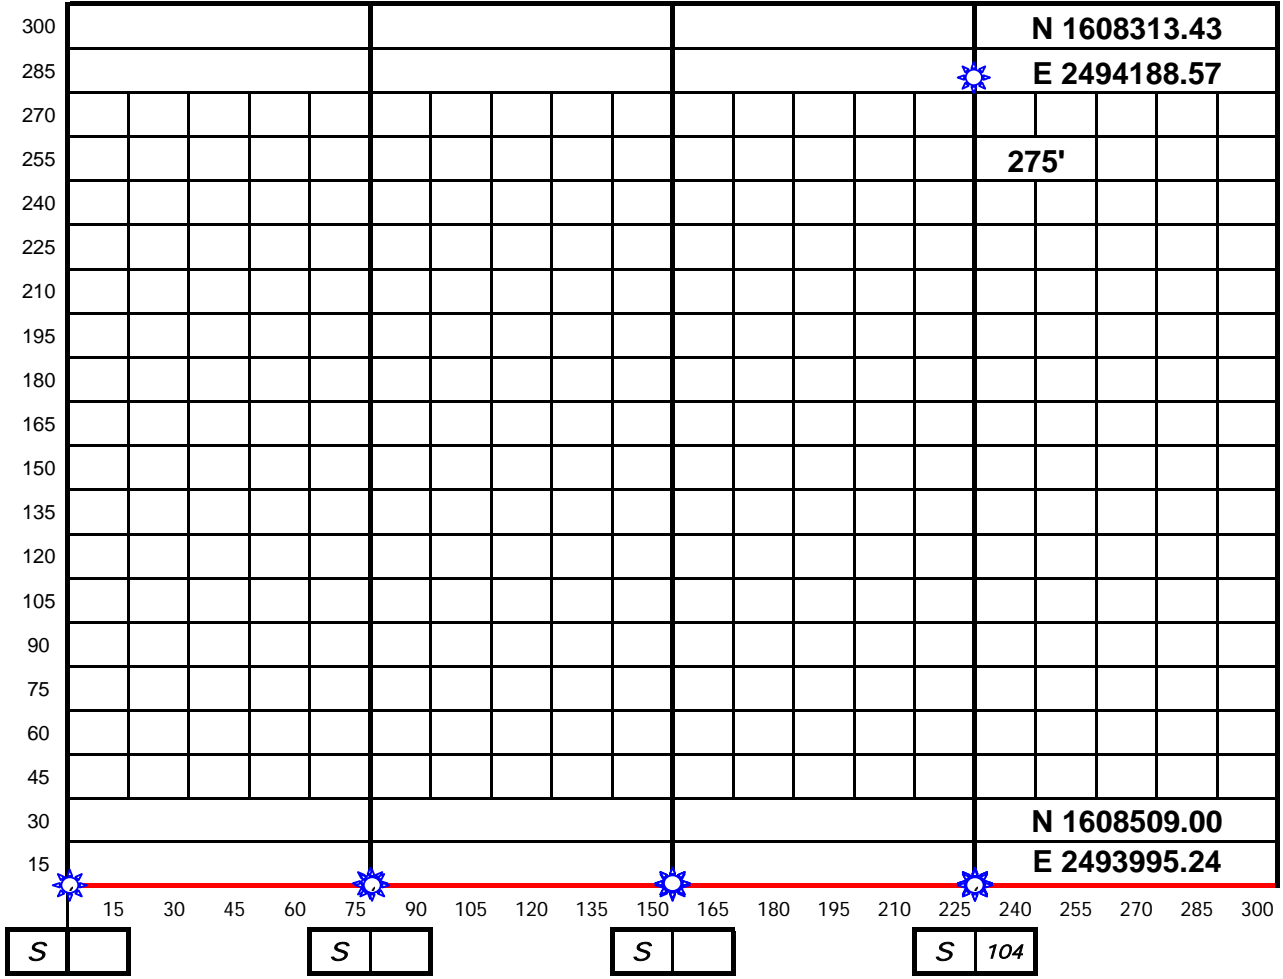


Start <input style="width: 100%; height: 20px;" type="text"/>	Start <input style="width: 100%; height: 20px;" type="text"/>	Start <input style="width: 100%; height: 20px;" type="text"/>	Start <input style="width: 100%; height: 20px;" type="text" value="4/16"/>
Finish <input style="width: 100%; height: 20px;" type="text"/>	Finish <input style="width: 100%; height: 20px;" type="text"/>	Finish <input style="width: 100%; height: 20px;" type="text"/>	Finish <input style="width: 100%; height: 20px;" type="text" value="4/16"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/16/2009	Completion Date:	4/16/2009
QC Date:		QA Date	

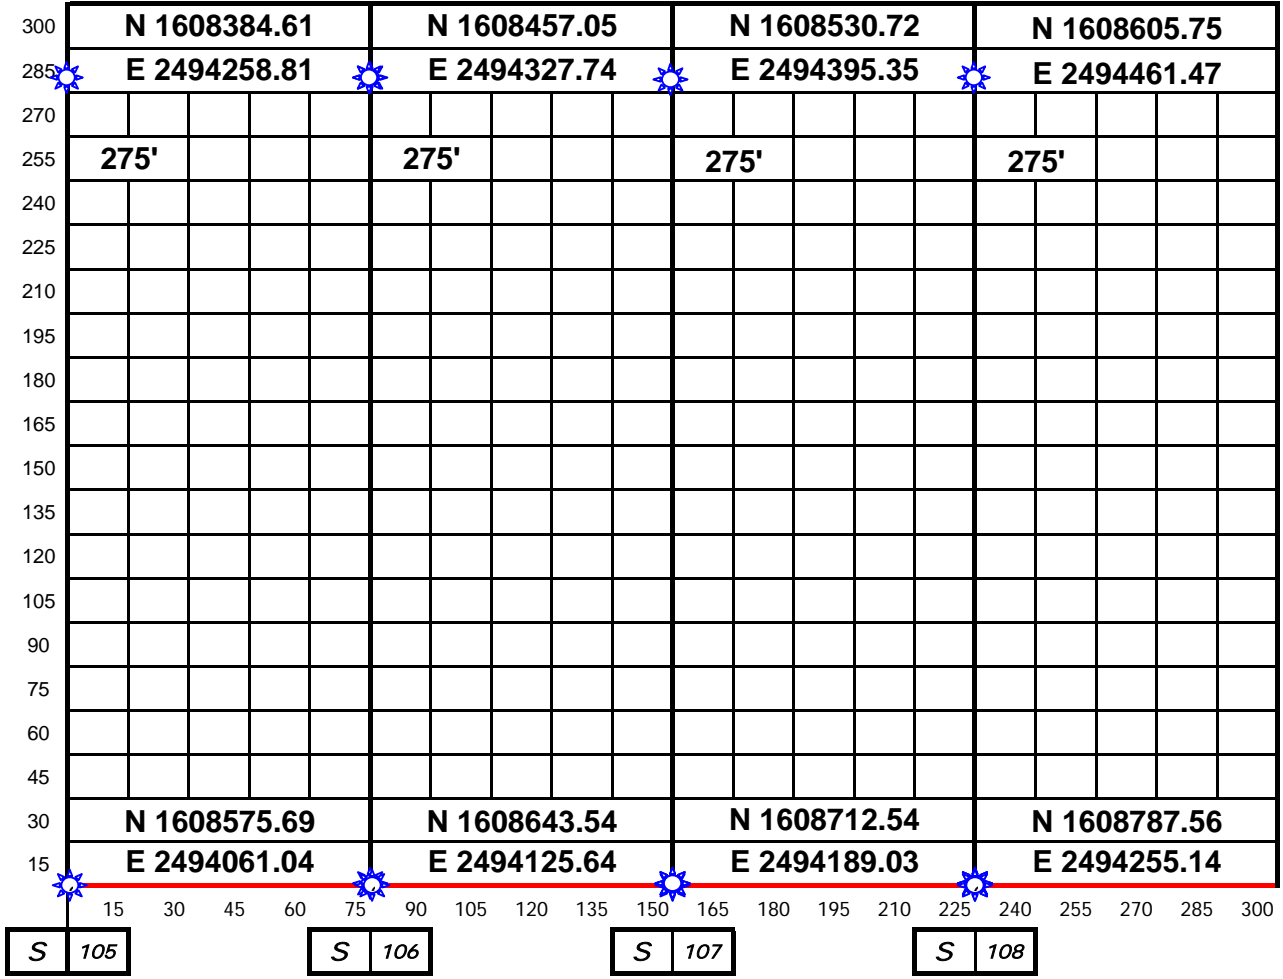


Start <input type="text" value="4/16"/>	Start <input type="text" value="4/16"/>	Start <input type="text" value="4/16"/>	Start <input type="text" value="4/16"/>
Finish <input type="text" value="4/16"/>	Finish <input type="text" value="4/16"/>	Finish <input type="text" value="4/16"/>	Finish <input type="text" value="4/16"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/16/2009	Completion Date:	4/16/2009
QC Date:		QA Date	

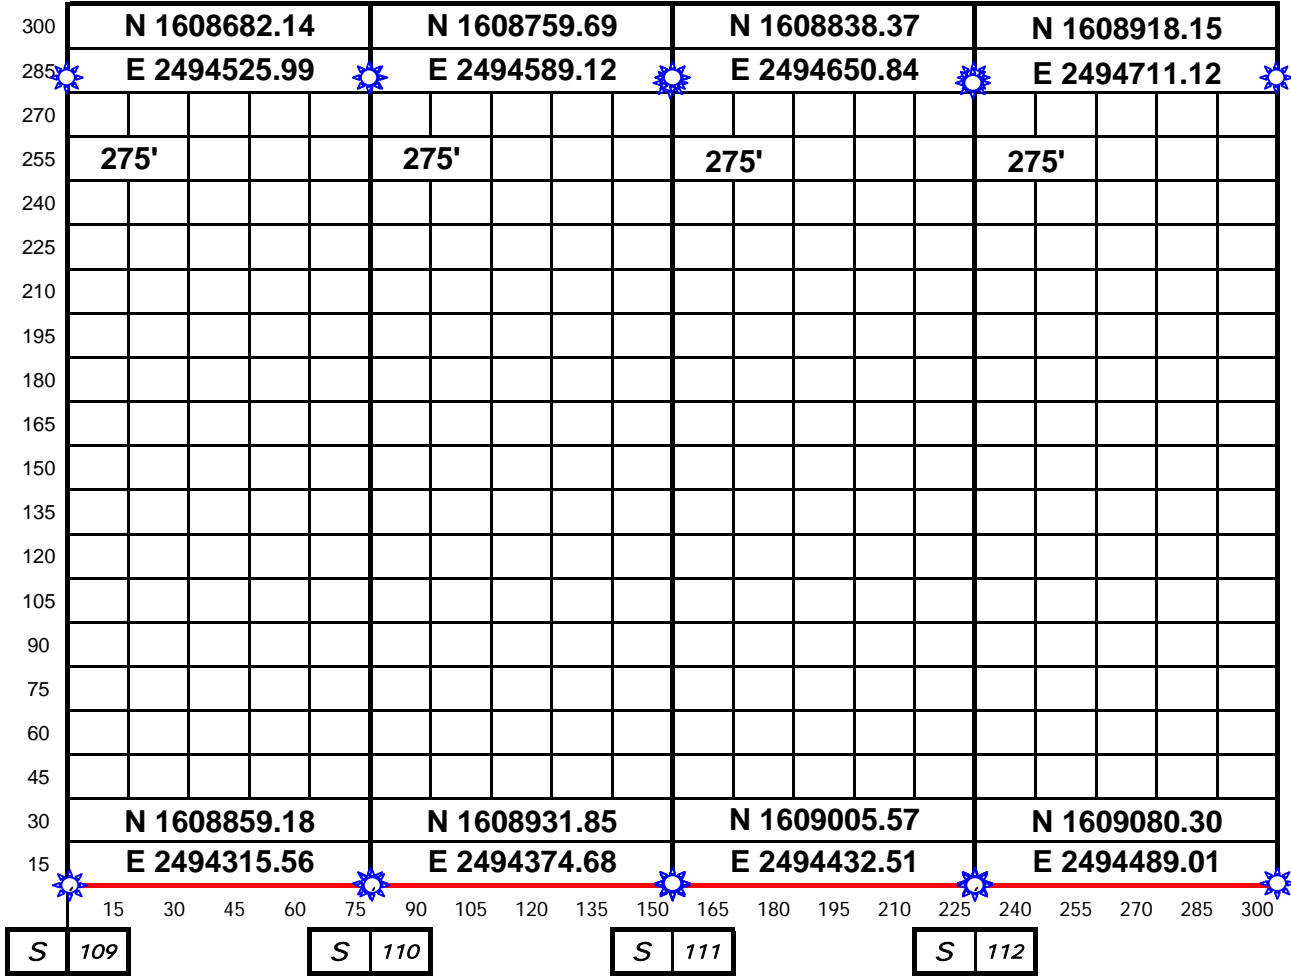


Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/16</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/16</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/16</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/16</div>
Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/16</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/16</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/16</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/16</div>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/15/2009	Completion Date:	4/16/2009
QC Date:		QA Date	

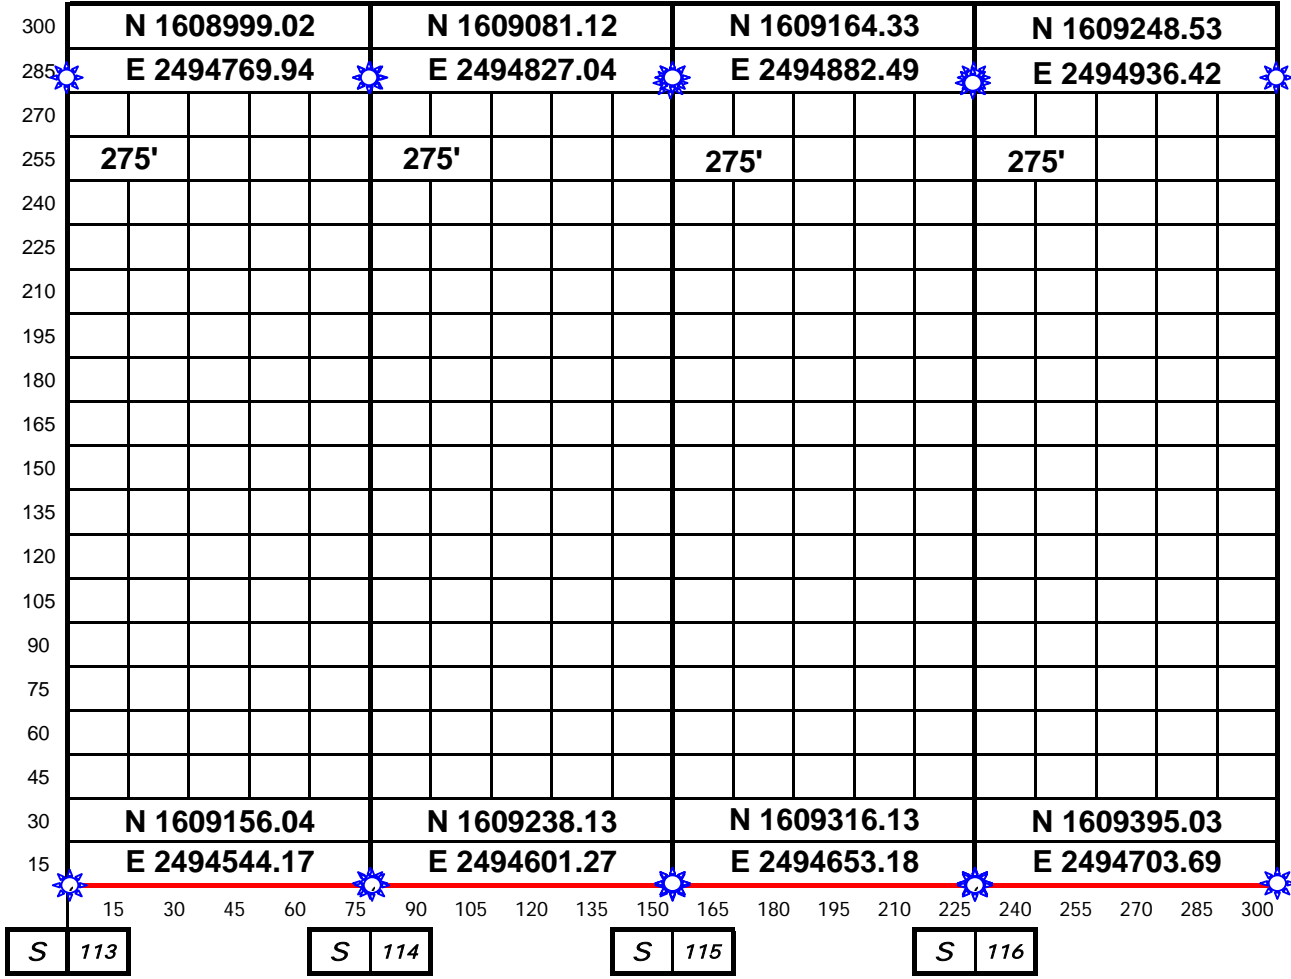


Start <input type="text" value="4/16"/>	Start <input type="text" value="4/16"/>	Start <input type="text" value="4/15"/>	Start <input type="text" value="4/15"/>
Finish <input type="text" value="4/16"/>	Finish <input type="text" value="4/16"/>	Finish <input type="text" value="4/15"/>	Finish <input type="text" value="4/15"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/15/2009	Completion Date:	4/15/2009
QC Date:		QA Date	

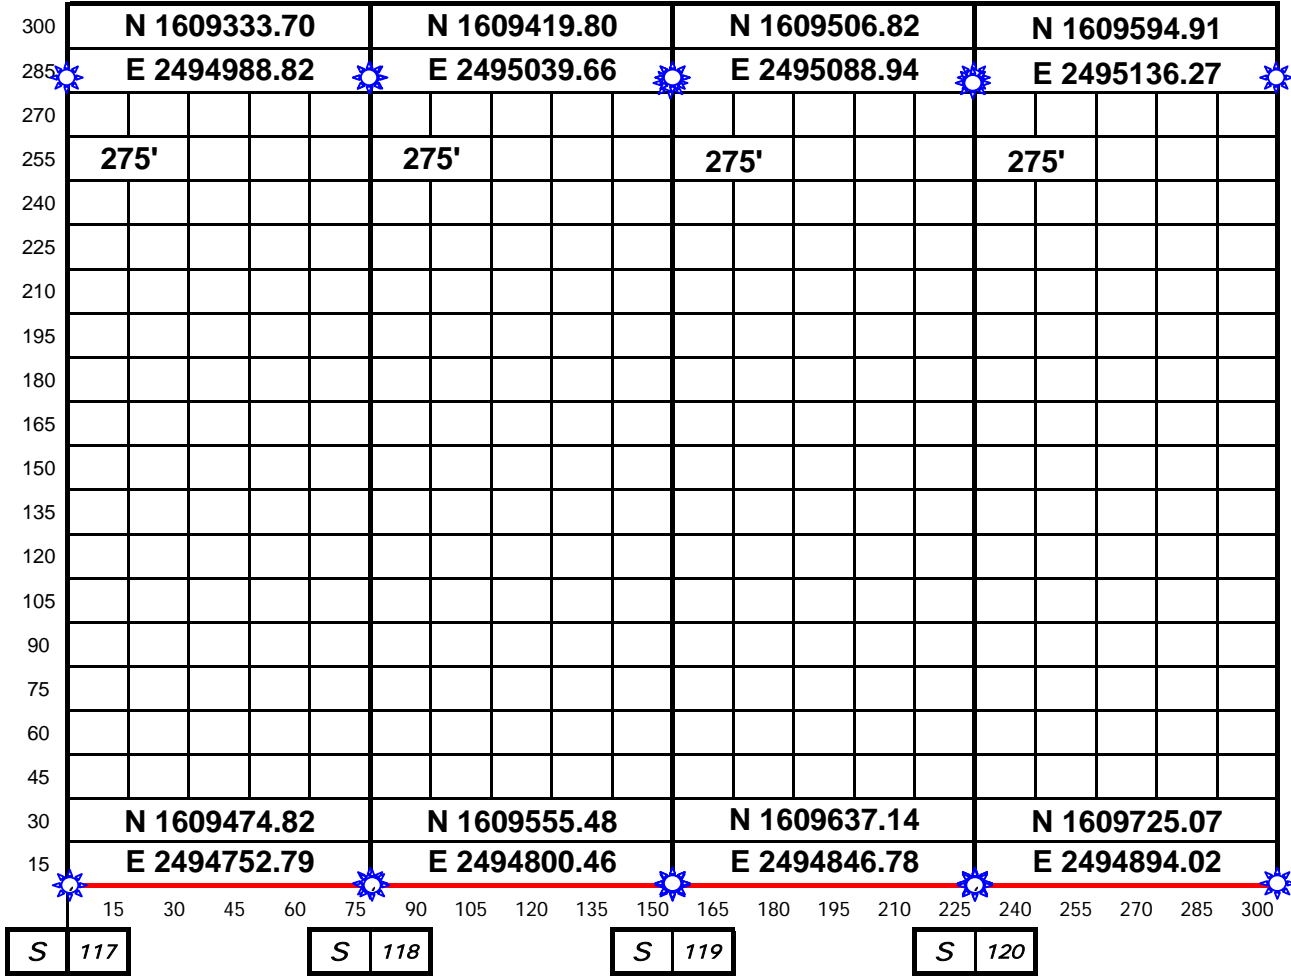


Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/15</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/15</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/15</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/15</div>
Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/15</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/15</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/15</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/15</div>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/15/2009	Completion Date:	4/15/2009
QC Date:		QA Date	

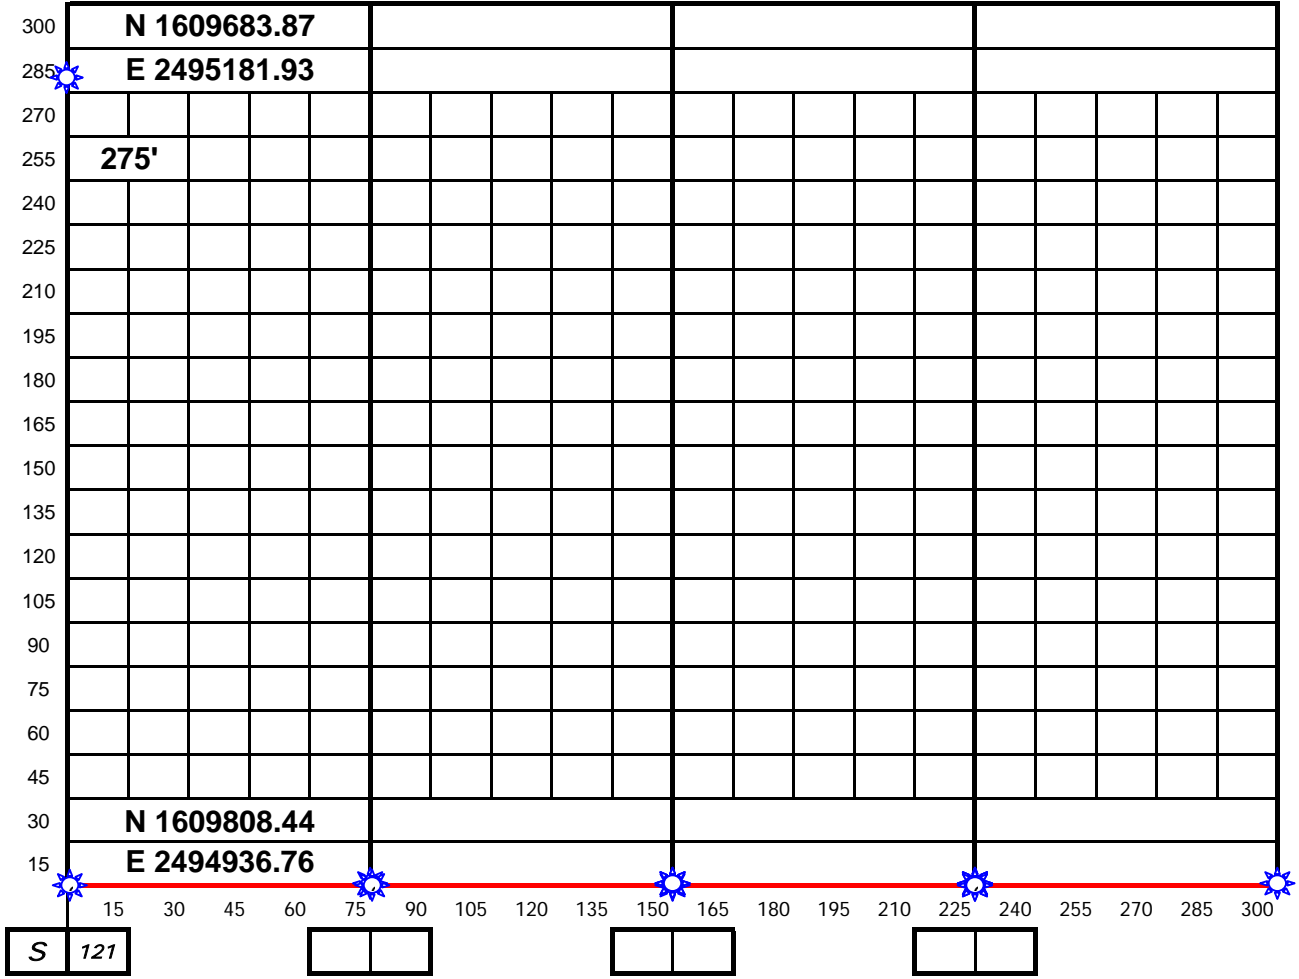


Start 4/15	Start 	Start 	Start
Finish 4/15	Finish 	Finish 	Finish
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	9/18/2008	Completion Date:	9/18/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

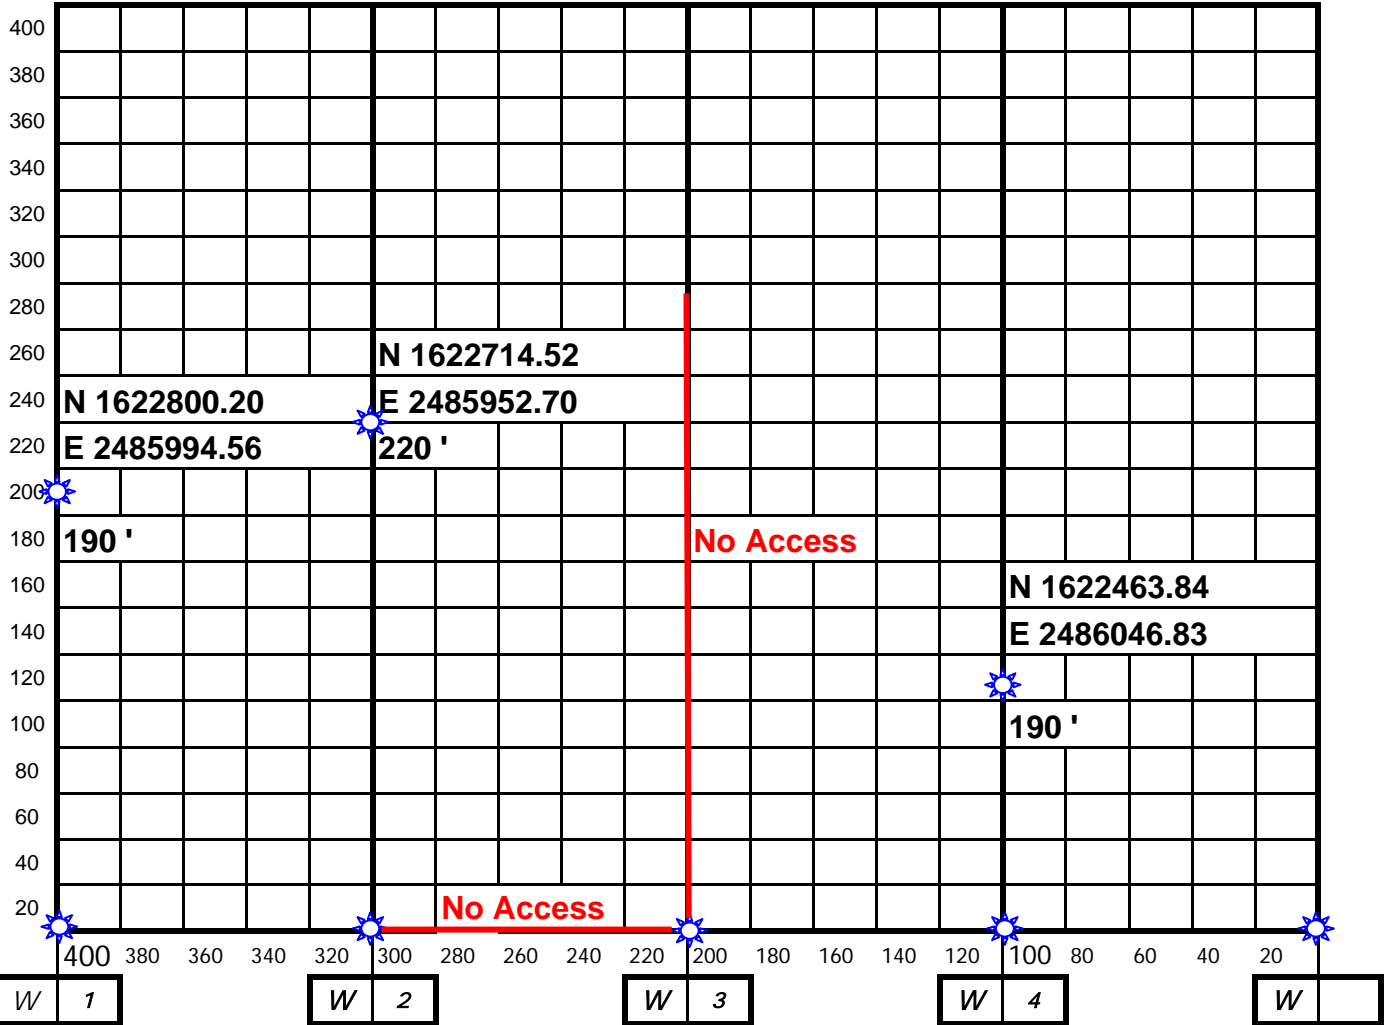

Start	Start	Start	Start	Start	
9/18	9/18	9/18	9/18		
Finish	Finish	Finish	Finish	Finish	
9/18	9/18	9/18	9/18		
	MEC		MD		STAKE #

Comments. Notes:


W4: 110' to arroyo

W3: No access

W1: End at cliff

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:		Completion Date:	
QC Date:		QC Signature:	
QA Date:		QA Signature:	

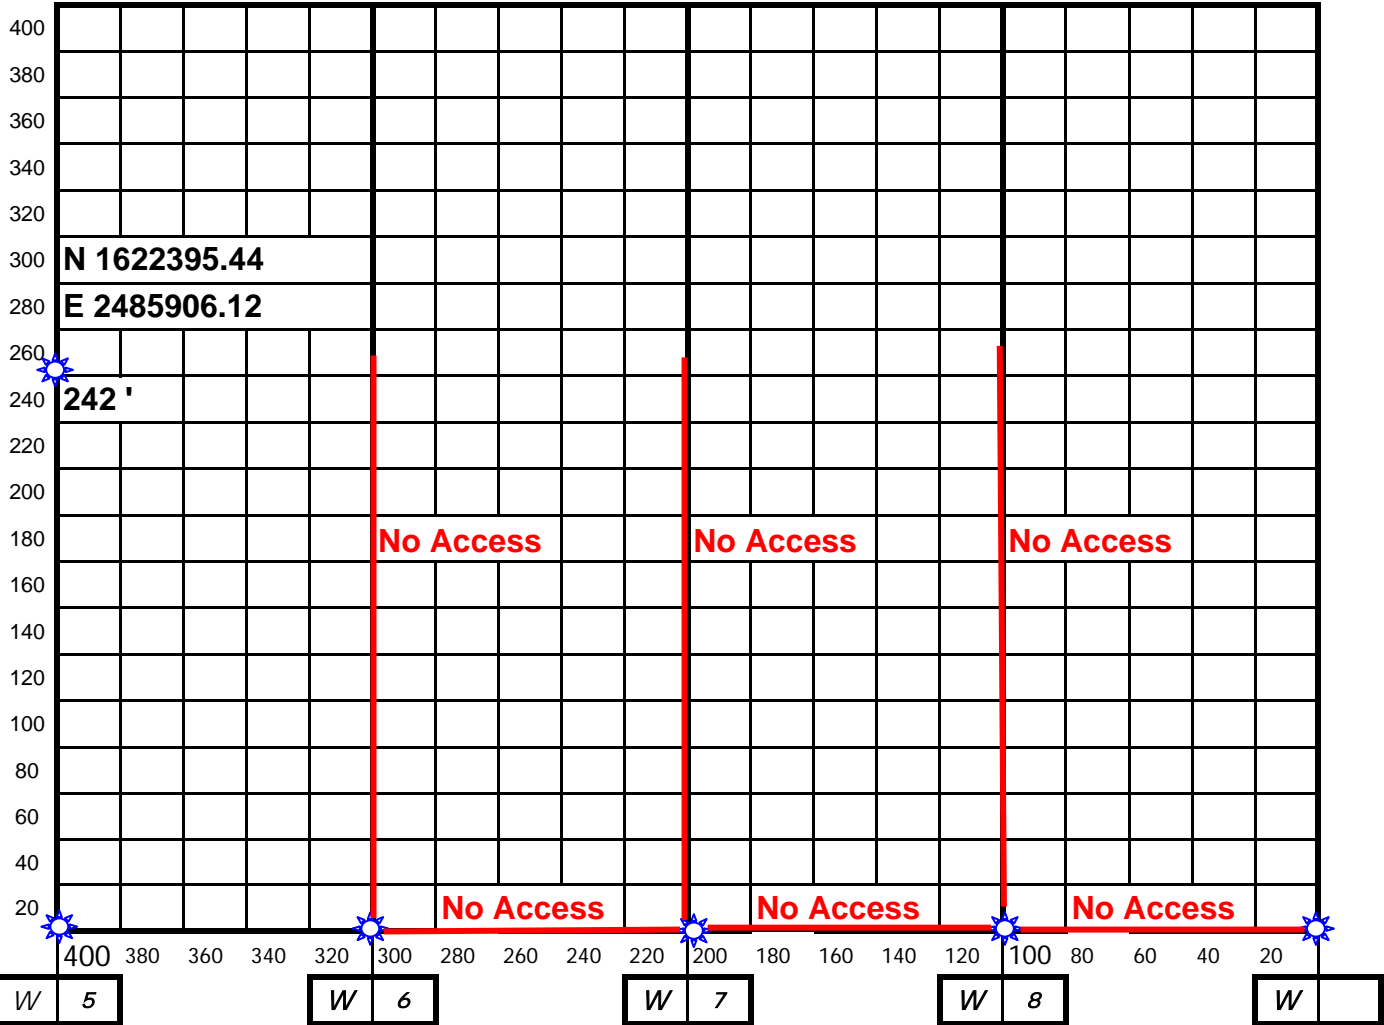


Start	Start	Start	Start	Start
Finish	Finish	Finish	Finish	Finish
	MEC		MD	
				STAKE #

Comments.Notes:

AW6-W8: Arroyo

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:		Completion Date:	
QC Date:		QC Signature:	
QA Date:		QA Signature:	

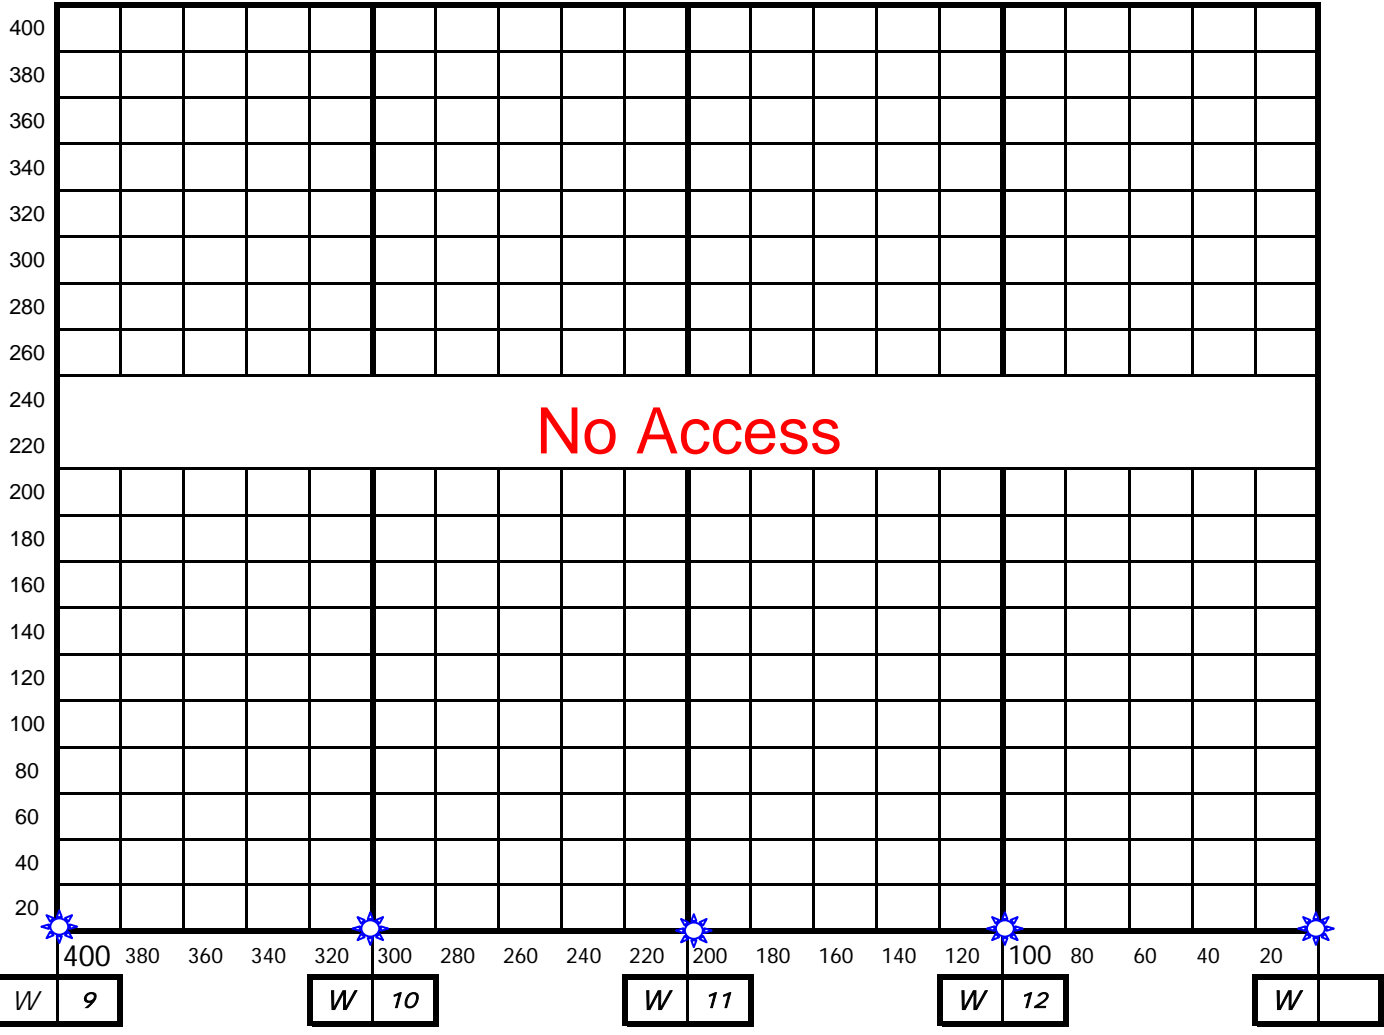


Start	Start	Start	Start	Start
Finish	Finish	Finish	Finish	Finish
MEC	MD	STAKE #		

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:		Completion Date:	
QC Date:		QC Signature:	
QA Date:		QA Signature:	

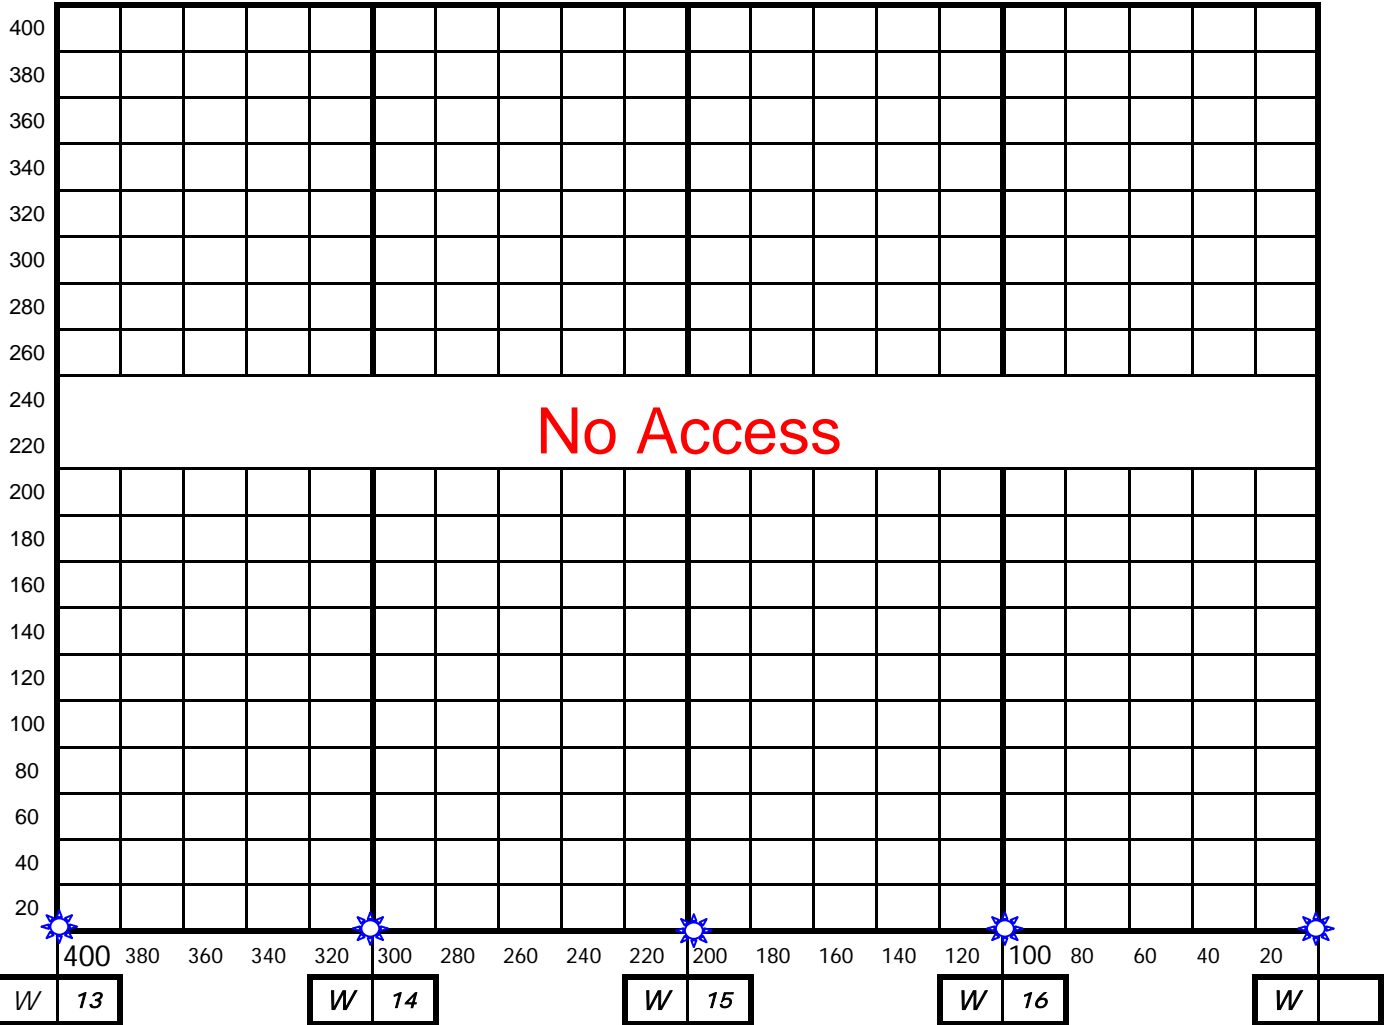


Start	Start	Start	Start	Start
Finish	Finish	Finish	Finish	Finish
MEC	MD	STAKE #		

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:		Completion Date:	
QC Date:		QC Signature:	
QA Date:		QA Signature:	

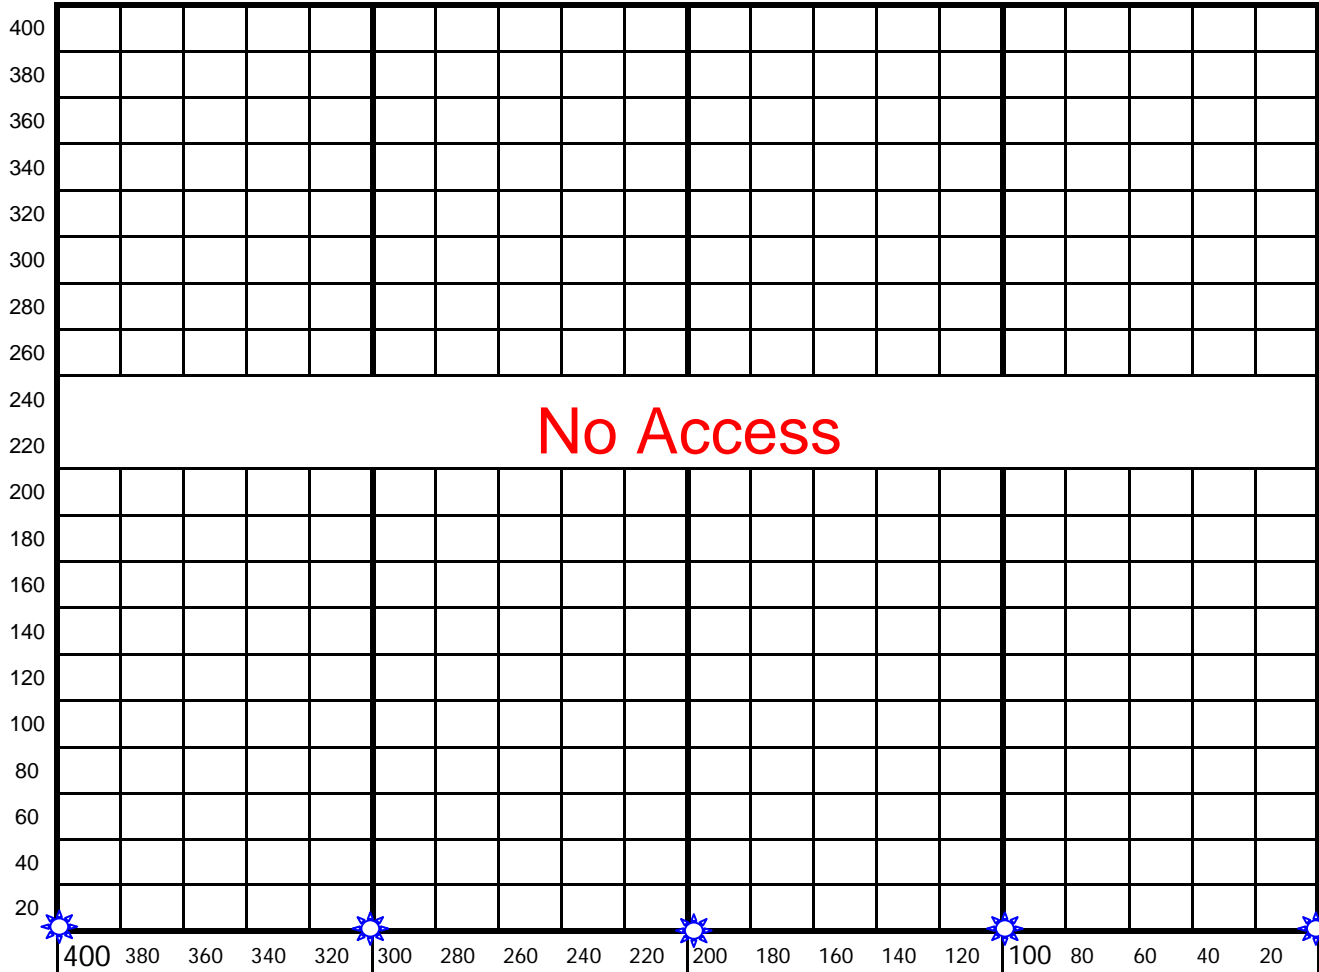


400	380	360	340	320	300	280	260	240	220	200	180	160	140	120	100	80	60	40	20
W	17	W	18	W	19	W	20	W											

Start	Start	Start	Start	Start
Finish	Finish	Finish	Finish	Finish
MEC	MD	STAKE #		

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:		Completion Date:	
QC Date:		QC Signature:	
QA Date:		QA Signature:	

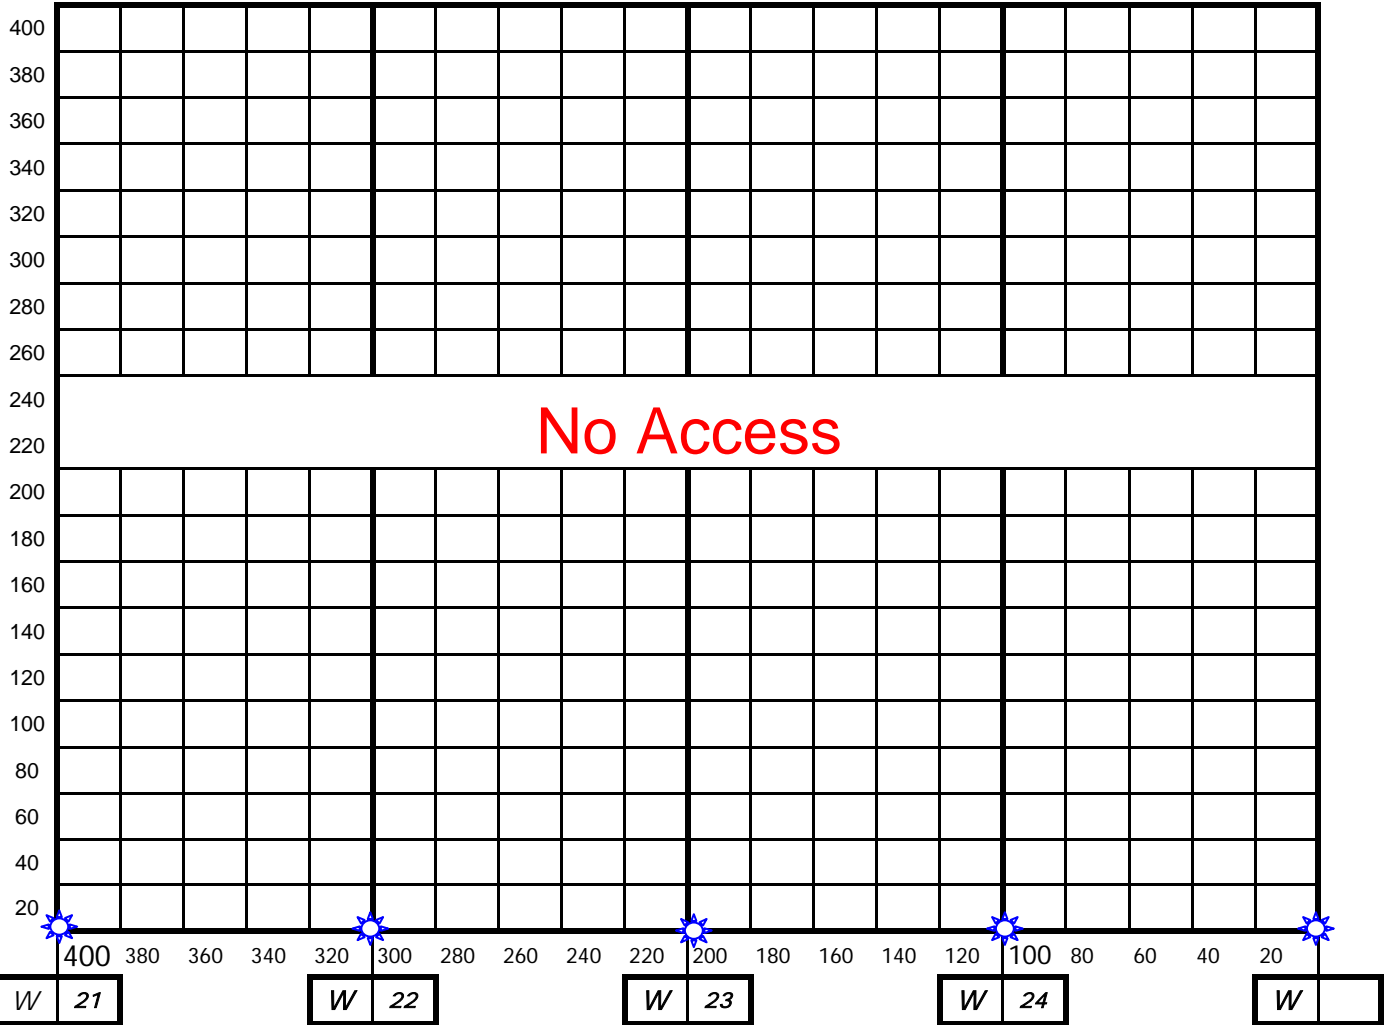


Start	Start	Start	Start	Start
Finish	Finish	Finish	Finish	Finish
MEC	MD	STAKE #		

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:		Completion Date:	
QC Date:		QC Signature:	
QA Date:		QA Signature:	

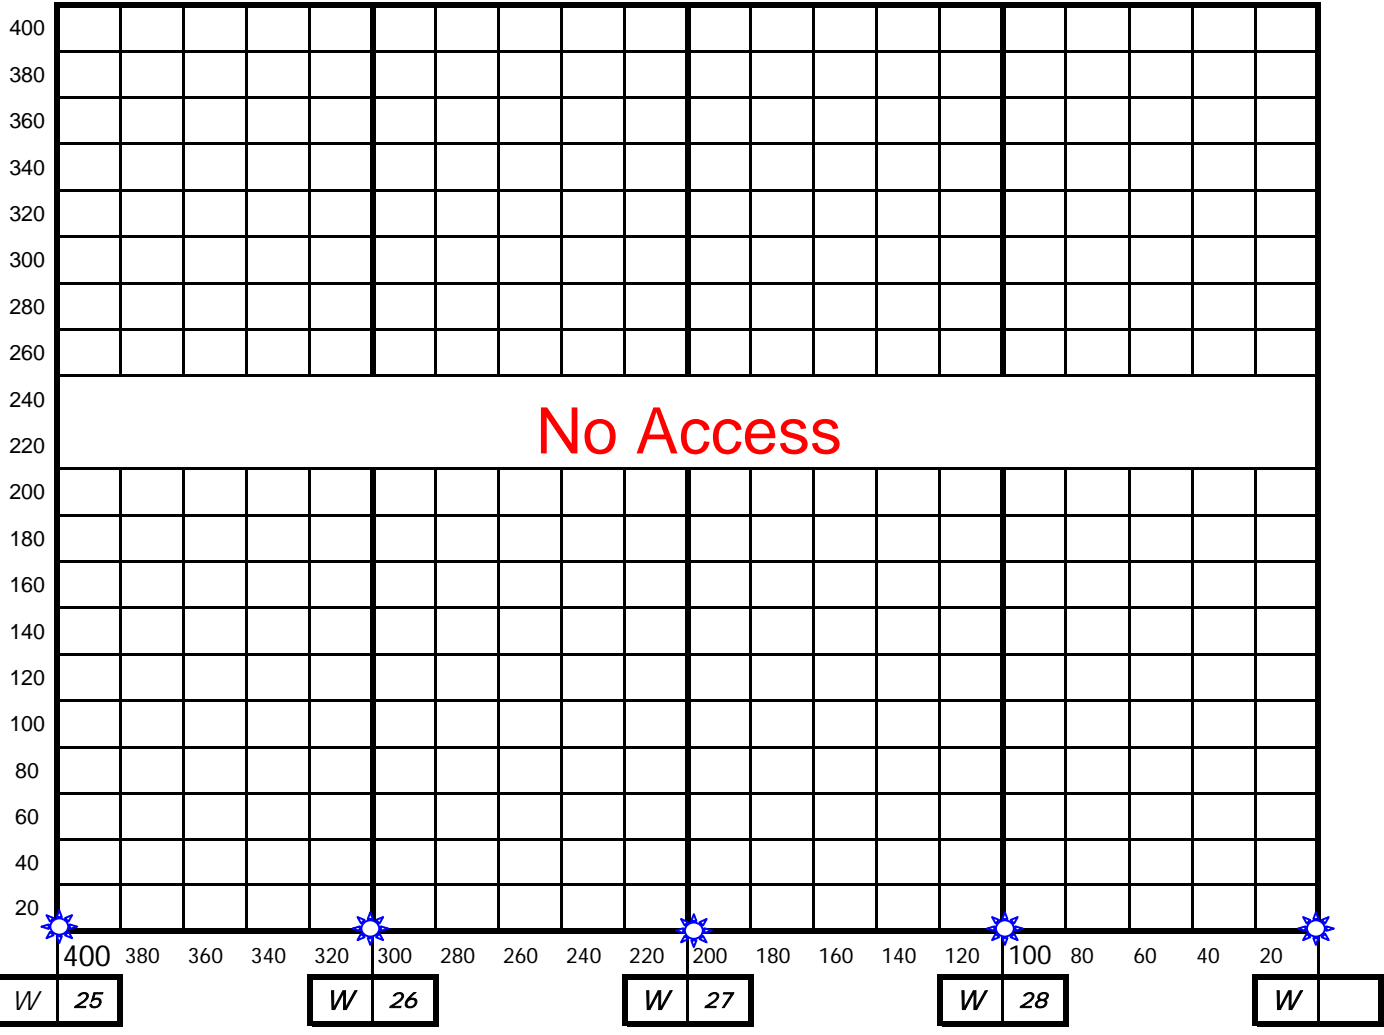


Start	Start	Start	Start	Start	
Finish	Finish	Finish	Finish	Finish	
	MEC		MD		STAKE #

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:		Completion Date:	
QC Date:		QC Signature:	
QA Date:		QA Signature:	

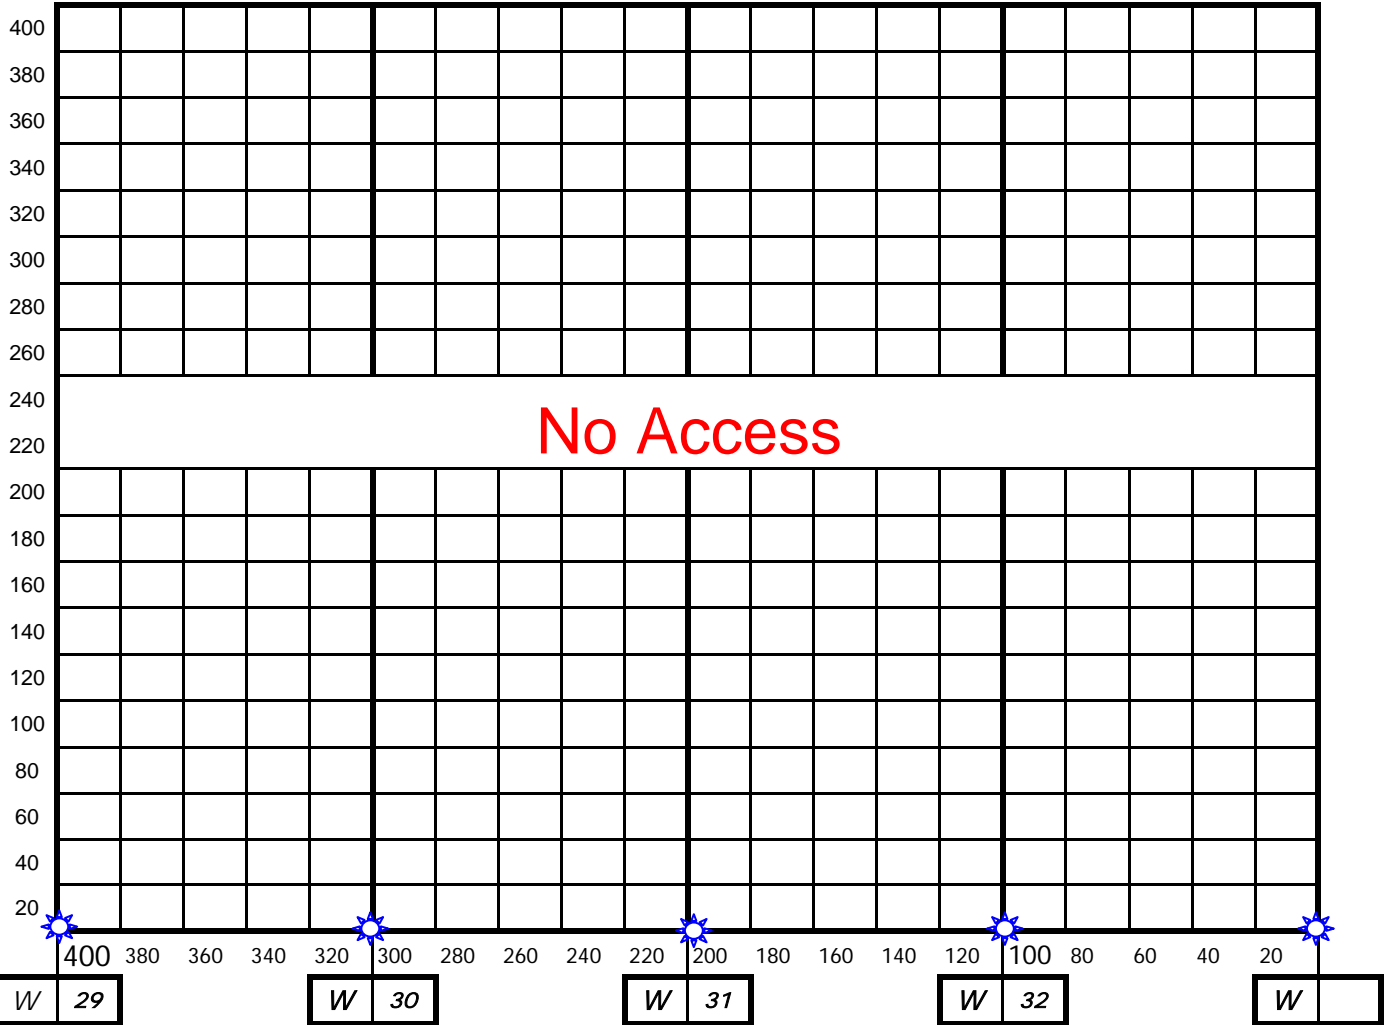


Start	Start	Start	Start	Start	
Finish	Finish	Finish	Finish	Finish	
	MEC		MD		STAKE #

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:		Completion Date:	
QC Date:		QC Signature:	
QA Date:		QA Signature:	

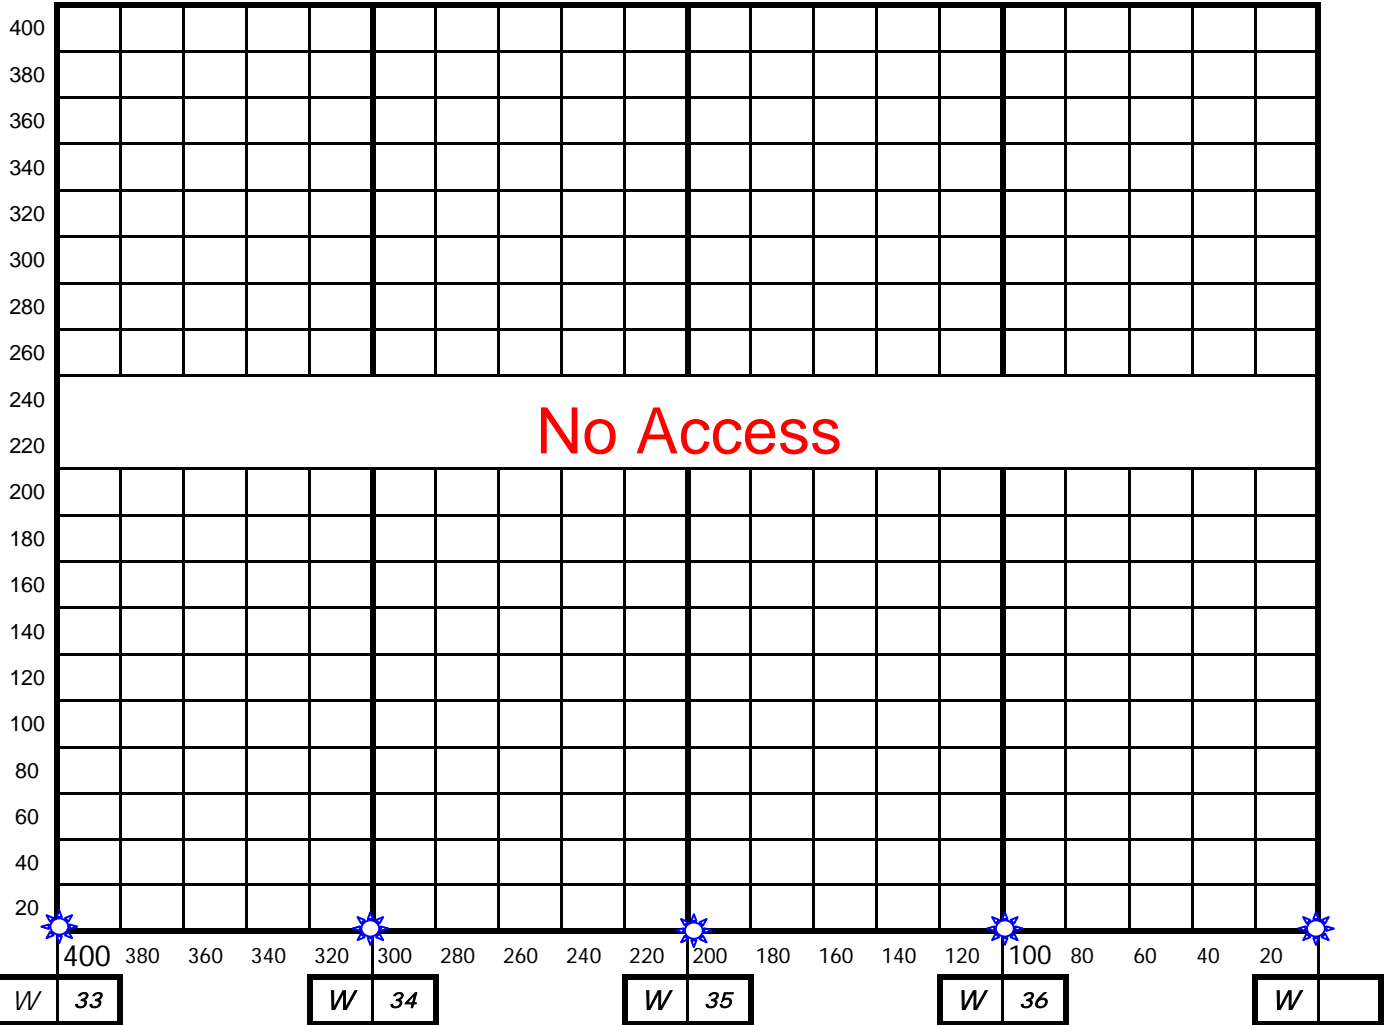


Start	Start	Start	Start	Start
Finish	Finish	Finish	Finish	Finish
MEC	MD	STAKE #		

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/27/2008	Completion Date:	8/27/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

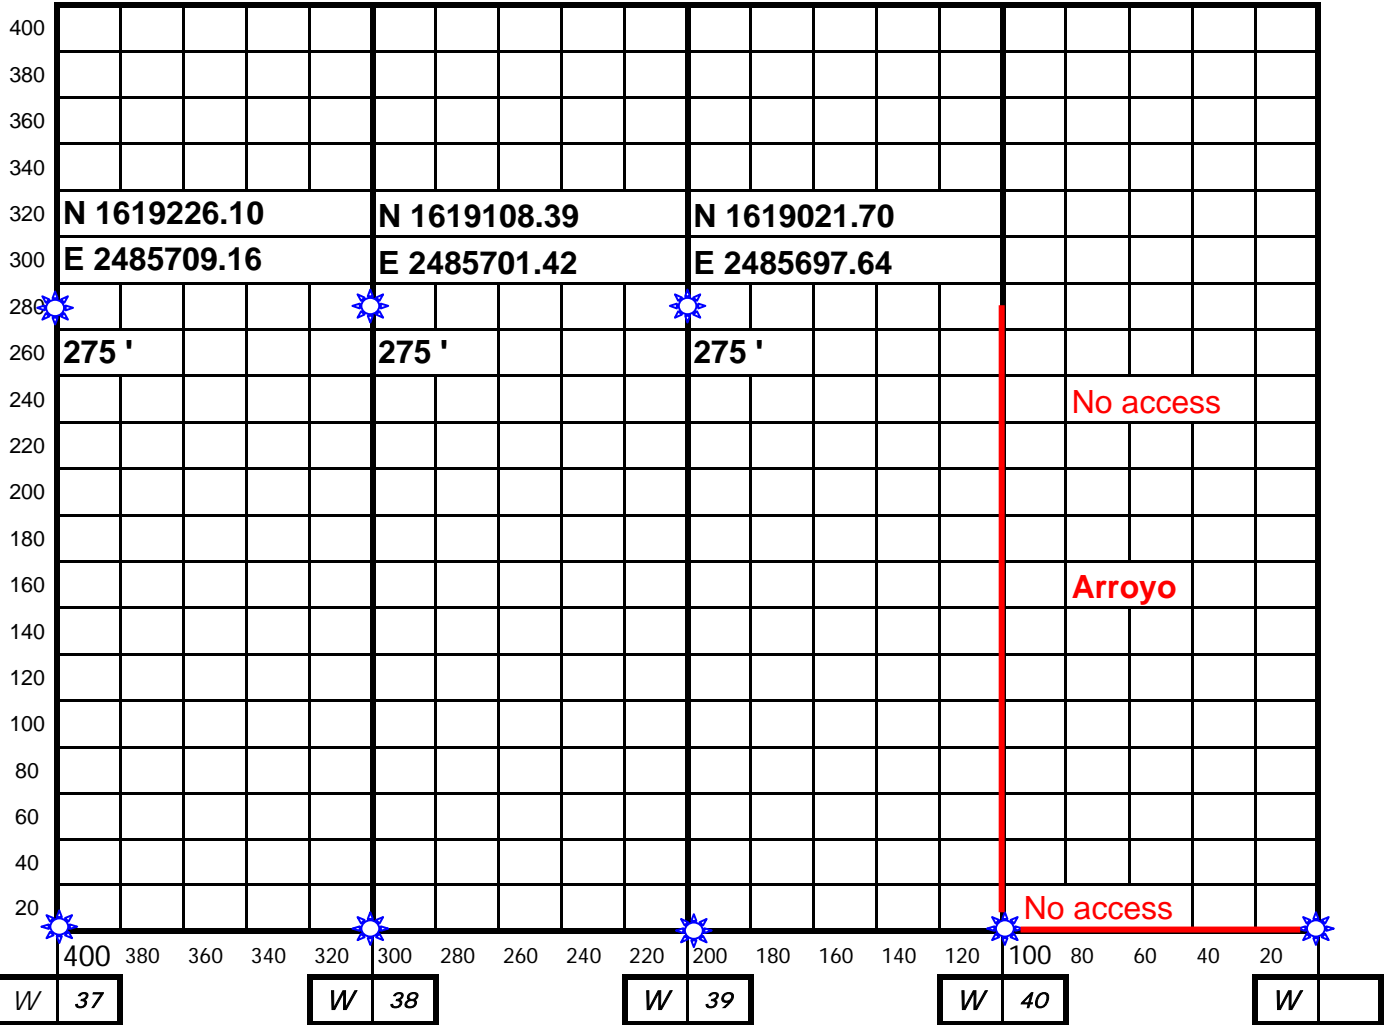


Start	Start	Start	Start	Start
8/27	8/27	8/27	8/27	
Finish	Finish	Finish	Finish	Finish
8/27	8/27	8/27	8/27	
MEC	MD	STAKE #		

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/27/2008	Completion Date:	8/27/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

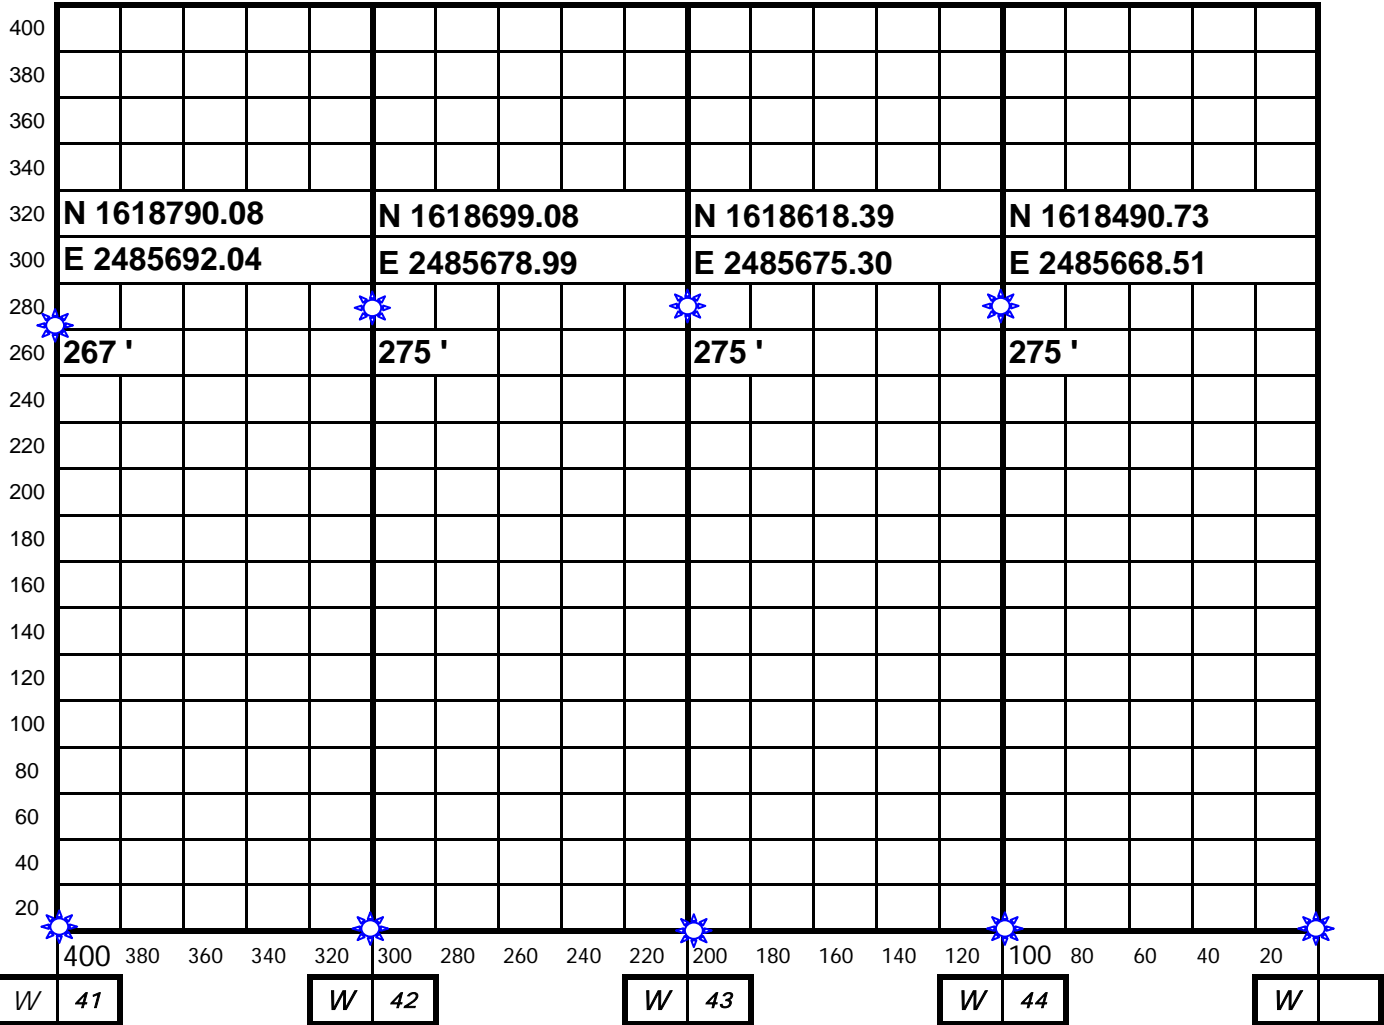

Start	Start	Start	Start	Start
<input type="text" value="8/27"/>	<input type="text" value="8/27"/>	<input type="text" value="8/27"/>	<input type="text" value="8/27"/>	<input type="text"/>
Finish	Finish	Finish	Finish	Finish
<input type="text" value="8/27"/>	<input type="text" value="8/27"/>	<input type="text" value="8/27"/>	<input type="text" value="8/27"/>	<input type="text"/>
	MEC		MD	
				STAKE #


Comments.Notes:

41: Ended in arroyo

43: Offset 50' West

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:		Completion Date:	
QC Date:		QC Signature:	
QA Date:		QA Signature:	

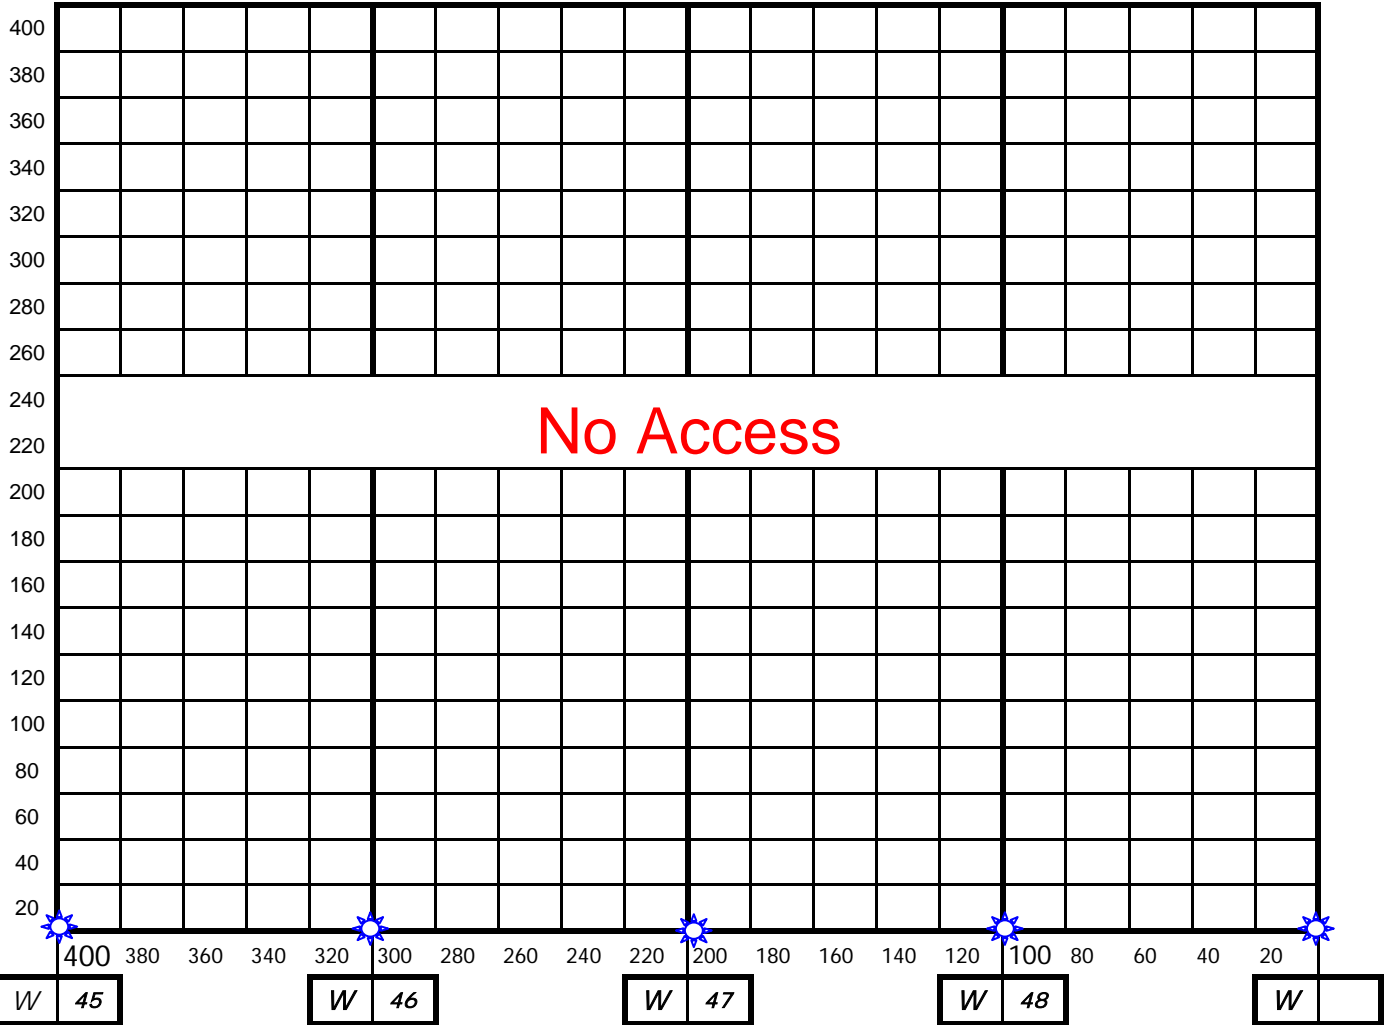


Start	Start	Start	Start	Start	
Finish	Finish	Finish	Finish	Finish	
	MEC		MD		STAKE #

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:		Completion Date:	
QC Date:		QC Signature:	
QA Date:		QA Signature:	

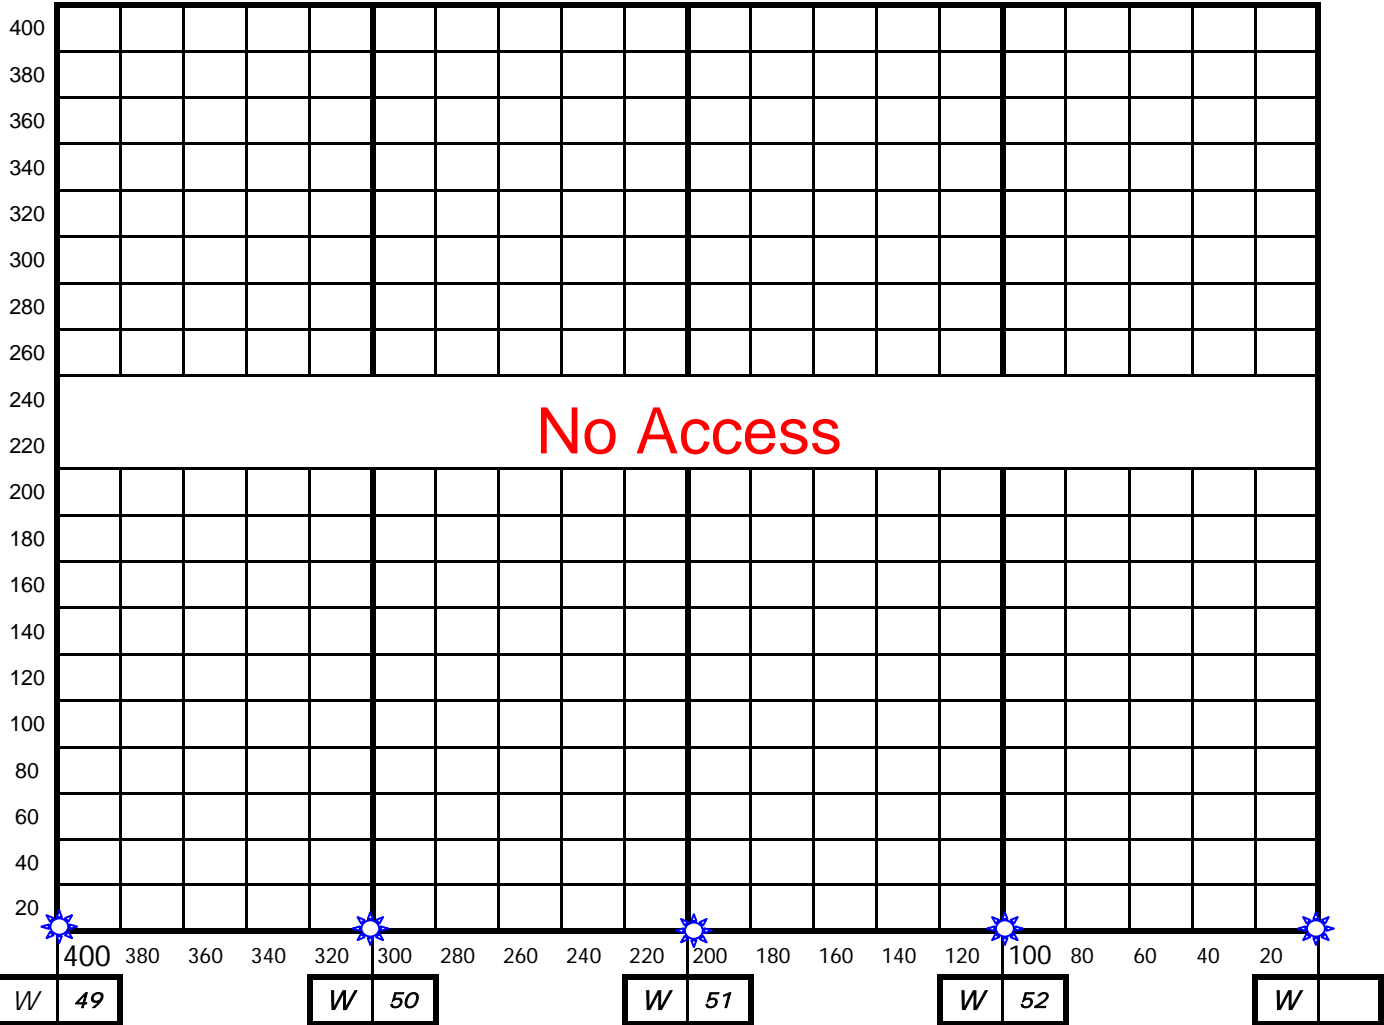


Start	Start	Start	Start	Start	
Finish	Finish	Finish	Finish	Finish	
	MEC		MD		STAKE #

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:		Completion Date:	
QC Date:		QC Signature:	
QA Date:		QA Signature:	

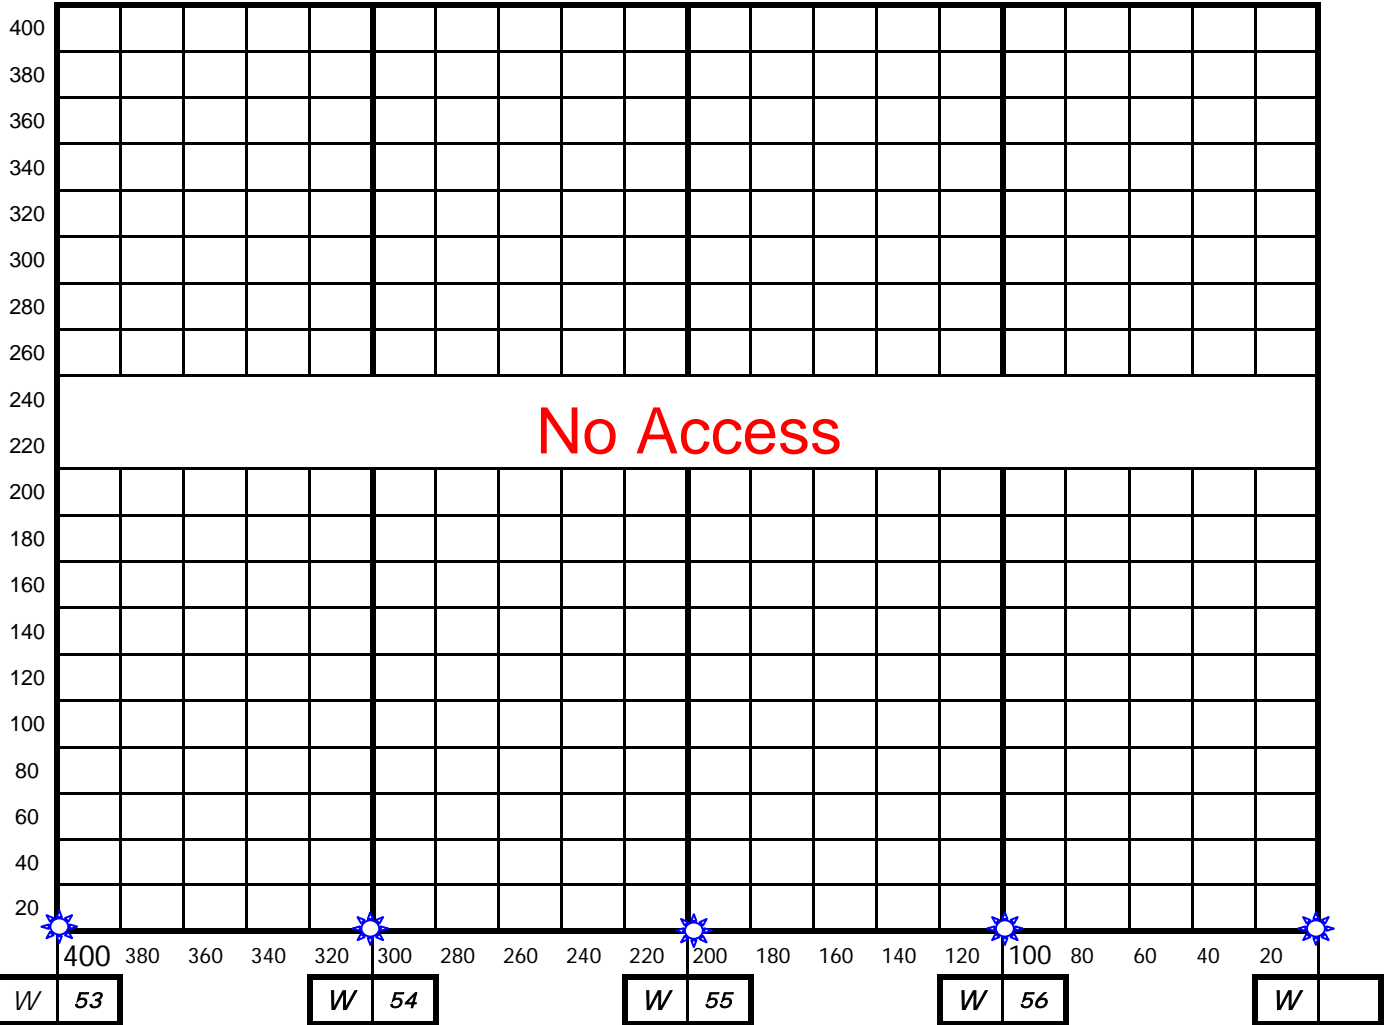


Start	Start	Start	Start	Start	
Finish	Finish	Finish	Finish	Finish	
	MEC		MD		STAKE #

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:		Completion Date:	
QC Date:		QC Signature:	
QA Date:		QA Signature:	

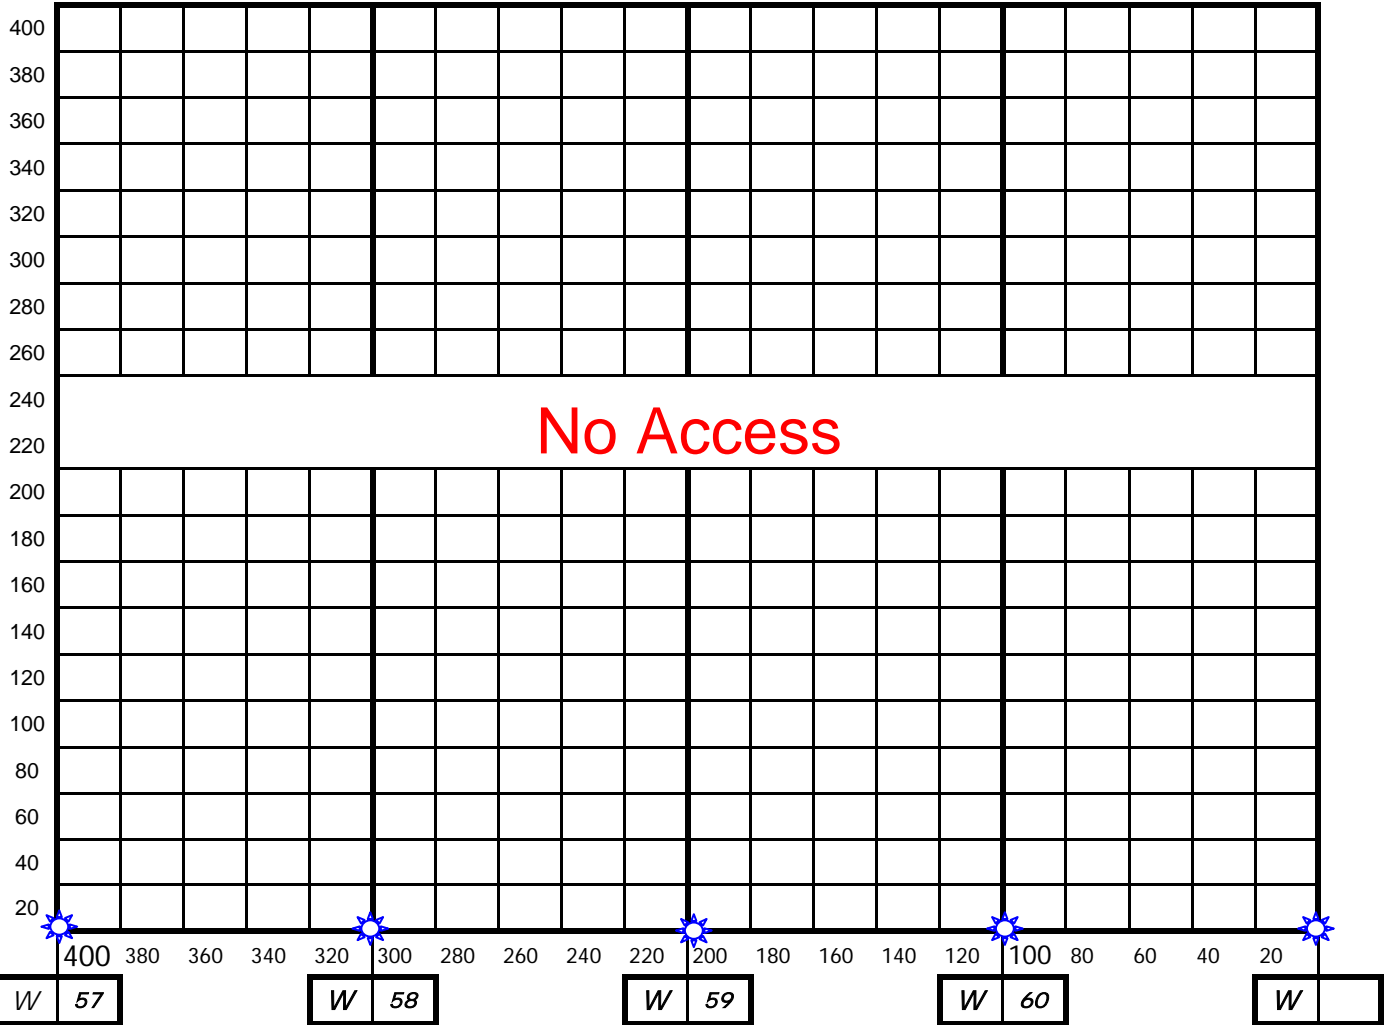


Start	Start	Start	Start	Start
Finish	Finish	Finish	Finish	Finish
MEC	MD	STAKE #		

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/27/2008	Completion Date:	8/27/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

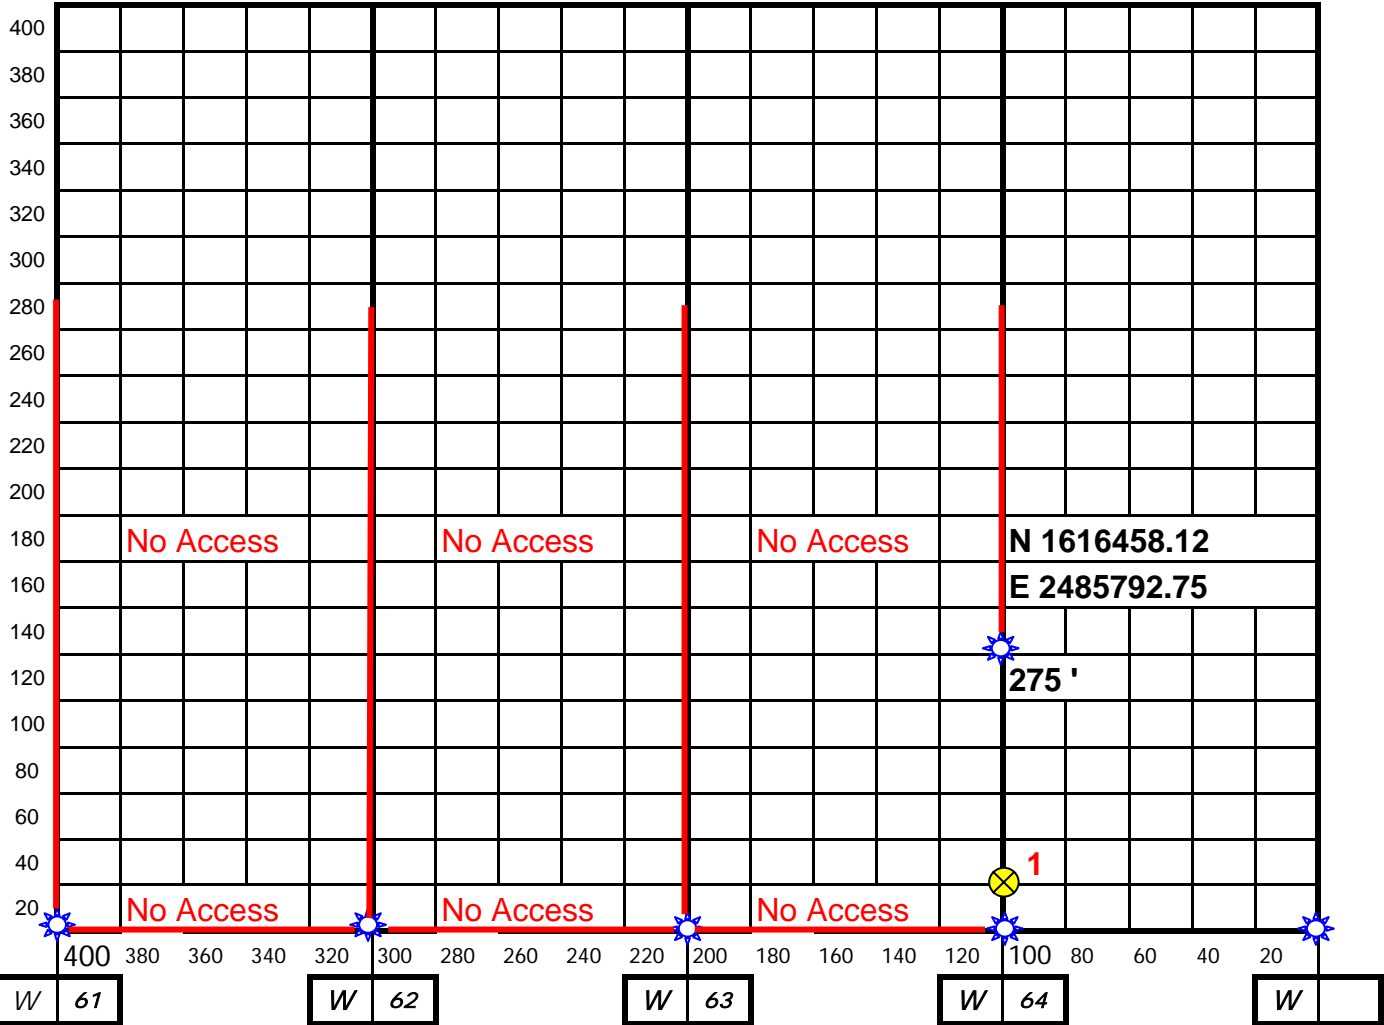

Start	Start	Start	Start	Start
			8/27	
Finish	Finish	Finish	Finish	Finish
			8/27	
MEC		MD		STAKE #

Comments. Notes:

61/62/63: No access due to terrain


64: Partial due to terrain

Anomalies

#	ID	Northing	Easting	Comments
1	64 A	1616465.51	2485819.33	Empty projo
2				
3				
4				
5				
6				
7				
8				
9				
10				
11				
12				
13				
14				
15				
16				
17				
18				
19				
20				
21				
22				
23				
24				
25				
26				
27				
28				
29				
30				
31				
32				
33				
34				
35				
36				
37				
38				
39				
40				
41				
42				
43				
44				

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/27/2008	Completion Date:	8/27/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

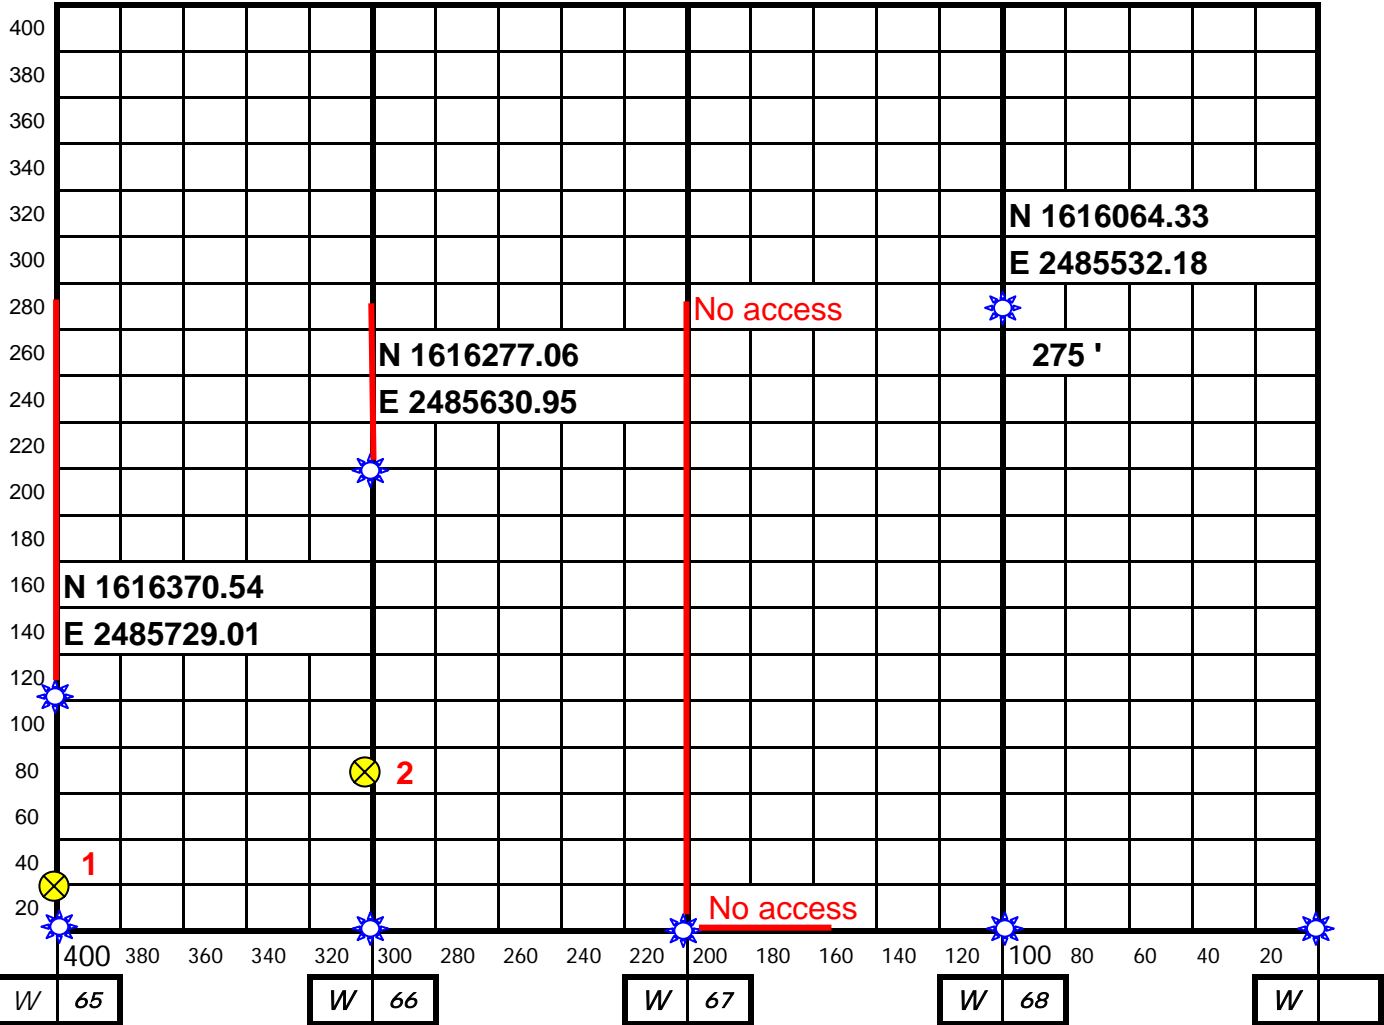

W	65	W	66	W	67	W	68	W	
---	----	---	----	---	----	---	----	---	--

Start	Start	Start	Start	Start
8/27	8/27	8/27	8/27	
Finish	Finish	Finish	Finish	Finish
8/27	8/27	8/27	8/27	
	MEC		MD	
				STAKE #

Comments.Notes:

65/66: Terrain past marked points are not accessible due to steep terrain


67: No access due to terrain

Anomalies

#	ID	Northing	Easting	Comments
1	65 A	1616364.72	249500.22	MD frag
2	66 A	1616279	2485738.5	MD frag
3				
4				
5				
6				
7				
8				
9				
10				
11				
12				
13				
14				
15				
16				
17				
18				
19				
20				
21				
22				
23				
24				
25				
26				
27				
28				
29				
30				
31				
32				
33				
34				
35				
36				
37				
38				
39				
40				
41				
42				
43				

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/27/2008	Completion Date:	8/27/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

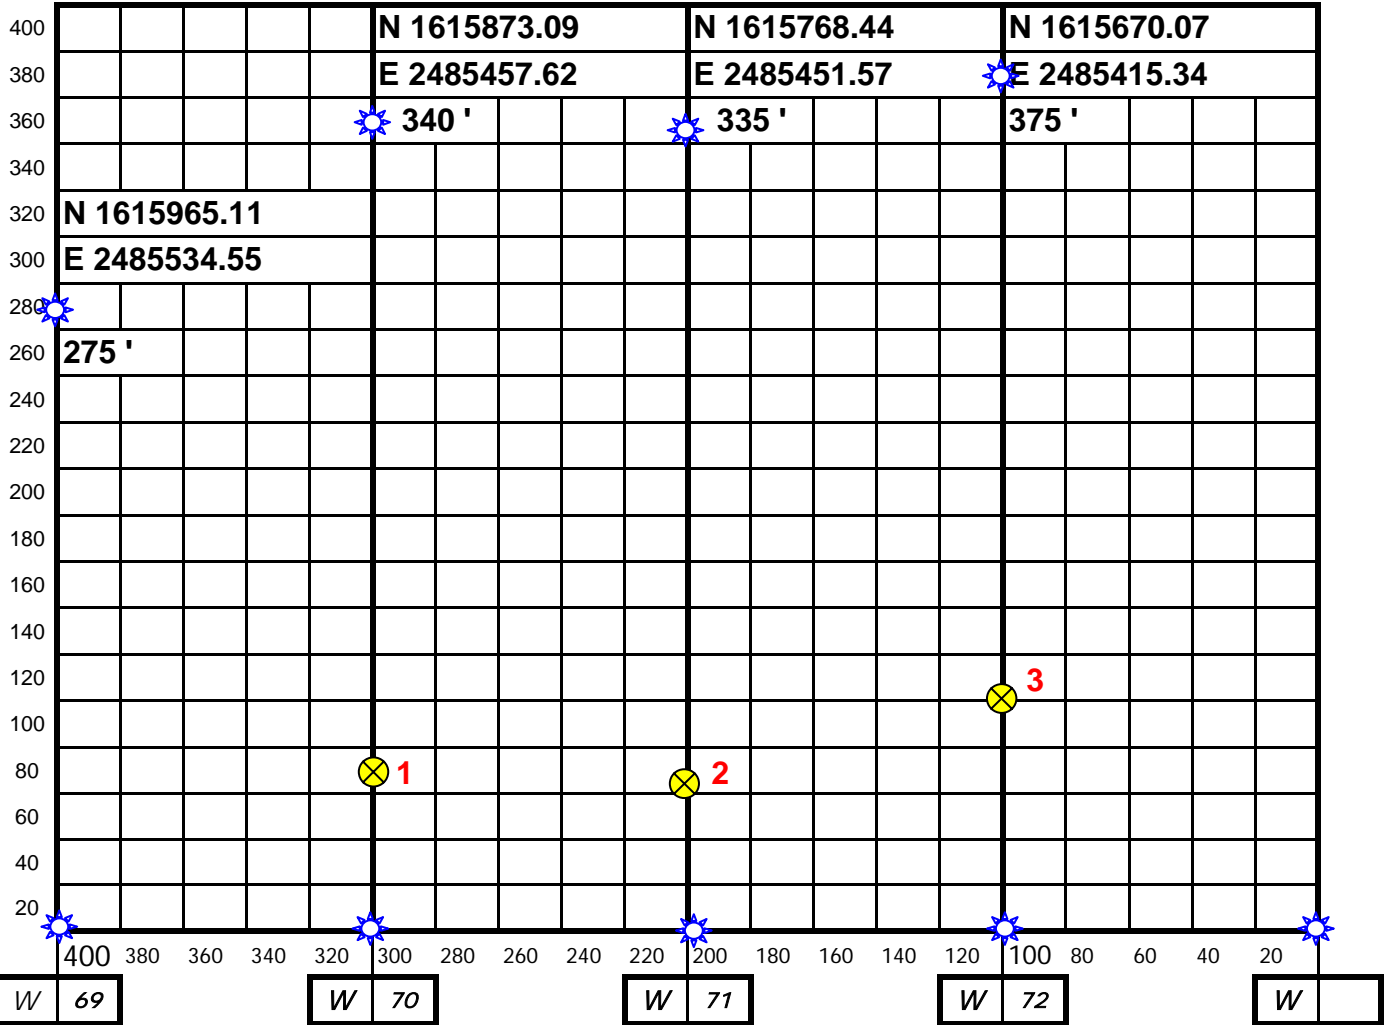

Start	Start	Start	Start	Start
<input type="text" value="8/27"/>	<input type="text" value="8/27"/>	<input type="text" value="8/27"/>	<input type="text" value="8/27"/>	<input type="text"/>
Finish	Finish	Finish	Finish	Finish
<input type="text" value="8/27"/>	<input type="text" value="8/27"/>	<input type="text" value="8/27"/>	<input type="text" value="8/27"/>	<input type="text"/>
MEC	MD	STAKE #		


Comments.Notes:

Anomalies

#	ID	Northing	Easting	Comments
1	70 A	1615874.03	2485737.1	MD frag
2	71 A	1615768.44	2485451.57	MD frag
3	72 A	1615679.26	2485692.99	MD frag
4				
5				
6				
7				
8				
9				
10				
11				
12				
13				
14				
15				
16				
17				
18				
19				
20				
21				
22				
23				
24				
25				
26				
27				
28				
29				
30				
31				
32				
33				
34				
35				
36				
37				
38				
39				
40				
41				
42				

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/27/2008	Completion Date:	9/11/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

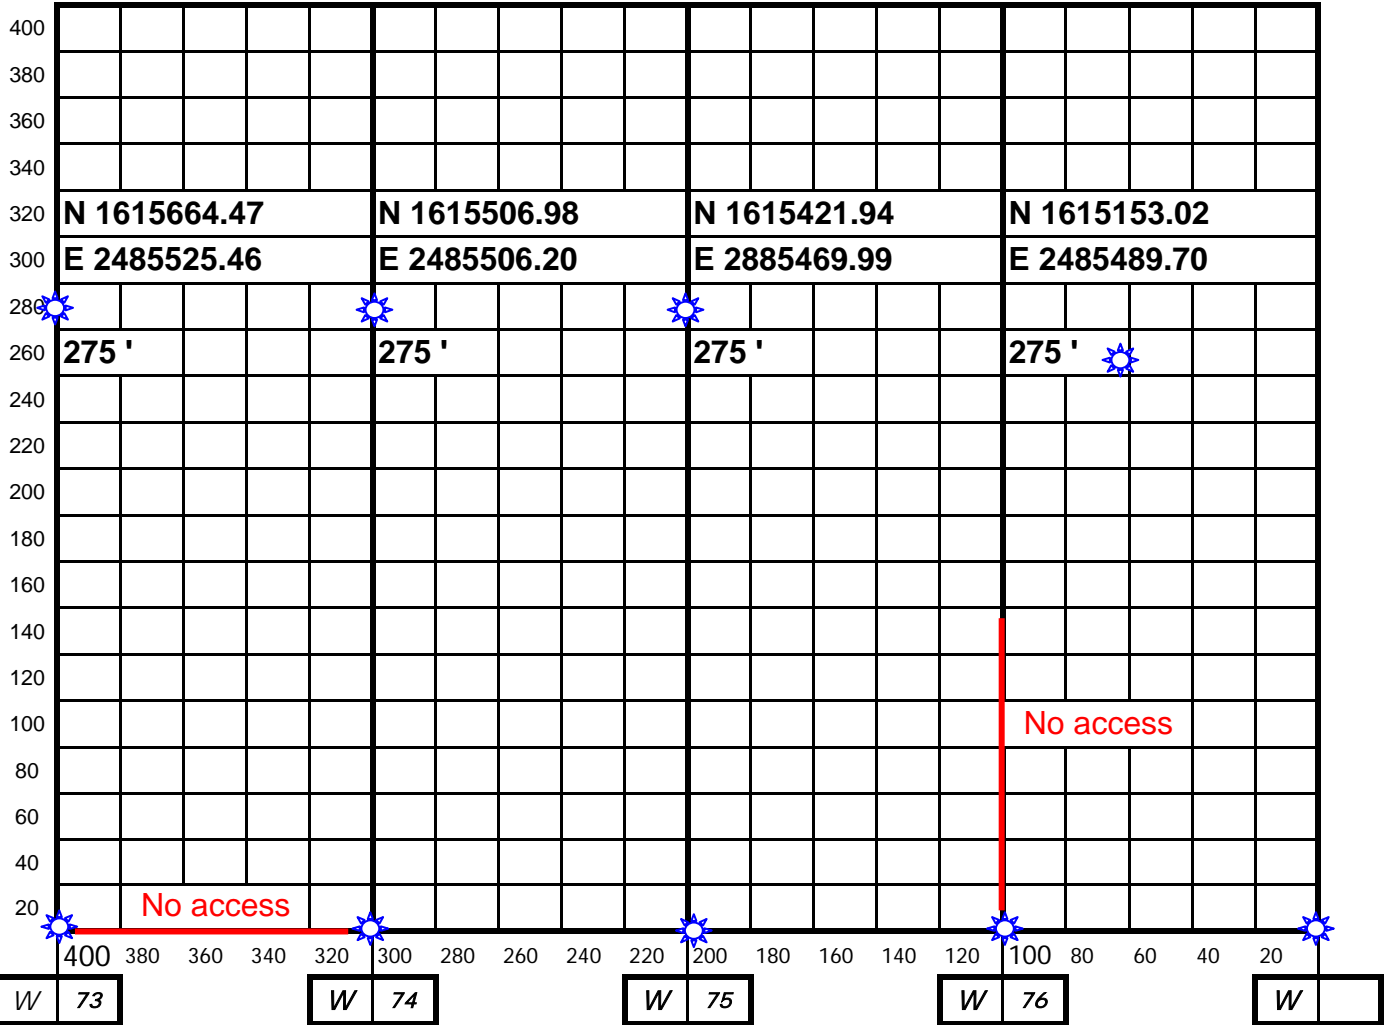


Start	Start	Start	Start	Start	
8/27	8/27	8/27	9/11		
Finish	Finish	Finish	Finish	Finish	
8/27	8/27	8/27	9/11		
	MEC		MD		STAKE #

Comments.Notes:

- 75: Stake offset 30 ' west side of arroyo
- 73 Base: Not accessible
- 76: Offset 25' to West

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	9/4/2008	Completion Date:	9/11/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

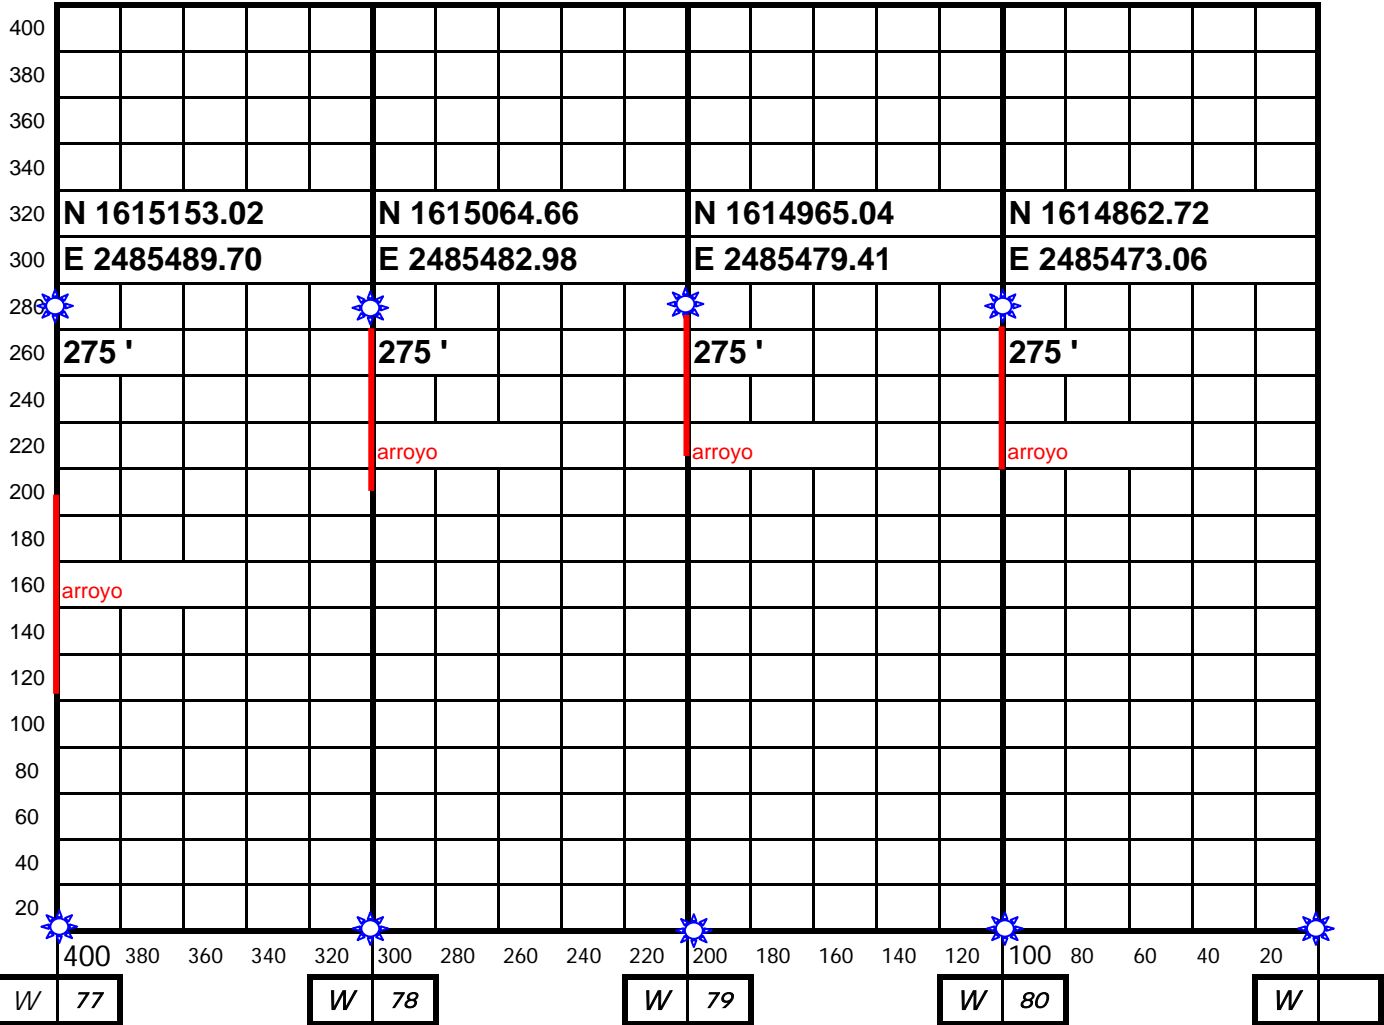


Start	Start	Start	Start	Start
9/11	9/4	9/4	9/4	
Finish	Finish	Finish	Finish	Finish
9/11	9/4	9/4	9/4	
MEC	MD	STAKE #		

Comments. Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/28/2008	Completion Date:	8/28/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

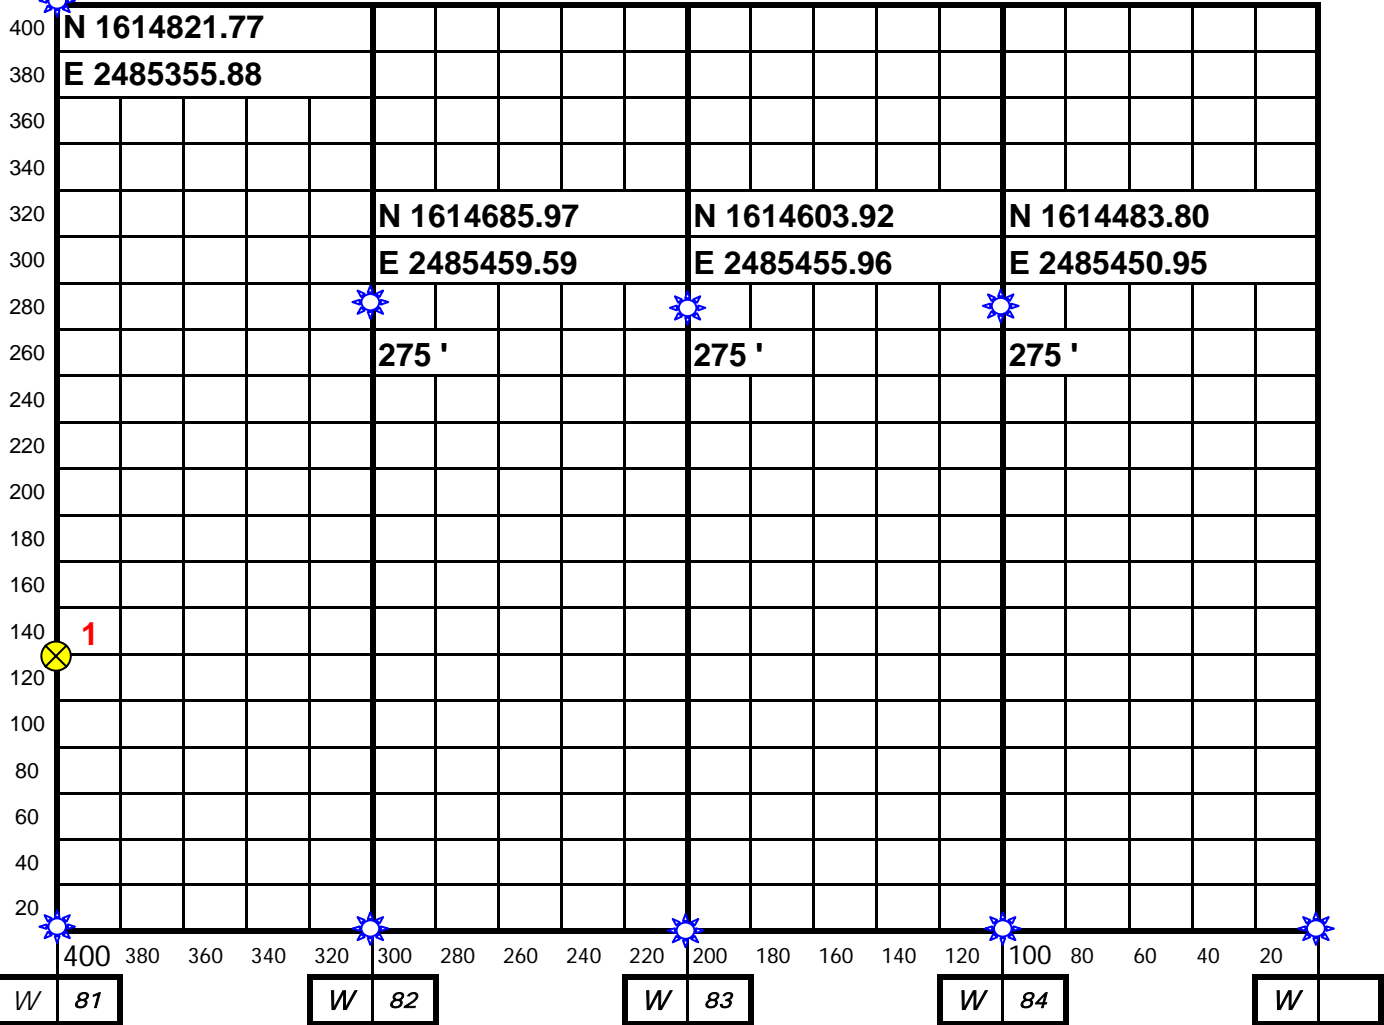

W	81	W	82	W	83	W	84	W	
---	----	---	----	---	----	---	----	---	--

Start	Start	Start	Start	Start	
8/28	8/28	8/28	8/28		
Finish	Finish	Finish	Finish	Finish	
8/28	8/28	8/28	8/28		
	MEC		MD		STAKE #


Comments. Notes:

Anomalies

#	ID	Northing	Easting	Comments
1	W 81.1	1614800.9	2485604.8	MD frag
2				
3				
4				
5				
6				
7				
8				
9				
10				
11				
12				
13				
14				
15				
16				
17				
18				
19				
20				
21				
22				
23				
24				
25				
26				
27				
28				
29				
30				
31				
32				
33				
34				
35				
36				
37				
38				
39				
40				
41				
42				
43				
44				

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:		Completion Date:	
QC Date:		QC Signature:	
QA Date:		QA Signature:	

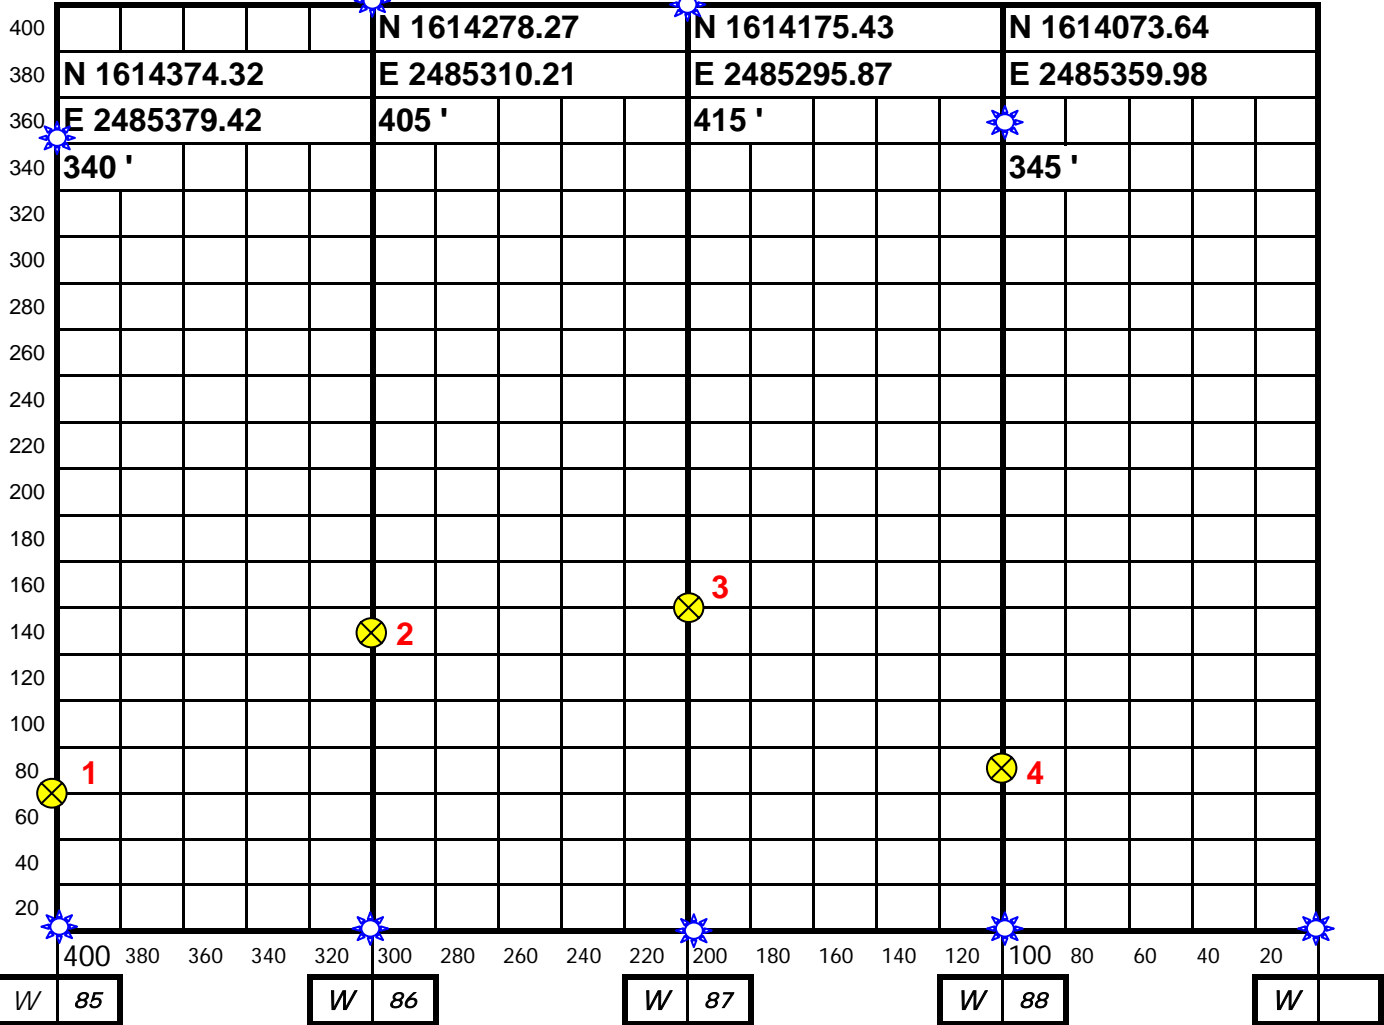

Start	Start	Start	Start	Start
8/28	8/28	8/28	8/28	
Finish	Finish	Finish	Finish	Finish
8/28	8/28	8/28	8/28	
	MEC		MD	
				STAKE #


Comments.Notes:

Anomalies

#	ID	Northing	Easting	Comments
1	85 A	1614374.08	2485657.68	MD frag
2	86 A	1614275.12	2485587.97	MD frag
3	87 A	1614160.96	2485578.71	MD frag
4	88 A	1614027.81	2485635.25	MD frag
5				
6				
7				
8				
9				
10				
11				
12				
13				
14				
15				
16				
17				
18				
19				
20				
21				
22				
23				
24				
25				
26				
27				
28				
29				
30				
31				
32				
33				
34				
35				
36				
37				
38				
39				
40				
41				
42				
43				
44				

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/28/2008	Completion Date:	8/28/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

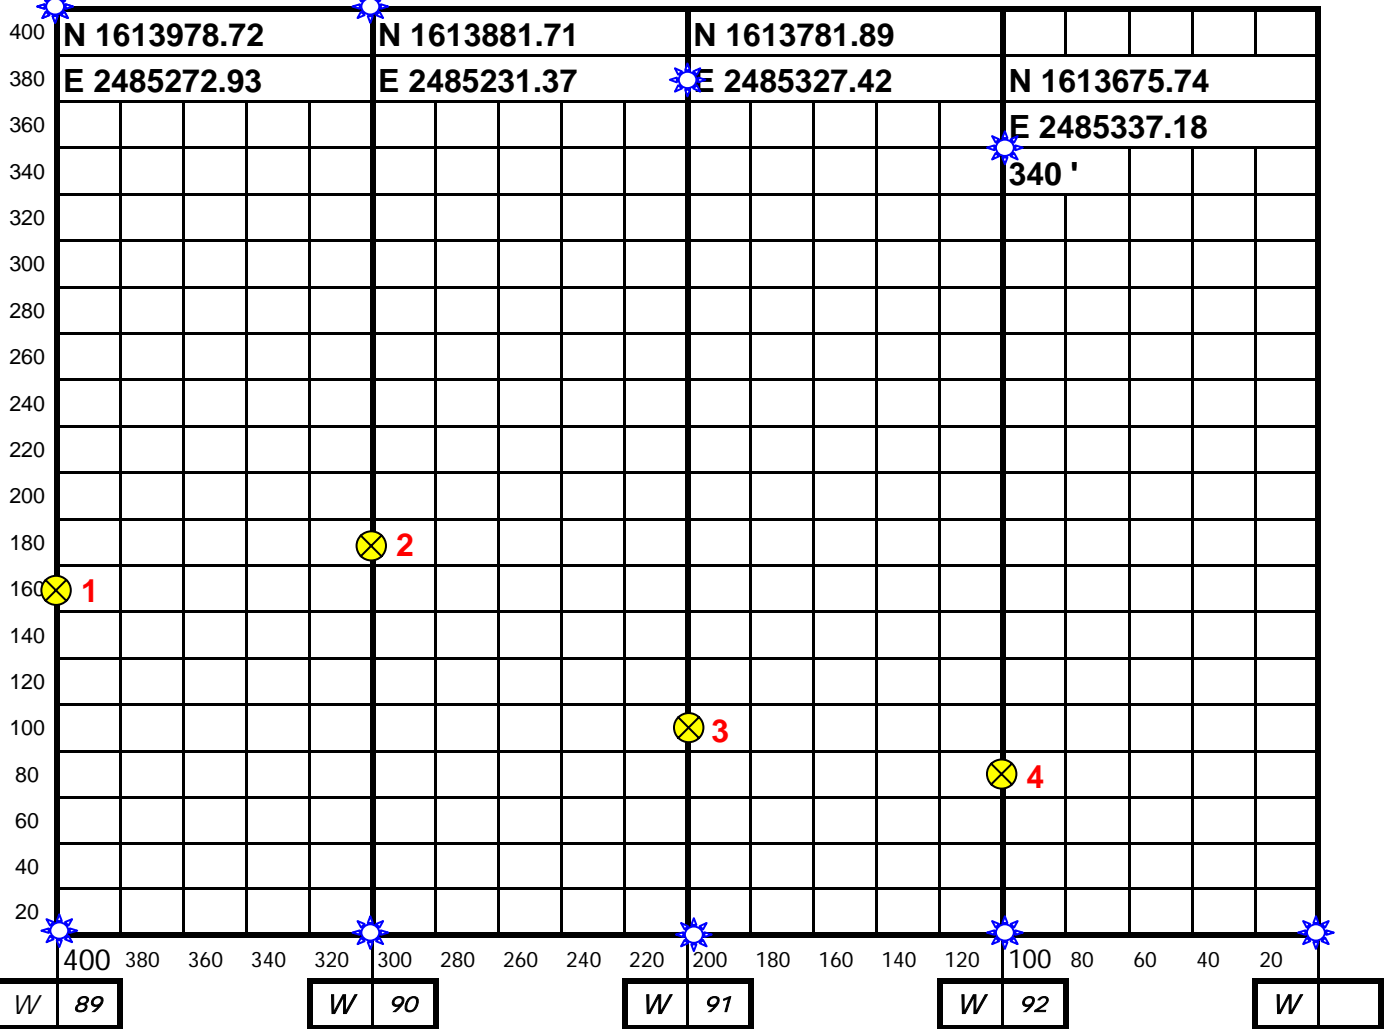

Start	Start	Start	Start	Start
8/28	8/28	8/28	8/28	
Finish	Finish	Finish	Finish	Finish
8/28	8/28	8/28	8/28	
MEC		MD		STAKE #


Comments/Notes:

Anomalies

#	ID	Northing	Easting	Comments
1	89 A	1613973.89	2485557.21	MD frag
2	90 A	1613871.41	2485523.7	MD frag
3	91 A	1613775.82	2485595.9	MD frag
4	92 A	1613674.59	2485616.78	MD frag
5				
6				
7				
8				
9				
10				
11				
12				
13				
14				
15				
16				
17				
18				
19				
20				
21				
22				
23				
24				
25				
26				
27				
28				
29				
30				
31				
32				
33				
34				
35				
36				
37				
38				
39				
40				
41				
42				
43				
44				

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	9/3/2008	Completion Date:	9/3/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

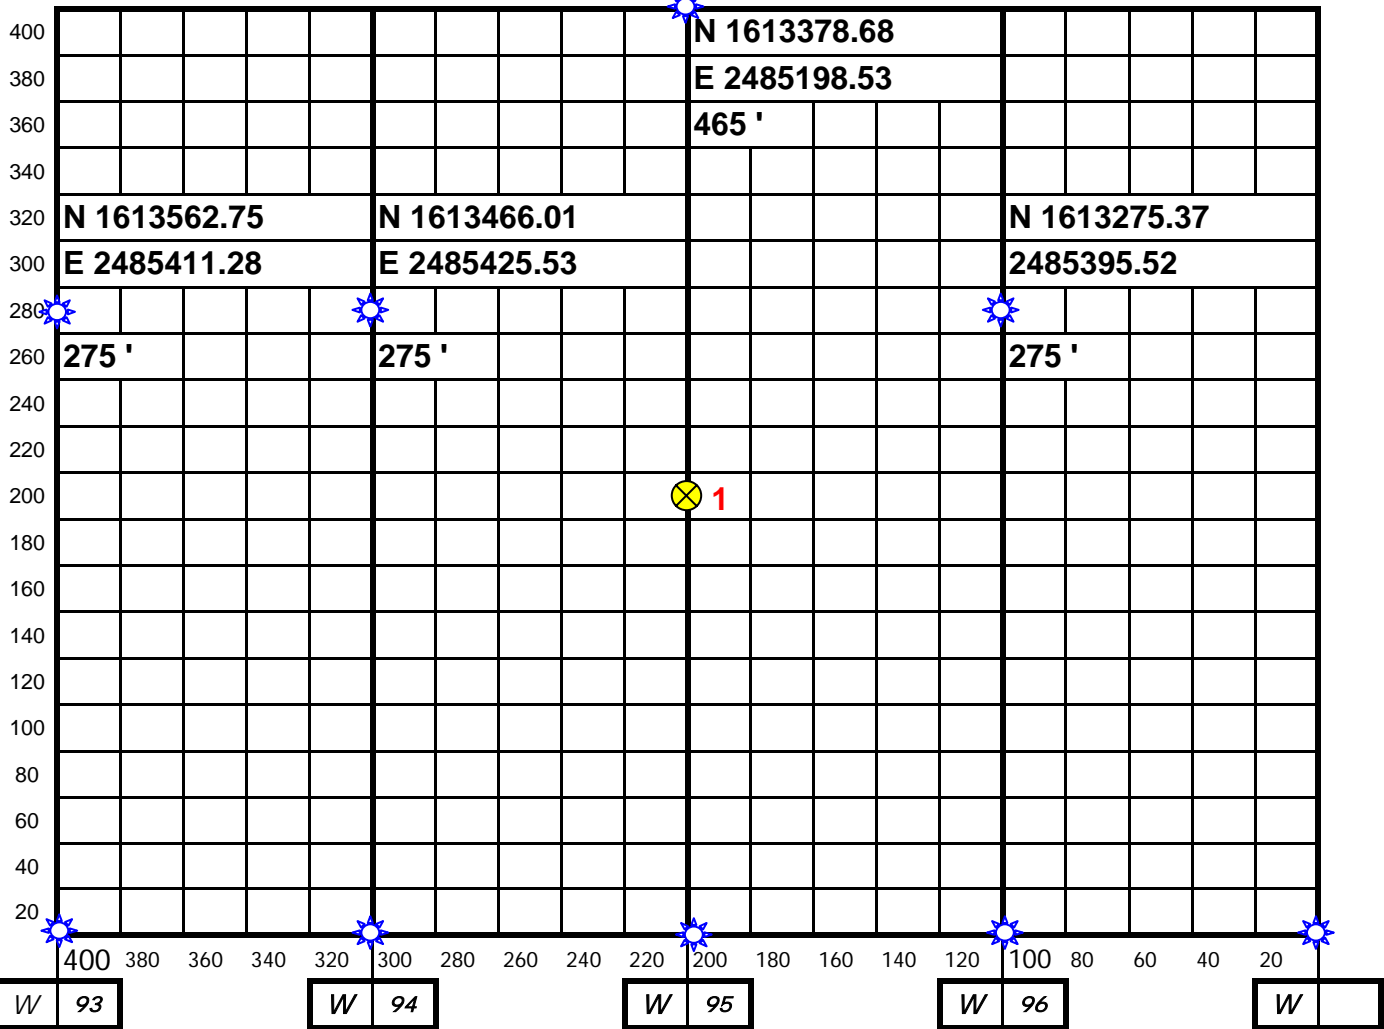

W	93	W	94	W	95	W	96	W	
---	----	---	----	---	----	---	----	---	--

Start	Start	Start	Start	Start
9/3	9/3	9/3	9/3	
Finish	Finish	Finish	Finish	Finish
9/3	9/3	9/3	9/3	
MEC		MD	STAKE #	

Comments.Notes:


93-96: EM-61 accessible

Anomalies

#	ID	Northing	Easting	Comments
1	95 A	1613373.41	2485488.26	MD frag
2				
3				
4				
5				
6				
7				
8				
9				
10				
11				
12				
13				
14				
15				
16				
17				
18				
19				
20				
21				
22				
23				
24				
25				
26				
27				
28				
29				
30				
31				
32				
33				
34				
35				
36				
37				
38				
39				
40				
41				
42				
43				

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	9/3/2008	Completion Date:	9/3/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

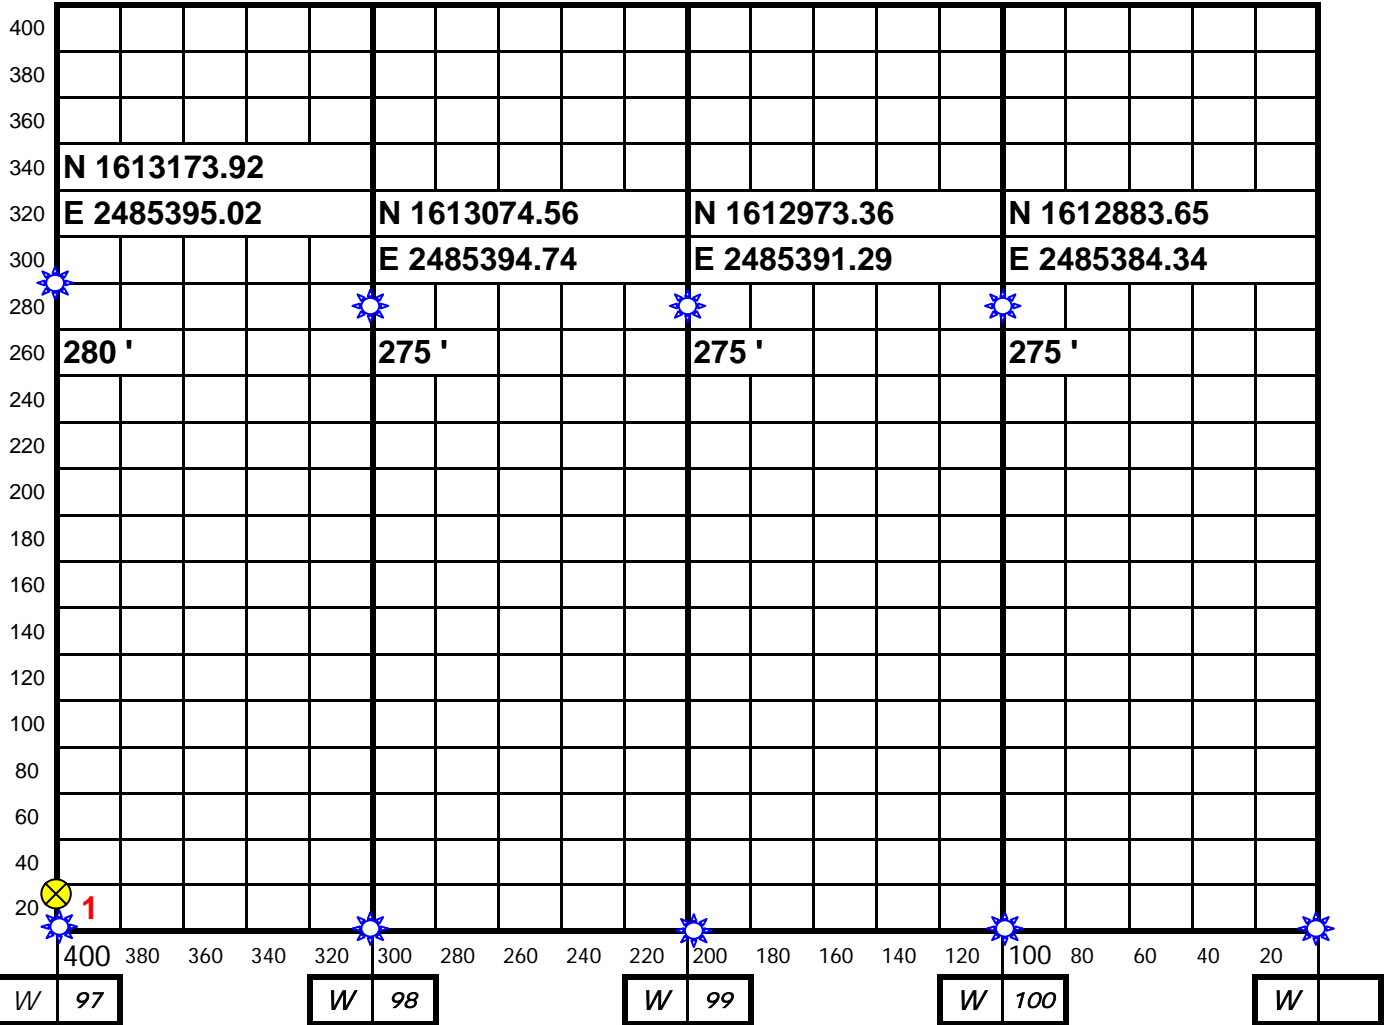

Start	Start	Start	Start	Start
<input type="text" value="9/3"/>	<input type="text" value="9/3"/>	<input type="text" value="9/3"/>	<input type="text" value="9/3"/>	<input type="text"/>
Finish	Finish	Finish	Finish	Finish
<input type="text" value="9/3"/>	<input type="text" value="9/3"/>	<input type="text" value="9/3"/>	<input type="text" value="9/3"/>	<input type="text"/>
	MEC		MD	
				STAKE #

Comments.Notes:


97-100 are EM-61 accessible

Anomalies

#	ID	Northing	Easting	Comments
1	97 A	1613168.35	2485654.42	MD frag
2				
3				
4				
5				
6				
7				
8				
9				
10				
11				
12				
13				
14				
15				
16				
17				
18				
19				
20				
21				
22				
23				
24				
25				
26				
27				
28				
29				
30				
31				
32				
33				
34				
35				
36				
37				
38				
39				
40				
41				
42				
43				

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	9/3/2008	Completion Date:	9/3/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

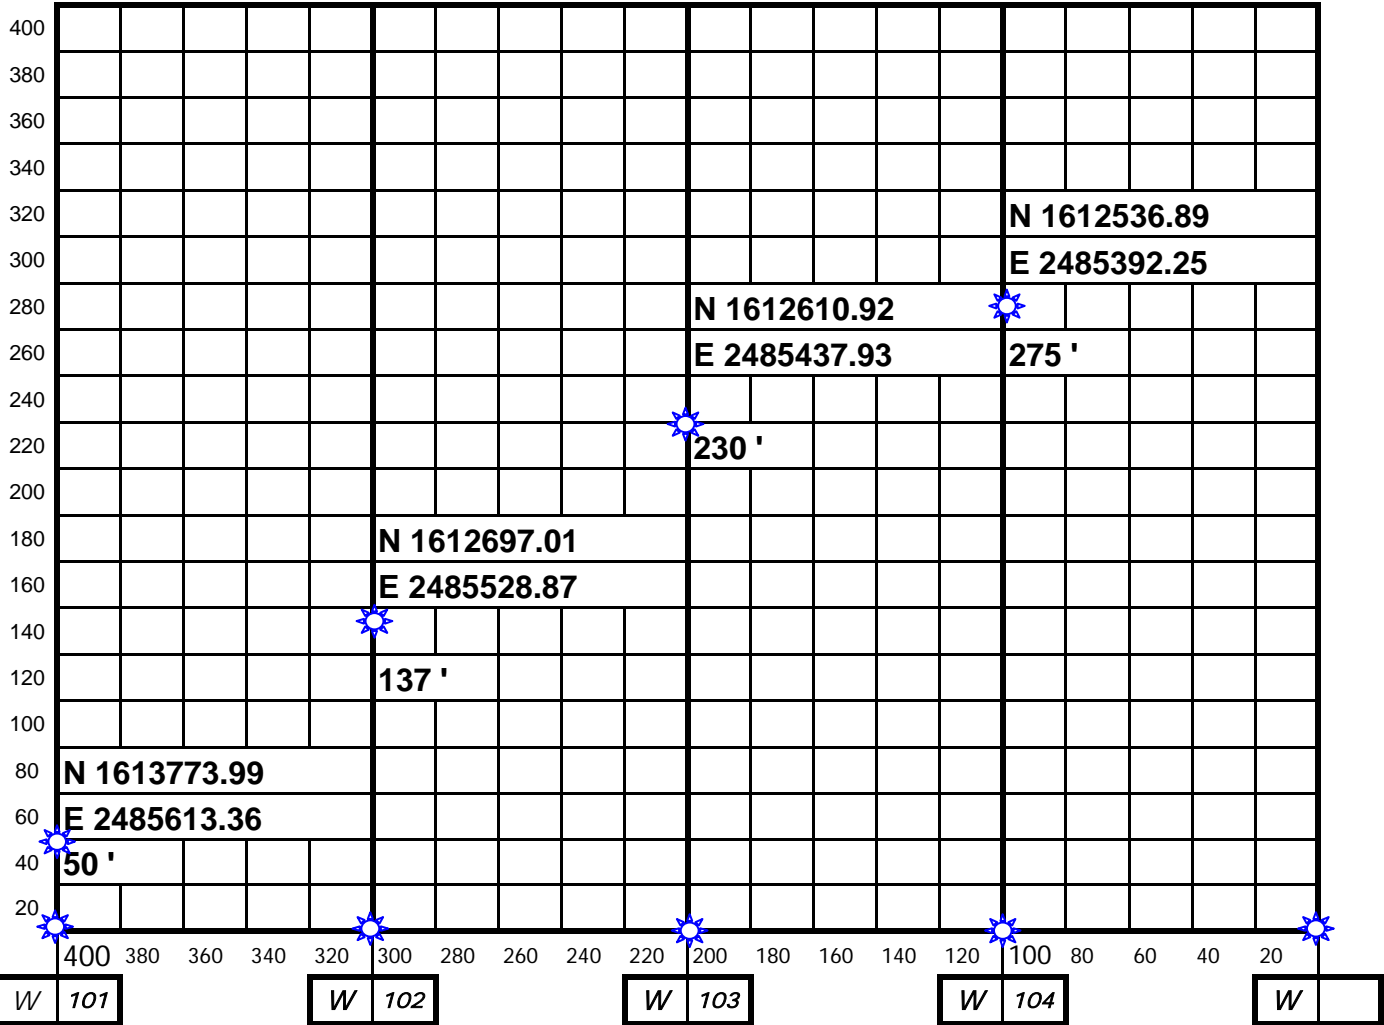

Start	Start	Start	Start	Start
<input type="text" value="9/3"/>	<input type="text" value="9/3"/>	<input type="text" value="9/3"/>	<input type="text" value="9/3"/>	<input type="text"/>
Finish	Finish	Finish	Finish	Finish
<input type="text" value="9/3"/>	<input type="text" value="9/3"/>	<input type="text" value="9/3"/>	<input type="text" value="9/3"/>	<input type="text"/>
MEC	MD	STAKE #		

Comments.Notes:


101- Stop 50' Arch Site EM 61Partials

102- Stop 137' Arch Site EM 61 Partials

103- Stop 230' Arch Site EM 61 Partials

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	9/3/2008	Completion Date:	9/3/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

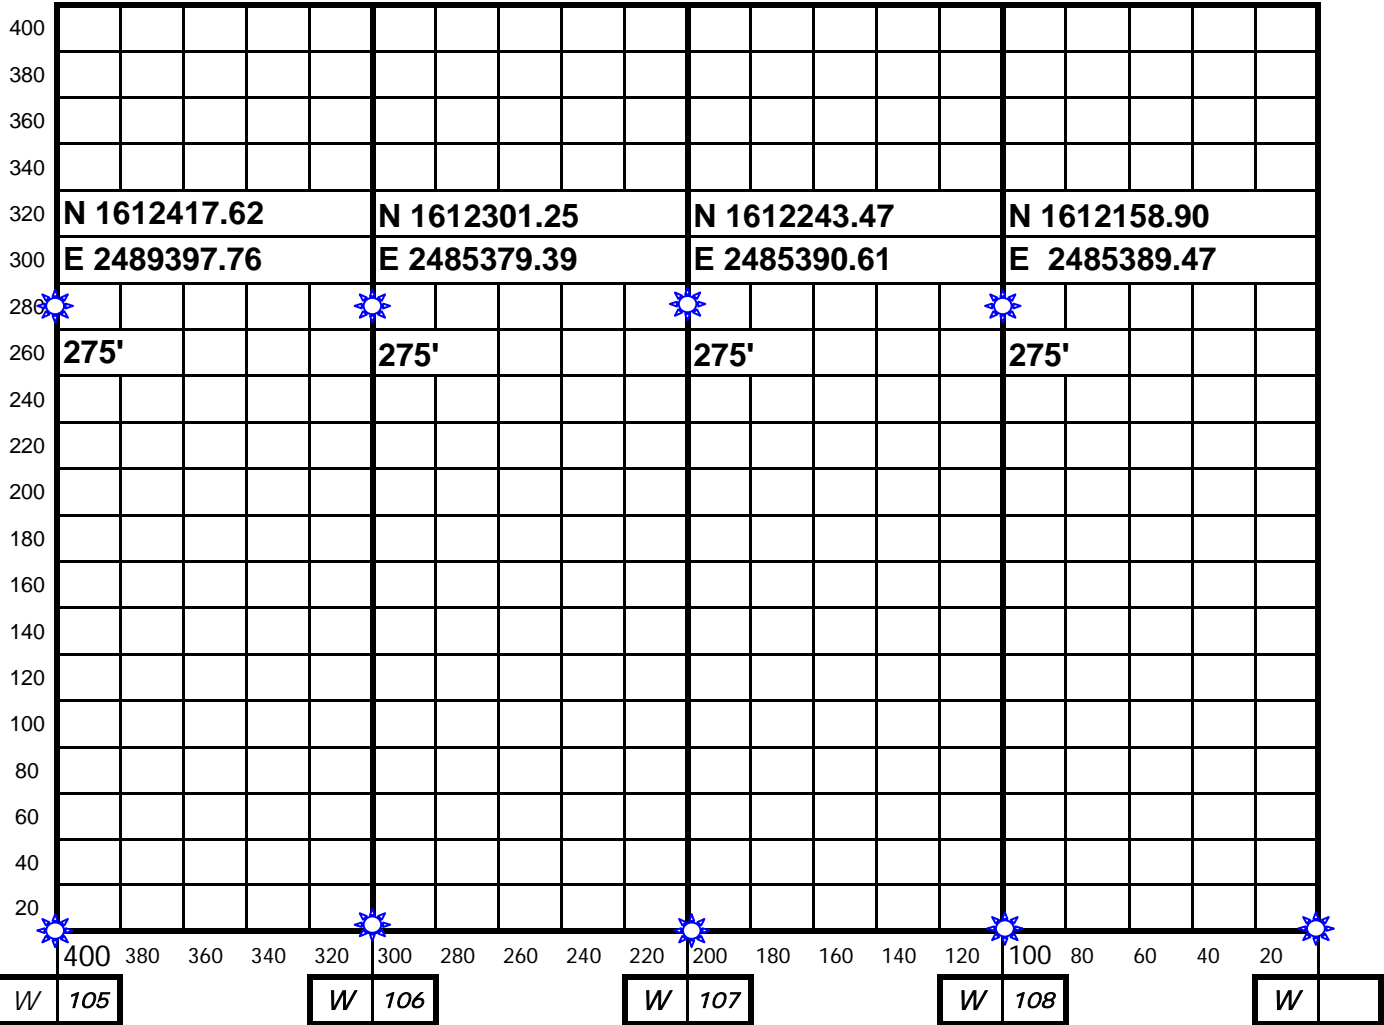

Start	Start	Start	Start	Start
9/3	9/3	9/3	9/3	9/3
Finish	Finish	Finish	Finish	Finish
9/3	9/3	9/3	9/3	9/3
MEC	MD	STAKE #		


Comments.Notes:

105 offset 10' East

ALL HILLS

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	9/3/2008	Completion Date:	9/4/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

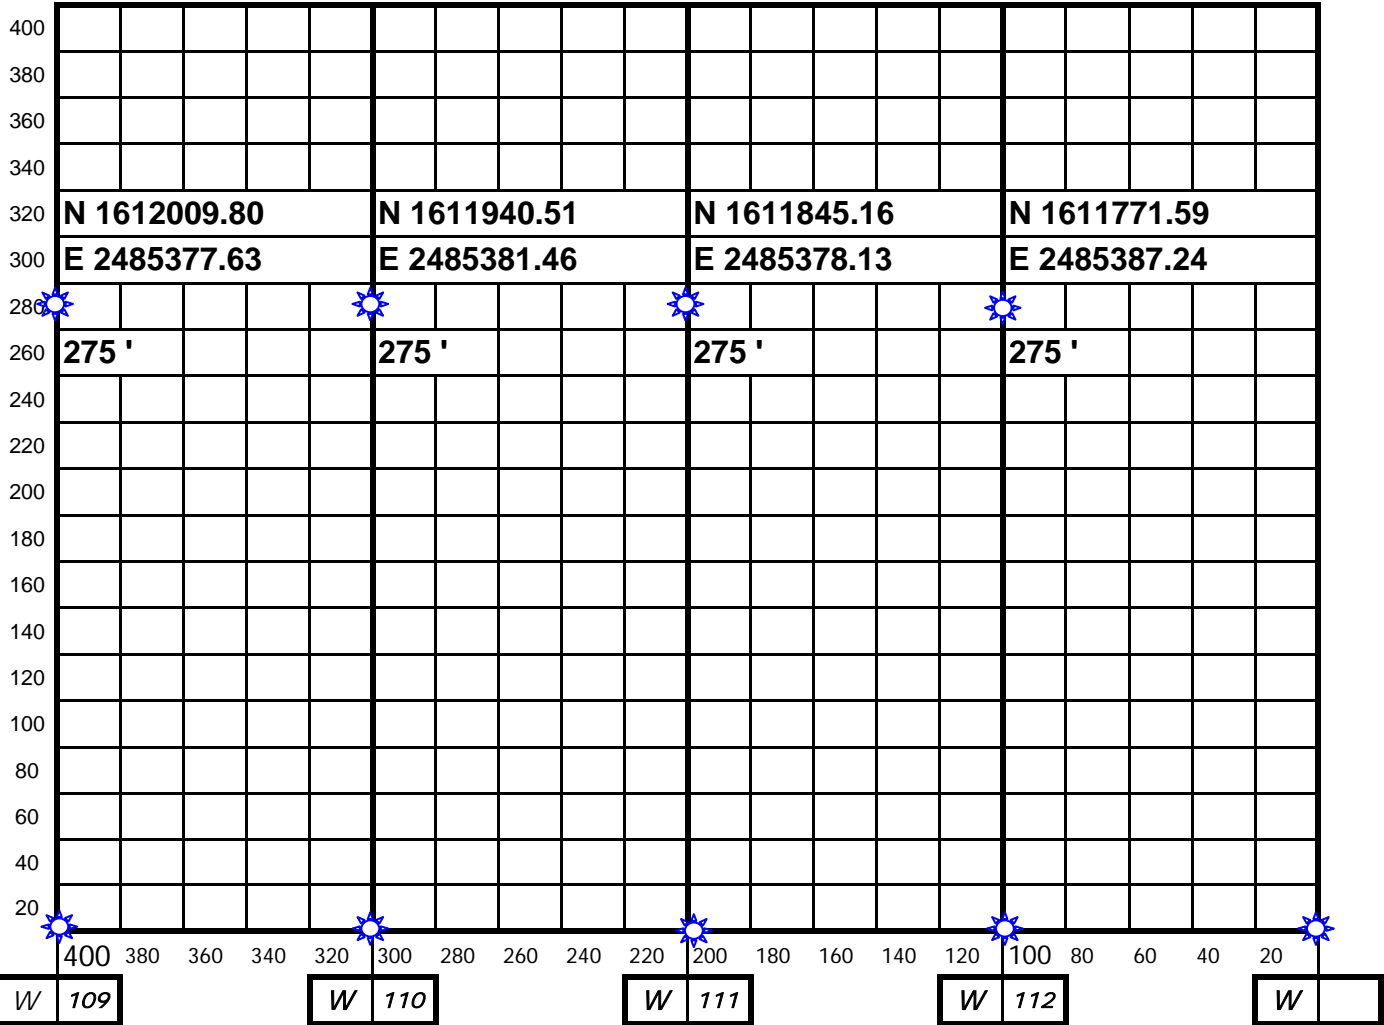


Start	Start	Start	Start	Start
9/3	9/3	9/4	4-Sep	
Finish	Finish	Finish	Finish	Finish
9/3	9/3	9/4	4-Sep	
MEC	MD	STAKE #		

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	9/4/2008	Completion Date:	9/4/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

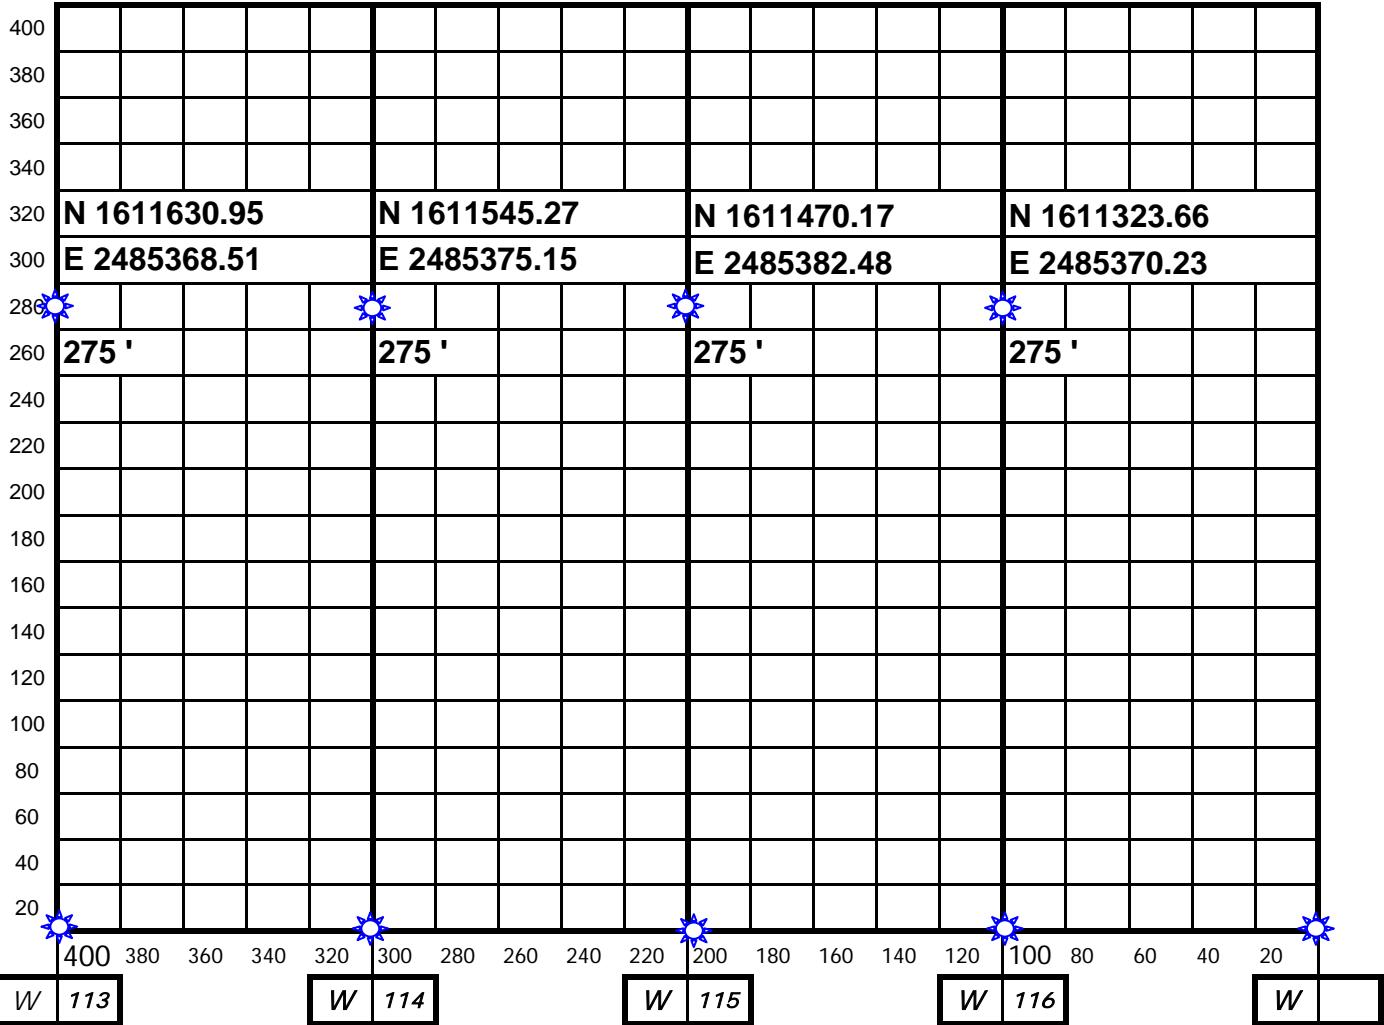


Start	Start	Start	Start	Start	
9/4	9/4	9/4	9/4		
Finish	Finish	Finish	Finish	Finish	
9/4	9/4	9/4	9/4		
	MEC		MD		STAKE #

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	9/4/2008	Completion Date:	9/4/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

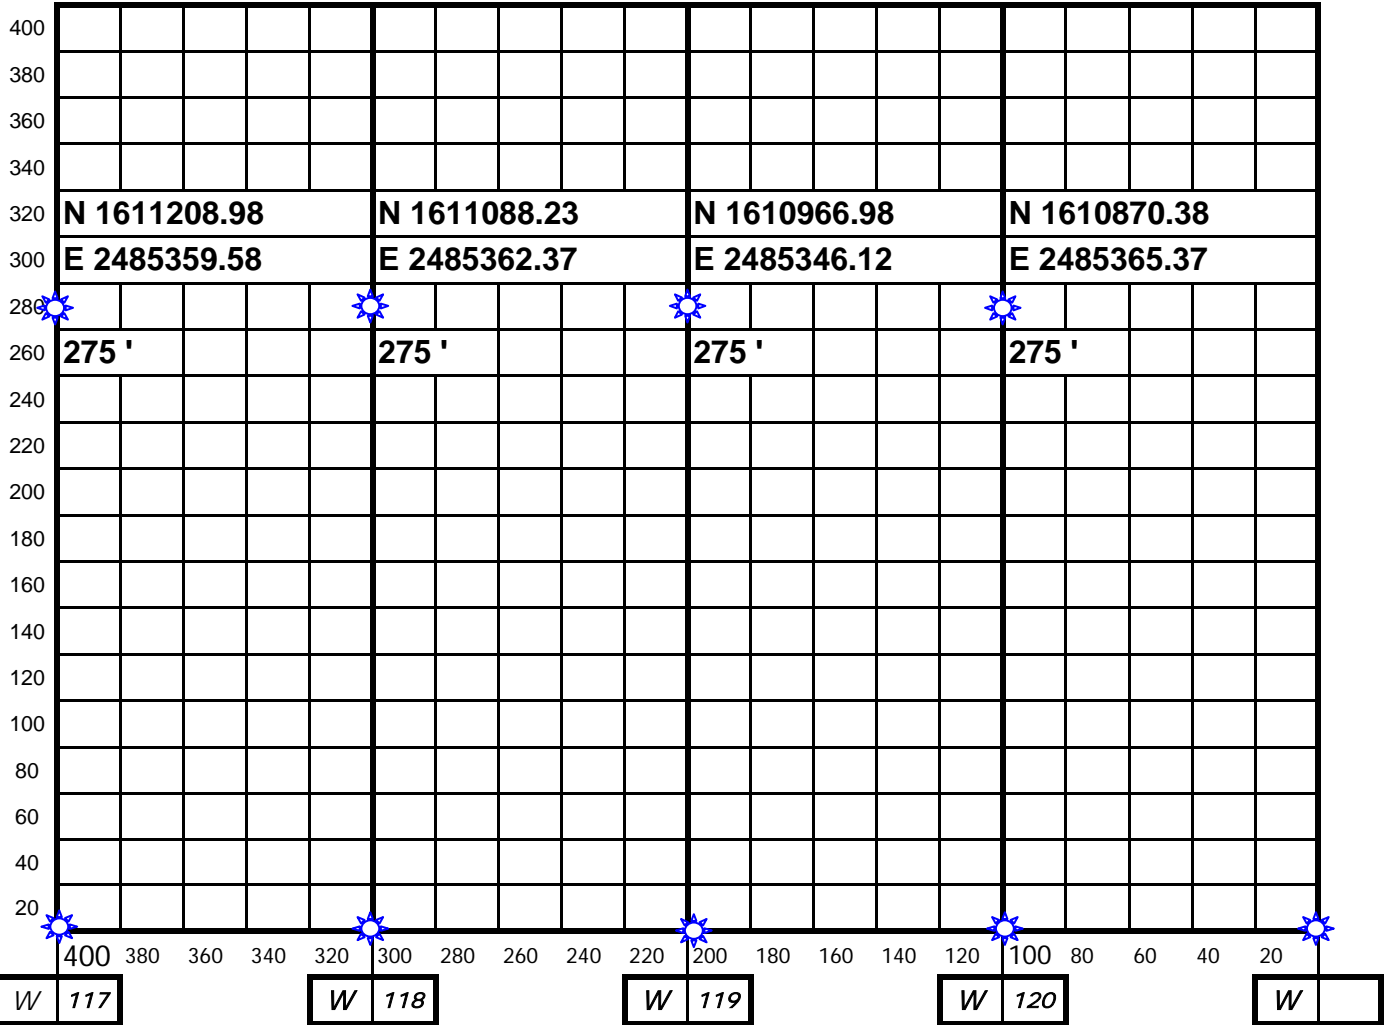


W 117	W 118	W 119	W 120	W
-------	-------	-------	-------	---

Start	Start	Start	Start	Start
9/4	9/4	9/4	9/4	
Finish	Finish	Finish	Finish	Finish
9/4	9/4	9/4	9/4	
	MEC		MD	
				STAKE #

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	9/4/2008	Completion Date:	9/4/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

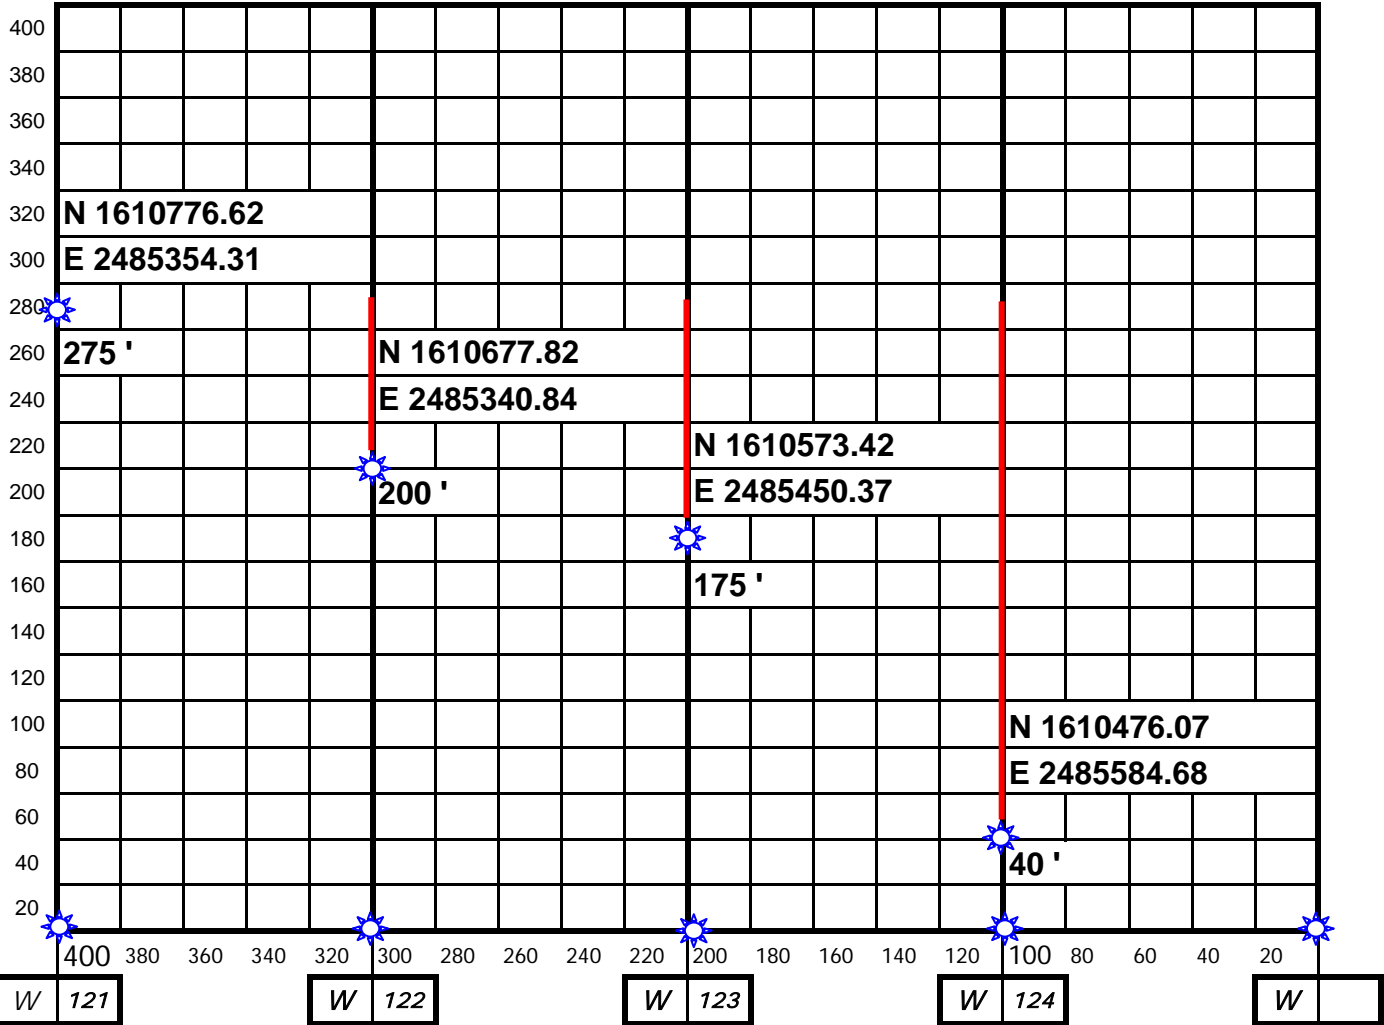


Start	Start	Start	Start	Start
9/4	9/4	9/4	9/4	
Finish	Finish	Finish	Finish	Finish
9/4	9/4	9/4	9/4	
	MEC		MD	
				STAKE #

Comments. Notes:

122/ 123/124: Partials due to terrain

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	9/4/2008	Completion Date:	9/4/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

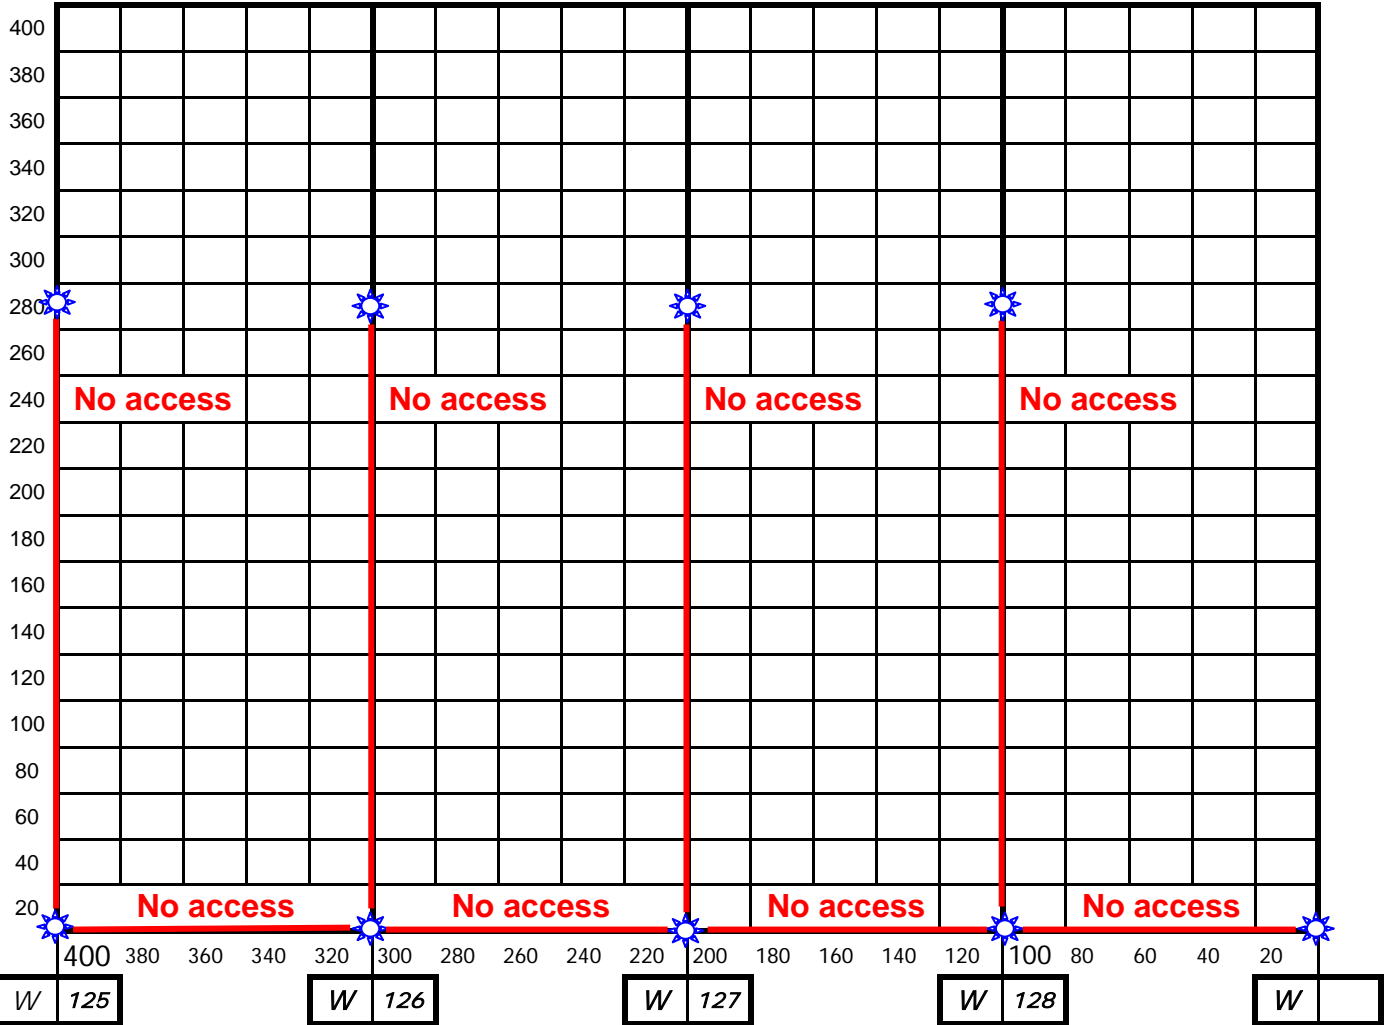


Start	Start	Start	Start	Start
<input type="text" value="9/4"/>	<input type="text" value="9/4"/>	<input type="text" value="9/4"/>	<input type="text" value="9/4"/>	<input type="text"/>
Finish	Finish	Finish	Finish	Finish
<input type="text" value="9/4"/>	<input type="text" value="9/4"/>	<input type="text" value="9/4"/>	<input type="text" value="9/4"/>	<input type="text"/>
MEC	MD	STAKE #		

Comments.Notes:

No access due to terrain

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/6/2009	Completion Date:	4/6/2009
QC Date:		QA Date	

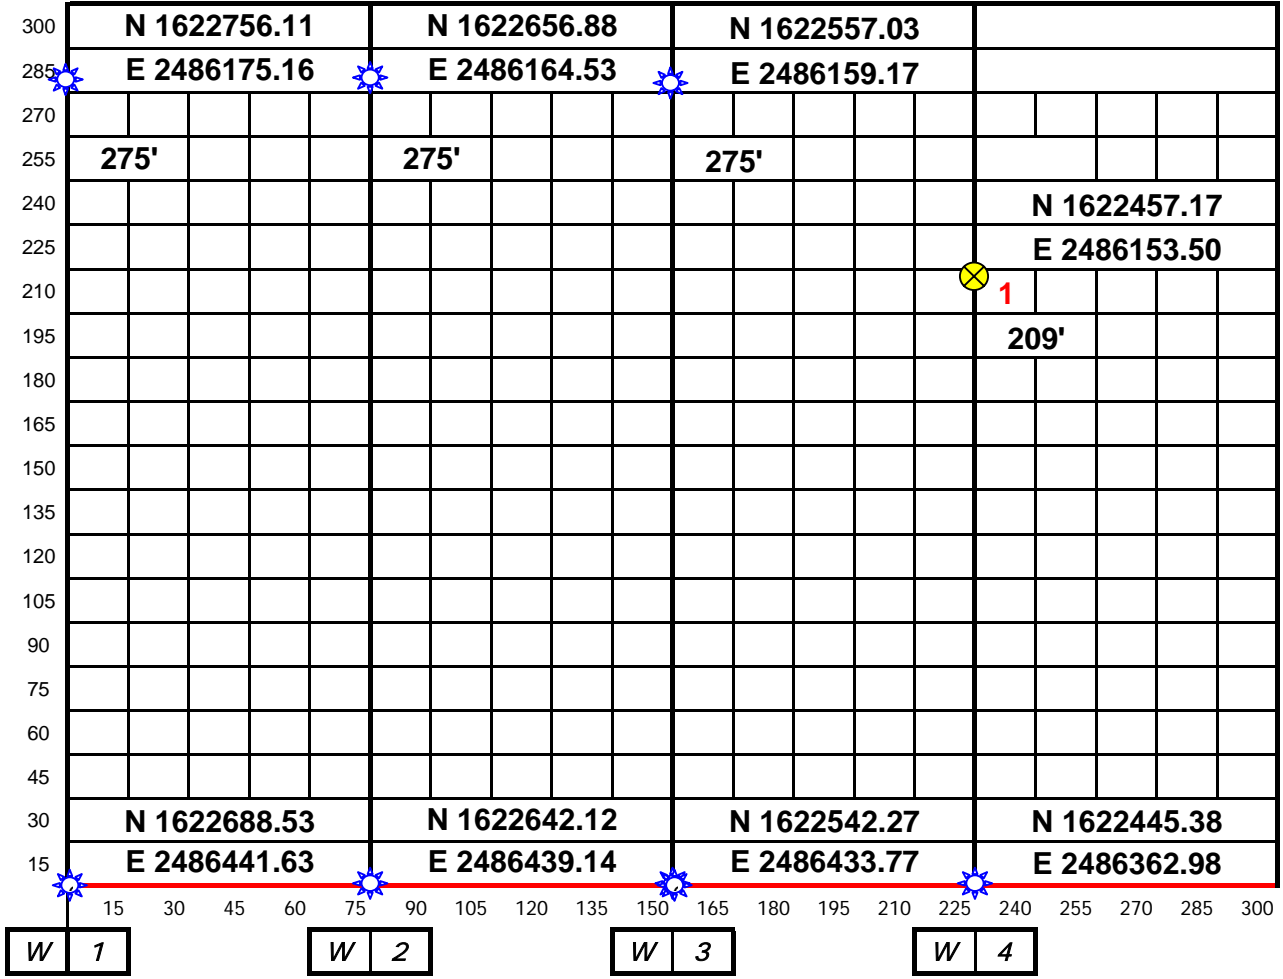


Start <input type="text" value="4/6"/>	Start <input type="text" value="4/6"/>	Start <input type="text" value="4/6"/>	Start <input type="text" value="4/6"/>
Finish <input type="text" value="4/6"/>	Finish <input type="text" value="4/6"/>	Finish <input type="text" value="4/6"/>	Finish <input type="text" value="4/6"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

1 Fragmentation

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/6/2009	Completion Date:	4/6/2009
QC Date:		QA Date	

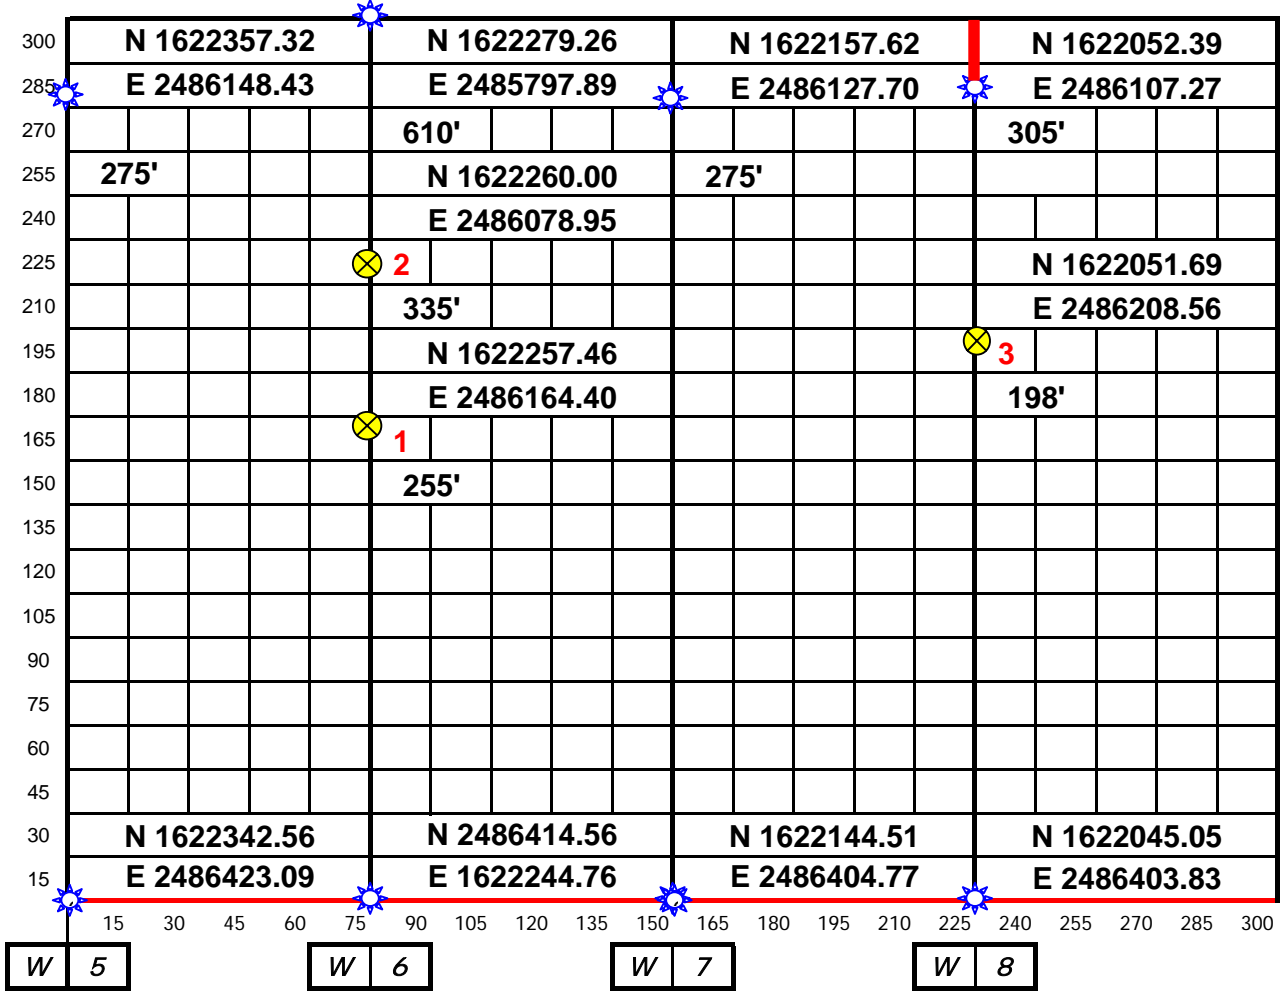

Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/6</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/6</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/6</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/6</div>
Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/6</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/6</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/6</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/6</div>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:


1 Fragmentation

2 Fragmentation

W8 No Access/Safety after 305 feet

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/6/2009	Completion Date:	4/6/2009
QC Date:		QA Date	

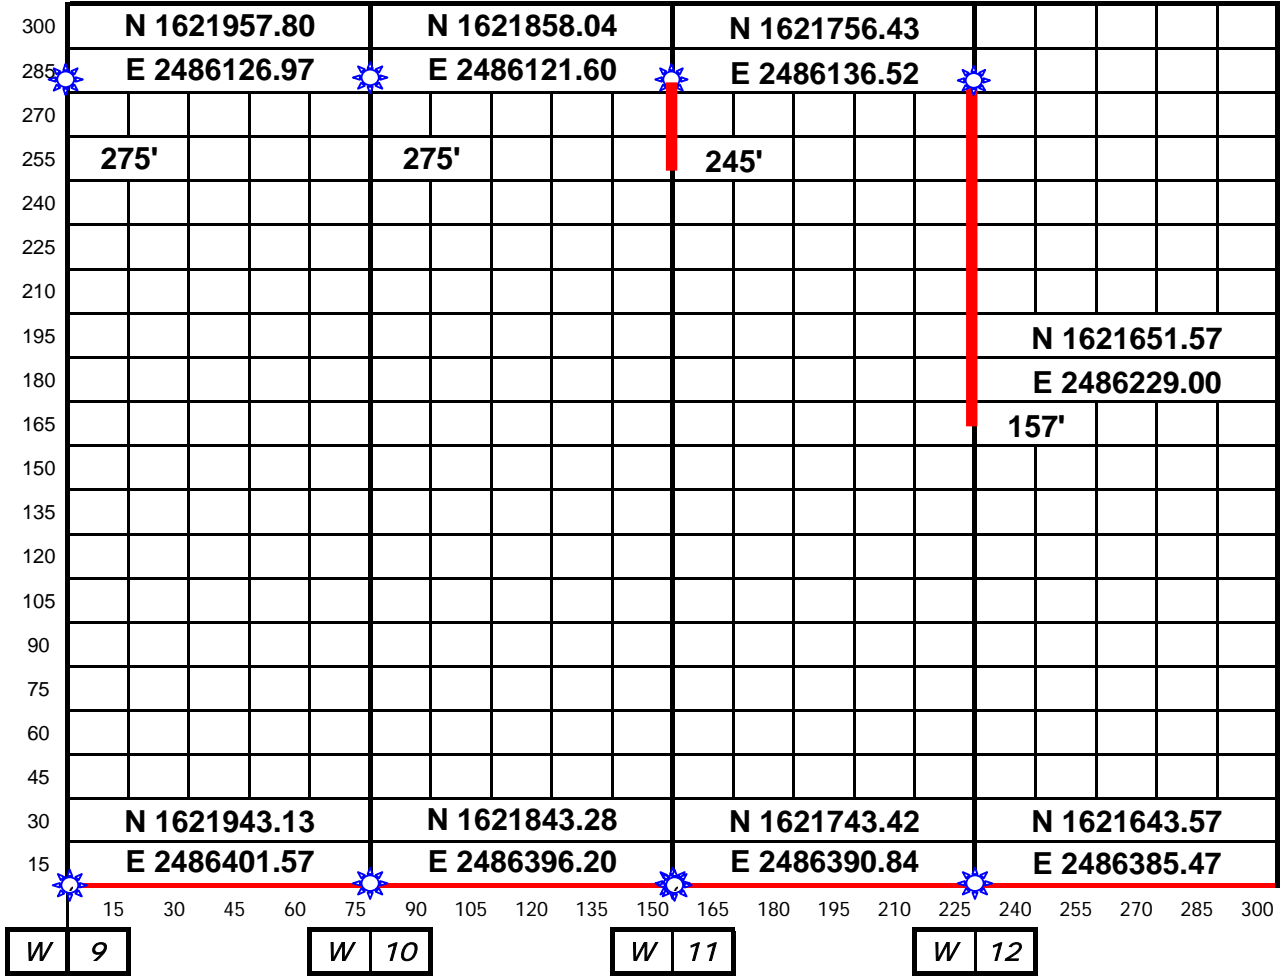

Start 4/6	Start 4/6	Start 4/6	Start 4/6
Finish 4/6	Finish 4/6	Finish 4/6	Finish 4/6
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	


Comments:

W11 No Access/Safety after 245 feet

W12 No Access/Safety after 157 feet

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/7/2009	Completion Date:	4/7/2009
QC Date:		QA Date	

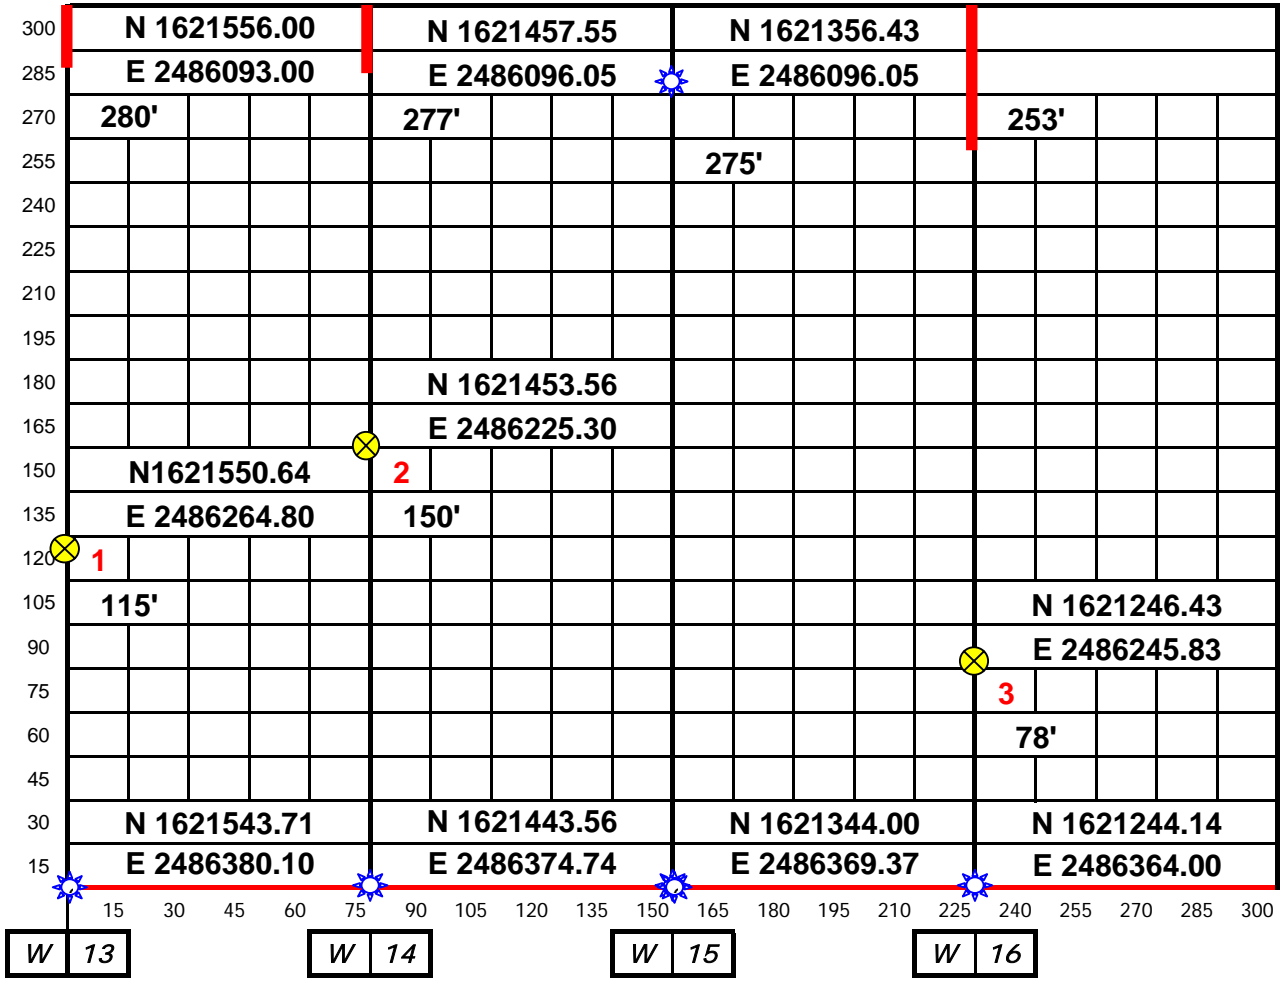

Start 4/7	Start 4/7	Start 4/7	Start 4/7
Finish 4/7	Finish 4/7	Finish 4/7	Finish 4/7
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

W13 No Access/Safety after 280 feet


W14 No Access/Safety after 277 feet

W16 No Access/Safety after 253 feet (Unable to get Lat/Long, no satellite connection)

1,2,3 Fragmentation

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/7/2009	Completion Date:	4/8/2009
QC Date:		QA Date	

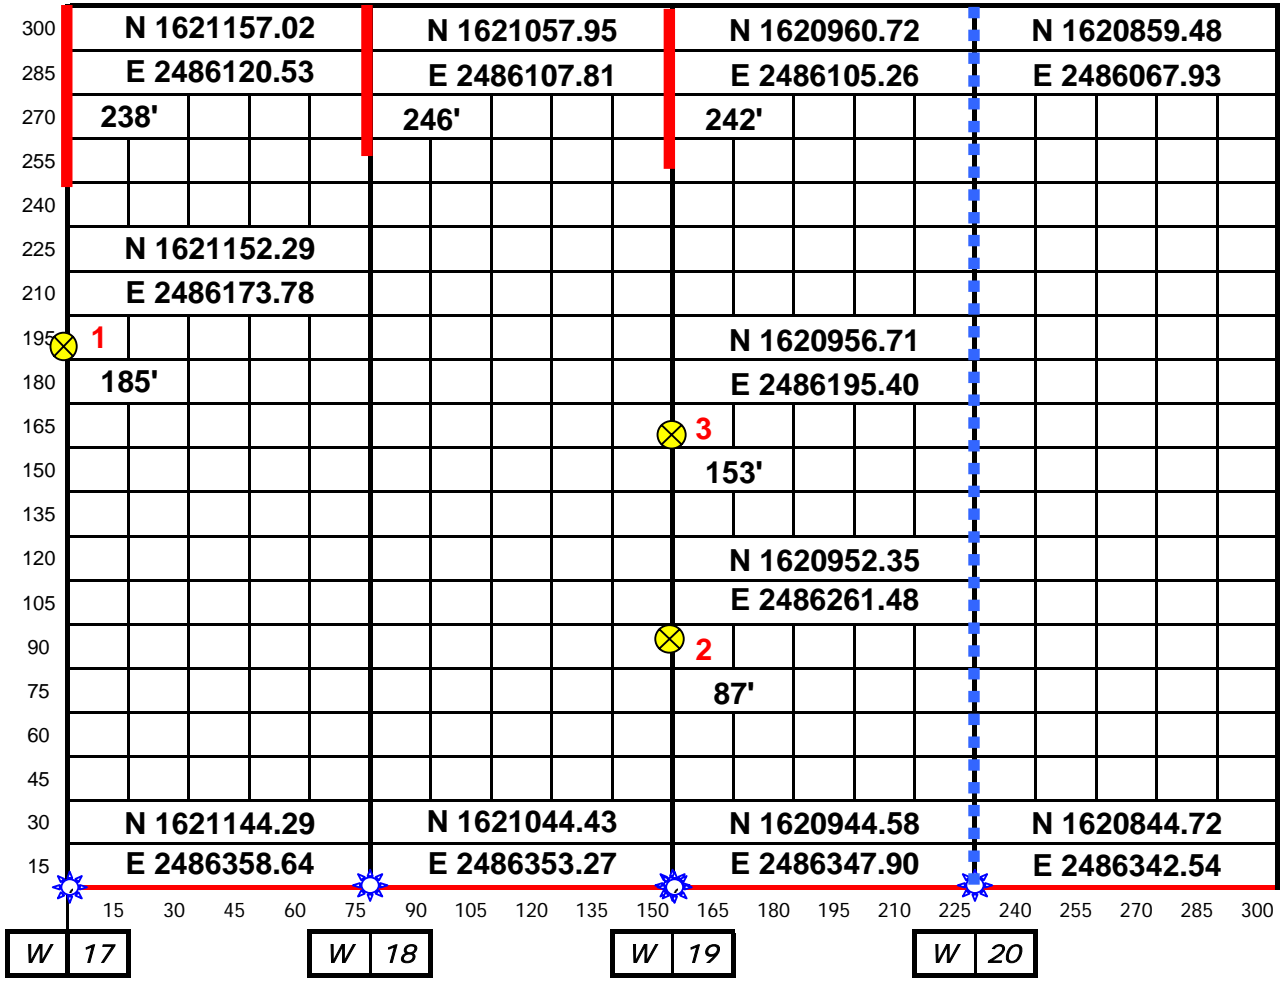


Start 4/7	Start 4/7	Start 4/7	Start 4/8
Finish 4/7	Finish 4/7	Finish 4/7	Finish 4/8
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

- W17 No Access/Safety after 238 feet 1,2,3 Fragmentation
- W18 No Access/Safety after 246 feet
- W19 No Access/Safety after 242 feet
- W20 No Access/Cultural (ARC Site)

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/8/2009	Completion Date:	4/8/2009
QC Date:		QA Date	

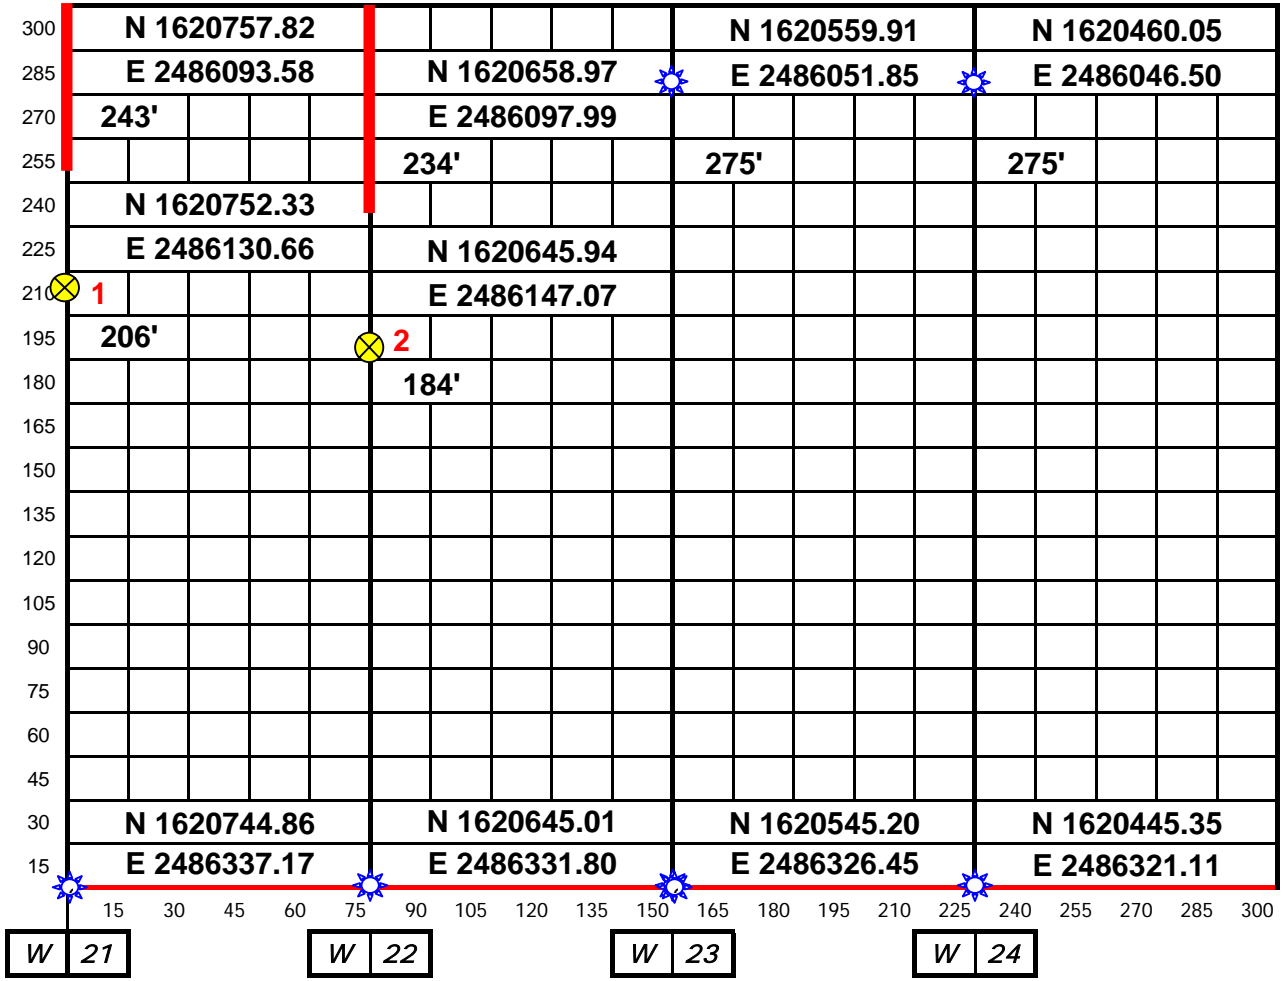

Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/8</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/8</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/8</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/8</div>
Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/8</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/8</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/8</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/8</div>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

W21 No Access/Safety after 243 feet


W22 No Access/Safety after 234 feet

1 Fragmentation

2 Fragmentation

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/8/2009	Completion Date:	4/8/2009
QC Date:		QA Date	

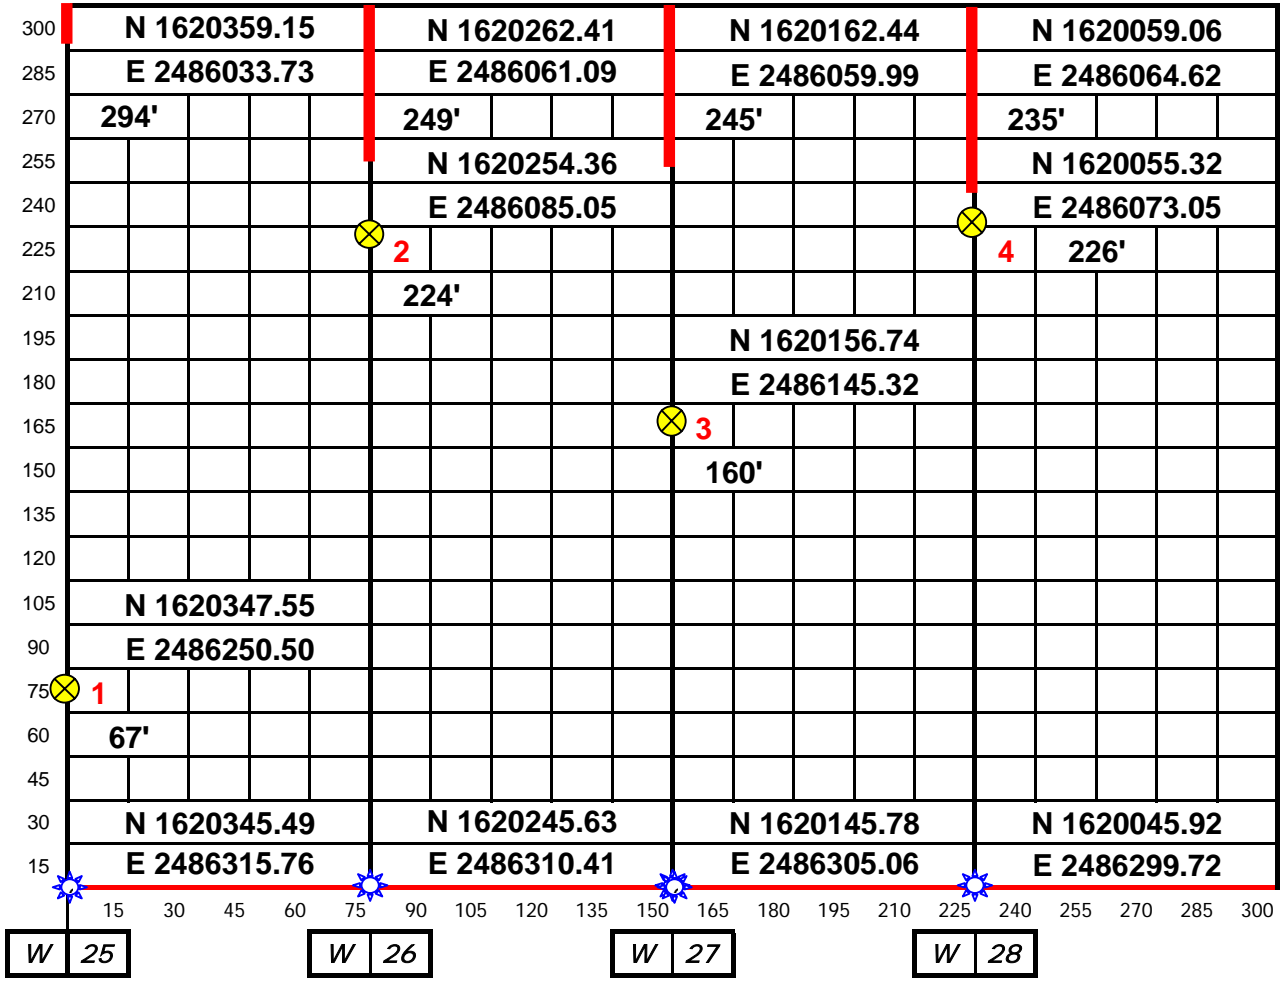


Start 4/8	Start 4/8	Start 4/8	Start 4/8
Finish 4/8	Finish 4/8	Finish 4/8	Finish 4/8
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

- Comments:**
- W25 No Access/Safety after 294 feet 1,2,3,4 Fragmentation
 - W26 No Access/Safety after 249 feet
 - W27 No Access/Safety after 245 feet
 - W28 No Access/Safety after 235 feet

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/8/2009	Completion Date:	4/8/2009
QC Date:		QA Date	

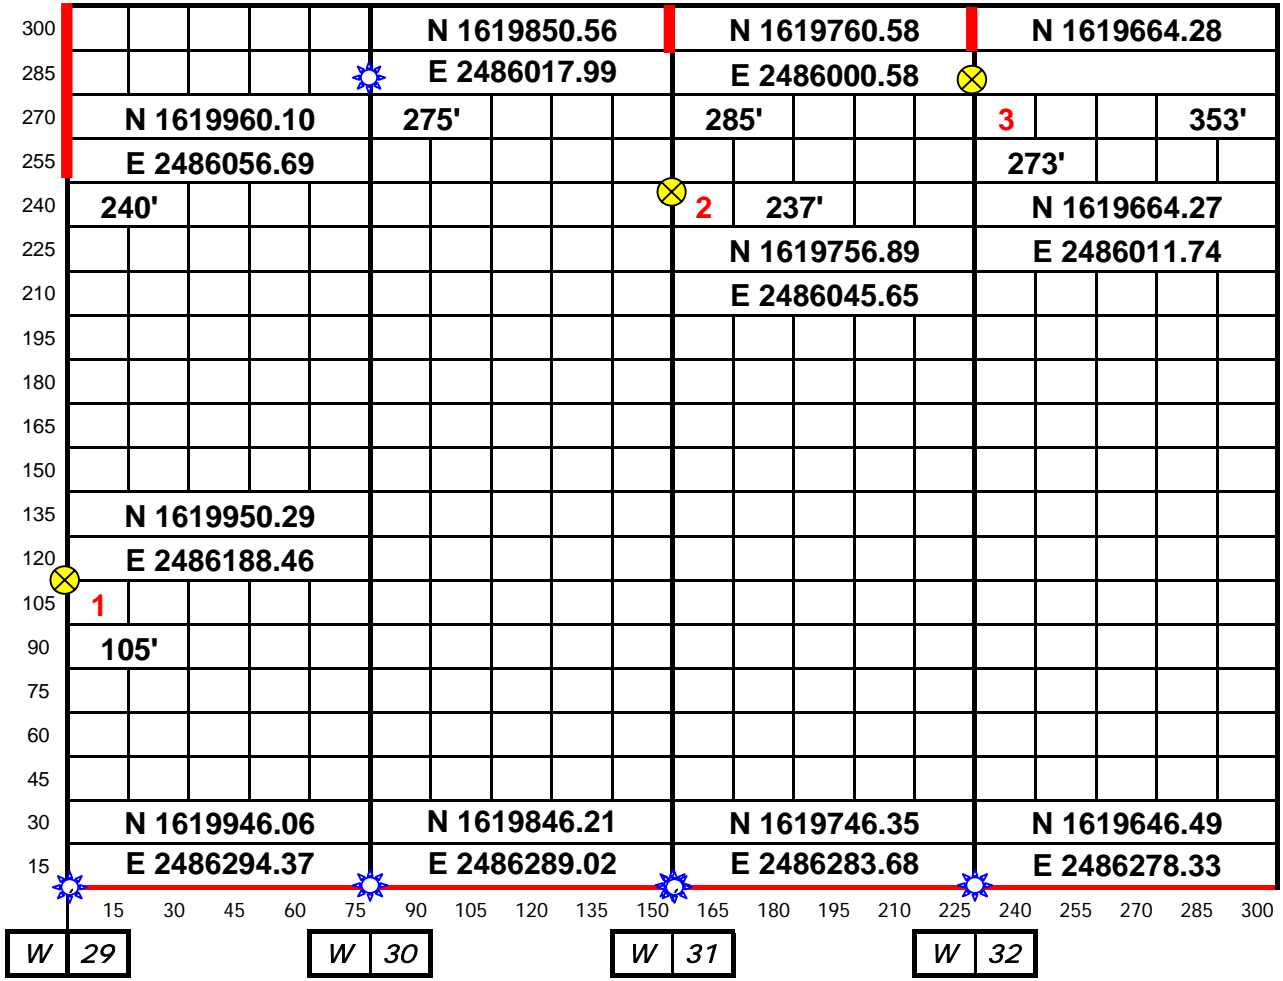

Start <input type="text" value="4/8"/>	Start <input type="text" value="4/8"/>	Start <input type="text" value="4/8"/>	Start <input type="text" value="4/8"/>
Finish <input type="text" value="4/8"/>	Finish <input type="text" value="4/8"/>	Finish <input type="text" value="4/8"/>	Finish <input type="text" value="4/8"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

- Comments:**
- W29** No Access/Safety after 240 feet


 - W31** No Access/Safety after 285 feet

 - W32** No Access/Safety after 353 feet

 - 1,2,3** Fragmentation

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/9/2009	Completion Date:	4/9/2009
QC Date:		QA Date	

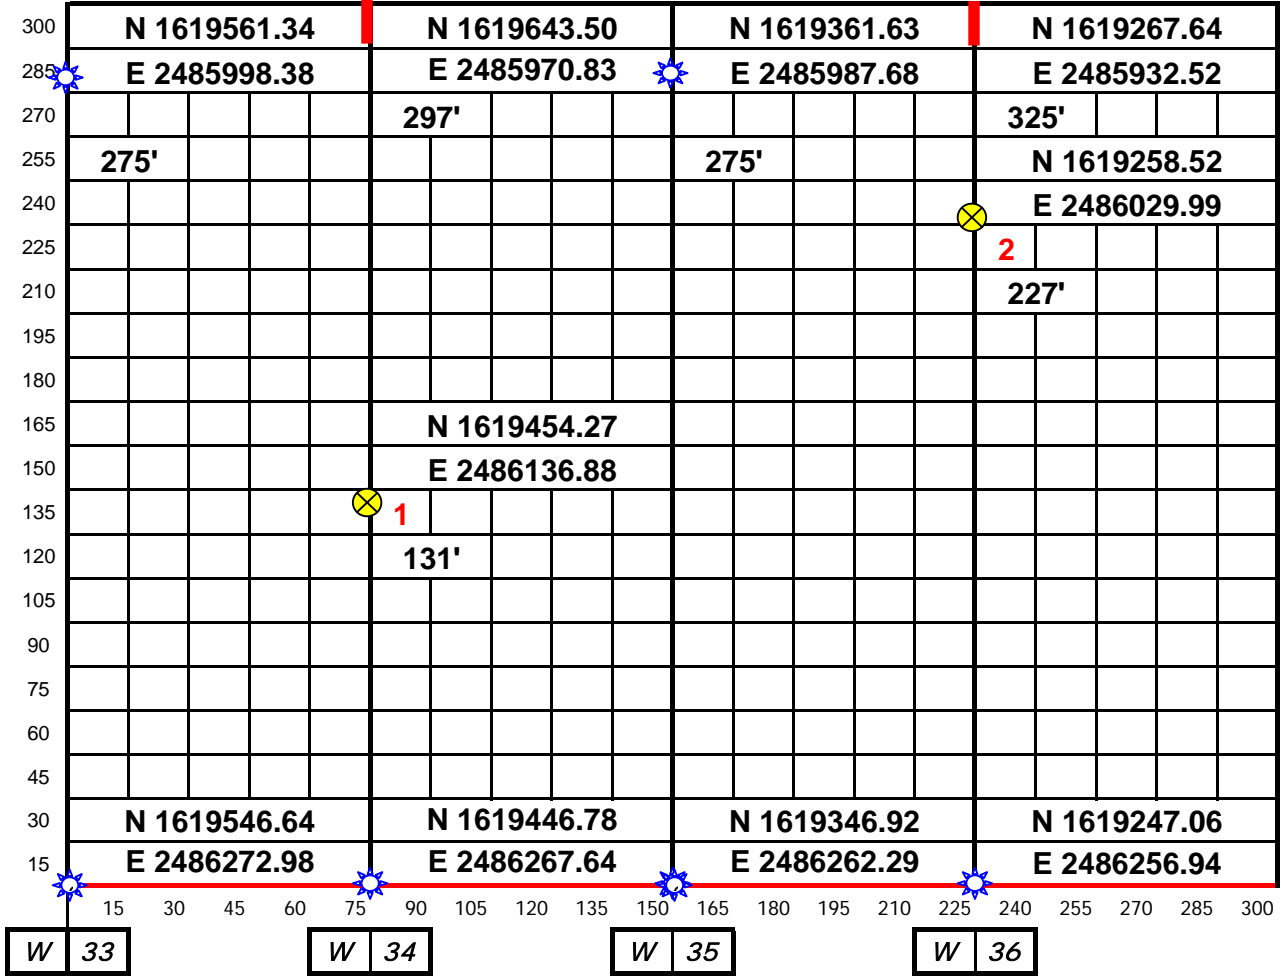

Start <input type="text" value="4/9"/>	Start <input type="text" value="4/9"/>	Start <input type="text" value="4/9"/>	Start <input type="text" value="4/9"/>
Finish <input type="text" value="4/9"/>	Finish <input type="text" value="4/9"/>	Finish <input type="text" value="4/9"/>	Finish <input type="text" value="4/9"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:


W34 No Access/Safety beyond 297 feet

W36 No Access/Safety beyond 325 feet

1,2 Fragmentation

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/9/2009	Completion Date:	4/9/2009
QC Date:		QA Date	

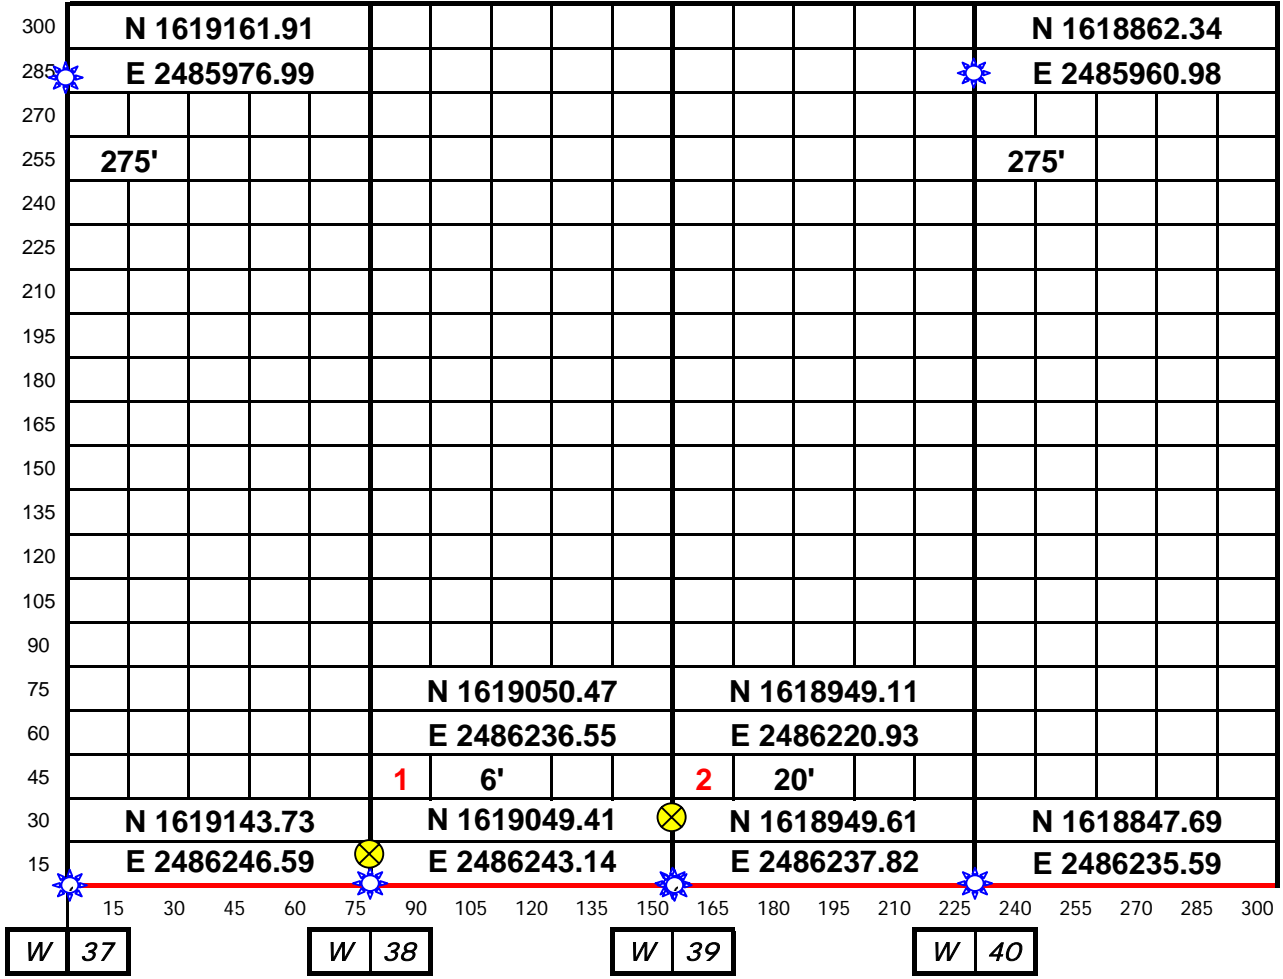


Start <input type="text" value="4/9"/>	Start <input type="text" value="4/9"/>	Start <input type="text" value="4/9"/>	Start <input type="text" value="4/9"/>
Finish <input type="text" value="4/9"/>	Finish <input type="text" value="4/9"/>	Finish <input type="text" value="4/9"/>	Finish <input type="text" value="4/9"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:
1,2 Fragmentation

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/9/2009	Completion Date:	
QC Date:		QA Date	

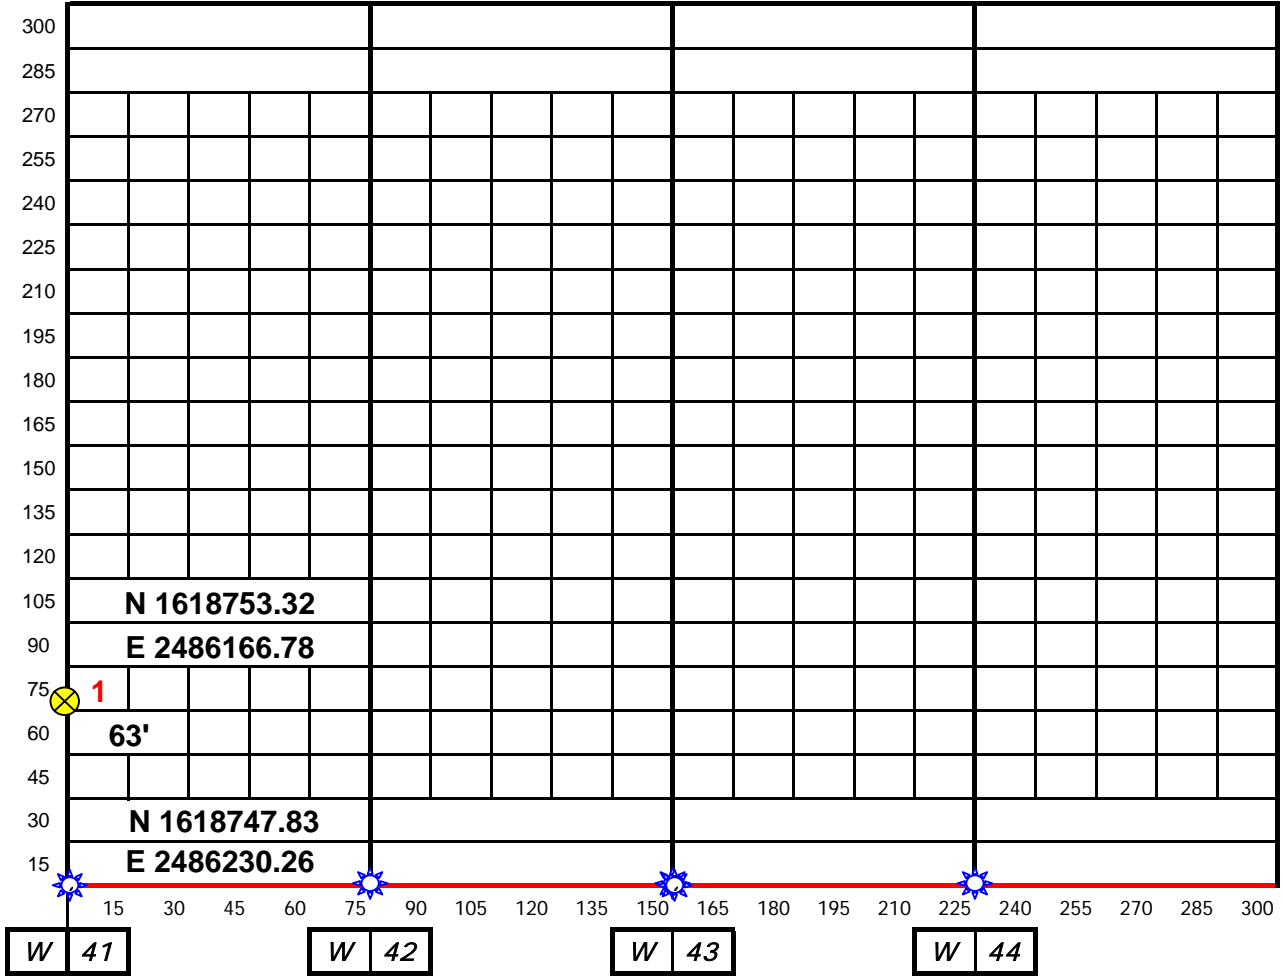


Start <input type="text" value="4/9"/>	Start <input type="text"/>	Start <input type="text"/>	Start <input type="text"/>
Finish <input type="text" value="4/9"/>	Finish <input type="text"/>	Finish <input type="text"/>	Finish <input type="text"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

1 Fragmentation

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/9/2009	Completion Date:	4/9/2009
QC Date:		QA Date	

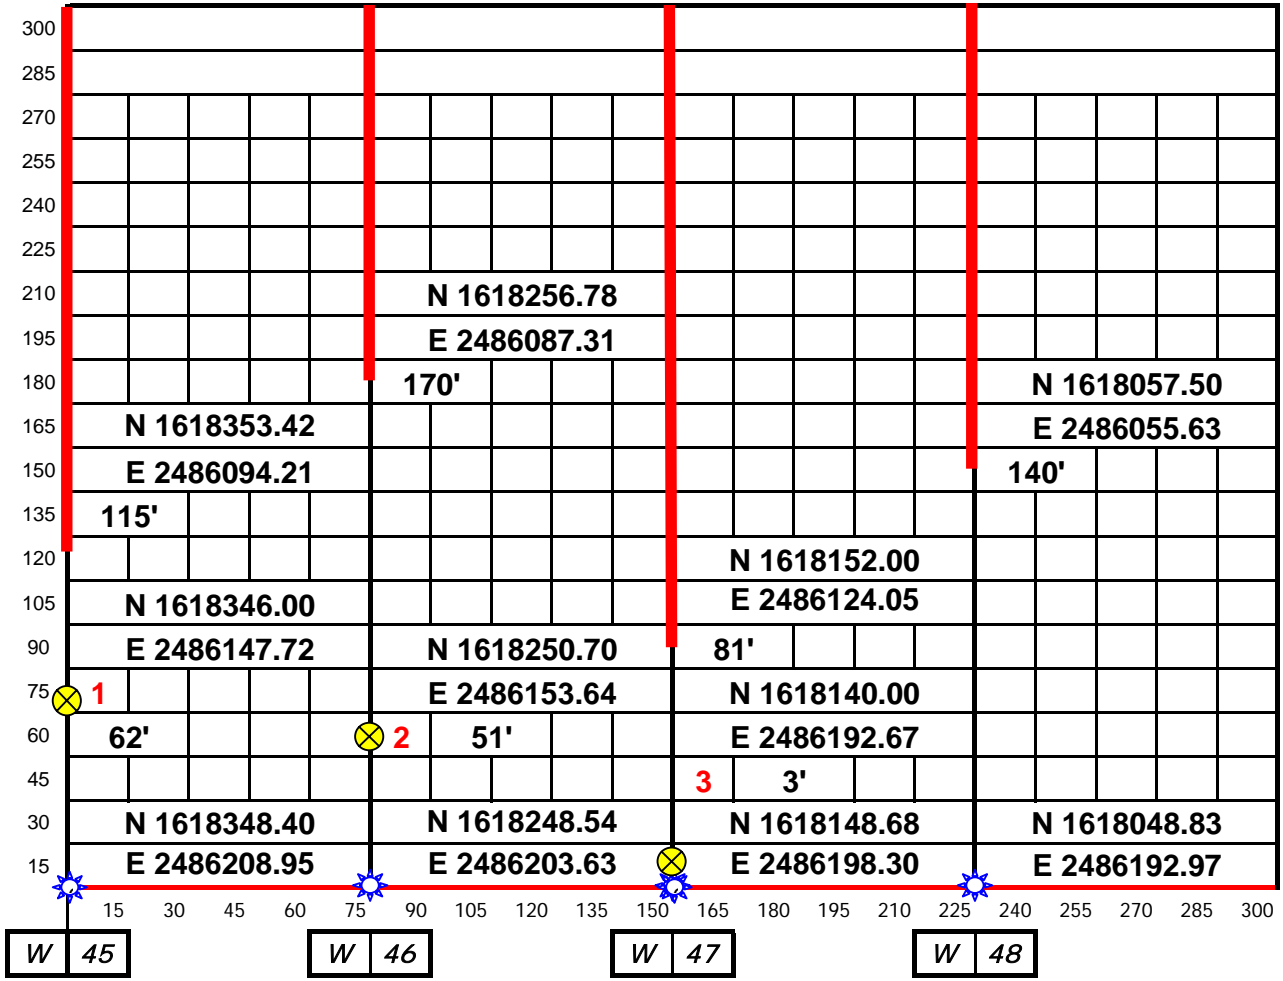

Comments:

- W45** No Access/Safety beyond 115 feet **1,2,3** Fragmentation


- W46** No Access/Safety beyond 170 feet

- W47** No Access/Safety beyond 81 feet

- W48** No Access/Safety beyond 140 feet

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/9/2009	Completion Date:	4/20/2009
QC Date:		QA Date	

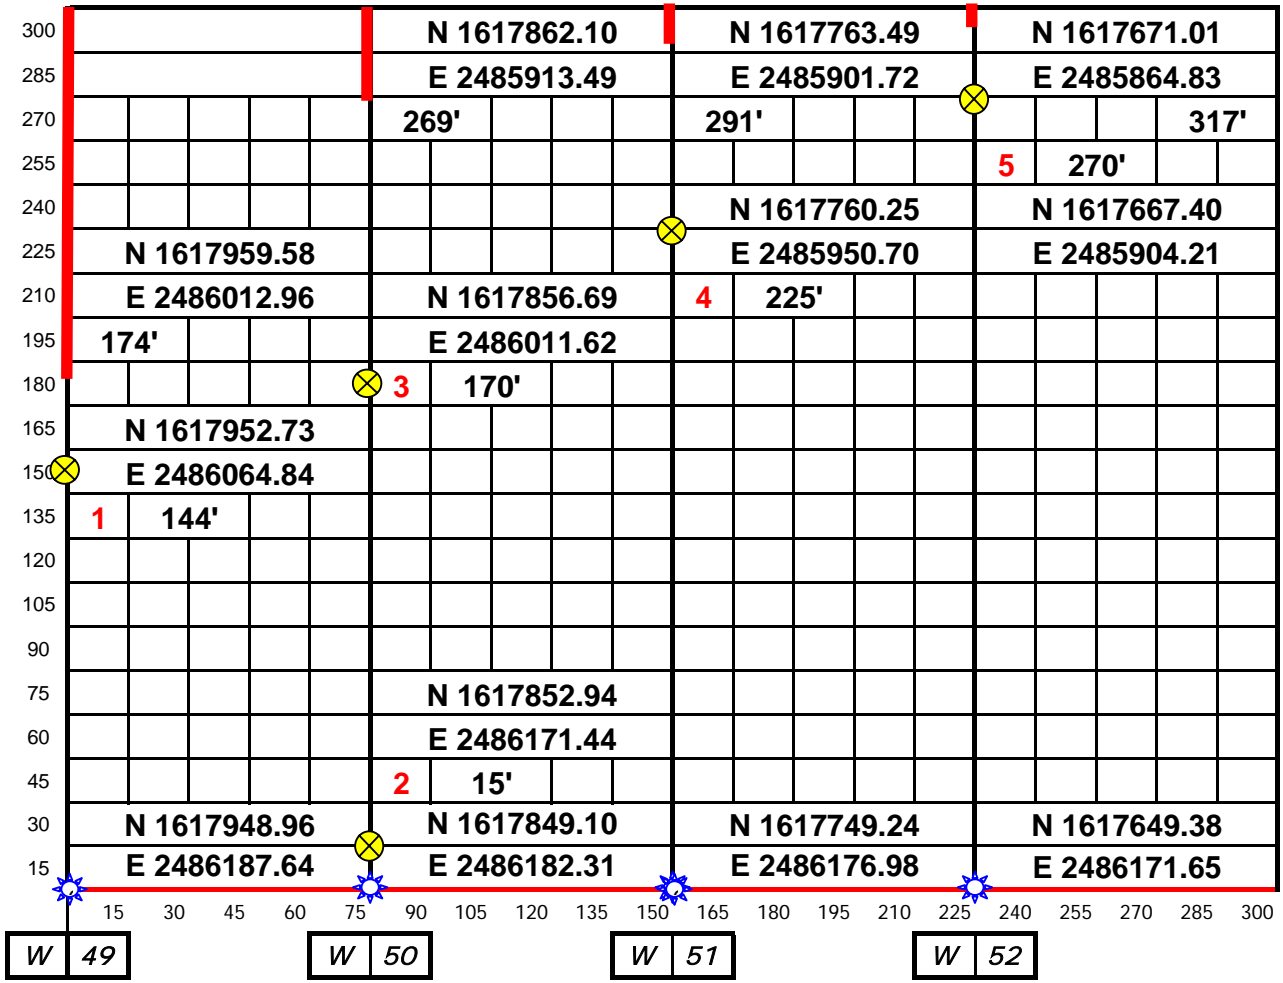

Start <input type="text" value="4/9"/>	Start <input type="text" value="4/20"/>	Start <input type="text" value="4/20"/>	Start <input type="text" value="4/20"/>
Finish <input type="text" value="4/9"/>	Finish <input type="text" value="4/20"/>	Finish <input type="text" value="4/20"/>	Finish <input type="text" value="4/20"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

W49 No Access/Safety beyond 174 feet **1,2,3,4,5** Fragmentation


W50 No Access/Safety beyond 269 feet

W51 No Access/Safety beyond 291 feet

W52 No Access/Safety beyond 317 feet

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/20/2009	Completion Date:	4/21/2009
QC Date:		QA Date	

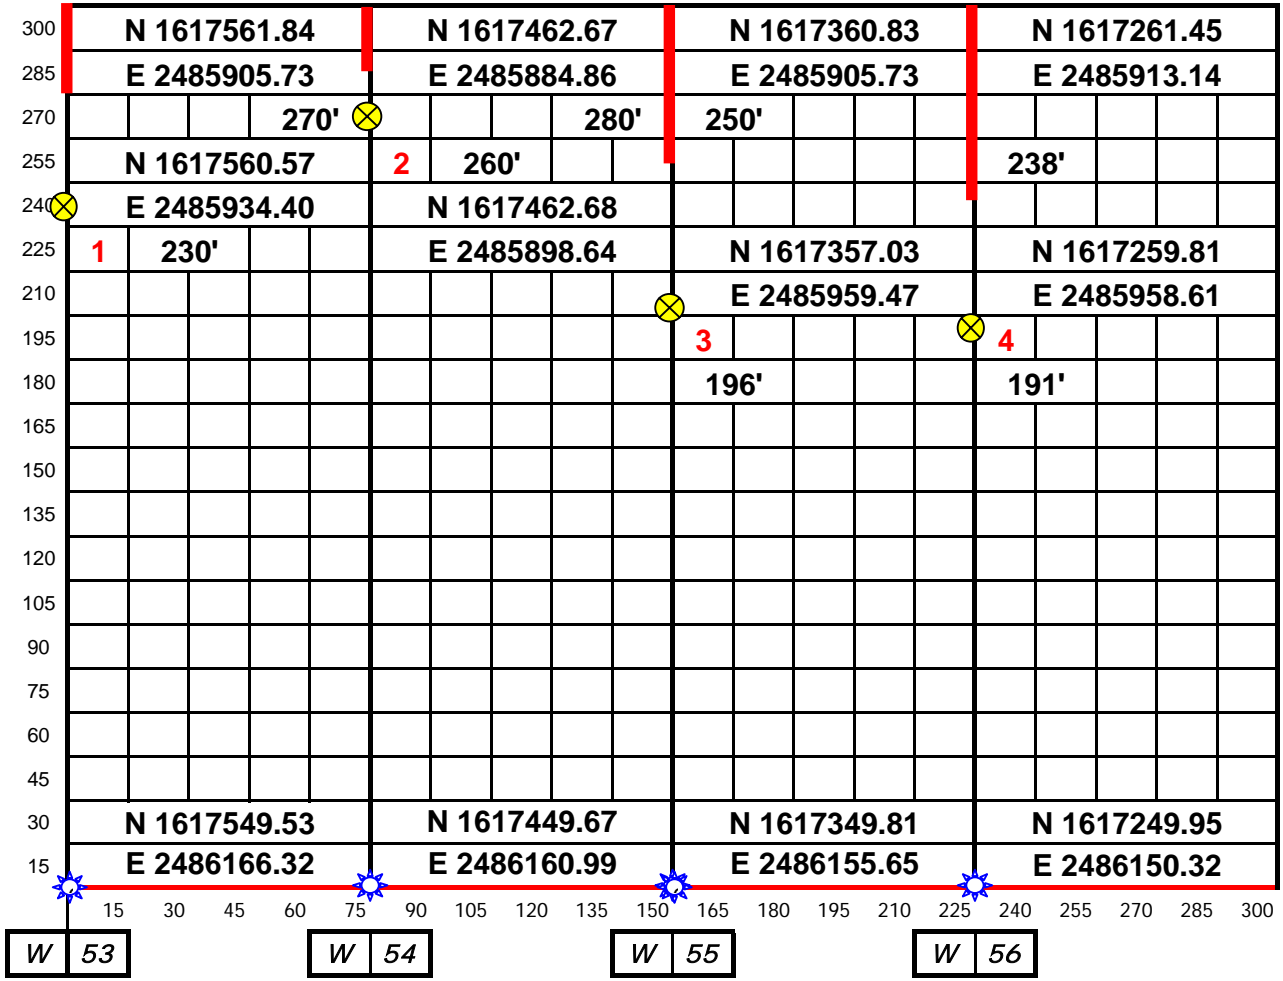


Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/20</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/21</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/21</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/21</div>
Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/20</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/21</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/21</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/21</div>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

- W53** No Access/Safety beyond 270 feet **1,2,3,4** Fragmentation
- W54** No Access/Safety beyond 280 feet
- W55** No Access/Safety beyond 250 feet
- W56** No Access/Safety beyond 238 feet

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/21/2009	Completion Date:	4/21/2009
QC Date:		QA Date	

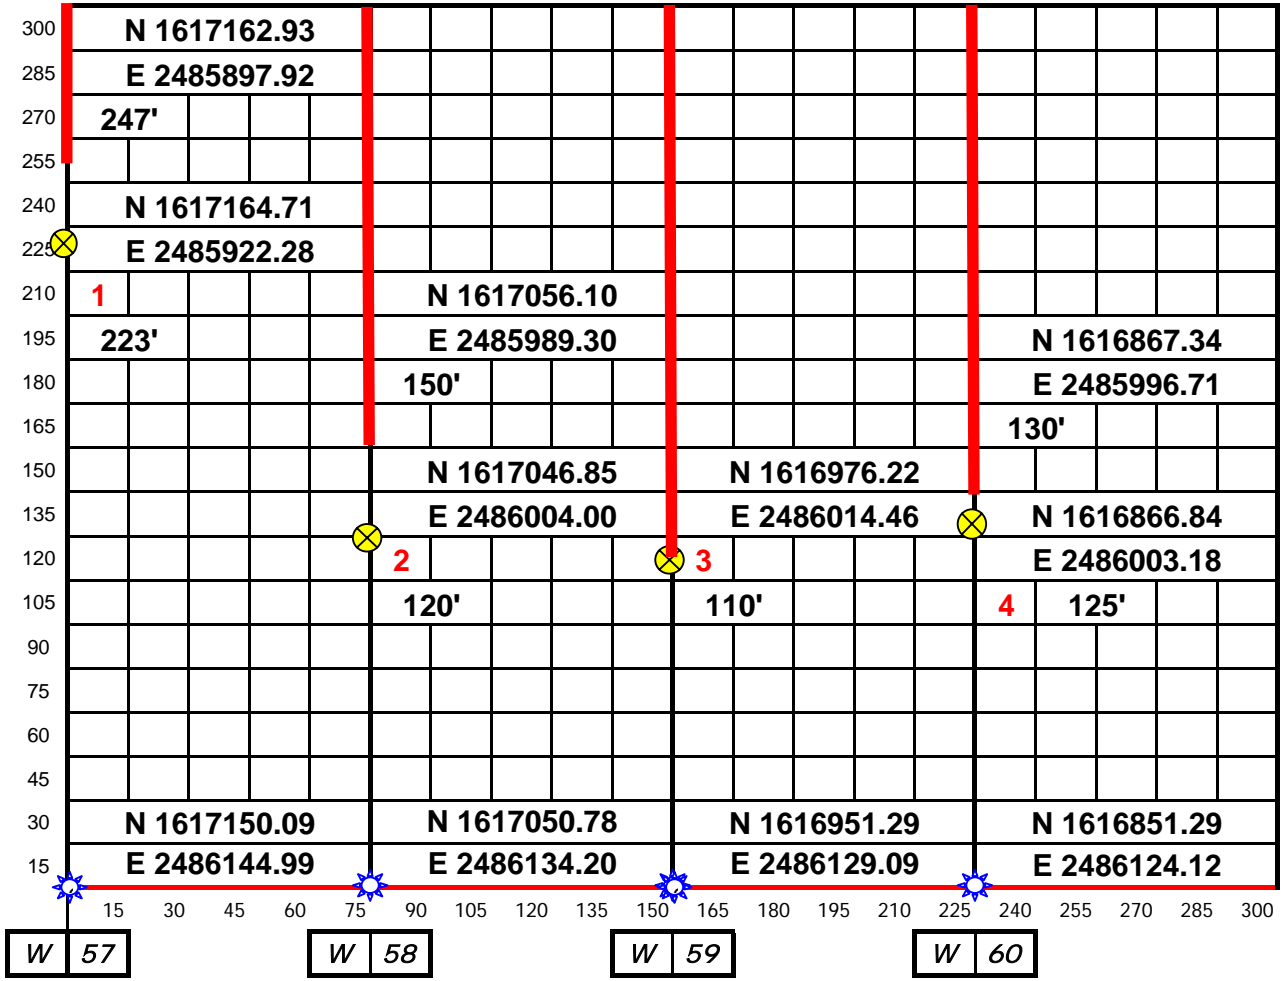

Start 4/21	Start 4/21	Start 4/21	Start 4/21
Finish 4/21	Finish 4/21	Finish 4/21	Finish 4/21
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

- Comments:**
- W57** No Access/Safety beyond 247 feet **1,2,3,4** Fragmentation


 - W58** No Access/Safety beyond 150 feet

 - W59** No Access/Safety beyond 110 feet

 - W60** No Access/Safety beyond 130 feet

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/20/2009	Completion Date:	4/20/2009
QC Date:		QA Date	

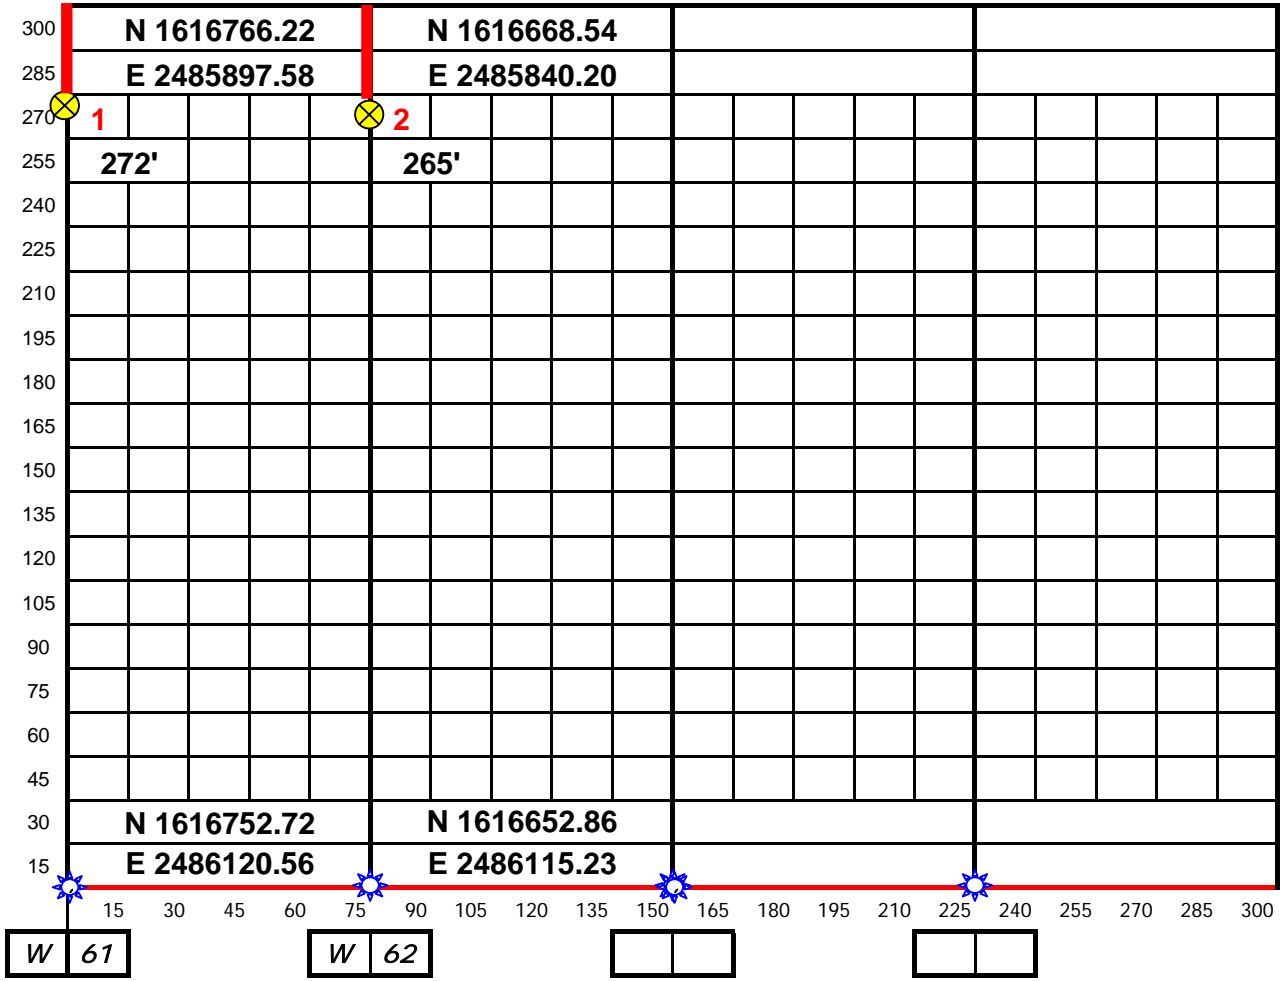

Start <input type="text" value="4/20"/>	Start <input type="text" value="4/20"/>	Start <input type="text"/>	Start <input type="text"/>
Finish <input type="text" value="4/20"/>	Finish <input type="text" value="4/20"/>	Finish <input type="text"/>	Finish <input type="text"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:


W61 No Access/Safety beyond 272 feet

W62 No Access/Safety beyond 265 feet

1,2 Fragmentation

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/3/2009	Completion Date:	4/3/2009
QC Date:		QA Date	

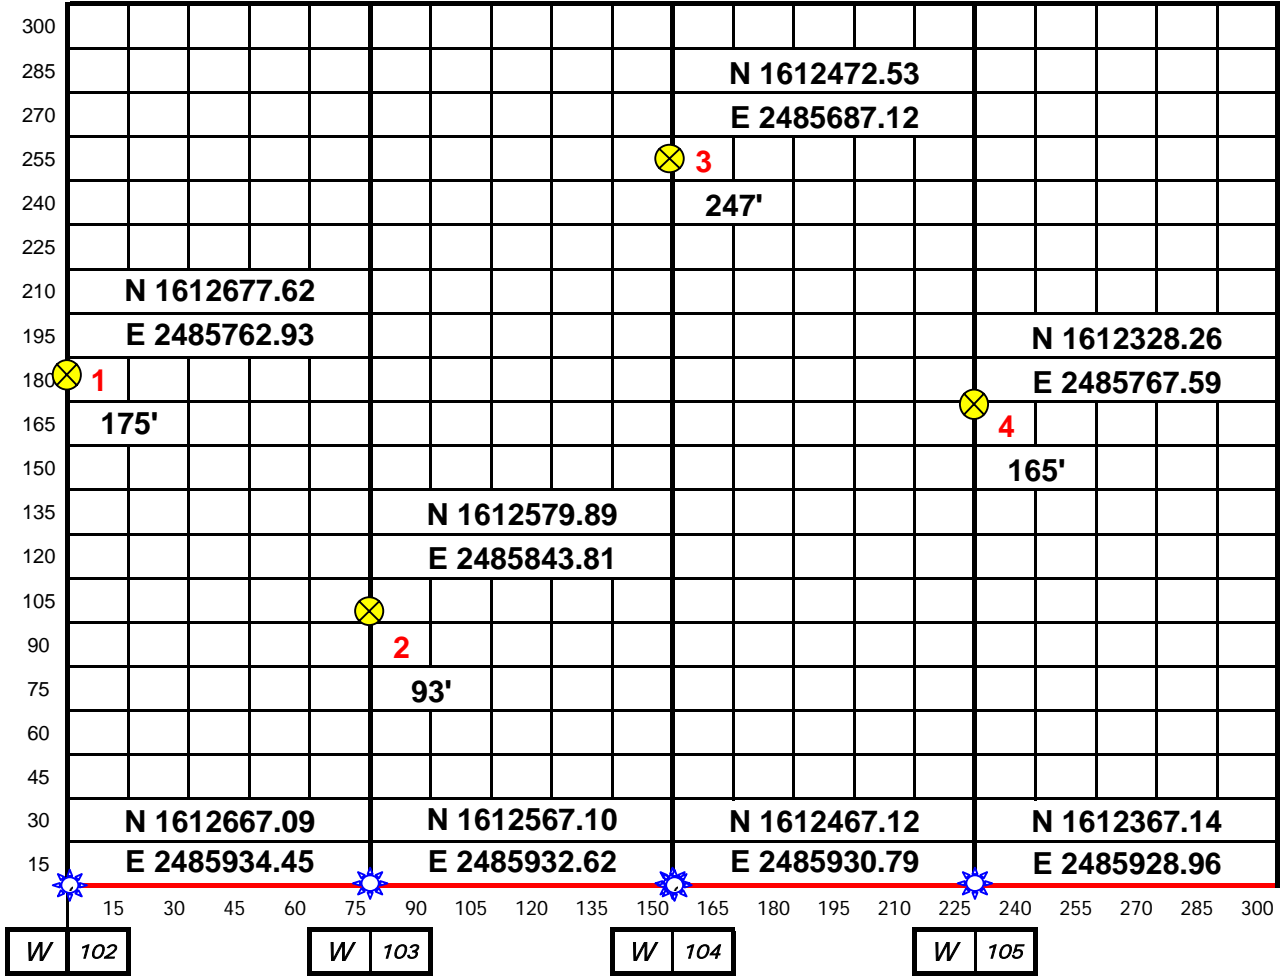

Start 4/3	Start 4/3	Start 4/3	Start 4/3
Finish 4/3	Finish 4/3	Finish 4/3	Finish 4/3
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

- Comments:**
- 1** Fragmentation


 - 2** Fragmentation

 - 3** Fragmentation

 - 4** Fragmentation

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/3/2009	Completion Date:	4/3/2009
QC Date:		QA Date	

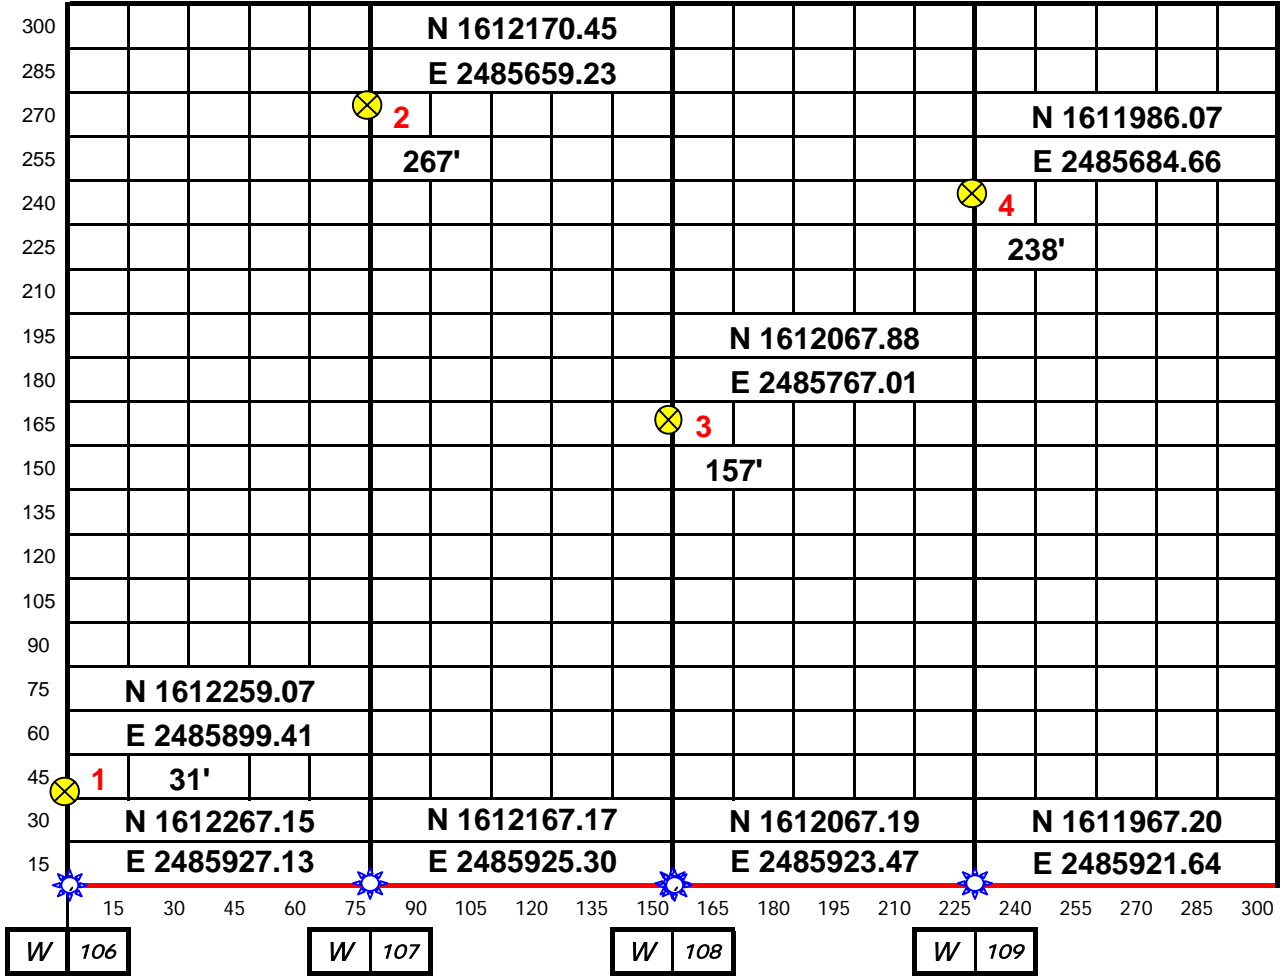


Start 4/3	Start 4/3	Start 4/3	Start 4/3
Finish 4/3	Finish 4/3	Finish 4/3	Finish 4/3
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

- 1 Fragmentation _____
- 2 Fragmentation _____
- 3 Fragmentation _____
- 4 Fragmentation _____

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/3/2009	Completion Date:	4/3/2009
QC Date:		QA Date	

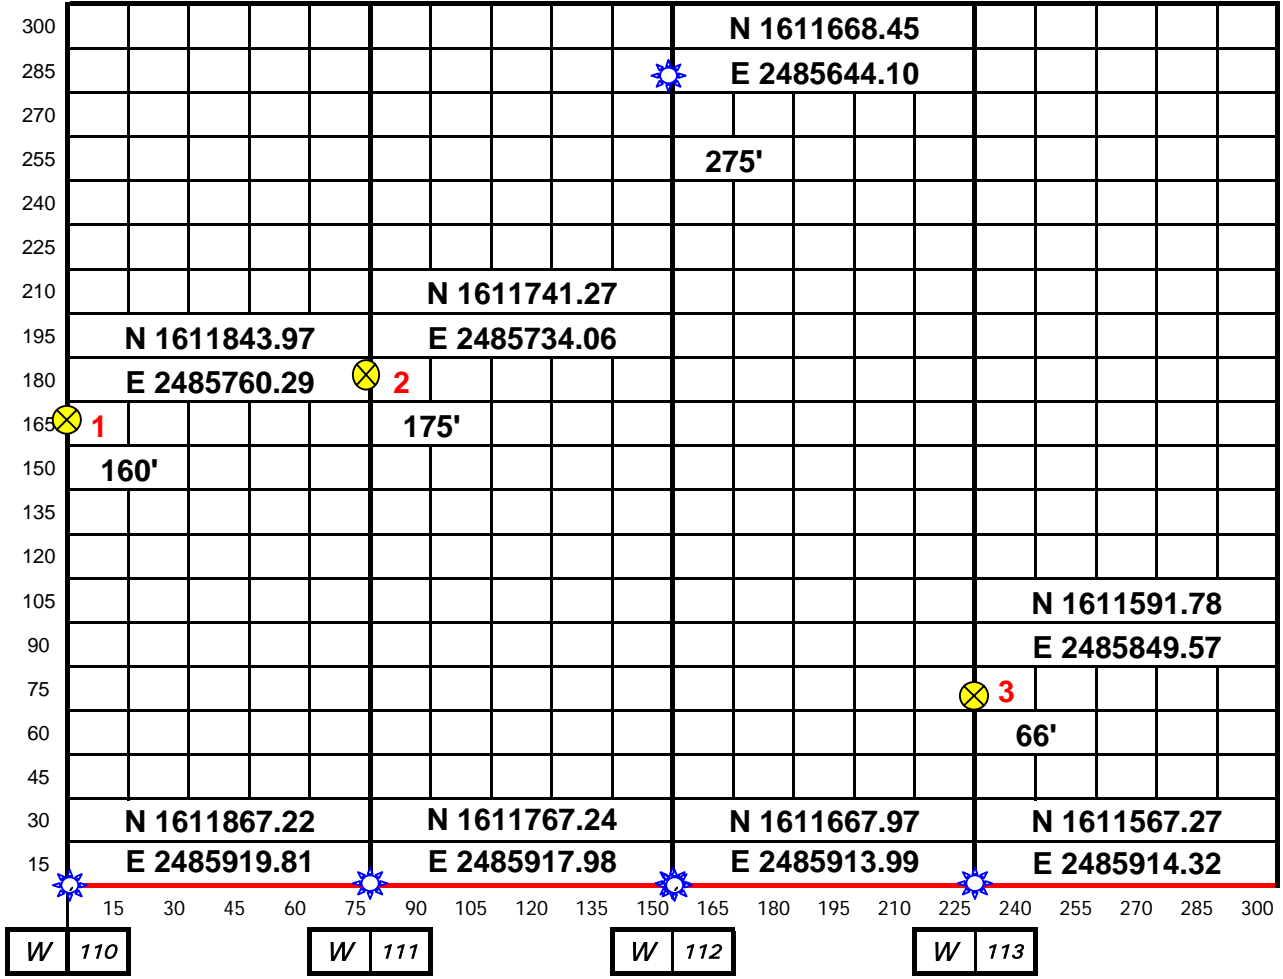

Start 4/3	Start 4/3	Start 4/3	Start 4/3
Finish 4/3	Finish 4/3	Finish 4/3	Finish 4/3
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:


1 Fragmentation _____

2 Fragmentation _____

3 Fragmentation _____

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/6/2009	Completion Date:	4/6/2009
QC Date:		QA Date	

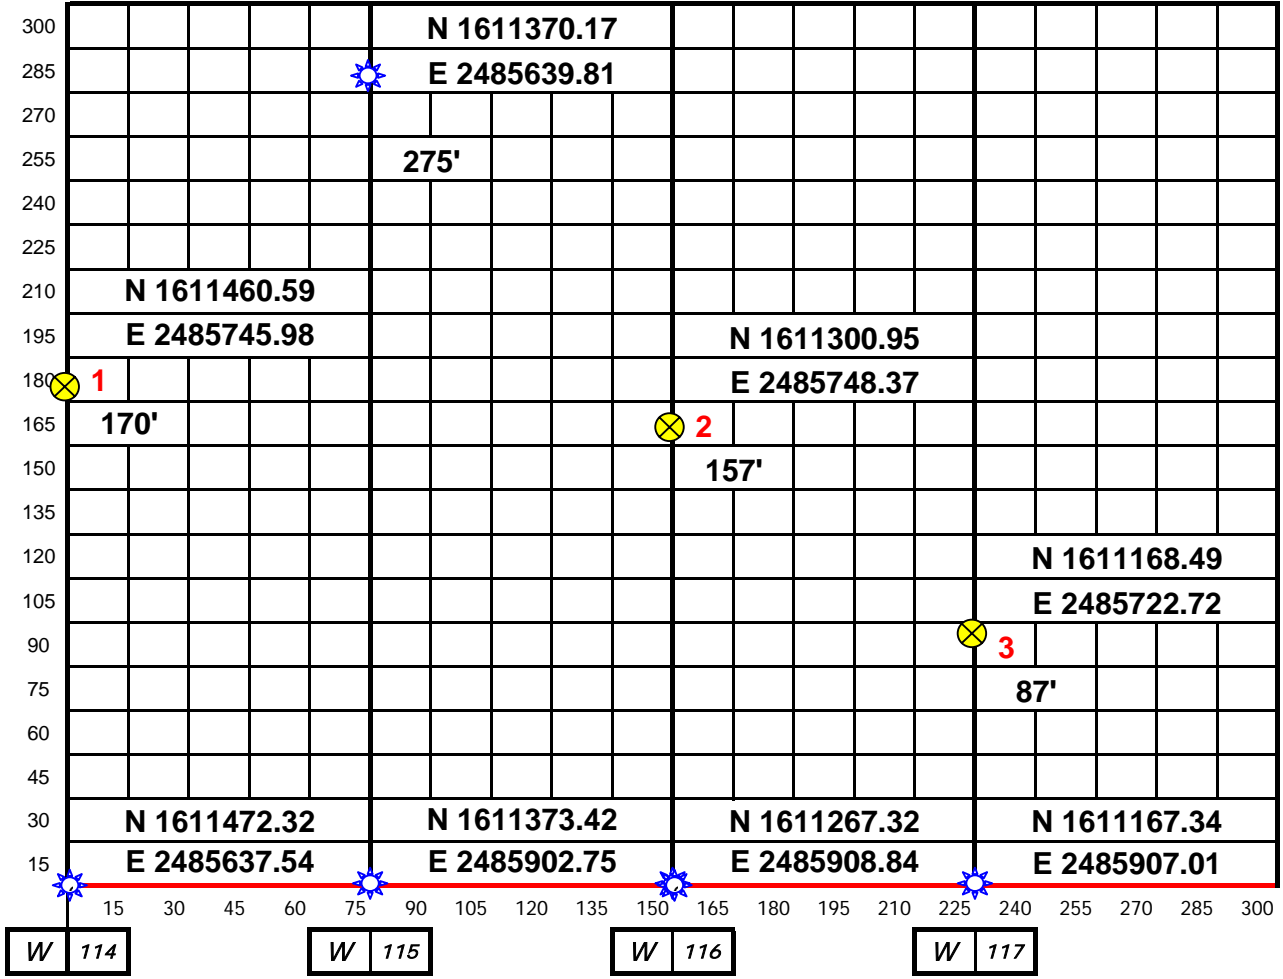

Start 4/6	Start 4/6	Start 4/6	Start 4/6
Finish 4/6	Finish 4/6	Finish 4/6	Finish 4/6
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:


1 Fragmentation

2 Fragmentation

3 Fragmentation

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/6/2009	Completion Date:	4/6/2009
QC Date:		QA Date	

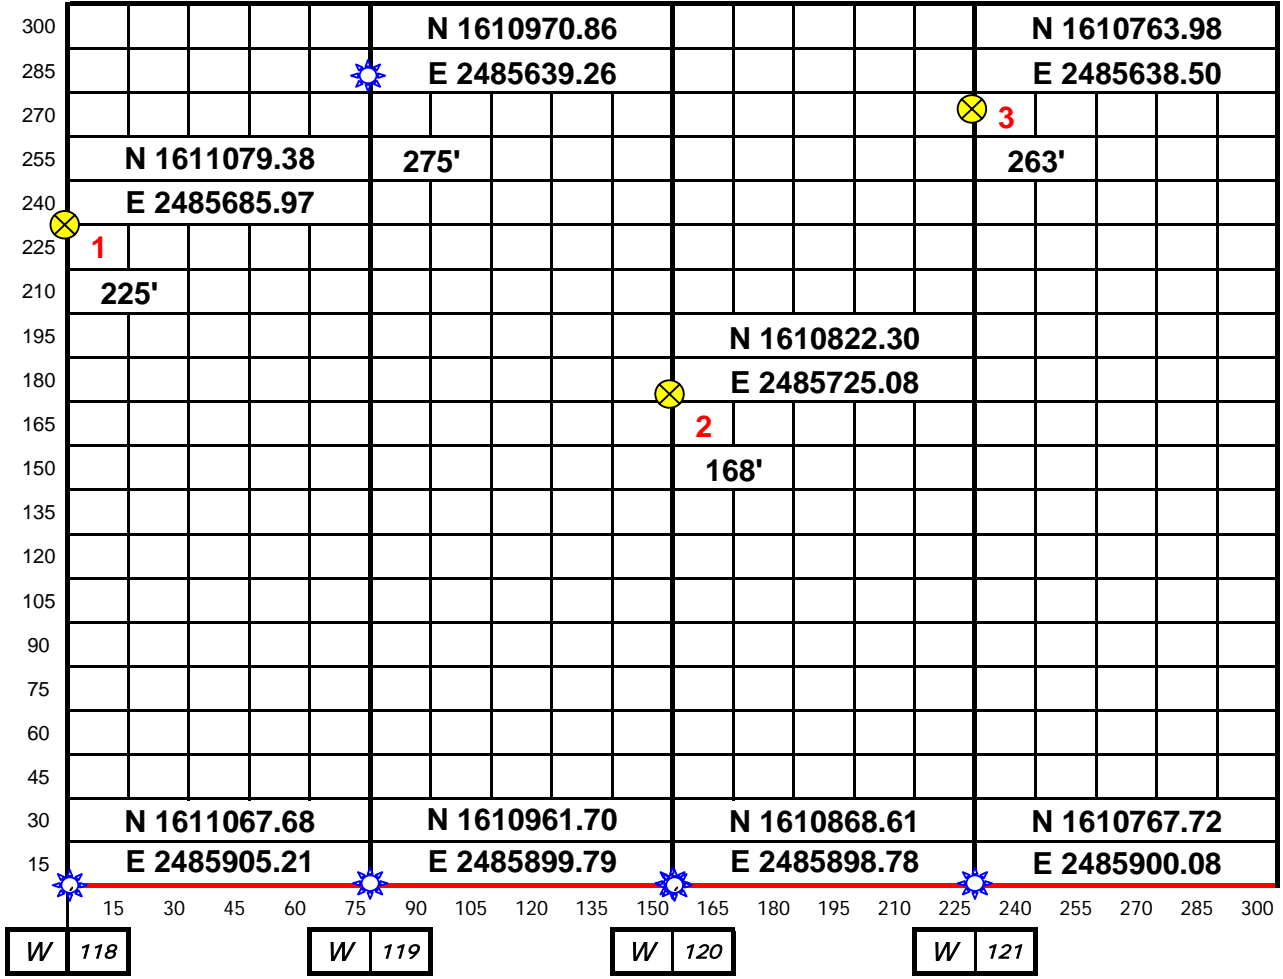

Start <input type="text" value="4/6"/>	Start <input type="text" value="4/6"/>	Start <input type="text" value="4/6"/>	Start <input type="text" value="4/6"/>
Finish <input type="text" value="4/6"/>	Finish <input type="text" value="4/6"/>	Finish <input type="text" value="4/6"/>	Finish <input type="text" value="4/6"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:


1 Fragmentation _____

2 Fragmentation _____

3 Fragmentation _____

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/6/2009	Completion Date:	4/7/2009
QC Date:		QA Date	

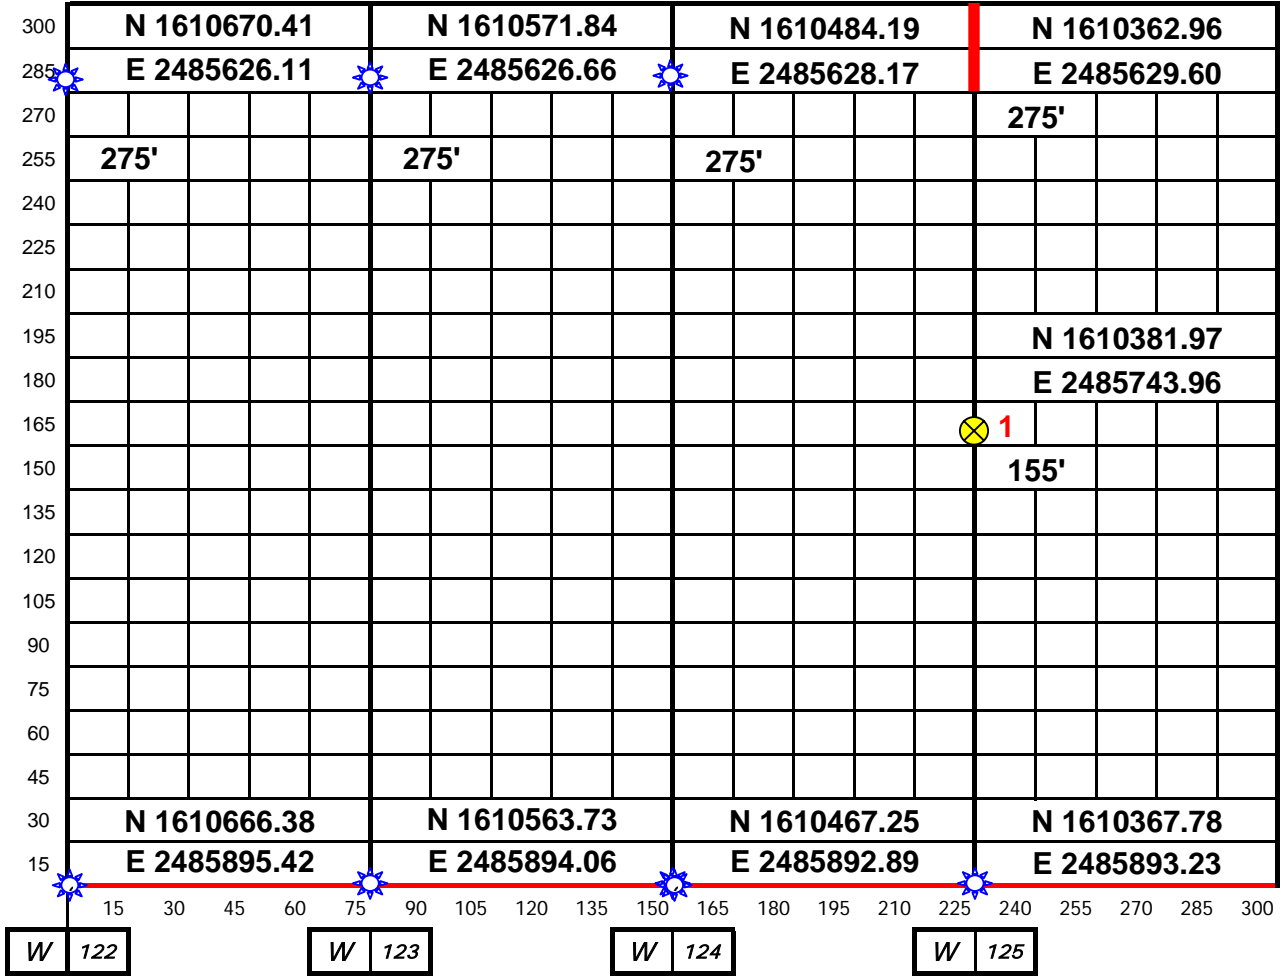

Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/6</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/6</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/6</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/7</div>
Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/6</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/6</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/6</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/7</div>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	


Comments:

1 Fragmentation

W125 No Access/Safety after 275 feet

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/7/2009	Completion Date:	4/7/2009
QC Date:		QA Date	

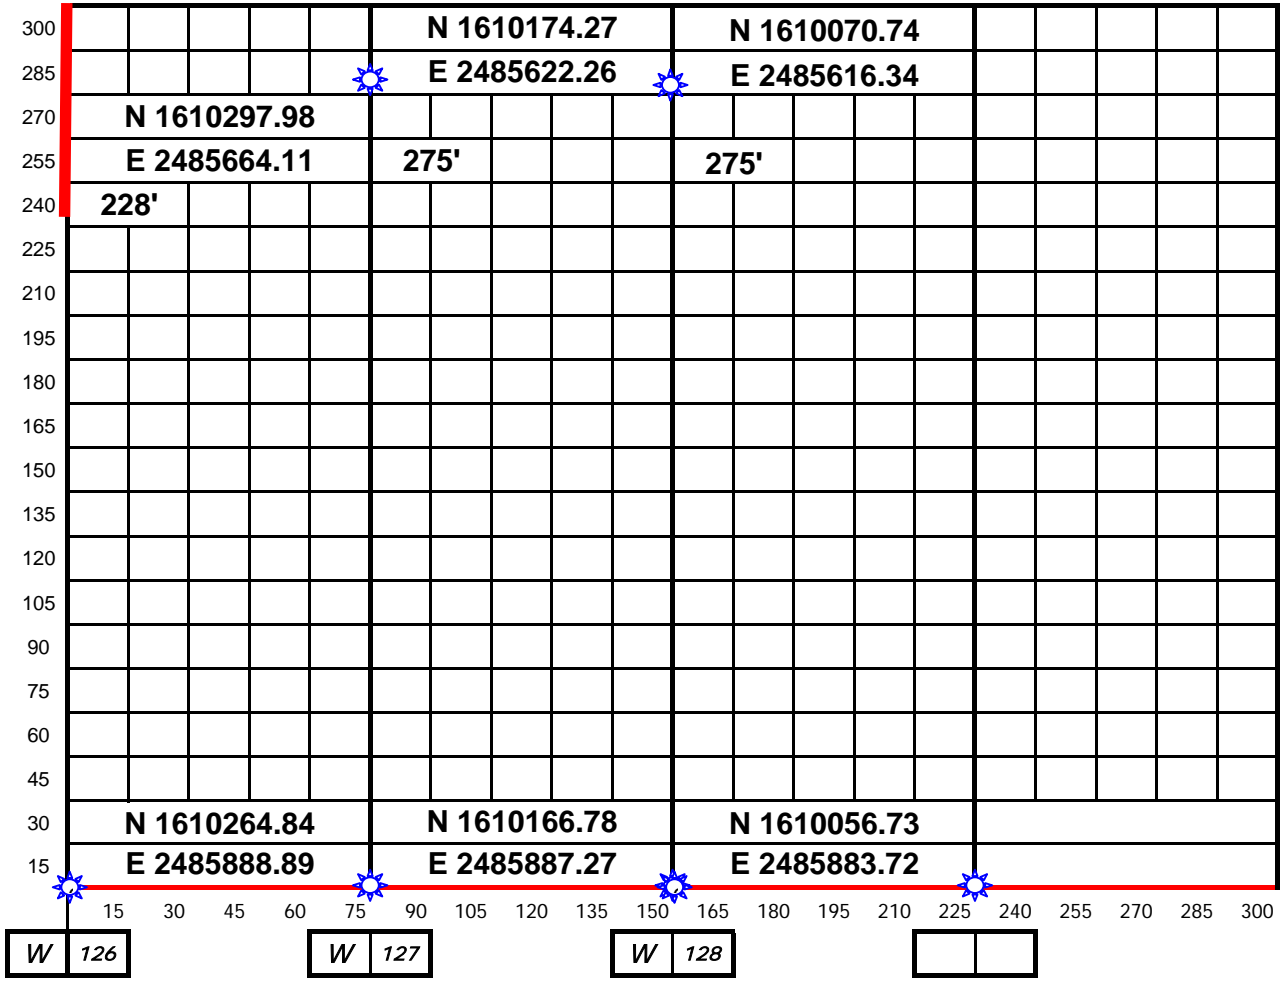


Start <input type="text" value="4/7"/>	Start <input type="text" value="4/7"/>	Start <input type="text" value="4/7"/>	Start <input type="text"/>
Finish <input type="text" value="4/7"/>	Finish <input type="text" value="4/7"/>	Finish <input type="text" value="4/7"/>	Finish <input type="text"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

W126 No Access/Safety after 228 feet

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	9/18/2008	Completion Date:	9/18/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

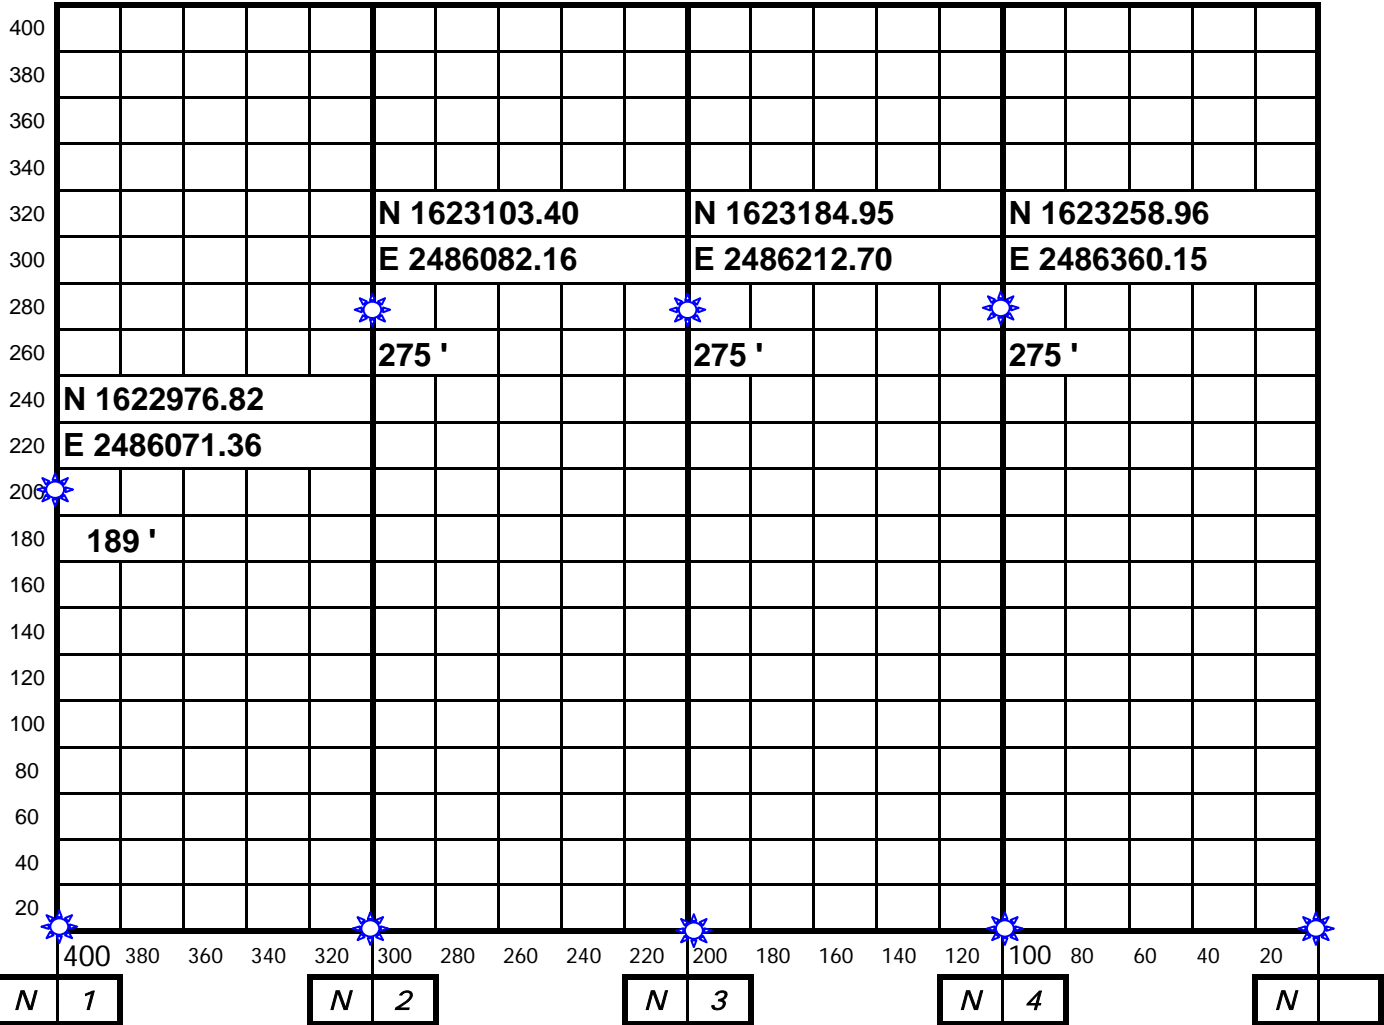


Start	Start	Start	Start	Start
9/18	9/18	9/18	9/18	
Finish	Finish	Finish	Finish	Finish
9/18	9/18	9/18	9/18	
MEC	MD	STAKE #		

Comments. Notes:

N1: Ended in cliff

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	9/18/2008	Completion Date:	9/18/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

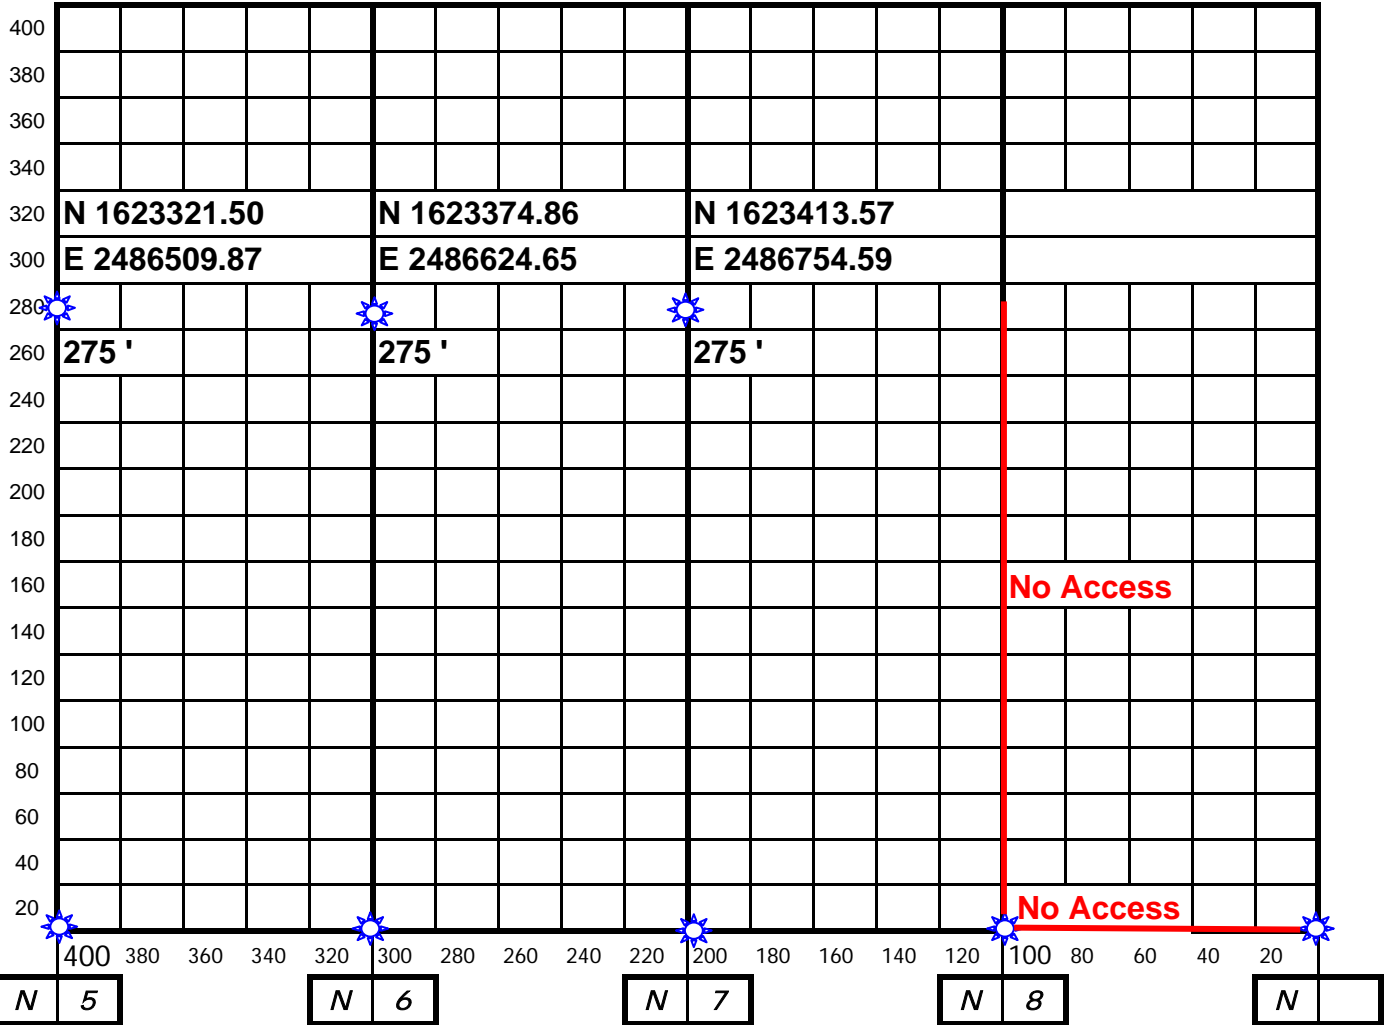


Start	Start	Start	Start	Start
9/18	9/18	9/18	9/18	
Finish	Finish	Finish	Finish	Finish
9/18	9/18	9/18	9/18	
MEC	MD	STAKE #		

Comments.Notes:

N7: Cliff

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:		Completion Date:	
QC Date:		QC Signature:	
QA Date:		QA Signature:	

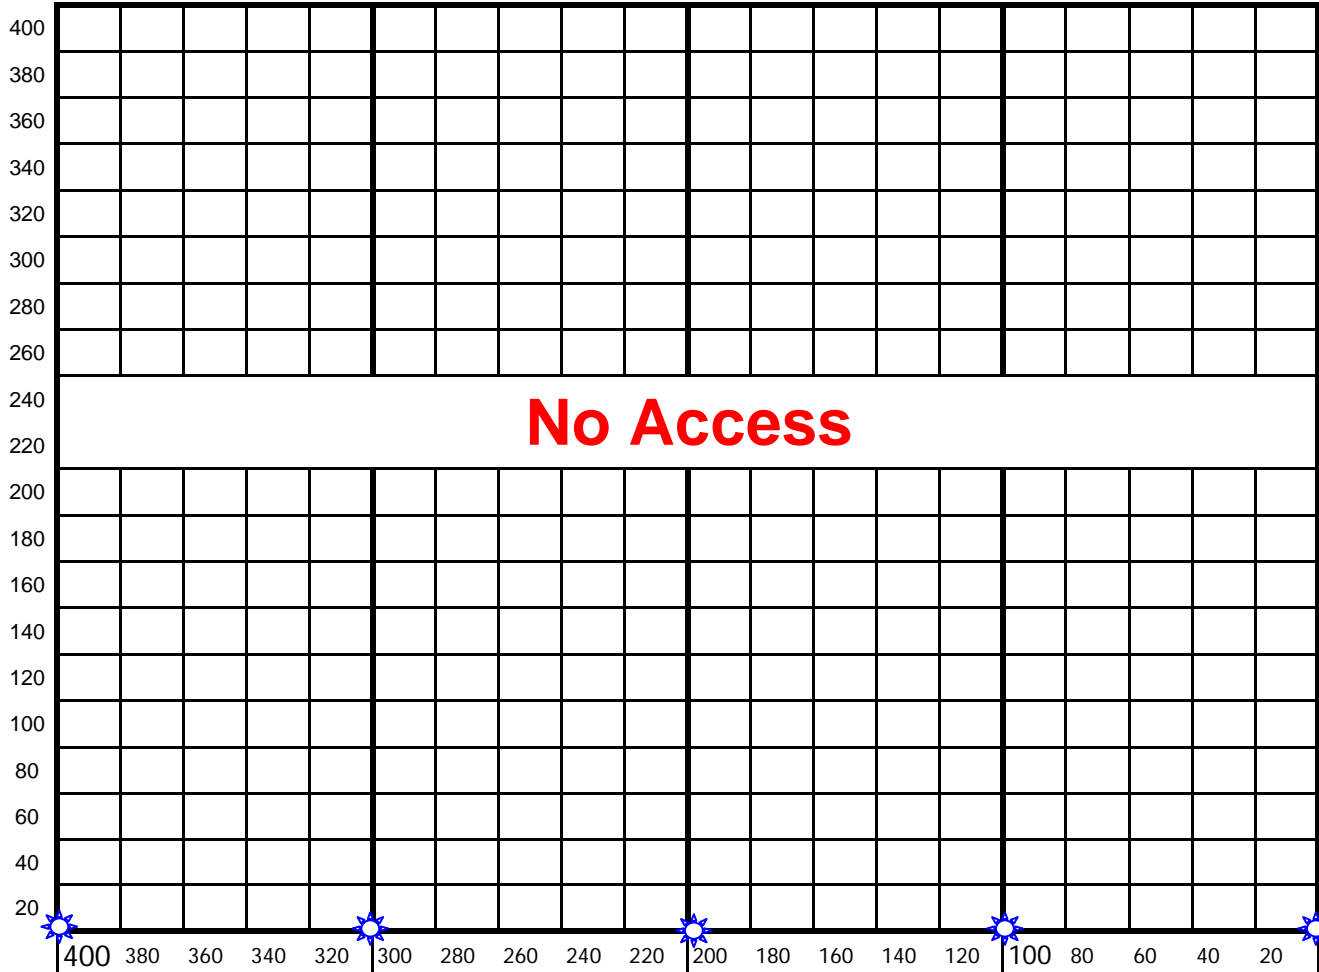


N	9	N	10	N	11	N	12	N	
---	---	---	----	---	----	---	----	---	--

Start	Start	Start	Start	Start	
<input style="width: 80%; height: 20px;" type="text"/>	<input style="width: 80%; height: 20px;" type="text"/>	<input style="width: 80%; height: 20px;" type="text"/>	<input style="width: 80%; height: 20px;" type="text"/>	<input style="width: 80%; height: 20px;" type="text"/>	
Finish	Finish	Finish	Finish	Finish	
<input style="width: 80%; height: 20px;" type="text"/>	<input style="width: 80%; height: 20px;" type="text"/>	<input style="width: 80%; height: 20px;" type="text"/>	<input style="width: 80%; height: 20px;" type="text"/>	<input style="width: 80%; height: 20px;" type="text"/>	
	MEC		MD		STAKE #

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:		Completion Date:	
QC Date:		QC Signature:	
QA Date:		QA Signature:	

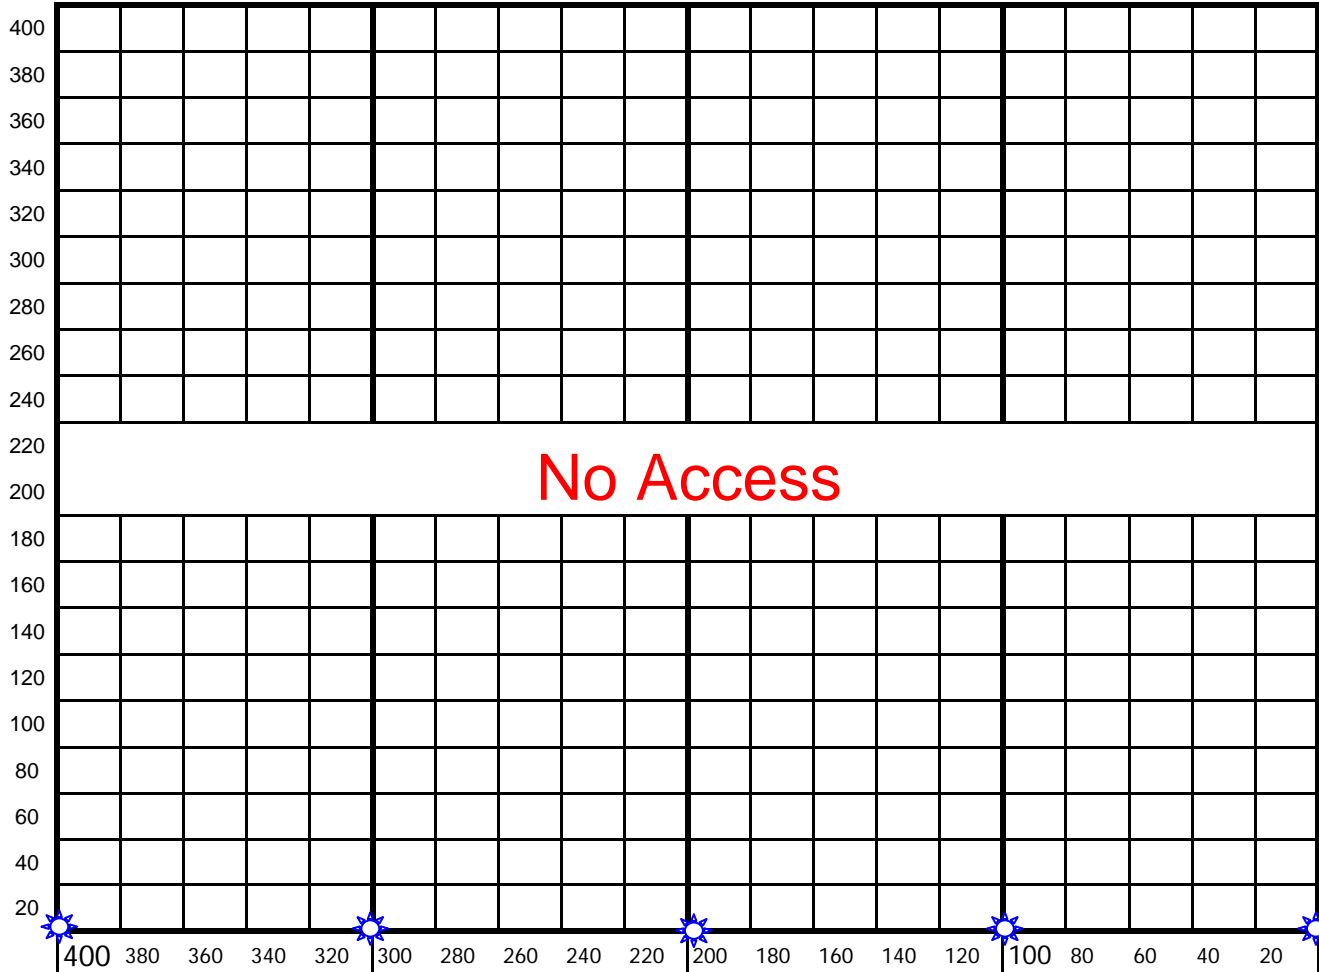


N	13	N	14	N	15	N	16	N	
---	----	---	----	---	----	---	----	---	--

Start	Start	Start	Start	Start	
<input style="width: 50px; height: 20px;" type="text"/>	<input style="width: 50px; height: 20px;" type="text"/>	<input style="width: 50px; height: 20px;" type="text"/>	<input style="width: 50px; height: 20px;" type="text"/>	<input style="width: 50px; height: 20px;" type="text"/>	
Finish	Finish	Finish	Finish	Finish	
<input style="width: 50px; height: 20px;" type="text"/>	<input style="width: 50px; height: 20px;" type="text"/>	<input style="width: 50px; height: 20px;" type="text"/>	<input style="width: 50px; height: 20px;" type="text"/>	<input style="width: 50px; height: 20px;" type="text"/>	
	MEC		MD		STAKE #

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:		Completion Date:	
QC Date:		QC Signature:	
QA Date:		QA Signature:	

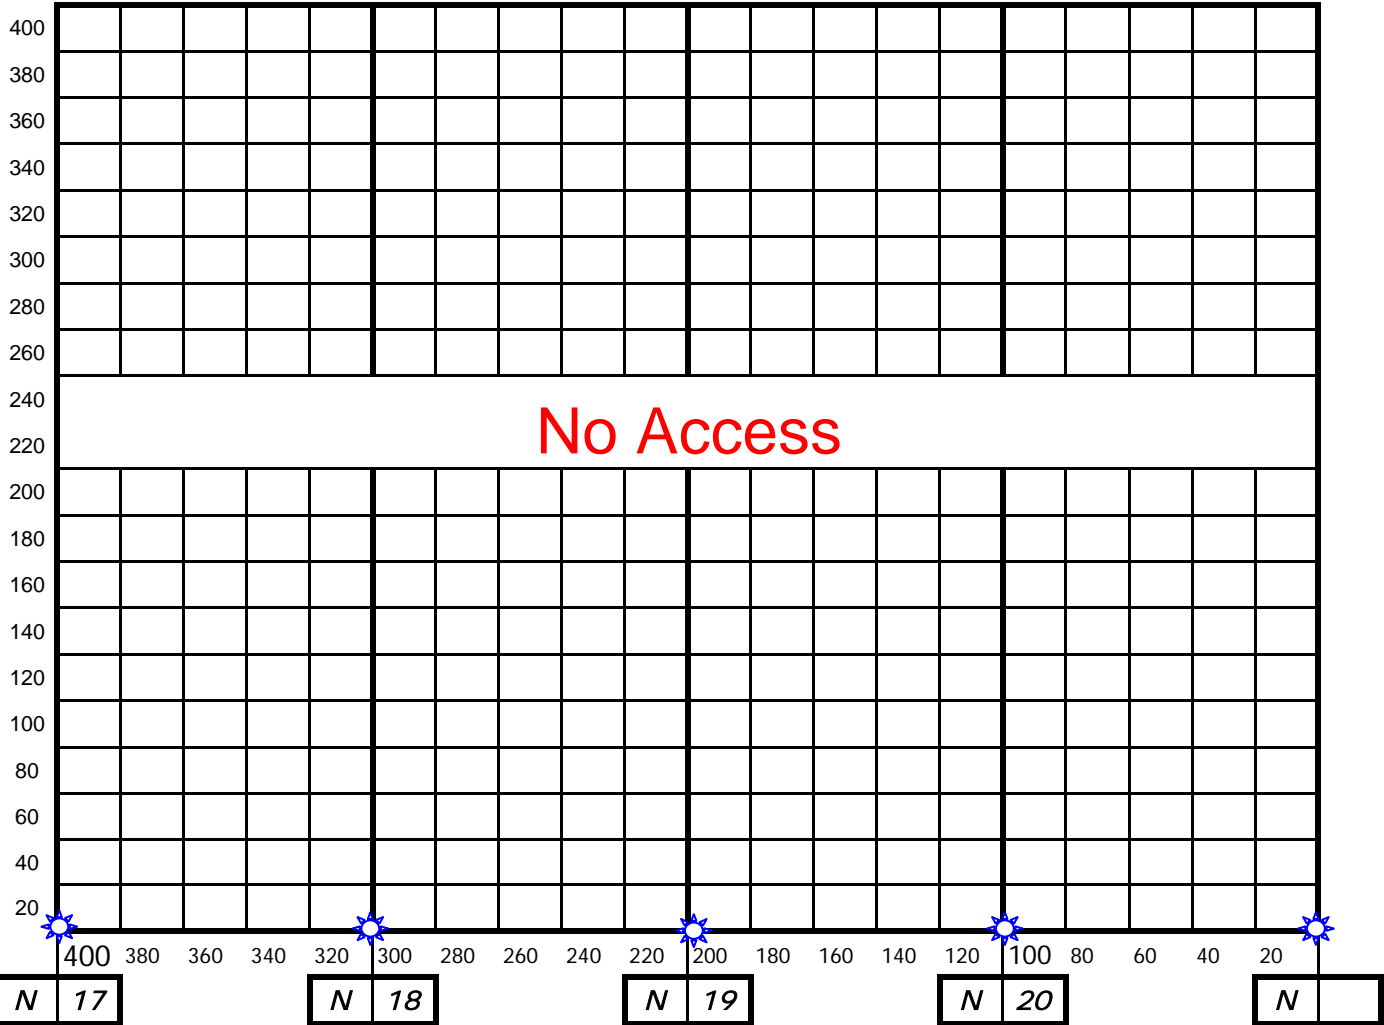


Start	Start	Start	Start	Start	
Finish	Finish	Finish	Finish	Finish	
	MEC		MD		STAKE #

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	9/5/2008	Completion Date:	9/5/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

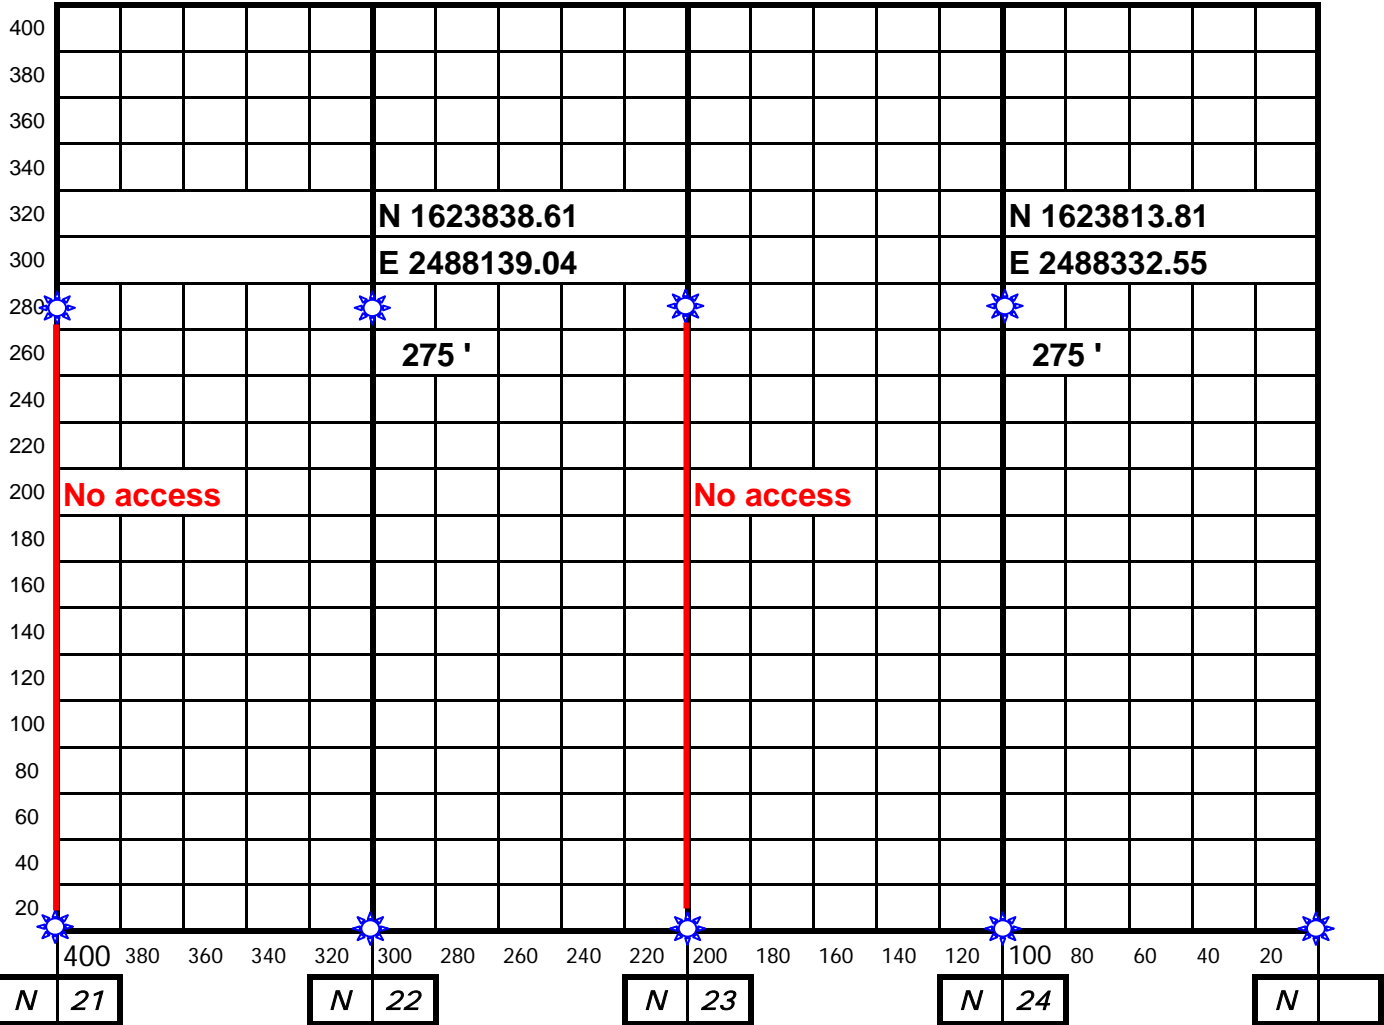


Start	Start	Start	Start	Start	
9/5	9/5	9/5	9/5		
Finish	Finish	Finish	Finish	Finish	
9/5	9/5	9/5	9/5		
	MEC		MD		STAKE #

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	9/5/2008	Completion Date:	9/5/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

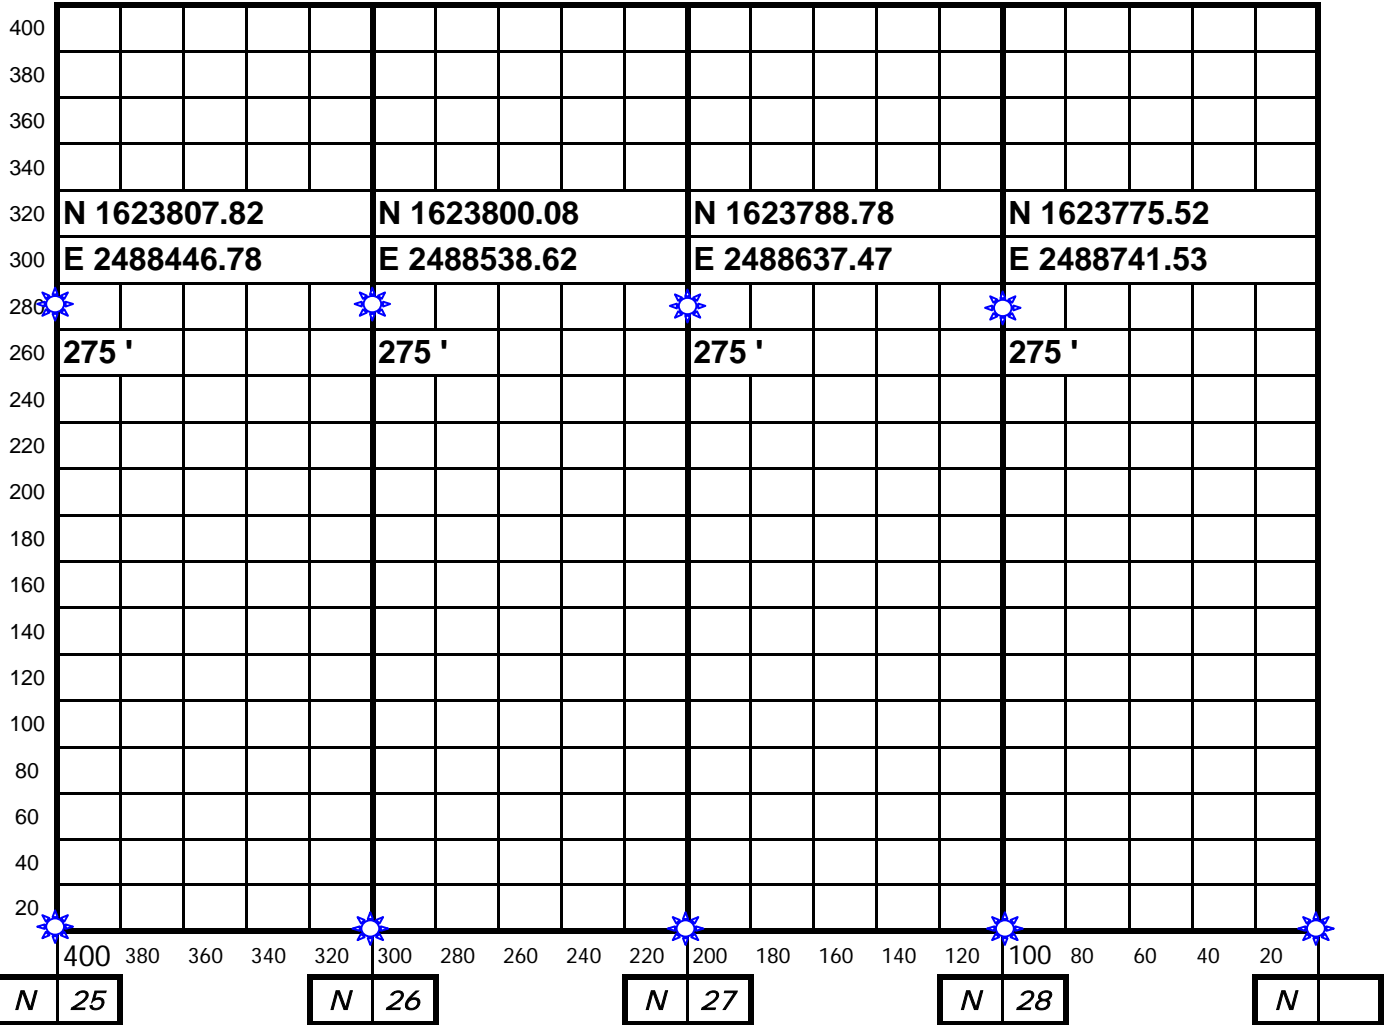


Start	Start	Start	Start	Start	
9/5	9/5	9/5	9/5		
Finish	Finish	Finish	Finish	Finish	
9/5	9/5	9/5	9/5		
	MEC		MD		STAKE #

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	9/5/2008	Completion Date:	9/5/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

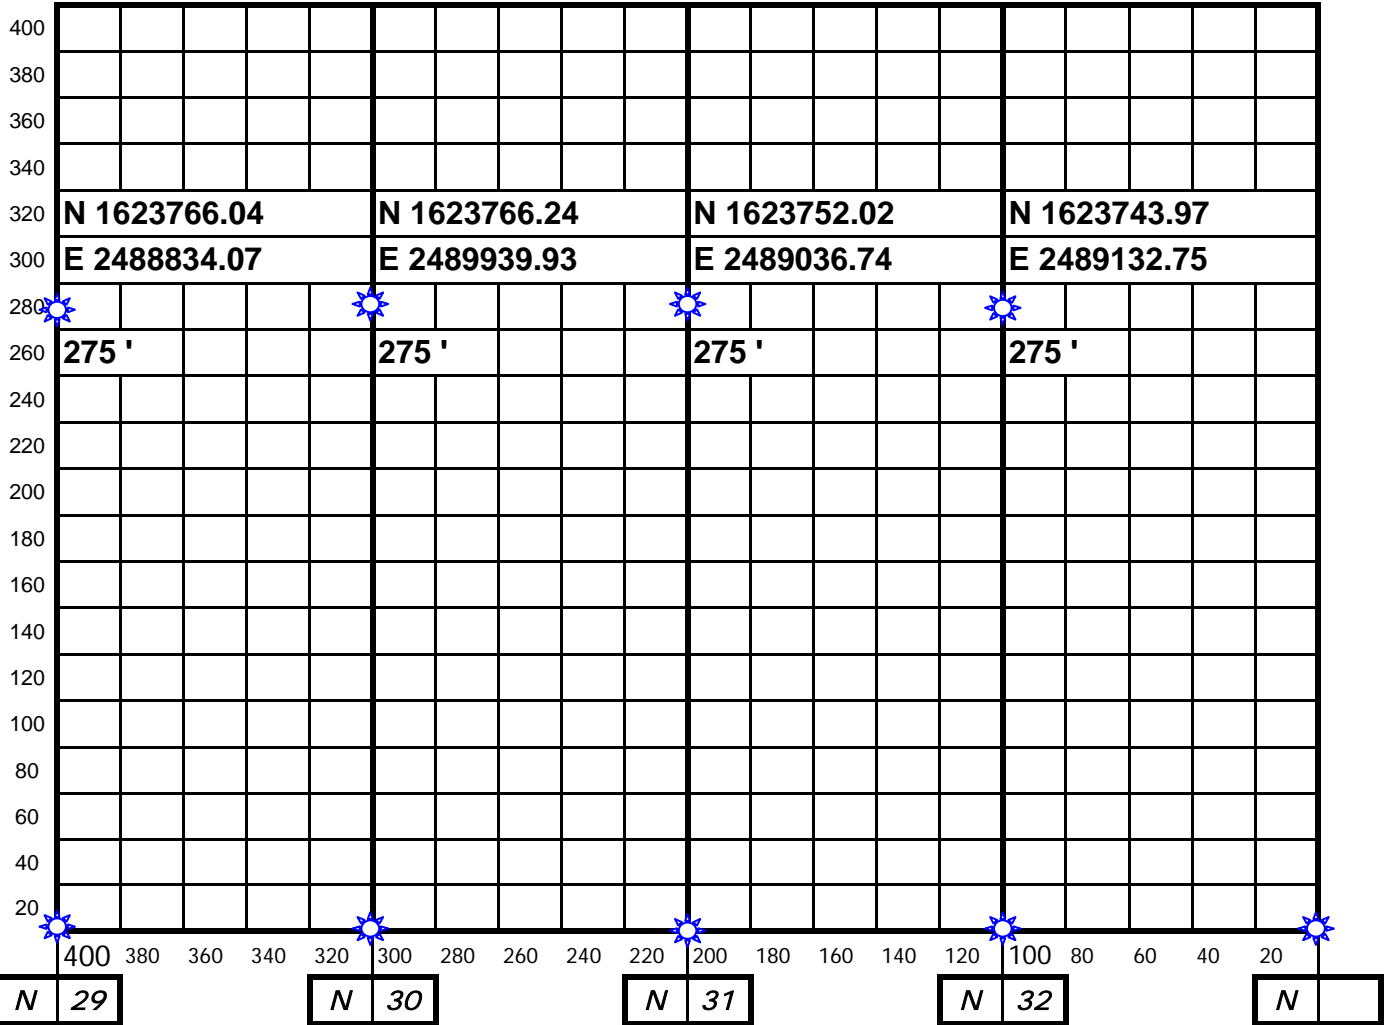


Start	Start	Start	Start	Start
9/5	9/5	9/5	9/5	
Finish	Finish	Finish	Finish	Finish
9/5	9/5	9/5	9/5	
	MEC		MD	
				STAKE #

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	9/5/2008	Completion Date:	9/5/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

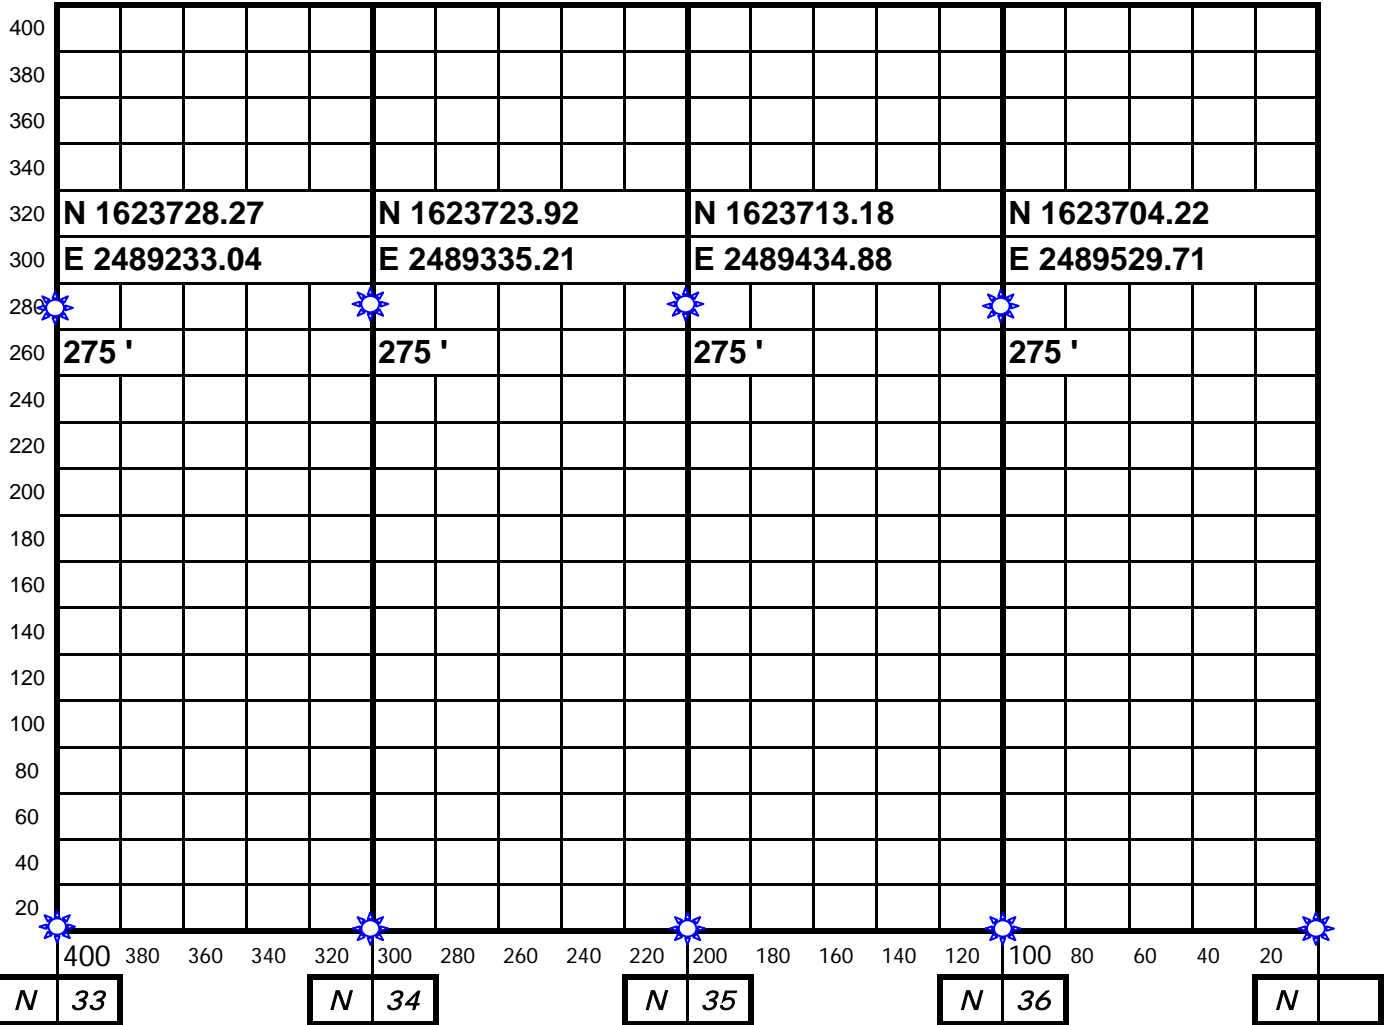


Start	Start	Start	Start	Start	
9/5	9/5	9/5	9/5		
Finish	Finish	Finish	Finish	Finish	
9/5	9/5	9/5	9/5		
	MEC		MD		STAKE #

Comments. Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/26/2008	Completion Date:	9/5/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

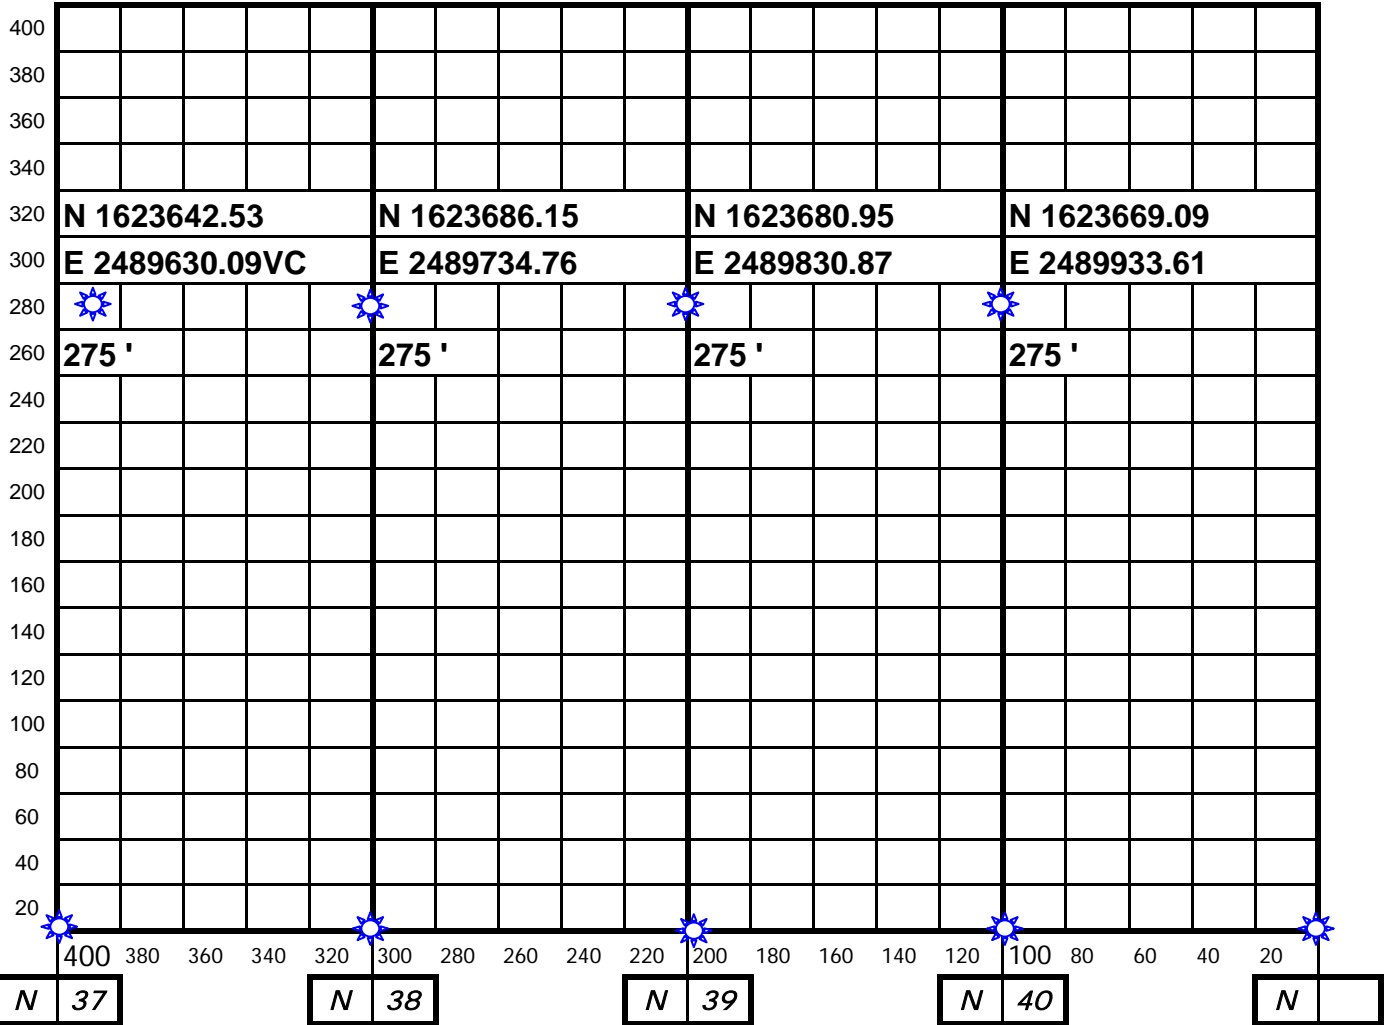


Start	Start	Start	Start	Start
9/5	8/26	8/26	8/26	
Finish	Finish	Finish	Finish	Finish
9/5	8/26	8/26	8/26	
MEC	MD	STAKE #		

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/26/2008	Completion Date:	8/26/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

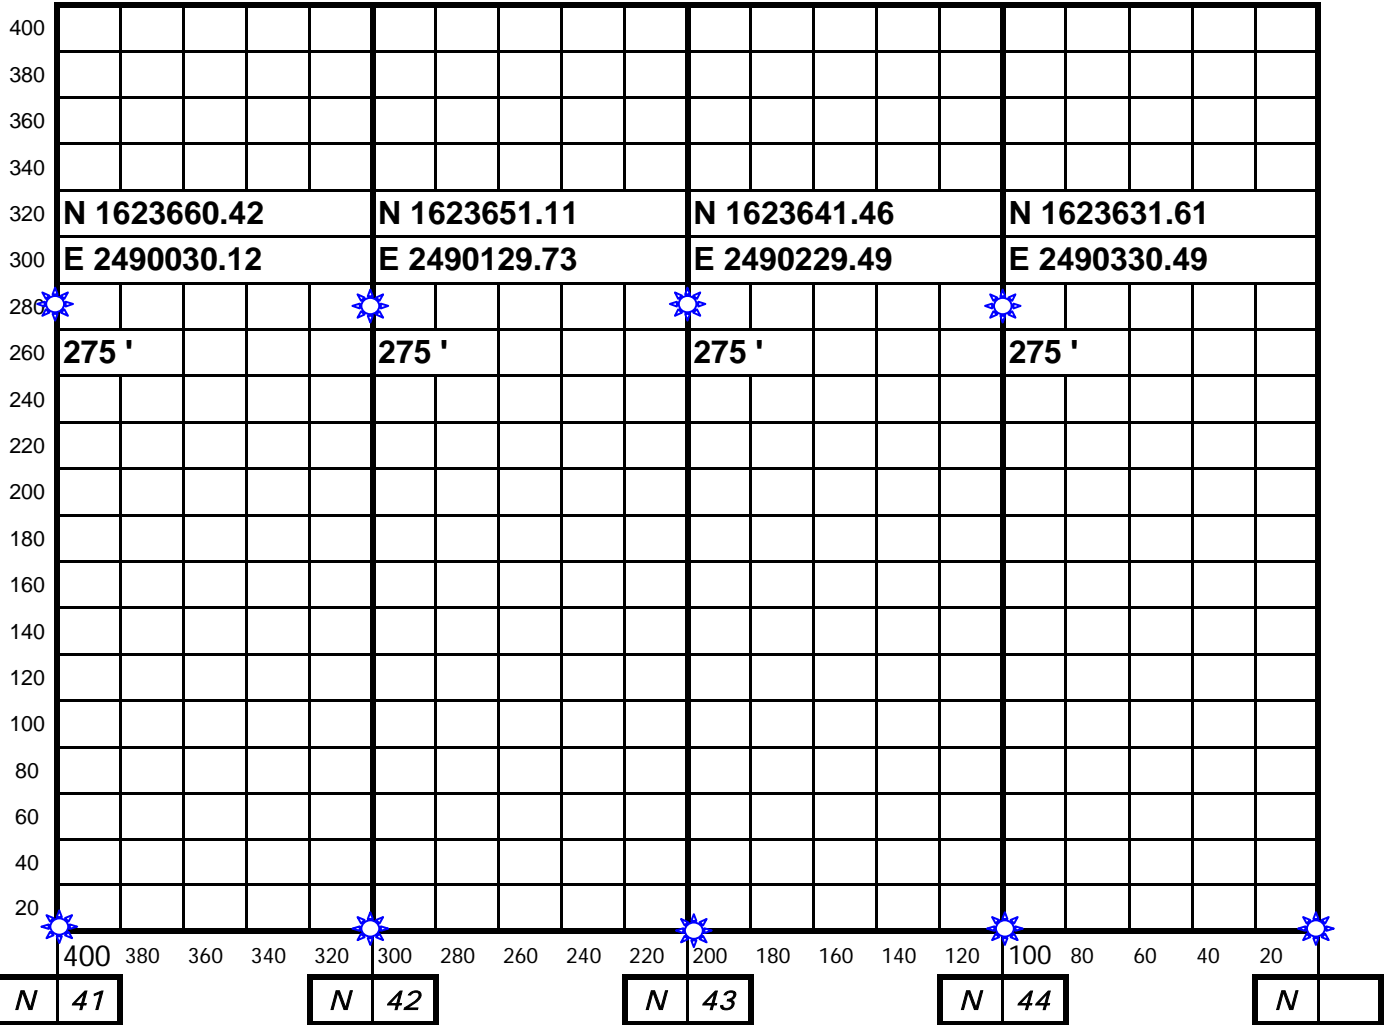


Start	Start	Start	Start	Start	
8/26	8/26	8/26	8/26		
Finish	Finish	Finish	Finish	Finish	
8/26	8/26	8/26	8/26		
	MEC		MD		STAKE #

Comments.Notes:

N41/ 43 are EM-61 accessible

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/26/2008	Completion Date:	8/26/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

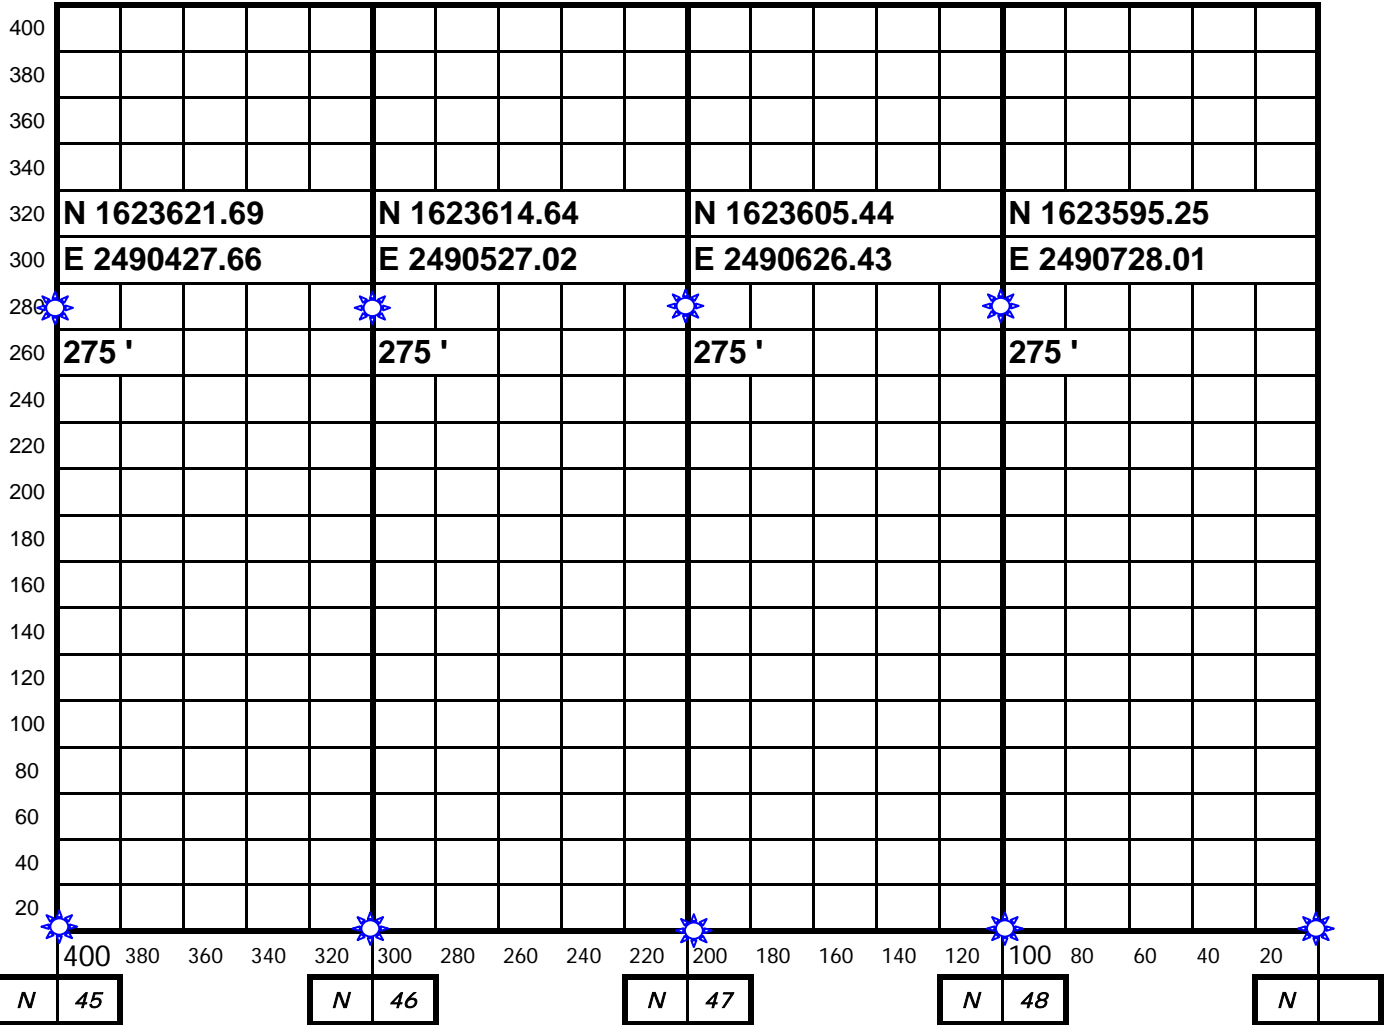


Start	Start	Start	Start	Start	
8/26	8/26	8/26	8/26		
Finish	Finish	Finish	Finish	Finish	
8/26	8/26	8/26	8/26		
	MEC		MD		STAKE #

Comments.Notes:

45-48 are EM-61 accessible

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/14/2008	Completion Date:	8/14/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

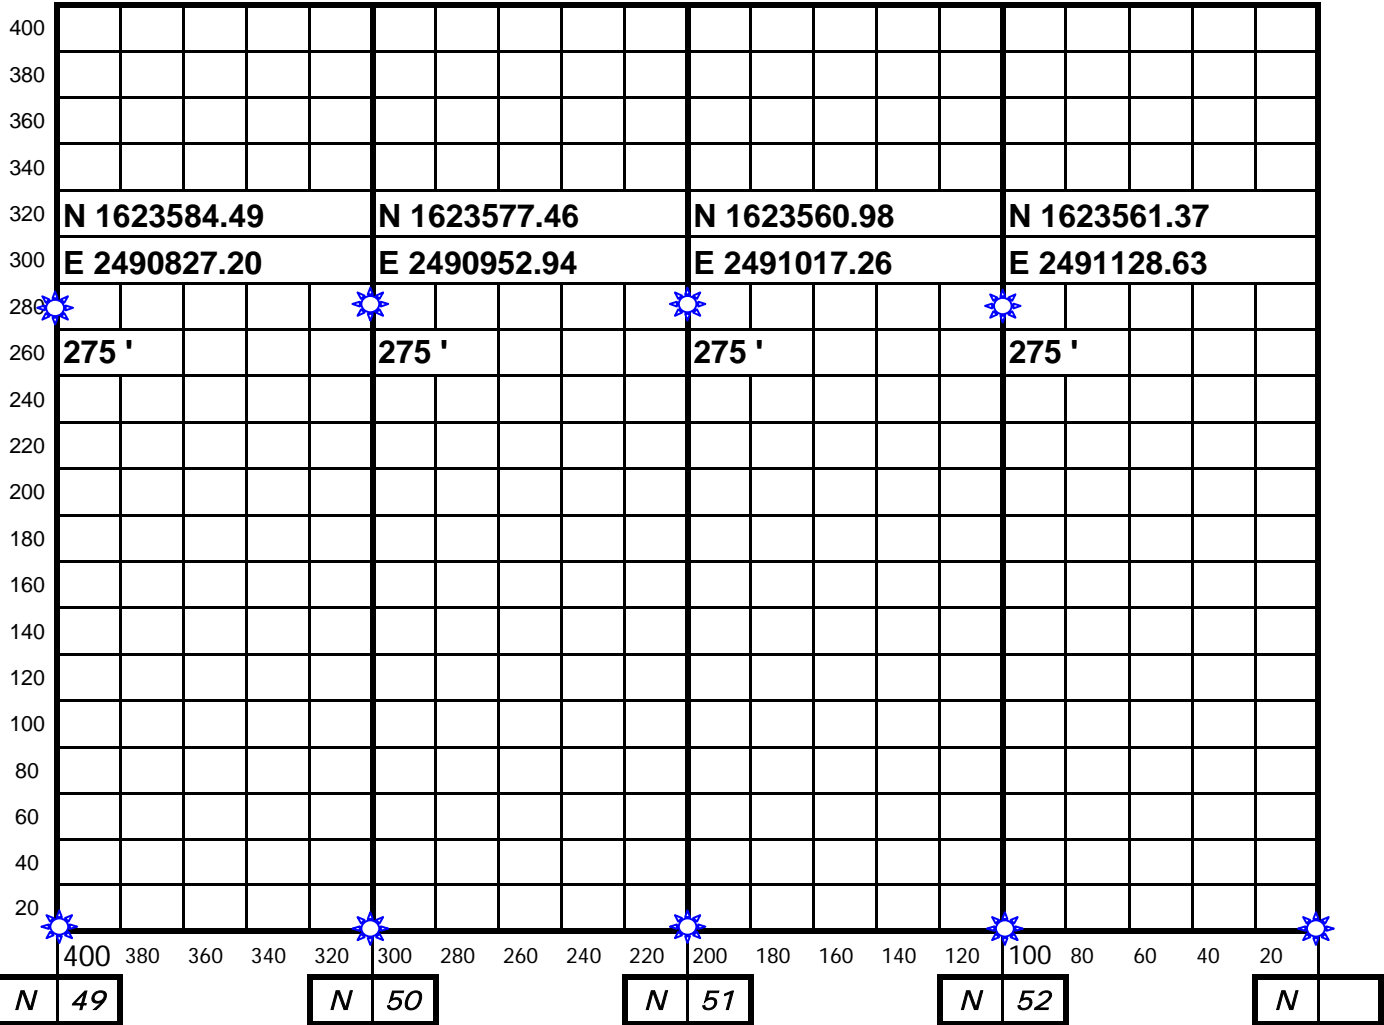


Start	Start	Start	Start	Start
		8/14	8/14	
Finish	Finish	Finish	Finish	Finish
		8/14	8/14	
	MEC		MD	
			STAKE #	

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/14/2008	Completion Date:	8/14/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

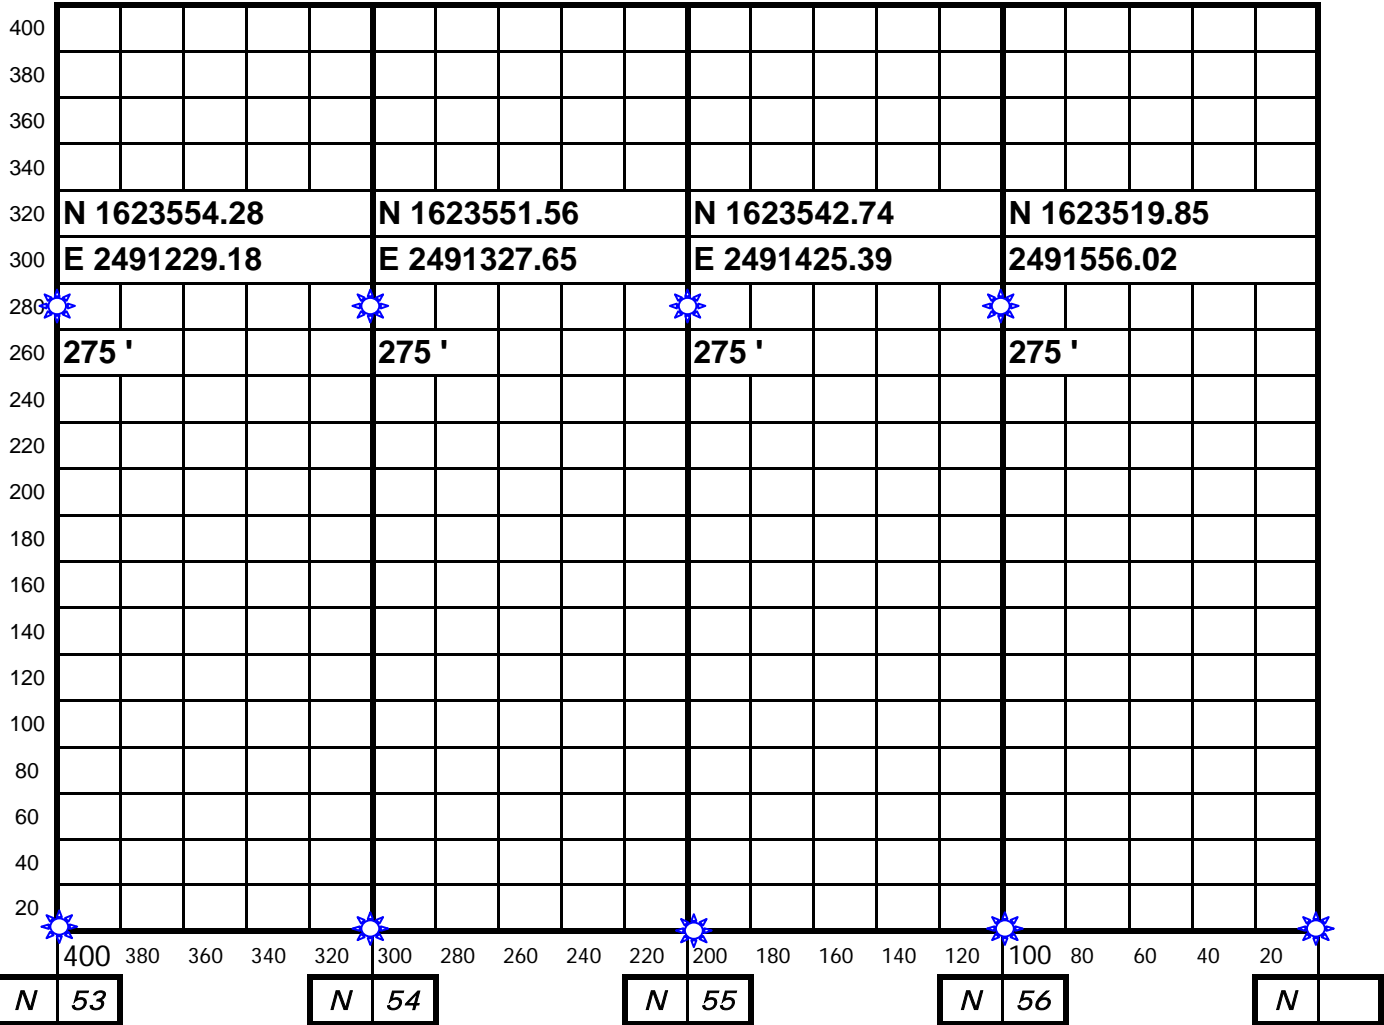


Start	Start	Start	Start	Start
8/14	8/14	8/14	8/14	
Finish	Finish	Finish	Finish	Finish
8/14	8/14	8/14	8/14	
MEC	MD	STAKE #		

Comments.Notes:

PIKA Transect Sheets

Project	Ft Wingate Kickout Deliniation	Project No.	W912BV-04--2016-DY02
Start Date:	8/14/2008	Completion Date:	8/14/2008
QC Date:		QC Signature:	
QA Date:		QA Signature:	

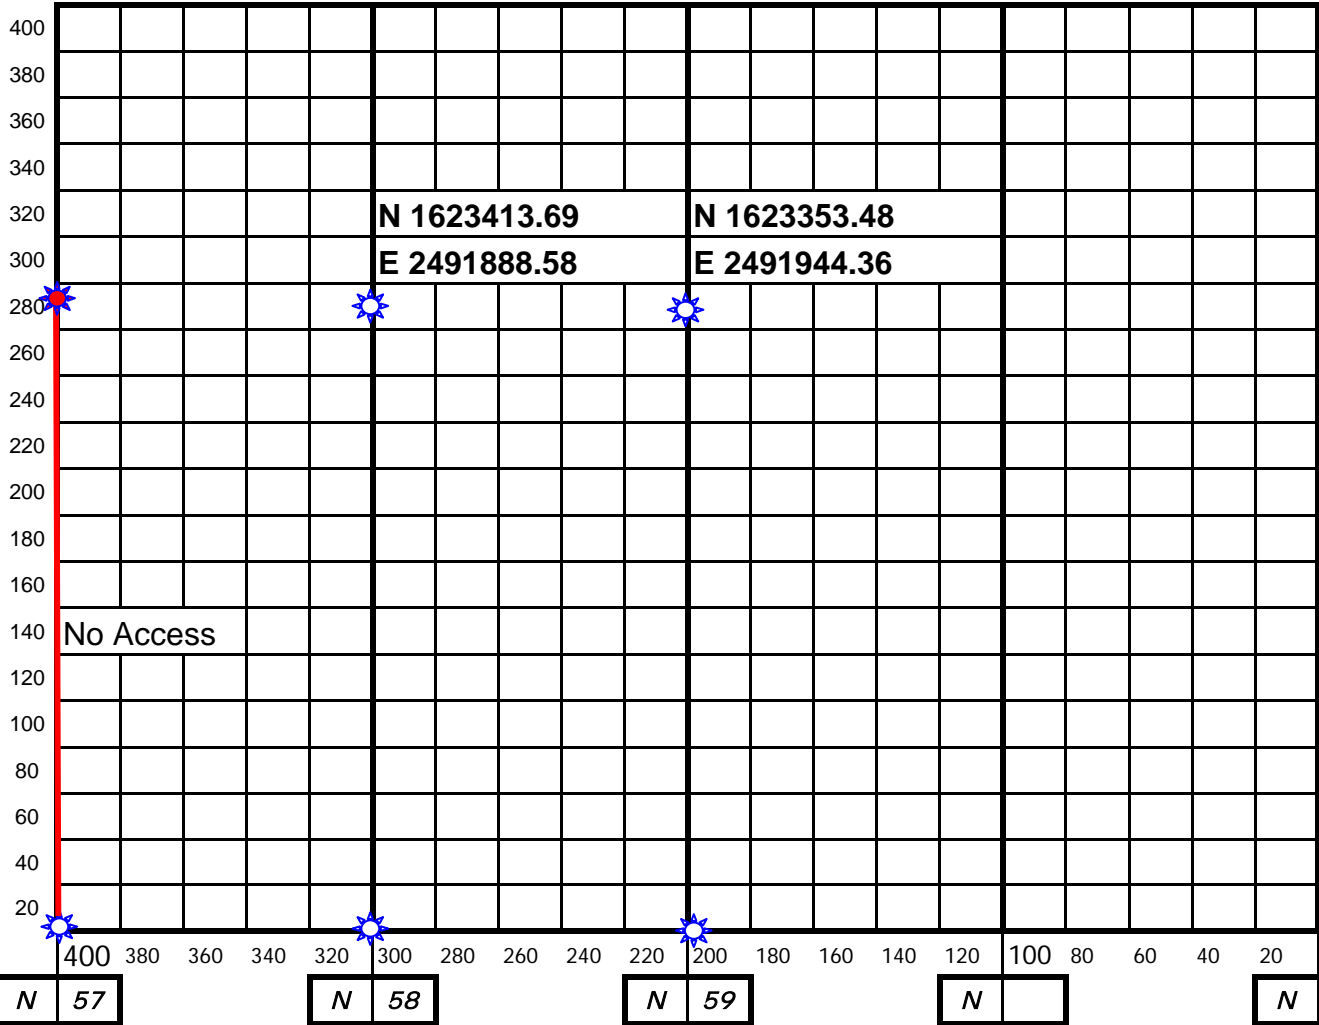

N	57	N	58	N	59	N		N	
---	----	---	----	---	----	---	--	---	--


Start	Start	Start	Start	Start	
8/14	8/14	8/14			
Finish	Finish	Finish	Finish	Finish	
8/14	8/14	8/14			
	MEC		MD		STAKE #

Comments.Notes:

N 57: Tribes did not want us to run this transect due to large archeological site

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/3/2009	Completion Date:	4/3/2009
QC Date:		QA Date	

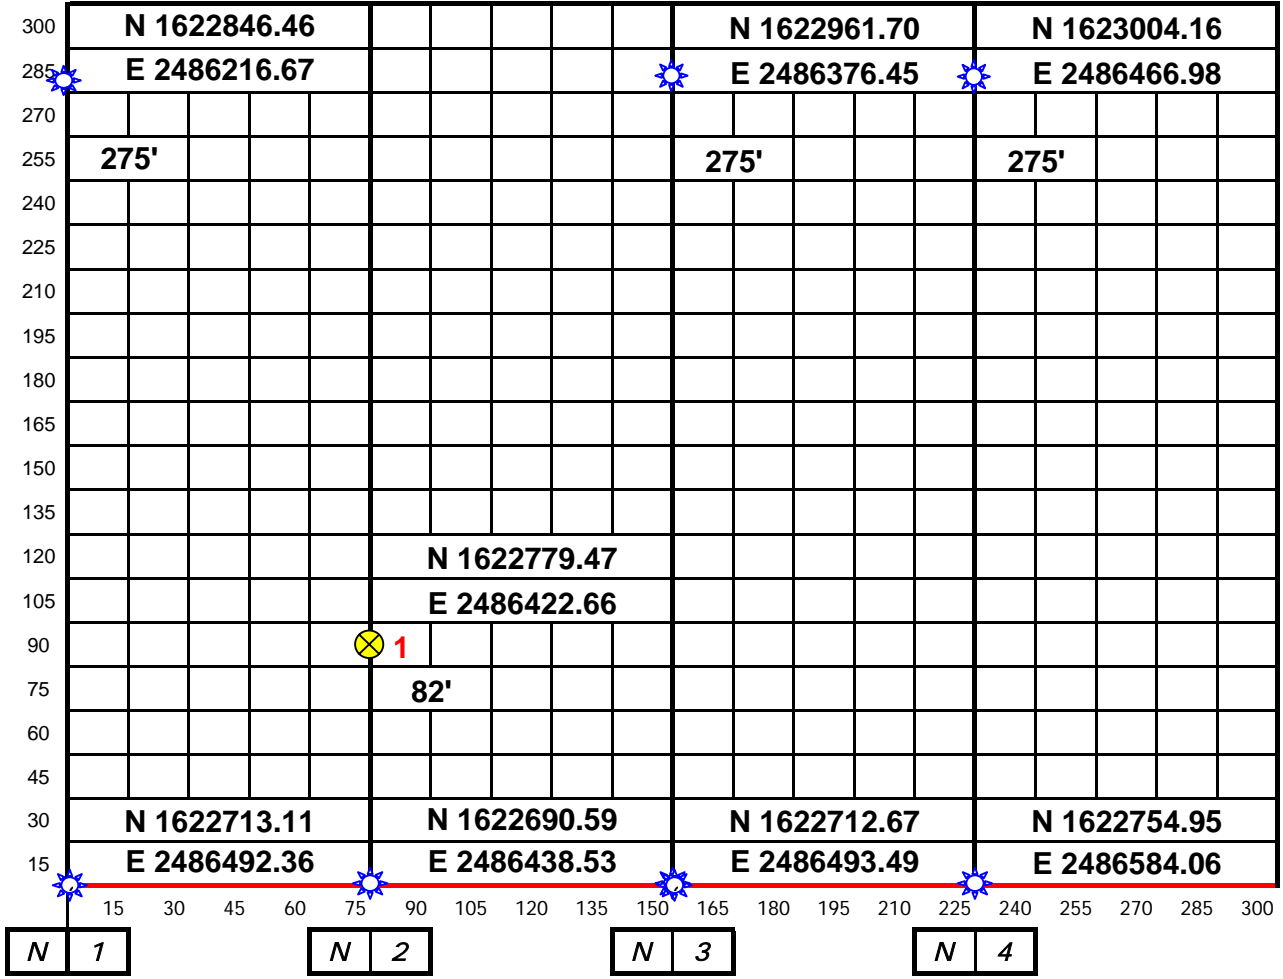


Start <input type="text" value="4/3"/>	Start <input type="text" value="4/3"/>	Start <input type="text" value="4/3"/>	Start <input type="text" value="4/3"/>
Finish <input type="text" value="4/3"/>	Finish <input type="text" value="4/3"/>	Finish <input type="text" value="4/3"/>	Finish <input type="text" value="4/3"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

1 Fragmentation

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/3/2009	Completion Date:	4/3/2009
QC Date:		QA Date	

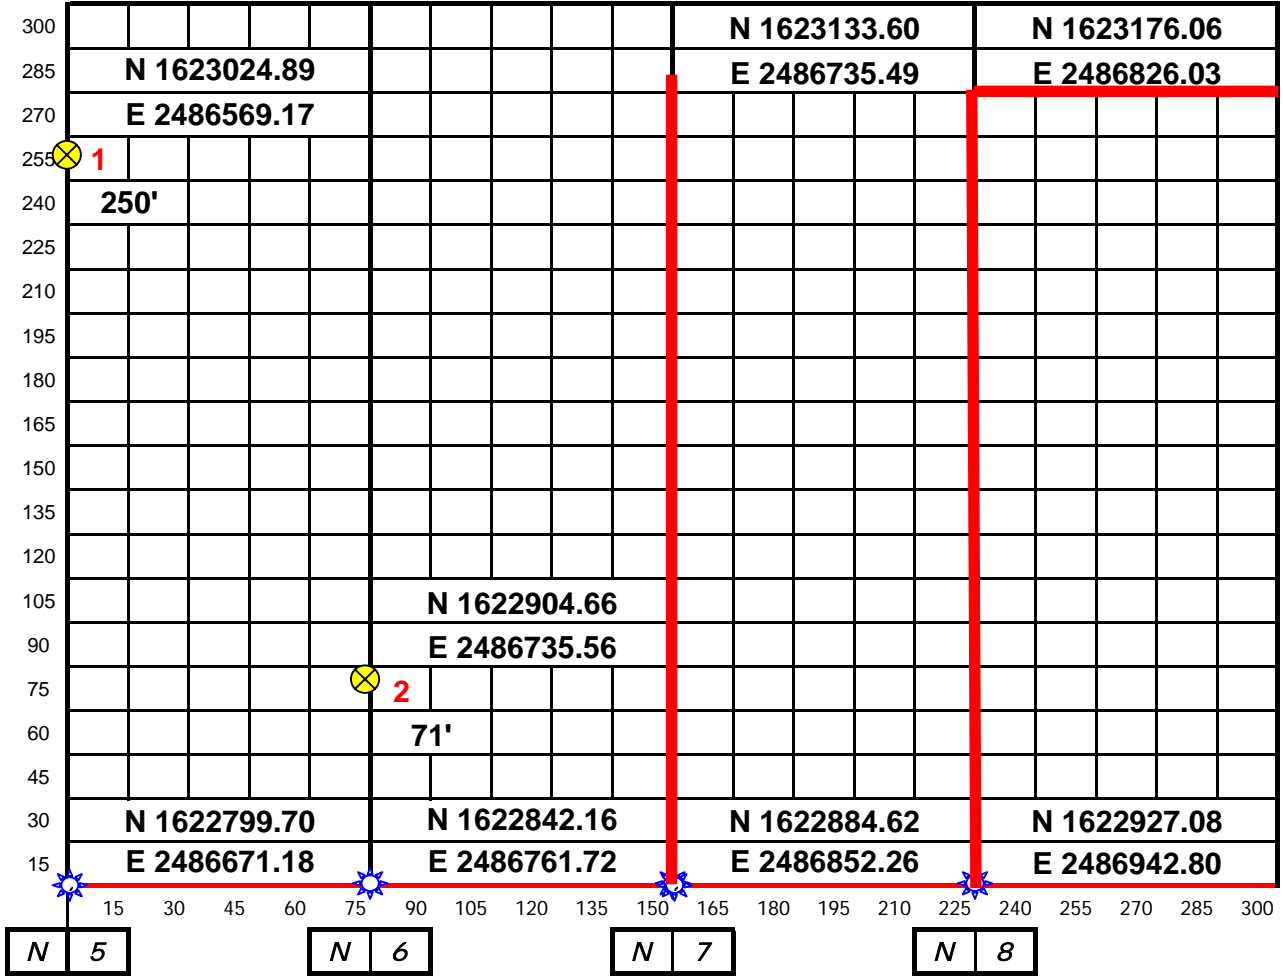

Start 4/3	Start 4/3	Start 4/3	Start 4/3
Finish 4/3	Finish 4/3	Finish 4/3	Finish 4/3
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:


1 Fragmentation

2 Fragmentation

N7/N8 No Access/Safety

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/3/2009	Completion Date:	4/3/2009
QC Date:		QA Date	

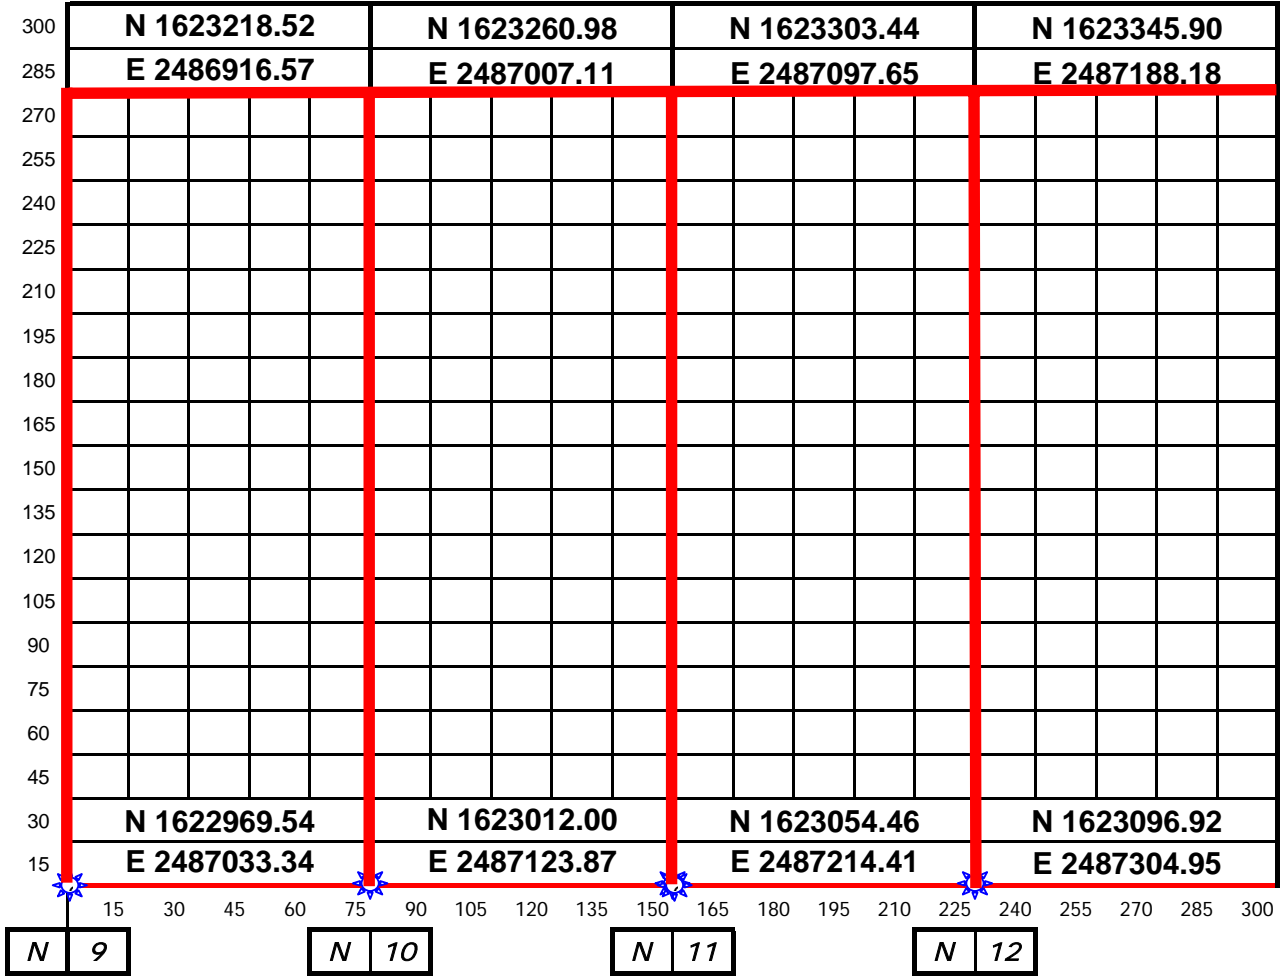


Start <input type="text" value="4/3"/>	Start <input type="text" value="4/3"/>	Start <input type="text" value="4/3"/>	Start <input type="text" value="4/3"/>
Finish <input type="text" value="4/3"/>	Finish <input type="text" value="4/3"/>	Finish <input type="text" value="4/3"/>	Finish <input type="text" value="4/3"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:
N9-N12 No Access/Safety

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/3/2009	Completion Date:	4/6/2009
QC Date:		QA Date	

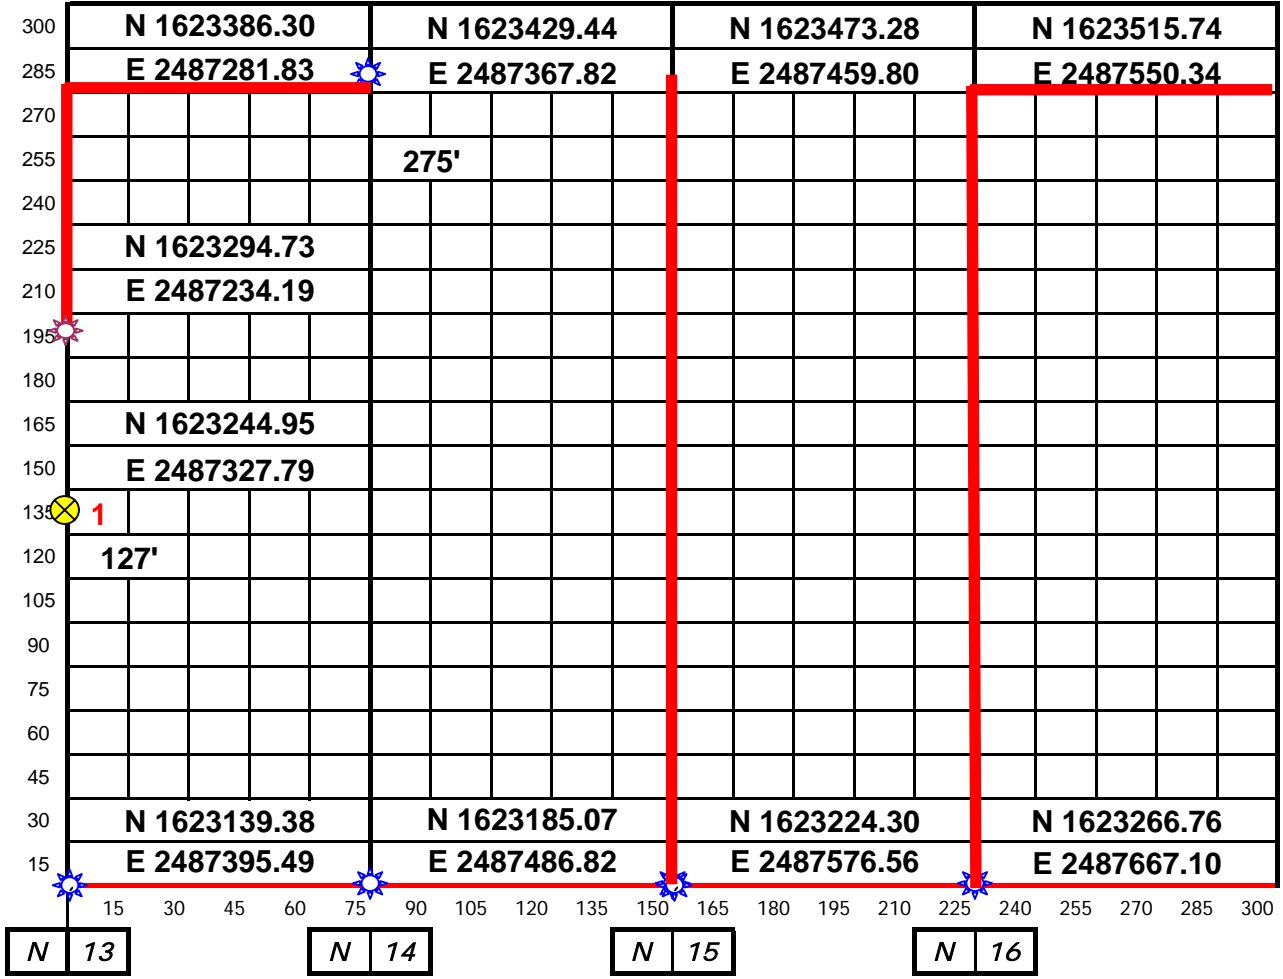


Start <input type="text" value="4/6"/>	Start <input type="text" value="4/3"/>	Start <input type="text" value="4/3"/>	Start <input type="text" value="4/3"/>
Finish <input type="text" value="4/6"/>	Finish <input type="text" value="4/3"/>	Finish <input type="text" value="4/3"/>	Finish <input type="text" value="4/3"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:
N13,N15,N16 No Access/Safety

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/2/2009	Completion Date:	4/3/2009
QC Date:		QA Date	

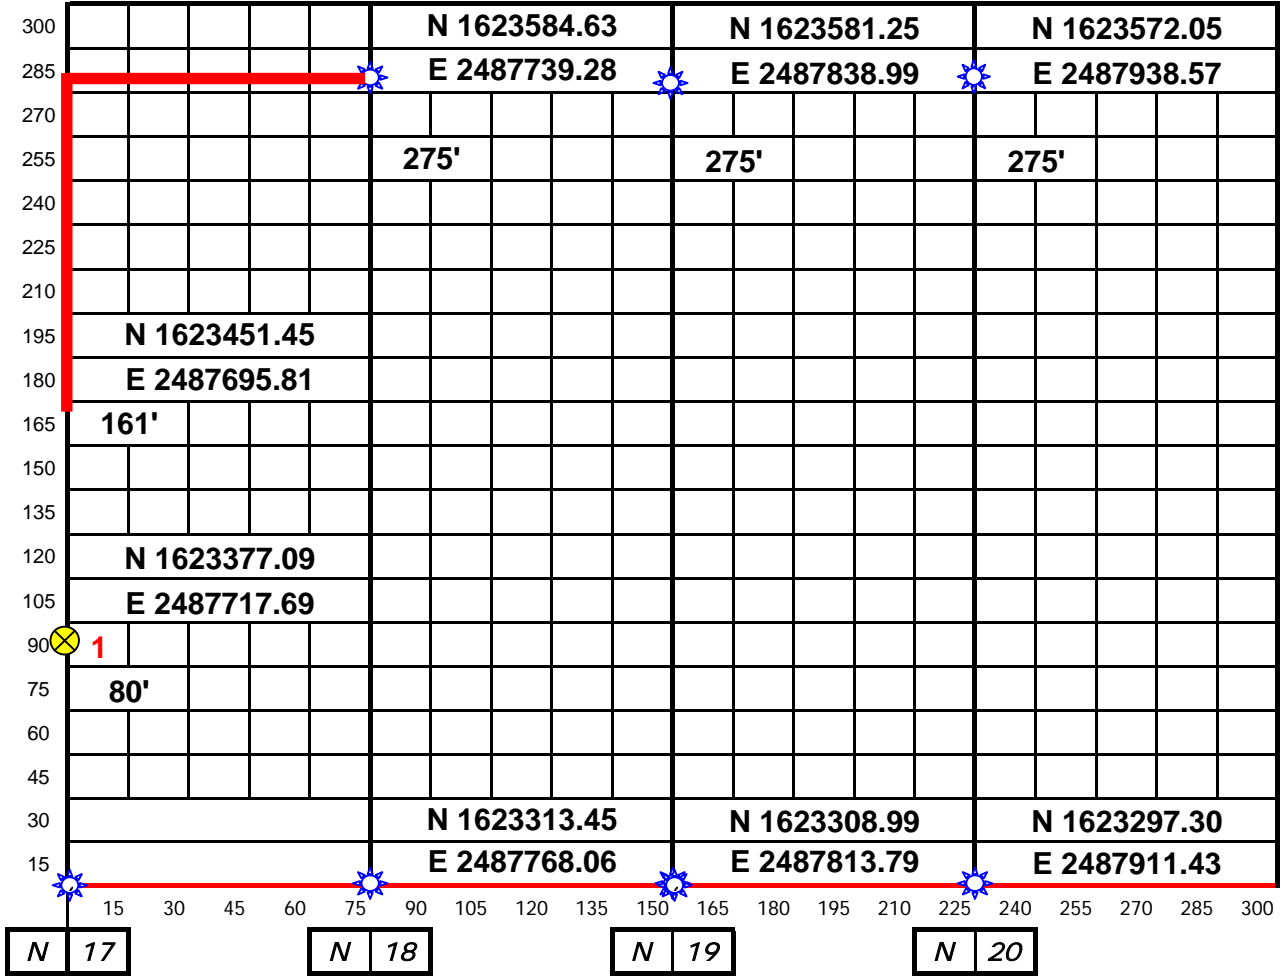

Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/3</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/2</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/2</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/2</div>
Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/3</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/2</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/2</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/2</div>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:


N18-N20 Very difficult access

1 Fragmentation

N17 No Access/Safety beyond 161 feet

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/1/2009	Completion Date:	4/2/2009
QC Date:		QA Date	

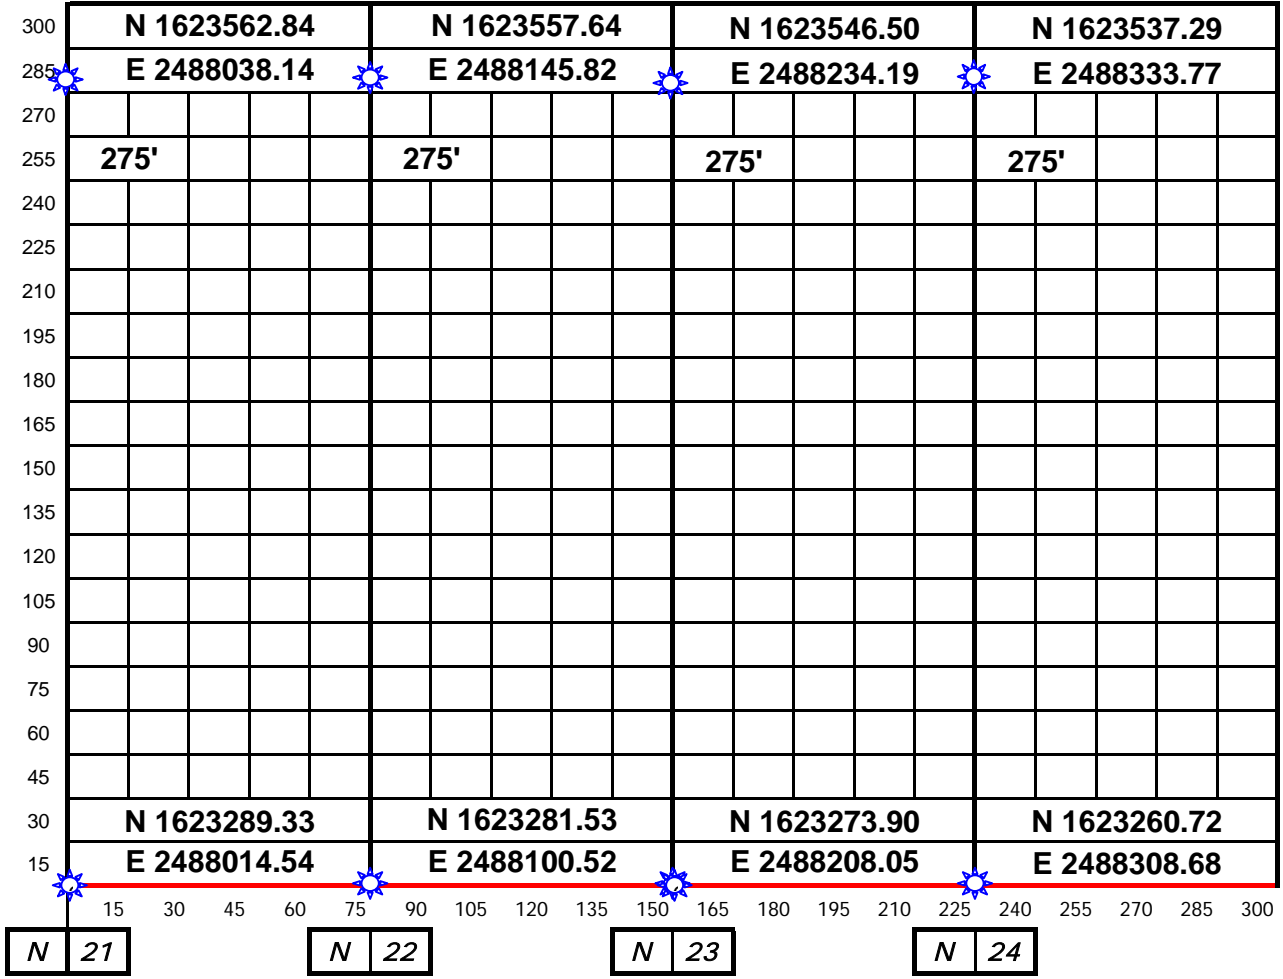


Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/2</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/1</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/1</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/1</div>
Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/2</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/1</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/1</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/1</div>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

N21 Very difficult access

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/1/2009	Completion Date:	4/1/2009
QC Date:		QA Date	

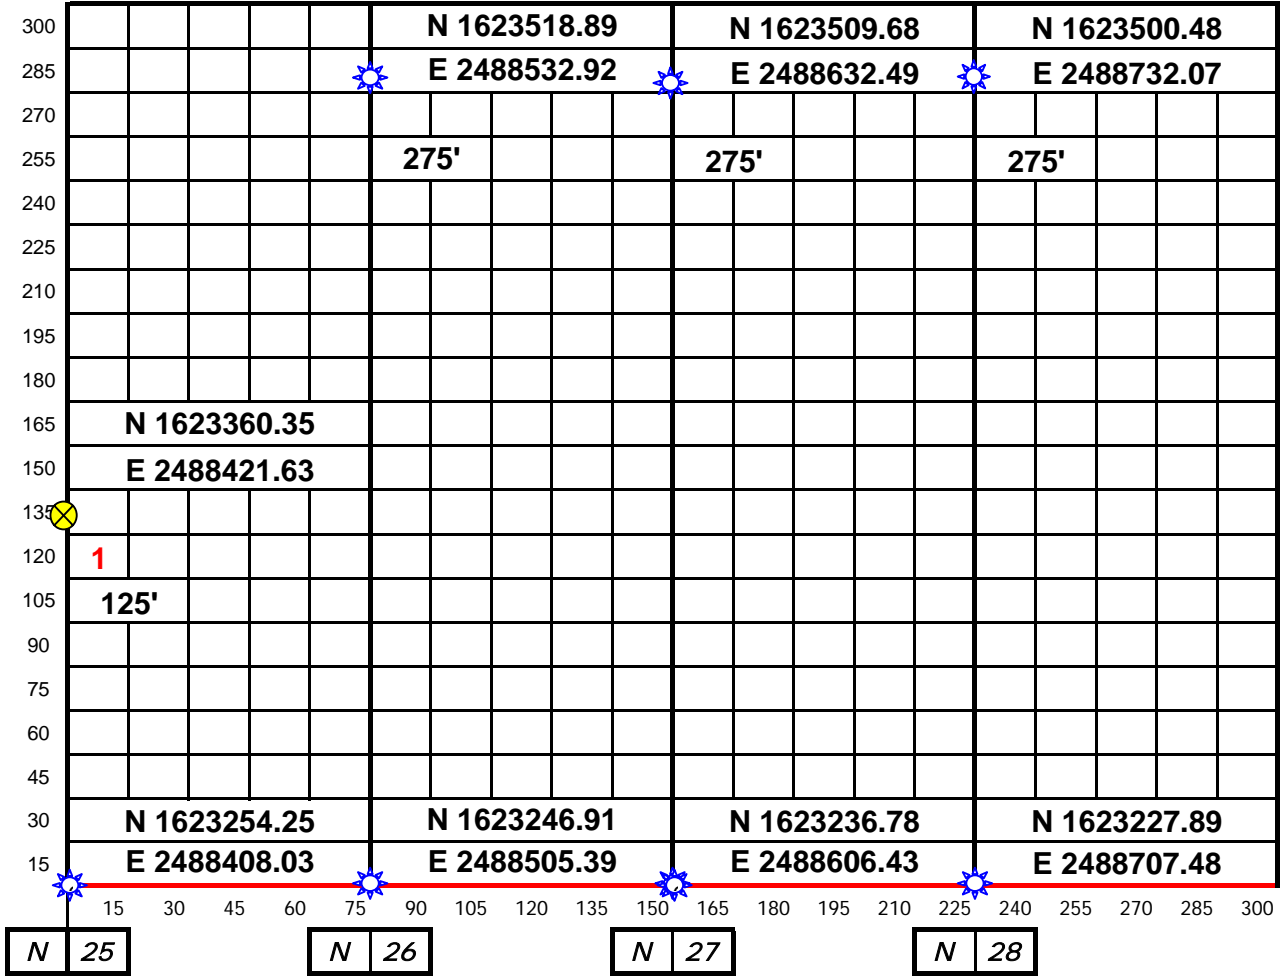


Start <input type="text" value="4/1"/>	Start <input type="text" value="4/1"/>	Start <input type="text" value="4/1"/>	Start <input type="text" value="4/1"/>
Finish <input type="text" value="4/1"/>	Finish <input type="text" value="4/1"/>	Finish <input type="text" value="4/1"/>	Finish <input type="text" value="4/1"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

1 Fragmentation

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/1/2009	Completion Date:	4/1/2009
QC Date:		QA Date	

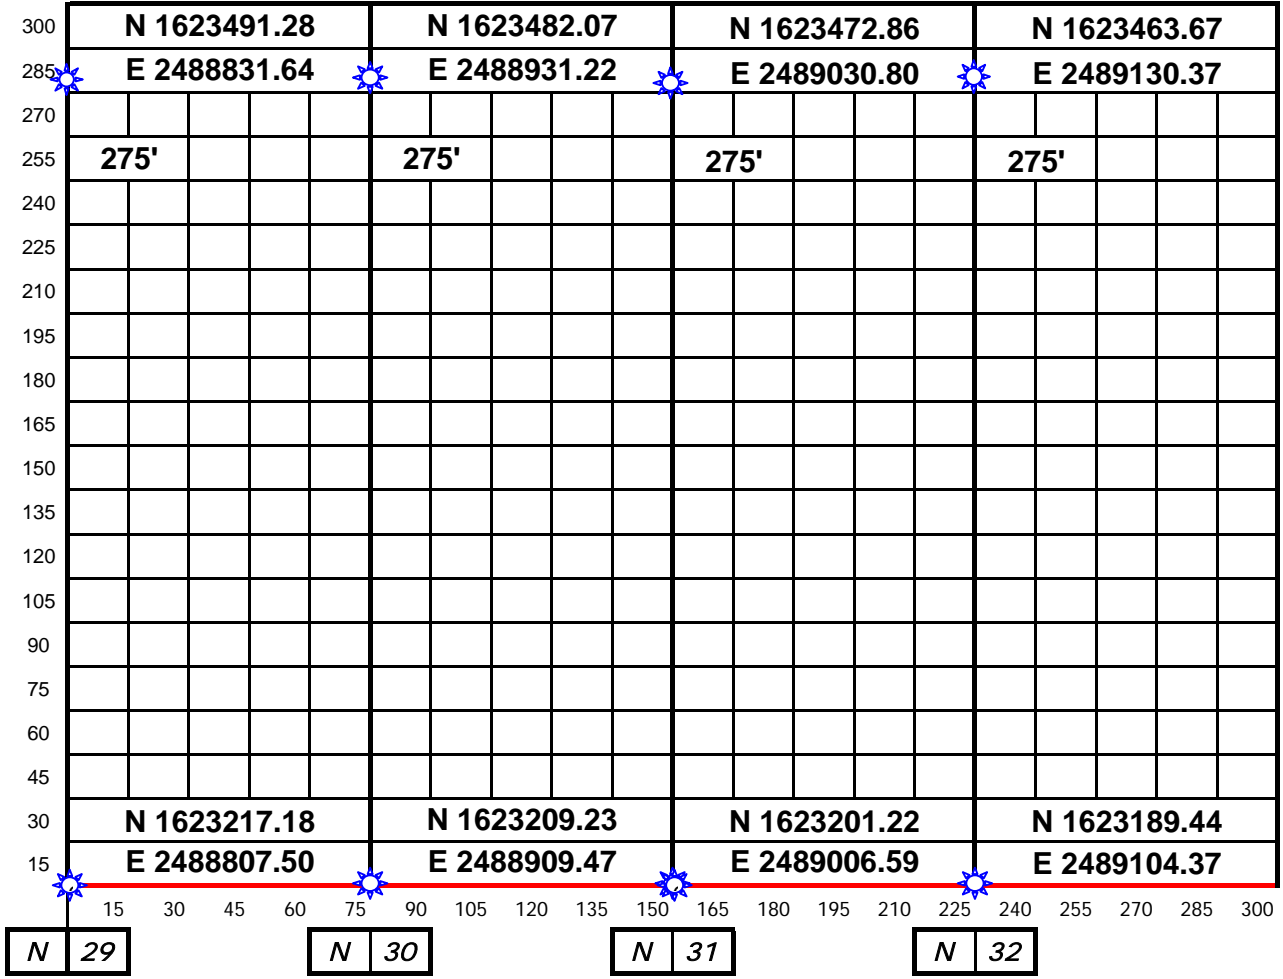


Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/1</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/1</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/1</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/1</div>
Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/1</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/1</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/1</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/1</div>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/1/2009	Completion Date:	4/2/2009
QC Date:		QA Date	

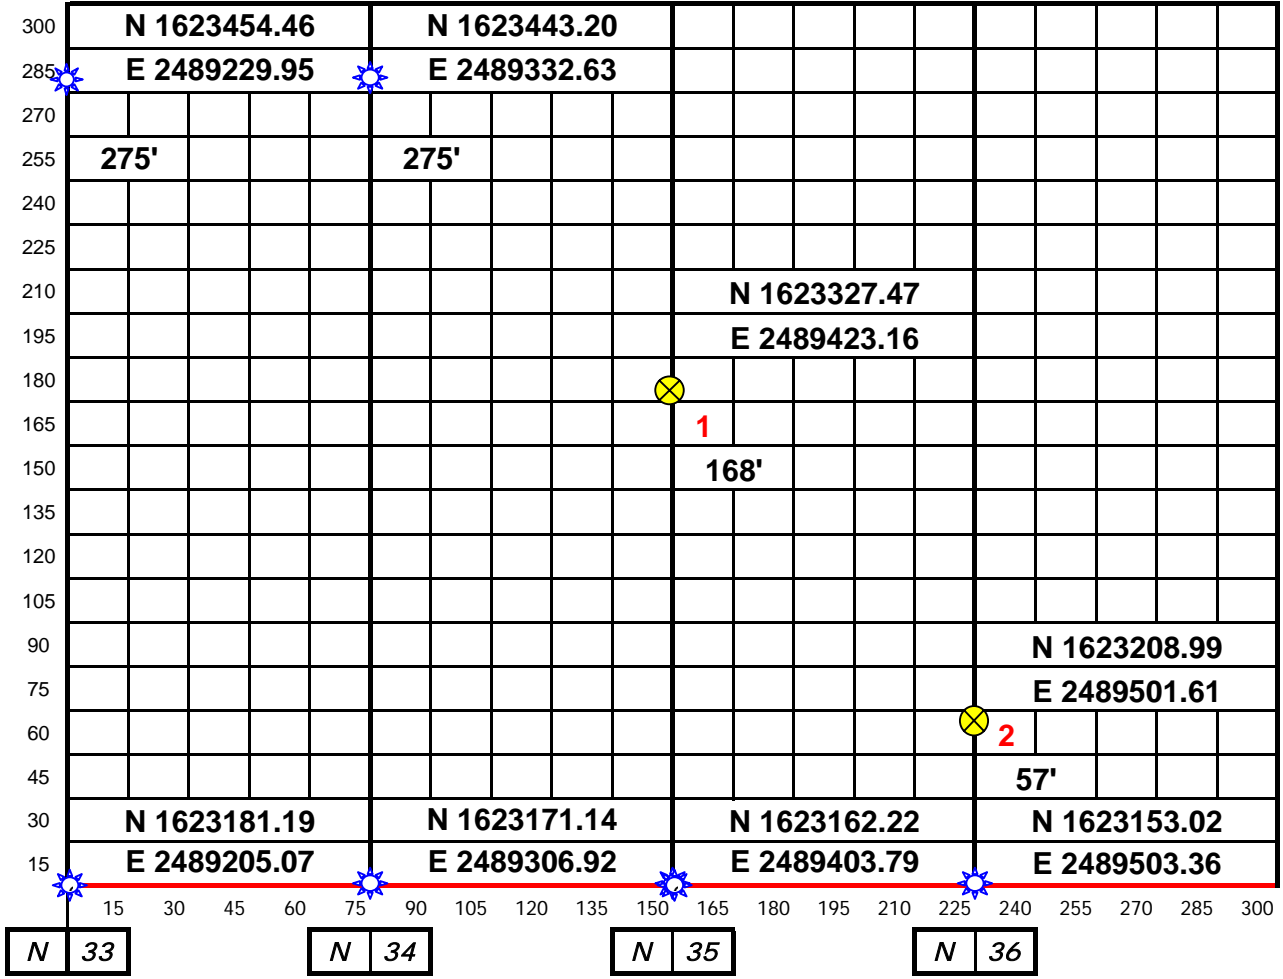

Start 4/1	Start 4/2	Start 4/2	Start 4/2
Finish 4/1	Finish 4/2	Finish 4/2	Finish 4/2
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	


Comments:

1 Fragmentation

2 Fragmentation

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/1/2009	Completion Date:	4/2/2009
QC Date:		QA Date	

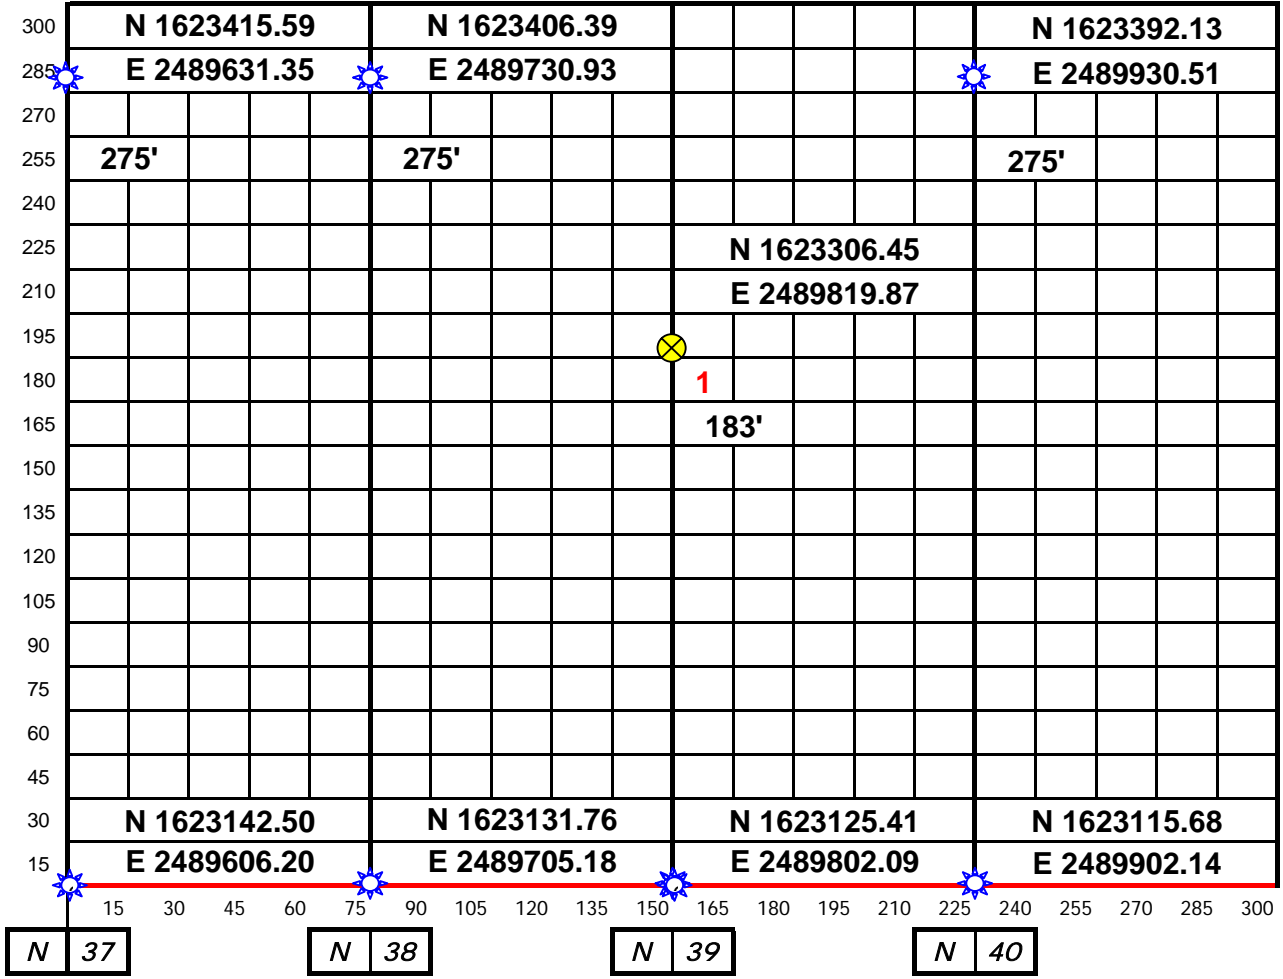


Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/2</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/2</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/2</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/1</div>
Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/2</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/2</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/2</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/1</div>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

1 Fragmentation

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/1/2009	Completion Date:	4/1/2009
QC Date:		QA Date	

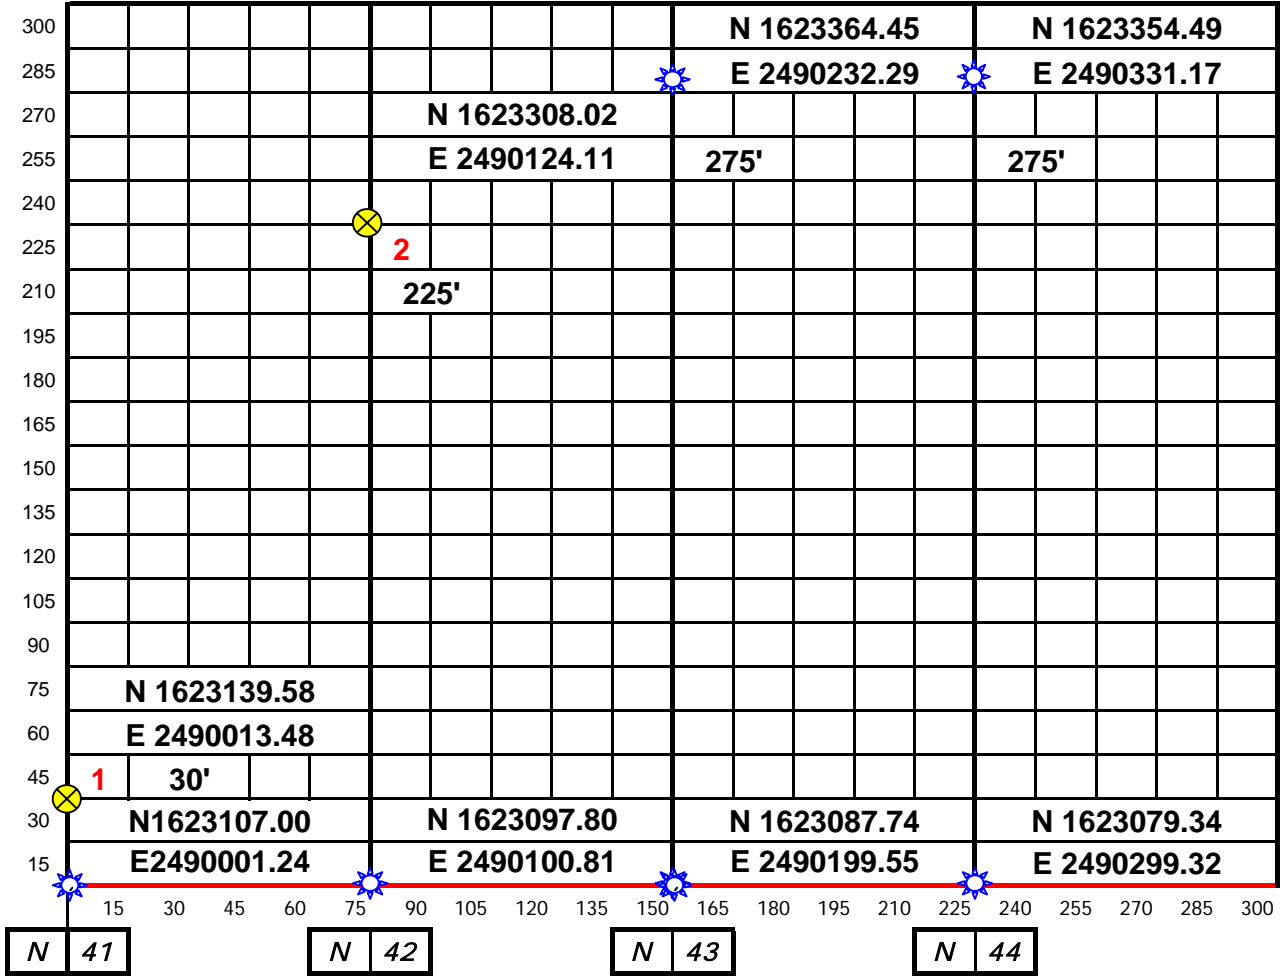

Start 4/1	Start 4/1	Start 4/1	Start 4/1
Finish 4/1	Finish 4/1	Finish 4/1	Finish 4/1
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	


Comments:

1 Fragmentation

2 Fragmentation

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/1/2009	Completion Date:	4/1/2009
QC Date:		QA Date	

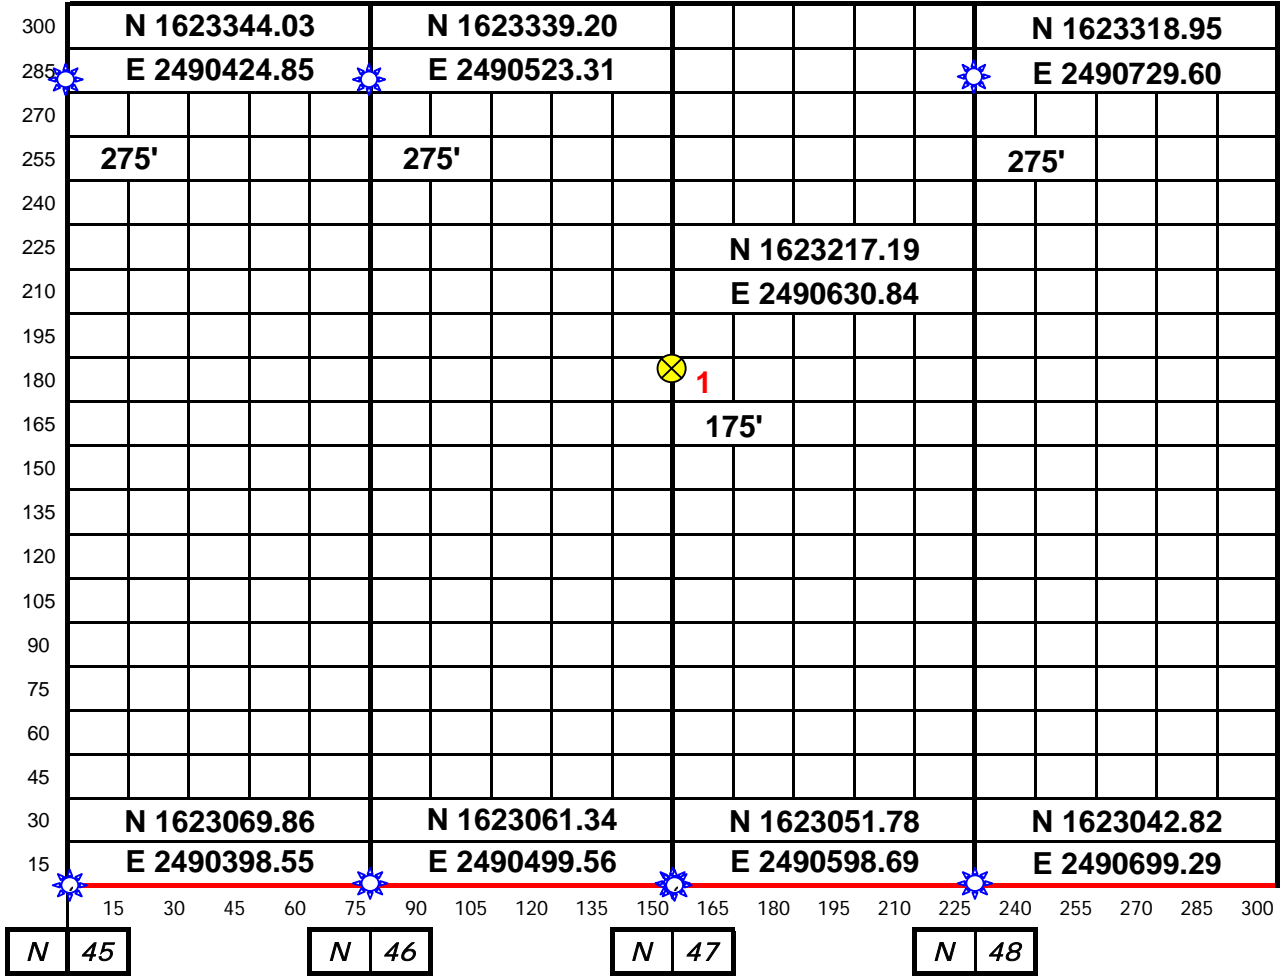


Start <input type="text" value="4/1"/>	Start <input type="text" value="4/1"/>	Start <input type="text" value="4/1"/>	Start <input type="text" value="4/1"/>
Finish <input type="text" value="4/1"/>	Finish <input type="text" value="4/1"/>	Finish <input type="text" value="4/1"/>	Finish <input type="text" value="4/1"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

1 Fragmentation

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/2/2009	Completion Date:	4/2/2009
QC Date:		QA Date	

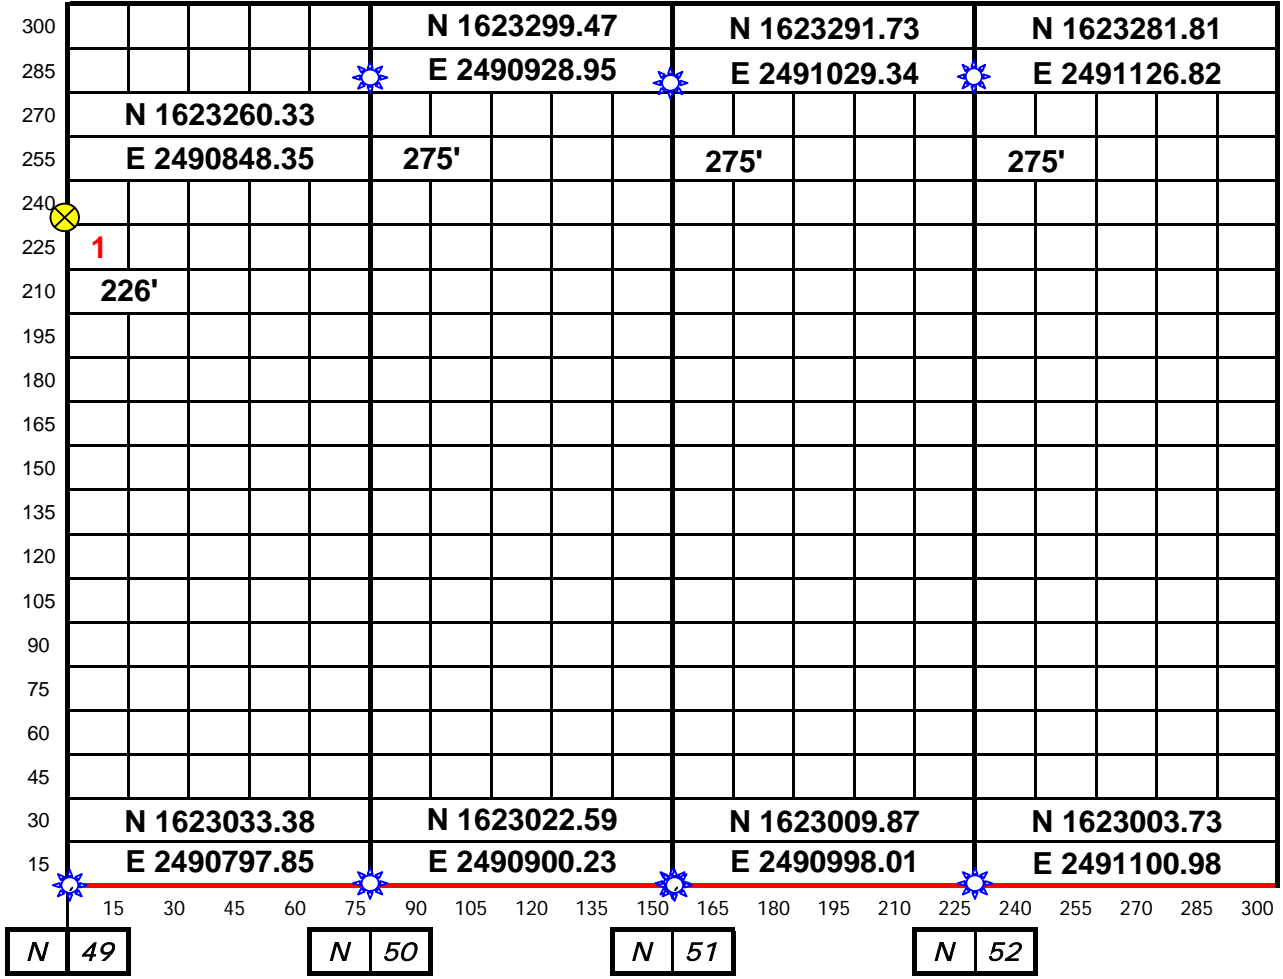


Start <input type="text" value="4/2"/>	Start <input type="text" value="4/2"/>	Start <input type="text" value="4/2"/>	Start <input type="text" value="4/2"/>
Finish <input type="text" value="4/2"/>	Finish <input type="text" value="4/2"/>	Finish <input type="text" value="4/2"/>	Finish <input type="text" value="4/2"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

1 Fragmentation

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/2/2009	Completion Date:	4/2/2009
QC Date:		QA Date	

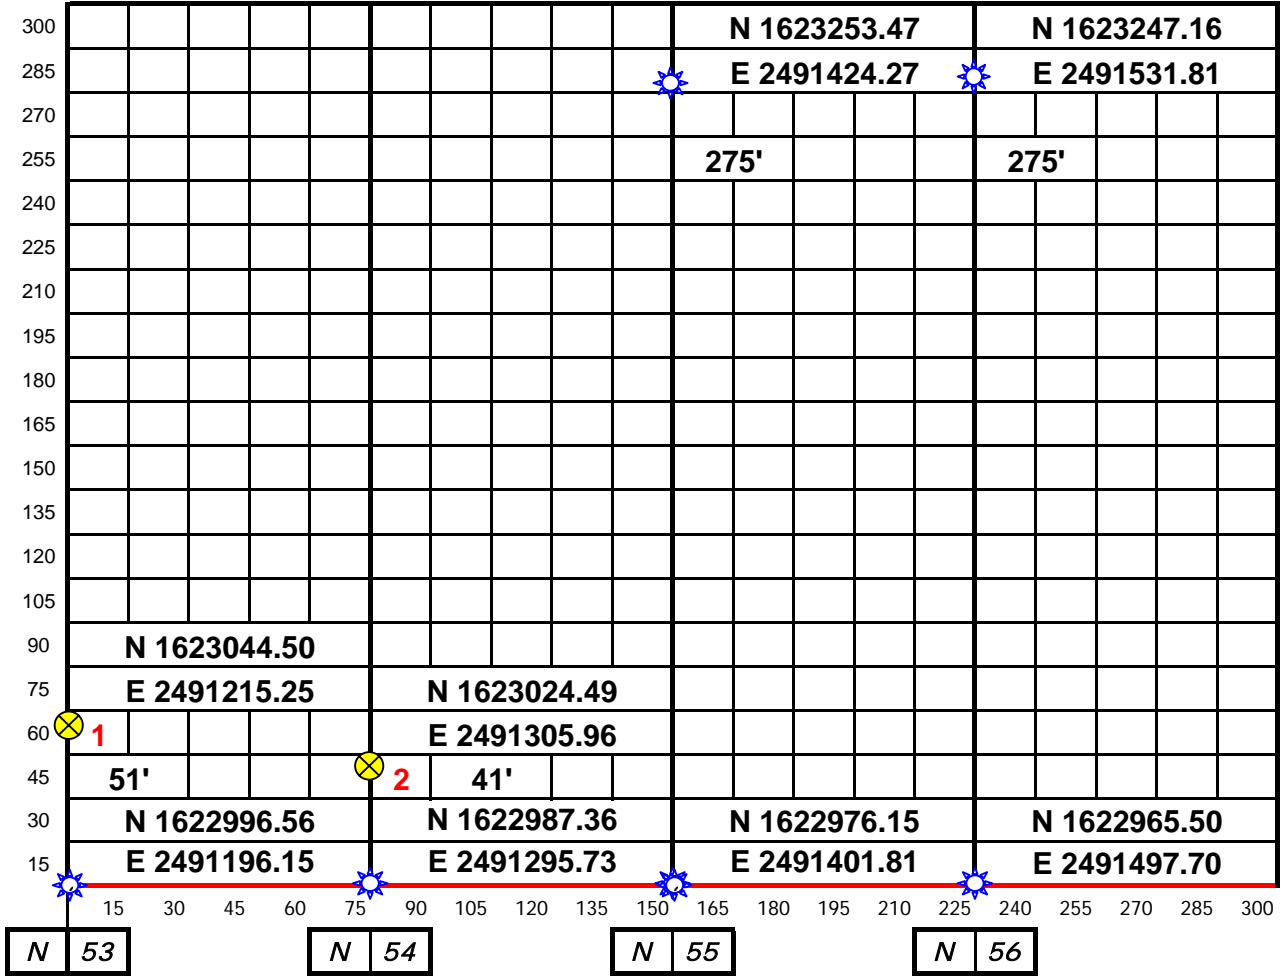

Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/2</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/2</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/2</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/2</div>
Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/2</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/2</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/2</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/2</div>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	


Comments:

1 Fragmentation

2 Fragmentation

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/2/2009	Completion Date:	4/2/2009
QC Date:		QA Date	

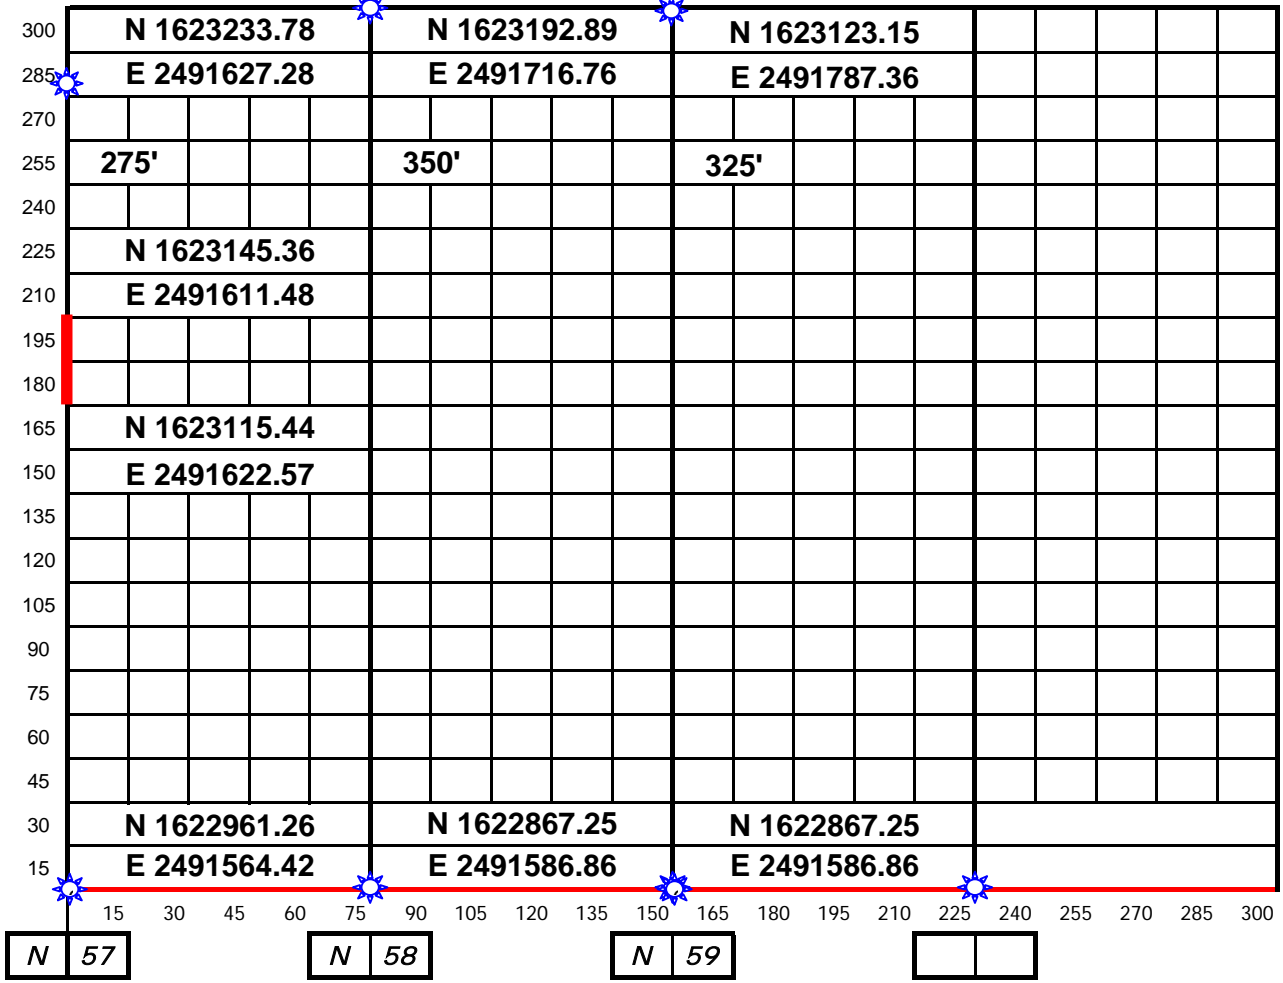


Start <input type="text" value="4/2"/>	Start <input type="text" value="4/2"/>	Start <input type="text" value="4/2"/>	Start <input type="text"/>
Finish <input type="text" value="4/2"/>	Finish <input type="text" value="4/2"/>	Finish <input type="text" value="4/2"/>	Finish <input type="text"/>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

N57 Arroyo Side Safety between 165 and 195 feet.

Fort Wingate Kick Out Delineation 2

Project	Ft Wingate Kickout Delineation	Project No.	W912BV-04--2016-DY02
Start Date:	4/20/2009	Completion Date:	4/20/2009
QC Date:		QA Date	

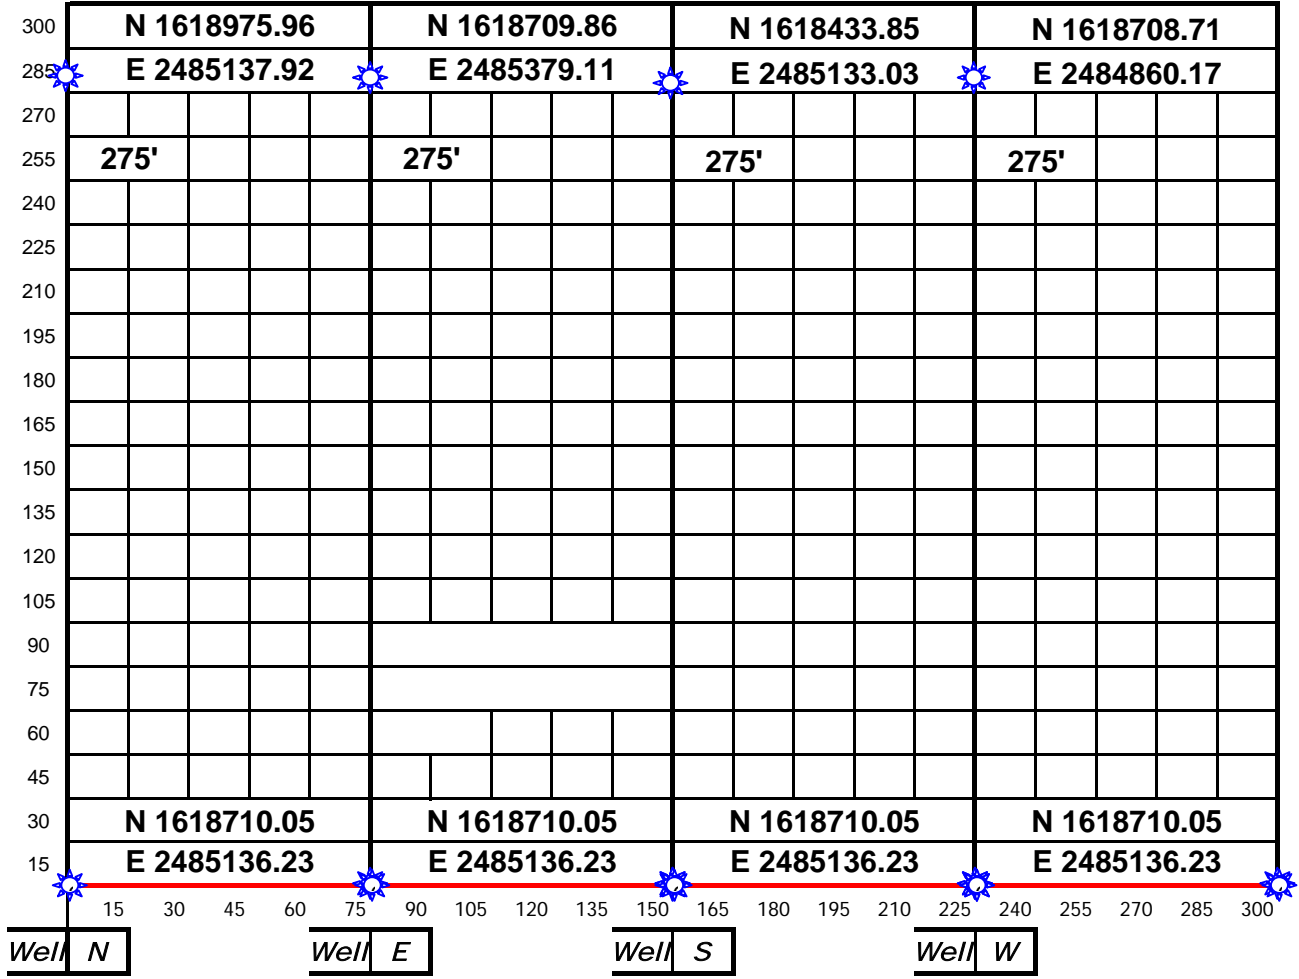

Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/20</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/20</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/20</div>	Start <div style="border: 1px solid black; padding: 2px; text-align: center;">4/20</div>
Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/20</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/20</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/20</div>	Finish <div style="border: 1px solid black; padding: 2px; text-align: center;">4/20</div>
MEC	MD	Stake	Starting Point/Ending Point
No Access/Safety	No Access/Cultural	Boundary Line	

Comments:

APPENDIX C
LIST OF TRANSECTS NOT INVESTIGATED

**U.S. ARMY CORPS OF ENGINEERS, ALBUQUERQUE DISTRICT
ORDNANCE AND EXPLOSIVE SECTION
MEMO**

To: MKM/PIKA

Date: 05/02/09

Time: 1030

Contract Number: W912BV-04-D-5 2016

**Project Location:
Fort Wingate Depot Activity**

Task Order: DY02

Subject Item(s): (Check all that apply):

- Work Plan
- Safety Violation
- Safety Comments
- Quality Control
- Other

Description: The following transects were deemed too steep and unsafe to investigate: N7,N8, N9,N10,N11, N12,N15,S35,S36,S37,S38,S39,S40,S41,S42,S43.S44,S45,S46,S47,S48,S49,S50,S51,S52,S53,S54, S55,S56,S57, S58, S59, S60, S61, S62 and W20. The following baselines were deemed too steep and unsafe to investigate: N8, N9, N10, N11, N12, N13, and N16.-----

NOTHING FOLLOWS


Prompt correction or compliance with contract specifications is requested. NO

ACTION TAKEN:



**David L. Holladay
CESWF OE Site Representative**

RECEIPT ACKNOWLEDGED:



Contractor's Representative

APPENDIX D
EXPLOSIVES ACCOUNTABILITY DOCUMENTATION

B.A.T.F. LICENSE/PERMIT #
 COONIE'S EXPLOSIVES &
 BLACK POWDER, INC.
 5-NM-025-26-8L-00163
 EXPIRES 11/1/08

UNIFORM BILL OF LADING (Not Negotiable)
COONIE'S EXPLOSIVES, INC.

P.O. BOX 2062 - 512 E. LEA
 HOBBS, NEW MEXICO 88240
 PHONE: 505 393-0166 or 393-4007 or 1-800-713-6321
 FAX 505-393-6060

EMERGENCY CONTACT
NUMBER: 1-800-255-3924

1028

Wice

S O L D T O	PIKA INTERNATIONAL INC	DATE	CUSTOMER P.O.
	12723 CAPRICORN DR, Suite 500	6-20-08	PO. - 0812137-005
	STAFFARD, TEXAS. 77477		Dewey Thed Ford
	Phone 340-5525 Fax 340-5595		Fed. Lic. # 5TX-157-33-81-01096
		Expires Sept. 1 2008 #33 USER H.E.	BATF-5400.4

No. pkg.	Quantity	Description, Brand & Size	Date Code	Price	I.D.	Price Ext.
1.	Bgs.	Blasting Agent 50 lb. Bags Ammonium Nitrate - W/Fuel Oil (ANFO)				
2.						
3.	Cs	Cord, Dentonating, 1.4D, UN0289, PGII, Explosive 1.4D, Ex #9202035				
4.						
5.	(30M Rolls)	Cord, Igniter, 1.4G, UN0066 PGII, Explosive 1.4G (Thermalite) EX #9512031				
6.	(100M Rolls)	Fuse, Igniter, 1.4G, UN0103 PGII, Explosive 1.4G (Mantitor) EX #8409080				
7.						
8.	Cs	Fuse, Safety, 1.4S, UN0105 PGII, Explosive 1.4S, Ex #9201092				
9.						
10.	Bx.	Detonators, Non Electric, For Blasting, 1.4B, UN0267, PGII Explosive 1.4B, Ex #8511062 (Mantespo #8 Fuse Caps)				
11.	2 BX.	80 only - Davey Dets - Electric - Blasting CAPS - 10.00 each.				800.00
12.		0-delay - SR - Seismic				
13.		Mfg. By Davey Bickford, SMC.				
14.		(16 FEB 1999)				
15.		Detonators Electric For Blasting			Pkg. Prep	20.00
16.		1.4S UN0456, Pg. II				
17.		Explosives 1.4S, EX. # 8409384			UPS/P & H/C.O.D.	40.00
18.					UPS HAZ. CHG	24.00
19.					3% HAZ OPER. CHG.	3.50
20.					DECLARED VALUE	3887.50
21.					TOTAL DUE	887.50

SHIP TO:
 Fort Wingate Army Depot - Bldg. 1-7 mi.
 East of Gallup - Historic Rt. 66
 Fort Wingate, N.M. 87316

ATTN: Dewey Thed Ford

Wire In Rec. 6/27/08

All notified Dewey
This will be shipped Mon. 6/27/08

UPS (TX) 874-7E2 UPS (NM) 792-442 RPS 682-171 C.O.D. - Pre-pd. - Bill to

0346312124# ZONE

(1 Fibreboard Box) X 6 lbs.

(Box size:) 12" X 12" X 8"

On book
 On card
 M.S.D.S Enclosed

OUR TERMS ARE NET - 30 DAYS

Purchaser agrees to a finance charge of 1.5% per month and to pay collection costs, including Attorney's fee. Title passes only upon full payment. No warranty, merchantability shall apply to this material. Purchaser hereby states that purchaser fully understands the proper handling and use of the explosives listed above and agrees to hold harmless and absolve the Coonie's Explosives and Black Powder, Inc. and suppliers from legal actions that may arise from use and handling of above explosive products being released to purchasers care and custody.

This is to certify that the above named articles are properly classified, described, packaged, marked and labeled and are in proper condition for transportation according to the applicable regulations of the Department of Transportation.

In case of an Emergency Call: 1-800-255-3924

Consignee X _____

INVOICES PAYABLE TO: **COONIE'S EXPLOSIVES, INC.**
 P.O. Box 2062
 Hobbs, NM 88240

Shipped By *ASR* Date *6-30-08* *Doc.* *Oh 6-20*

EXP.

INBOUND shipment TO Ft WINGATE 7-9-52
received by S WARDLE & D THEO FEED
Quantity is correct

copy (MIBAWD skymant TO FT(WASTE 6-25-08)
 RECEIVED BY S. WARDLE & D. THE D FARD 1029
 QUANTITY IS CORRECT

Freight Bill Number: 379953294 RO TNBR Number: DATE: 06/23/2008

Shipper: OWEN OIL TOOL 12001 COUNTY ROAD 1000 GODLLEY TX 76044-3141 US

Consignee: PIKA INTERNATIONAL FORT WINGATE ARMY DEPOT HISTOCIRC RT 66 FORT WINGATE NM 87316 US

Trailer # 2300216

PIECES	HU	HM	DESCRIPTION	WGT(LBS)	MMFC	PCF CLASS	RATE	TOTAL CHARGES
1	X		1-817-396-4570 :SHIP PHONE # CTN, CHARGES, SHAPED, COMMERCIAL CHARGES 1.45, UN0441, PGII PALLET WEIGHT EMERGENCY CONTACT: 800.424.930 HAZARDOUS MATERIAL CHARGE FUEL SURCHG LTL SHPT23.50%	31		085		
1			PREPAID - WILL INVOICE	51				0.00

Delv. Driver & #: *158797*

Date: 6-25-08 Arrive: *1114* Depart: *158797*

of Skids: 1 # of Pcs: OS&D #:

Received by: *THANK YOU!*

Shipment received in apparent good order with wrap intact unless otherwise noted.

Over Damage Exceptions:

Short Wrap Broken

Bill of Lading Number 1303128

P.O. Number

Page 1 of 1

FedEx Freight

P.O. BOX 649002 SAN JOSE, CA 95164 fedex.com 1.866.393.4585

LONG-HAUL RELIABILITY

CONSIGNEE DELIVERY RECEIPT

1029

FOR CHEMICAL EMERGENCY
Spill, Leak, Fire, Exposure or Accident
CALL CHEMTREC
800-424-9300

WESTERN EXPLOSIVES SYSTEMS COMPANY
6875 SOUTH 900 EAST
MIDVALE, UTAH 84047
(801) 484-6557
(801) 884-6871



A Dyno Nobel Distributor

WO:36930

1 Clarkdale BATF 9-AZ-019-20-7D-11321
1 Rillitto BATF 9-AZ-019-20-7D-00205

1 Ft. Wingate BATF 5-NM-006-20-6A-12063
1 P&M BATF 5-NM-031-20-5L-12061

WESCO

TO: <i>PIKA</i>	Shipping date: <i>07 01 08</i>	Customer P.O. NO. <i>0812132 003</i>
ATF#	ROUTE PLAN: <i>1 40 WEST TO EX-11</i>	
FROM: <i>WESCO GRANTS MILAN</i>	RETURN ROUTE PLAN:	

SHIPPING DESCRIPTION	Shipped		Returned		TYPE PKGS.	IDENT. NO. EXEM DOT-E
	NO. PKGS.	NET EXPL CONTENT	NO. PKGS.	NET EXPL CONTENT		
Explosive, blasting, type A	1.1D	UN 0081	II			
Boosters	1.1D	UN 0042	II	1		
Explosive, blasting, type E	1.1D	UN 0241	II			
Cord, detonating	1.1D	UN 0065	II	1		
Detonators, electric	1.1B	UN 0030	II			
Detonators, non-electric	1.1B	UN 0029	II			
Detonator assemblies, non-electric	1.1B	UN 0360	II			
Detonators, electric	1.4B	UN 0255	II			
Detonator assemblies, non-electric	1.4B	UN 0361	II			
Articles, explosives, N.O.S.	1.4S	UN 0349	II			
Explosives, blasting, type B	1.5D	UN 0331	II			
Explosives, blasting, type E	1.5D	UN 0332	II			
Ammonium nitrate-fuel oil mixture	1.5D	NA 0331	II			
Oxidizing, liquid, N.O.S. (Ammonium nitrate)	5.1	UN 3139	III			
Diesel Fuel	3	UN 1202	III			
Ammonium nitrate	5.1	UN 1942	III			

This is to certify that the above named materials are properly classified, described, packaged, marked and labeled and are in proper condition for transportation according to the applicable regulation of the department of transportation

SHIPPER'S SIGNATURE *[Signature]*

This shipment is within limitations prescribed for cargo aircraft.

Buyer assumes all risk and liability for results obtained by the use of the material covered by this order. Buyer acknowledges that there may be federal, and/or state laws regulating the use and/or possession of the material covered by this order and buyer assumes full responsibility for compliance with said laws.

WESCO CODE	COMPANY PRODUCT DESCRIPTION	CODE DATE	QTY SHIPPED	QTY RETURNED	QTY SOLD
	<i>Austin Black (4) Boosters</i>	<i>09AP08</i>	<i>50</i>		<i>50</i>
	<i>PRIMA LINE 21 100 gr 1/4</i>	<i>165E04</i>	<i>1606'</i>		<i>1600'</i>

Mileage *50* Standby

We certify that the above articles were received in good condition. I will heed the IMA recommendations and warnings on the use and handling of explosives.

COSIGNEE-RECEIVER

DATE

7-1-08

copy

INBOUNDS shipment to FT WALKER 7-1-08
RECEIVED BY S. WARD & D. THELFORD
QUANTITY IS CORRECT



Fort Wingate

Weekly Explosive Inventory

Magazine B-1028

Date:
7/3/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Detonators, Electric, Non-delay	80	80	0	0	80

Inventories This Month:	
Date	Personnel
07/03/08	Scott Wardell John Clifford

Dewey Thedford
Site Manager, FWADA



Fort Wingate

Weekly Explosive Inventory

Magazine B-1028

Date:
7/11/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Detonators, Electric, Non-delay	0	80	0	0	80

<u>Inventories This Month:</u>	
Date	Personnel
07/03/08	Dewey Thedford Scott Wardell
07/11/08	Scott Wardell John Clifford

Dewey Thedford
Site Manager, FWADA



Fort Wingate Weekly Explosive Inventory Magazine B-1028

Date:
7/17/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Detonators, Electric, Non-delay	0	80	0	0	80

Inventories This Month:			
Date	Personnel		
07/09/08	Dewey Thedford	Scott Wardell	
07/11/08	Scott Wardell	John Clifford	
07/17/08	John Reott	Dewey Thedford	

 Dewey Thedford
 Site Manager, FWADA



Fort Wingate Weekly Explosive Inventory Magazine B-1028

Date:
7/24/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Detonators, Electric, Non-delay	0	80	0	0	80

Inventories This Month:		
Date	Personnel	
07/09/08	Dewey Thedford	Scott Wardell
07/11/08	Scott Wardell	John Clifford
07/17/08	John Reott	Dewey Thedford
07/24/08	John Reott	Tom Knapp/USACOE

Dewey Thedford
Site Manager, FWADA



Fort Wingate
Weekly Explosive Inventory
Magazine B-1028

Date:
7/31/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Detonators, Electric, Non-delay	0	80	0	0	80

Inventories This Month:

Date	Personnel
07/09/08 Dewey Thedford	Scott Wardell
07/11/08 Scott Wardell	John Clifford
07/17/08 John Reott	Dewey Thedford
07/24/08 John Reott	Tom Knapp/USACOE
07/31/08 John Reott	Cameron Wenzel

Dewey Thedford
Site Manager, FWADA




Fort Wingate Weekly Explosive Inventory Magazine B-1028

Date:
8/7/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Detonators, Electric, Non-delay	0	80	0	0	80

Inventories This Month:		
Date	Personnel	
08/07/08	Dewey Thedford	John Reott



 Dewey Thedford
 Site Manager, FWADA



Fort Wingate Weekly Explosive Inventory Magazine B-1028

Date:
8/14/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Detonators, Electric, Non-delay	0	80	0	0	80

Inventories This Month:

Date	Personnel	
08/07/08	Dewey Thedford	John Reott
08/14/08	Dewey Thedford	John Reott

Dewey Thedford
Site Manager, FWADA



Fort Wingate Weekly Explosive Inventory Magazine B-1028

Date:
8/21/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Detonators, Electric, Non-delay	0	80	0	0	80

Inventories This Month:		
Date	Personnel	
08/07/08	Dewey Thedford	John Reott
08/14/08	Dewey Thedford	John Reott
08/21/08	Dewey Thedford	John Reott

Dewey Thedford
Site Manager, FWADA



Fort Wingate

Weekly Explosive Inventory

Magazine B-1028

Date:
8/28/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Detonators, Electric, Non-delay	0	80	0	0	80

Inventories This Month:		
Date	Personnel	
08/07/08	Dewey Thedford	John Reott
08/14/08	Dewey Thedford	John Reott
08/21/08	Dewey Thedford	John Reott
08/28/08	Dewey Thedford	John Reott

Dewey Thedford
Site Manager, FWADA



Fort Wingate

Weekly Explosive Inventory

Magazine B-1028

Date:
9/5/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Detonators, Electric, Non-delay	0	80	0	0	80

Inventories This Month:		
Date	Personnel	
09/05/08	Dewey Thedford	John Reott

Dewey Thedford
Site Manager, FWADA



Fort Wingate

Weekly Explosive Inventory

Magazine B-1028

Date:
9/11/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Detonators, Electric, Non-delay	0	80	0	0	80

Inventories This Month:		
Date	Personnel	
09/05/08	Dewey Thedford	John Reott
09/11/08	Dewey Thedford	John Reott

Dewey Thedford
Site Manager, FWADA



Fort Wingate Weekly Explosive Inventory Magazine B-1028

Date:
9/18/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Detonators, Electric, Non-delay	0	80	0	0	80

Inventories This Month:

Date	Personnel	
09/05/08	Dewey Thedford	John Reott
09/11/08	Dewey Thedford	John Reott
09/18/08	Dewey Thedford	John Reott

Dewey Thedford
Site Manager, FWADA



Fort Wingate Weekly Explosive Inventory Magazine B-1028

Date:
9/25/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Detonators, Electric, Non-delay	0	80	0	0	80
					0
Items shipped to Camp Bonneville by R&R Trucking					

Inventories This Month:

Date	Personnel	
09/05/08	Dewey Thedford	John Reott
09/11/08	Dewey Thedford	John Reott
09/18/08	Dewey Thedford	John Reott
09/25/08	Dewey Thedford	John Reott

Dewey Thedford
Site Manager, FWADA



Fort Wingate

Weekly Explosive Inventory

Magazine B-1029

Date:
6/26/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Charges, Shaped, Commercial 19Gr	50	50	0	0	50

Inventories This Month:

Date	Personnel	
06/26/08	Dewey Thedford	Scott Wardle

Dewey Thedford
Site Manager, FWADA




Fort Wingate
Weekly Explosive Inventory
Magazine B-1029

Date:
7/3/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Detonating Cord, 100 Gr	1600	1600'	0	0	1600'
Boosters, 3/4 Lb, Black Cap	50	50	0	0	50
Charges, Shaped, Commercial 19 Gr	0	50	0	0	50

Inventories This Month:		
Date	Personnel	
07/03/08	Dewey Thedford	Scott Wardell



Dewey Thedford
Site Manager, FWADA



Fort Wingate

Weekly Explosive Inventory

Magazine B-1029

Date:
7/11/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Detonating Cord, 100 Gr	0	1600'	0	0	1600'
Boosters, 3/4 Lb, Black Cap	0	50	0	0	50
Charges, Shaped, Commercial 19 Gr	0	50	0	0	50

Inventories This Month:	
Date	Personnel
07/03/08	Dewey Thedford Scott Wardell
07/11/08	Scott wardell John Clifford

Dewey Thedford
Site Manager, FWADA



Fort Wingate

Weekly Explosive Inventory

Magazine B-1029

Date:
7/17/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Detonating Cord, 100 Gr	0	1600'	0	0	1600'
Boosters, 3/4 Lb, Black Cap	0	50	0	0	50
Charges, Shaped, Commercial 19 Gr	0	50	0	0	50

Inventories This Month:		
Date	Personnel	
07/01/08	Dewey Thedford	Scott Wardell
07/11/08	Scott Wardell	John Clifford
07/17/08	John Reott	Dewey Thedford

Dewey Thedford
Site Manager, FWADA



Fort Wingate

Weekly Explosive Inventory

Magazine B-1029

Date:
7/24/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Detonating Cord, 100 Gr	0	1600'	0	0	1600'
Boosters, 3/4 Lb, Black Cap	0	50	0	0	50
Charges, Shaped, Commercial 19 Gr	0	50	0	0	50

Inventories This Month:		
Date	Personnel	
07/01/08	Dewey Thedford	Scott Wardell
07/11/08	Scott Wardell	John Clifford
07/17/08	John Reott	Dewey Thedford
07/24/08	John Reott	Tom Knapp/USACOE

Dewey Thedford
Site Manager, FWADA




Fort Wingate
Weekly Explosive Inventory
Magazine B-1029

Date:
 7/31/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Detonating Cord, 100 Gr	0	1600'	0	0	1600'
Boosters, 3/4 Lb, Black Cap	0	50	0	0	50
Charges, Shaped, Commercial 19 Gr	0	50	0	0	50

<u>Inventories This Month:</u>		
<u>Date</u>	<u>Personnel</u>	
07/01/08	Dewey Thedford	Scott Wardell
07/11/08	Scott Wardell	John Clifford
07/17/08	John Reott	Dewey Thedford
07/24/08	John Reott	Tom Knapp/USACOE
07/31/08	John Reott	Cameron Wenzel



 Dewey Thedford
 Site Manager, FWADA



Fort Wingate Weekly Explosive Inventory Magazine B-1029

Date:
8/7/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Detonating Cord, 100 Gr	0	1600'	0	0	1600'
Boosters, 3/4 Lb, Black Cap	0	50	0	0	50
Charges, Shaped, Commercial 19 Gr	0	50	0	0	50

Inventories This Month:		
Date	Personnel	
08/07/08	Dewey Thedford	John Reott

 Dewey Thedford
 Site Manager, FWADA



Fort Wingate Weekly Explosive Inventory Magazine B-1029

Date:
8/14/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Detonating Cord, 100 Gr	0	1600'	0	0	1600'
Boosters, 3/4 Lb, Black Cap	0	50	0	0	50
Charges, Shaped, Commercial 19 Gr	0	50	0	0	50

Inventories This Month:

Date	Personnel	
08/07/08	Dewey Thedford	John Reott
08/14/08	Dewey Thedford	John Reott

Dewey Thedford
Site Manager, FWADA



Fort Wingate


Weekly Explosive Inventory

Magazine B-1029

Date:
8/21/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Detonating Cord, 100 Gr	0	1600'	0	0	1600'
Boosters, 3/4 Lb, Black Cap	0	50	0	0	50
Charges, Shaped, Commercial 19 Gr	0	50	0	0	50

Inventories This Month:		
Date	Personnel	
08/07/08	Dewey Thedford	John Reott
08/14/08	Dewey Thedford	John Reott
08/21/08	Dewey Thedford	John Reott



Dewey Thedford
Site Manager, FWADA



Fort Wingate

Weekly Explosive Inventory

Magazine B-1029

Date:
8/28/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Detonating Cord, 100 Gr	0	1600'	0	0	1600'
Boosters, 3/4 Lb, Black Cap	0	50	0	0	50
Charges, Shaped, Commercial 19 Gr	0	50	0	0	50

Inventories This Month:		
Date	Personnel	
08/07/08	Dewey Thedford	John Reott
08/14/08	Dewey Thedford	John Reott
08/21/08	Dewey Thedford	John Reott
08/28/08	Dewey Thedford	John Reott

Dewey Thedford
Site Manager, FWADA



Fort Wingate Weekly Explosive Inventory Magazine B-1029

Date:
9/5/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Detonating Cord, 100 Gr	0	1600'	0	0	1600'
Boosters, 3/4 Lb, Black Cap	0	50	0	0	50
Charges, Shaped, Commercial 19 Gr	0	50	0	0	50

<u>Inventories This Month:</u>		
Date	Personnel	
09/05/08	Dewey Thedford	John Reott

Dewey Thedford
Site Manager, FWADA




Fort Wingate
Weekly Explosive Inventory
Magazine B-1029

Date:
9/11/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Detonating Cord, 100 Gr	0	1600'	0	0	1600'
Boosters, 3/4 Lb, Black Cap	0	50	0	0	50
Charges, Shaped, Commercial 19 Gr	0	50	0	0	50

Inventories This Month:		
Date	Personnel	
09/05/08	Dewey Thedford	John Reott
09/11/08	Dewey Thedford	John Reott



Dewey Thedford
Site Manager, FWADA



Fort Wingate Weekly Explosive Inventory Magazine B-1029

Date:
9/18/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Detonating Cord, 100 Gr	0	1600'	0	0	1600'
Boosters, 3/4 Lb, Black Cap	0	50	0	0	50
Charges, Shaped, Commercial 19 Gr	0	50	0	0	50

Inventories This Month:

Date	Personnel	
09/05/08	Dewey Thedford	John Reott
09/11/08	Dewey Thedford	John Reott
09/18/08	Dewey Thedford	John Reott

Dewey Thedford
Site Manager, FWADA



Fort Wingate Weekly Explosive Inventory Magazine B-1029

Date:
9/25/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Detonating Cord, 100 Gr	0	1600'	0	0	0
Boosters, 3/4 Lb, Black Cap	0	50	0	0	0
Charges, Shaped, Commercial 19 Gr	0	50	0	0	0
Items shipped to Camp Bonneville by R&R Trucking					

Inventories This Month:

Date	Personnel	
09/05/08	Dewey Thedford	John Reott
09/11/08	Dewey Thedford	John Reott
09/18/08	Dewey Thedford	John Reott
09/25/08	Dewey Thedford	John Reott

Dewey Thedford
Site Manager, FWADA



Fort Wingate Weekly Explosive Inventory Magazine B-1038

Date:
6/26/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Pistol Flare	1	1	0	0	1
M-9 Smoke Cannisters	1	1	0	0	1
Grenade Fuse	2	2	0	0	2
M-120 Fuse	3	3	0	0	3

Inventories This Month:

Date	Personnel
06/26/08	Dewey Thedford Scott Wardel

Dewey Thedford
Site Manager, FWADA



Fort Wingate Weekly Explosive Inventory Magazine B-1038

Date:
7/3/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Pistol Flare	0	1	0	0	1
M-9 Smoke Cannisters	1	2	0	0	2
Grenade Fuse	0	2	0	0	2
M-120 Fuse	4	7	0	0	7

Inventories This Month:

Date	Personnel
07/03/08	Dewey Thedford Scott Wardel

Dewey Thedford
Site Manager, FWADA



Fort Wingate Weekly Explosive Inventory Magazine B-1038

Date:
7/11/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Pistol Flare	0	1	0	0	1
M-9 Smoke Canisters	1	3	0	0	3
Grenade Fuse	0	2	0	0	2
M-120 Fuse	5	12	0	0	12

Inventories This Month:

Date	Personnel	
07/03/08	Dewey Thedford	Scott Wardell
07/11/08	Scott Wardell	John Clifford

 Dewey Thedford
 Site Manager, FWADA



Fort Wingate Weekly Explosive Inventory Magazine B-1038

Date:
7/17/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Pistol Flare	0	1	0	0	1
M-9 Smoke Canisters	13	16	0	0	16
Grenade Fuse	0	2	0	0	2
M-120 Fuse	11	23	0	0	23
Impact Nose Fuse	1	1	0	0	1

Inventories This Month:

Date	Personnel	
07/03/08	Dewey Thedford	Scott Wardell
07/11/08	Scott Wardell	John Clifford
07/17/08	Dewey Thedford	Scott Wardell

Dewey Thedford
Site Manager, FWADA



Fort Wingate Weekly Explosive Inventory Magazine B-1038

Date:
7/24/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Pistol Flare	0	1	0	0	1
M-9 Smoke Canisters	0	16	0	0	16
Grenade Fuse	0	2	0	0	2
M-120 Fuse	3	26	0	0	26
Impact Nose Fuse	1	2	0	0	2
Booster	1	1	0	0	1

Inventories This Month:

Date	Personnel	
07/03/08	Dewey Thedford	Scott Wardell
07/11/08	Scott Wardell	John Clifford
07/17/08	John Reott	Dewey Thedford
07/24/08	John Reott	Tom Knapp

Dewey Thedford
Site Manager, FWADA



Fort Wingate Weekly Explosive Inventory Magazine B-1038

Date:
7/31/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Pistol Flare	0	1	0	0	1
M-9 Smoke Canisters	0	16	0	0	16
Grenade Fuse	1	3	0	0	3
M-120 Fuse	2	28	0	0	28
Impact Nose Fuse	1	3	0	0	3
Booster	0	1	0	0	1

Inventories This Month:

Date	Personnel	
07/03/08	Dewey Thedford	Scott Wardell
07/11/08	Scott Wardell	John Clifford
07/17/08	John Reott	Dewey Thedford
07/24/08	John Reott	Tom Knapp
07/31/08	John Reott	Cameron Wenzel

Dewey Thedford
Site Manager, FWADA



Fort Wingate Weekly Explosive Inventory Magazine B-1038

Date:
8/7/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Pistol Flare	0	1	0	0	1
M-9 Smoke Canisters	0	16	0	0	16
Grenade Fuse	0	3	0	0	3
M-120 Fuse	3	31	0	0	31
Impact Nose Fuse	2	5	0	0	5
Booster	0	1	0	0	1

Inventories This Month:

Date	Personnel
08/07/08	Dewey Thedford John Reott

Dewey Thedford
Site Manager, FWADA



Fort Wingate Weekly Explosive Inventory Magazine B-1038

Date:
8/14/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Pistol Flare	0	1	0	0	1
M-9 Smoke Canisters	0	16	0	0	16
Grenade Fuse	0	3	0	0	3
M-120 Fuse	0	31	0	0	31
Impact Nose Fuse	0	5	0	0	5
Booster	0	1	0	0	1

Inventories This Month:

Date	Personnel	
08/07/08	Dewey Thedford	John Reott
08/14/08	Dewey Thedford	John Reott

Dewey Thedford
Site Manager, FWADA



Fort Wingate Weekly Explosive Inventory Magazine B-1038

Date:
8/21/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Pistol Flare	0	1	0	0	1
M-9 Smoke Canisters	0	16	0	0	16
Grenade Fuse	0	3	0	0	3
M-120 Fuse	0	31	0	0	31
Impact Nose Fuse	0	5	0	0	5
Booster	0	1	0	0	1

Inventories This Month:

Date	Personnel	
08/07/08	Dewey Thedford	John Reott
08/14/08	Dewey Thedford	John Reott
08/21/08	Dewey Thedford	John Reott

Dewey Thedford
Site Manager, FWADA



Fort Wingate Weekly Explosive Inventory Magazine B-1038

Date:
8/28/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Pistol Flare	0	1	0	0	1
M-9 Smoke Canisters	0	16	0	0	16
Grenade Fuse	0	3	0	0	3
M-120 Fuse	0	31	0	0	31
Impact Nose Fuse	0	5	0	0	5
Booster	0	1	0	0	1

Inventories This Month:

Date	Personnel	
08/07/08	Dewey Thedford	John Reott
08/14/08	Dewey Thedford	John Reott
08/21/08	Dewey Thedford	John Reott
08/28/08	Dewey Thedford	John Reott

Dewey Thedford
Site Manager, FWADA



Fort Wingate
Weekly Explosive Inventory
Magazine B-1038

Date:
9/5/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Pistol Flare	0	1	0	0	1
M-9 Smoke Canisters	0	16	0	0	16
Grenade Fuse	0	3	0	0	3
M-120 Fuse	0	31	0	0	31
Impact Nose Fuse	0	5	0	0	5
Booster	0	1	0	0	1

Inventories This Month:

Date	Personnel
09/05/08	Dewey Thedford John Reott

Dewey Thedford
Site Manager, FWADA



Fort Wingate
Weekly Explosive Inventory
Magazine B-1038

Date:
9/11/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Pistol Flare	0	1	0	0	1
M-9 Smoke Canisters	0	16	0	0	16
Grenade Fuse	0	3	0	0	3
M-120 Fuse	0	31	0	0	31
Impact Nose Fuse	0	5	0	0	5
Booster	0	1	0	0	1

Inventories This Month:

Date	Personnel	
09/05/08	Dewey Thedford	John Reott
09/11/08	Dewey Thedford	John Reott

Dewey Thedford
Site Manager, FWADA



Fort Wingate Weekly Explosive Inventory Magazine B-1038

Date:
9/18/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Pistol Flare	0	1	0	0	1
M-9 Smoke Canisters	0	16	0	0	16
Grenade Fuse	0	3	0	0	3
M-120 Fuse	0	31	0	0	31
Impact Nose Fuse	0	5	0	0	5
Booster	0	1	0	0	1

Inventories This Month:

Date	Personnel	
09/05/08	Dewey Thedford	John Reott
09/11/08	Dewey Thedford	John Reott
09/18/08	Dewey Thedford	John Reott

Dewey Thedford
Site Manager, FWADA



Fort Wingate Weekly Explosive Inventory Magazine B-1038

Date:
9/25/2008

Materials	Received This Week	Received to Date	Used This Week	Used to Date	Quantity on Hand
Pistol Flare	0	1	0	0	1
M-9 Smoke Canisters	0	16	0	0	16
Grenade Fuse	0	3	0	0	3
M-120 Fuse	0	31	0	0	31
Impact Nose Fuse	0	5	0	0	5
Booster	0	1	0	0	1

Items turned over to FWDA

Inventories This Month:

Date	Personnel	
09/05/08	Dewey Thedford	John Reott
09/11/08	Dewey Thedford	John Reott
09/18/08	Dewey Thedford	John Reott
09/25/08	Dewey Thedford	John Reott

Dewey Thedford
Site Manager, FWADA

FWAD/Mike Scoville

FWAD/Mike Chee

RTR TRUCKING

(Name of carrier)

(SCAC)

On Collect on Delivery shipments, the letters "COD" must appear before consignee's name or as otherwise provided in Item 430, Sec. 1.

TO:
 Consignee CAMP BONNEVILLE (PIKA INTERNATIONAL)
 Street 23201 NE PLUSS ROAD, BLDG T-4366
 City VANCOUVER State WA Zip Code 98682
(360) 566-6985

FROM:
 Shipper FORT WINGATE ARMY DEPOT
 Street 7 MILES EAST OF GALLUP, ROUTE 66
 City FORT WINGATE State NM Zip Code 87316
 24 hr. Emergency Contact Tel. No. 1-800-424-9300

Route _____ Vehicle Number _____

No. of Units & Container Type	HM	BASIC DESCRIPTION Proper Shipping Name, Hazard Class or UN or NA Number, Packing Group or UN or NA Number, Hazard Class, Packing Group	TOTAL QUANTITY (Weight, Volume, Gallons, etc.)	WEIGHT (Subject to Correction)	RATE	CHARGES (For Carrier Use Only)
1	X	DETONATORS, NON-ELECTRIC, For BLASTING 1.4B, UN0267, PG II (ERG 114) 80 EA NEW 163 LBS	6 LBS			
1	X	BOOSTERS, 1.1D, UN0042, PG II (ERG-112) 50 EA., 37.5 NEW LBS	42 LBS			
1	X	CORD, DETONATIONS, 1.1D, UN0065, PG II, (ERG 112) 18.4 NEW LBS. 16 FT	30 LBS			
1	X	CTN CHARGES, SNAPRO COMMERCIAL, 1.4S, UN0441, PG II (ERG 114) 2.09 NEW LBS 50 EA.	31 LBS			
Rec's: FORT WINGATE: CAMPBELL WENTZ CRL 281-383-8237 REPAIR/LEGAL: 330-703-8237						

PLACARDS TENDERED: YES NO

Note — (1) Where the rate is dependent on value, shippers are required to state specifically in writing the agreed or declared value of the property, as follows: "The agreed or declared value of the property is hereby specifically stated by the shipper to be not exceeding _____ per _____."
 (2) Where the applicable tariff provisions specify a limitation of the carrier's liability absent a release or a value declaration by the shipper and the shipper does not release the carrier's liability or declare a value, the carrier's liability shall be limited to the extent provided by such provisions. See NMFC Item 172.
 (3) Commodities requiring special or additional care or attention in handling or stowing must be so marked and packaged as to ensure safe transportation. See Section 2(e) of Item 360, Bills of Lading, Freight Bills and Statements of Charges and Section 1(a) of the Contract Terms and Conditions for a list of such articles.

I hereby declare that the contents of this consignment are fully and accurately described above by the proper shipping name and are classified, packaged, marked and labeled/placarded, and are in all respects in proper condition for transport according to applicable international and national governmental regulations.

[Signature] Signature

REMIT C.O.D. TO: ADDRESS

COD

Amt: \$

Subject to Section 7 of the conditions, if this shipment is to be delivered to the consignee without recourse on the consignor, the consignor shall sign the following statement:

The carrier shall not make delivery of this shipment without payment of freight and all other lawful charges.

[Signature] (Signature of Consignor)

C.O.D. FEE: PREPAID COLLECT \$

TOTAL CHARGES \$

FREIGHT CHARGES
 FREIGHT PREPAID Check box if charges are to be collect
 except when box at right is checked

RECEIVED, subject to the classifications and tariffs in effect on the date of the issue of this Bill of Lading, the property described above in apparent good order, except as noted (contents and condition of contents of packages unknown), marked, consigned, and destined as indicated above which said carrier (the word carrier being understood throughout this contract as meaning any person or corporation in possession of the property under the contract) agrees to carry to its usual place of delivery at said destination, if on its route, otherwise to deliver to another carrier on the route to said destination. It is mutually agreed as to each carrier of all or any of, said property over all or any portion of said route to des-

tionation and as to each party at any time interested in all or any said property, that every service to be performed hereunder shall be subject to all the bill of lading terms and conditions in the governing classification on the date of shipment.

Shipper hereby certifies that he is familiar with all the lading terms and conditions in the governing classification and the said terms and conditions are hereby agreed to by the shipper and accepted for himself and his assigna.

SHIPPER PIKA INTERNATIONAL, INC

PER Dewayn M. [Signature]

CARRIER Sharon Waldon / Carl Risner

PER

DATE

3

APPENDIX E
QC TARGET LIST

**EM61-MK2 Target List
September 2008**

ID	Easting (ft)	Northing (ft)	Magnitude (mV)	Description
1	2489839.60	1623474.70	2.3	Barbed Wire
2	2489716.40	1623456.20	17.5	Multiple hot rocks and asphalt
3	2489716.60	1623407.50	3.4	Hot Rock, edge of road
4	2489903.50	1623390.50	6.3	No Contact
5	2489925.00	1623390.50	2.5	1" Wire
6	2490131.90	1623368.00	2.5	No Contact
7	2490224.70	1623367.30	2.9	No Contact
8	2490725.30	1623314.50	3.5	No Contact
9	2490728.90	1623513.60	2.7	No Contact
10	2490623.50	1623542.00	4.9	No Contact
11	2490623.40	1623598.60	2.2	No Contact
12	2490519.20	1623519.30	2.3	Benchmark
13	2490526.40	1623332.30	3.3	No Contact
14	2490426.20	1623566.60	6.4	No Contact
15	2490325.30	1623585.40	5.6	Metal Scrap
16	2490325.20	1623483.60	2.7	No Contact
17	2490326.30	1623356.00	4.7	No Contact
18	2490119.90	1623522.80	4.1	No Contact
19	2492075.79	1622646.71	7.4	Wire
20	2492134.82	1622745.52	2.8	Cable
21	2492120.47	1622745.30	8.8	Cable
22	2492164.42	1622935.35	8.1	Cable
23	2492801.48	1620015.04	6.8	4" Wire
24	2492997.72	1618600.27	2.6	Banding
25	2493045.64	1618484.49	2.6	Banding
26	2493052.47	1618482.67	3.6	Wire
27	2493155.13	1618360.43	2.1	No Contact
28	2493141.97	1618264.07	5.8	Middle of asphalt road
29	2493132.72	1618257.54	30.3	Rebar
30	2493082.34	1618162.82	1745.1	Culvert

**EM61-MK2 Target List
September 2008 (Continued)**

ID	Easting (ft)	Northing (ft)	Magnitude (mV)	Description
31	2493220.20	1617918.38	3.6	Nail
32	2493208.79	1617855.37	10.1	Wire
33	2493217.22	1617845.31	3.1	Wire
34	2493394.98	1617633.73	4.7	Small Metal
35	2493360.93	1617538.77	2.7	Barbed Wire
36	2493407.26	1617394.18	4.8	Wire
37	2493562.54	1617147.02	7.7	Soda Can
38	2492840.54	1620030.29	3.1	Tin Lid
39	2492850.56	1619224.15	2.3	No Contact
40	2492777.72	1619934.64	2.5	Nail
41	2492889.06	1619813.09	2.6	Nail
42	2492885.63	1619804.59	3.6	Banding
43	2492842.06	1619826.03	6.5	Rebar
44	2492830.62	1619831.92	81.7	Small Metal
45	2492766.82	1619828.53	2.8	Wire
46	2492728.14	1619829.40	5.5	Wire
47	2492635.04	1619750.24	10.8	Metal Can
48	2492672.94	1619614.27	3.4	4" nail
49	2492987.60	1619438.49	7.4	Banding
50	2485485.67	1615739.96	3.1	Bolt
51	2485472.62	1615672.25	2.7	Screw
52	2485409.71	1615291.92	3.5	Tin Lid
53	2485441.66	1614996.53	4.7	Pop Top
54	2485443.02	1614983.01	2.7	Barbed Wire
55	2485429.94	1614664.86	4.0	Piece of Chain Link
56	2485427.66	1614403.03	2.4	No Contact
57	2485312.23	1614150.86	3.7	Barbed Wire
58	2485179.17	1614044.42	4.1	Nail
59	2485157.90	1613970.37	2.5	No Contact
60	2485191.92	1613968.27	3.9	Barbed Wire

**EM61-MK2 Target List
September 2008 (Continued)**

ID	Easting (ft)	Northing (ft)	Magnitude (mV)	Description
61	2485263.57	1613990.89	2.6	Nail
62	2485272.66	1613993.83	2.9	Barbed Wire
63	2485331.30	1613996.01	4.0	Soda Can
64	2485368.77	1613994.86	12.8	Sardine can
65	2485552.70	1613728.67	29.3	Rebar
66	2485546.70	1613694.87	4.8	Nail
67	2485577.02	1613584.35	2.9	Staple
68	2485536.50	1613437.78	2.9	Staple
69	2485520.29	1613402.67	96.6	Paint Can
70	2485559.44	1613295.42	20.2	Soup Can
71	2485567.22	1613263.52	11.4	Hot Rock
72	2485556.45	1613211.63	47.1	Hand trowel
73	2485535.15	1613190.61	10.7	Chain Link
74	2485540.53	1613009.24	3.0	Pop Top
75	2485569.72	1612714.55	3.0	Staple
76	2485528.42	1612682.47	2.7	Drill Bit
April-2009				
77	2490009.08	1623337.22	6.5	GPO
78	2490058.00	1623330.21	14.6	GPO
79	2490458.80	1623304.69	3.6	Wire
80	2490613.70	1623288.74	1.6	0.1 lb Aluminum
81	2490838.68	1623279.94	1.8	0.2 lb Aluminum
82	2490958.52	1623270.89	11.0	0.5 lb Spike
83	2486226.03	1618962.71	5.1	Metal Debris
84	2486203.18	1619068.48	4.3	1 lb Frag
85	2486203.91	1619095.17	1.6	Wire
86	2486204.22	1619125.51	16.7	Wire
87	2486203.90	1619156.52	2.0	0.1 lb Frag
88	2486205.98	1619184.10	20.4	1 lb Frag
89	2486207.91	1619207.53	23.7	2 lb fFrag

**EM61-MK2 Target List
April 2009 (Continued)**

ID	Easting (ft)	Northing (ft)	Magnitude (mV)	Description
90	2486228.07	1619515.83	2.7	0.1 lb Frag
91	2486234.15	1619586.08	6.4	0.1 lb Frag
92	2486236.19	1619604.64	3.7	0.1 lb Frag
93	2486237.49	1619617.98	4.3	0.5 lb frag
94	2486238.89	1619633.21	4.4	0.1 lb Frag
95	2486254.82	1619773.25	4.1	Barb Wire
96	2495407.38	1609578.01	30.3	Buried Cable
97	2485855.33	1611232.25	6.0	Wire
98	2485869.81	1611305.82	2.1	3 lb MD
99	2485874.80	1611369.71	10.0	Metal Can
100	2485794.66	1611513.88	5.1	Wire
101	2485786.17	1611524.82	18.3	0.5 lb MD
102	2485877.84	1611829.00	6.9	Bolt
103	2485865.83	1611934.44	41.7	2 lb MD
104	2485854.26	1612130.12	33.2	2 lb MD
105	2485851.90	1612138.74	3.5	0.5 lb MD
106	2485835.96	1612200.02	3.4	0.5 lb MD
107	2485833.17	1612255.51	28.9	Barb Wire
108	2485830.43	1612269.19	2.0	0.5 lb MD
109	2485824.52	1612303.39	98.2	0.5 lb MD
110	2485822.54	1612311.01	7.9	0.5 lb MD
111	2485790.99	1612395.98	8.5	Nail
112	2485778.74	1612486.79	3.6	0.5 lb MD
113	2485765.45	1612556.34	13.7	0.5 lb MD
114	2485760.62	1612563.56	2.0	0.5 lb MD
115	2485729.42	1612747.63	5.6	Aluminum Can
116	2485735.35	1612804.15	5.5	0.5 lb MD
117	2485735.66	1612943.32	43.1	0.5 lb MD
118	2486219.93	1618790.19	2.2	0.5 lb MD
119	2486219.56	1618887.14	4.6	0.5 lb MD

**EM61-MK2 Target List
April 2009 (Continued)**

ID	Easting (ft)	Northing (ft)	Magnitude (mV)	Description
120	2486218.64	1618892.70	7.9	Barb Wire
121	2486216.26	1618903.17	6.0	Wire
122	2486222.28	1618988.40	2.5	Barb Wire
123	2486221.68	1619050.55	13.5	Barb Wire
124	2486228.55	1619238.61	8.1	Fencing Material
125	2486234.47	1619380.45	6.8	Wire
126	2486259.26	1619726.64	16.4	Horseshoe
127	2486271.58	1619896.45	8.6	0.5 lb MD
128	2486281.70	1620010.32	22.8	Wire
129	2486264.96	1619892.20	4.5	Wire
130	2486249.81	1619796.99	2.0	0.5 lb MD
131	2486241.45	1619735.03	4.2	0.5 lb MD
132	2486178.50	1619435.86	2.3	Wire
133	2486174.44	1619398.94	8.4	Nail
134	2486167.79	1619346.12	5.2	Nail
135	2486166.50	1619339.03	2.5	Fence Staple
136	2486117.78	1619003.57	10.1	0.5 lb MD
137	2486124.42	1618834.51	19.5	0.5 lb MD

Note: Coordinates are reported in NAD83 New Mexico State Plane West, US Survey Feet

APPENDIX F
DAILY REPORTS



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 8/11/08		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Reott		
WEATHER: Partly cloudy			TEMPERATURE: High: 79 Low: 51		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
Commence Kick out /Transect Investigation					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	8/11/08
2	John Reott	SSHO/QC	10	PIKA	8/11/08
3	Mike Fiedler	Tech 3/Team Leader	10	PIKA	8/11/08
4	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	8/11/08
5	John Clifford	Tech 2	10	PIKA	8/11/08
6	Joel Pullem	Tech 2	10	PIKA	8/11/08
7	Thomas Holland	Tech 1	10	PIKA	8/11/08
8	Dennis Anaya	Tech 1	10	PIKA	8/11/08
9	Michael Bradford	Tech 1	10	PIKA	8/11/08
10					
11					
12					
13					
14					
15					
16					
17					
18					
19					
20					
Total work hours on this job this date			90	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			2290	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			2380	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					
N/A					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137


WORK PERFORMED TODAY	
0630 – Task Order and safety meeting at office	
0700 – Gear set-up for Kick-out Investigation	
0730 – Teams investigating routes into work areas	
0900 – Downloaded data into Trimble Handhelds	
1200 – Break for lunch	
1230 – Return to work	
1300 – Kickoff meeting at Bldg 31 with Zuni and Navaho Tribal representatives, Cory Woods, Paul Hanneman	
1530 – Meeting adjourned	
1600 – Team meeting for pre-operational issues	
1700 – Secure for the day	
Transects Completed: 00	
Transects to Date: 00	
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED	
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS	
QA/QC INSPECTION RESULTS AND COMMENTS	
Grids QC checked: 00	Grids QA checked: 00
Total Grids: 00	Total Grids: 00
SAFETY INSPECTION RESULTS AND COMMENTS	
CHANGE ORDER(S): NA	
Original Scope:	
Proposed Change(s):	
Rational for Change(s):	
Approved by:	
COMING WORK PREPARATIONS AND ARRANGEMENTS	
Start Kick out investigations	
NOTES/COMMENTS	
SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)	



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS	
USACOE Safety/Slappy Harmon on site	
VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.	
SIGNATURE: 	DATE: 8/11/08



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 8/12/08		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Reott		
WEATHER: Partly cloudy			TEMPERATURE: High: 83 Low: 53		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
Commence Kick out /Transect Investigation					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	8/12/08
2	John Reott	SSHO/QC	10	PIKA	8/12/08
3	Mike Fiedler	Tech 3/Team Leader	10	PIKA	8/12/08
4	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	8/12/08
5	John Clifford	Tech 2	10	PIKA	8/12/08
6	Joel Pullem	Tech 2	10	PIKA	8/12/08
7	Thomas Holland	Tech 1	10	PIKA	8/12/08
8	Dennis Anaya	Tech 1	10	PIKA	8/12/08
9	Michael Bradford	Tech 1	10	PIKA	8/12/08
10	Genevieve Pino	Archaeologist	10	Navaho Tribes	8/12/08
11	Eugene Bowkaty	Archaeologist	10	Zuni Tribes	8/12/08
12					
13					
14					
15					
16					
17					
18					
19					
20					
Total work hours on this job this date			110	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			2380	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			2490	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					
N/A					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

WORK PERFORMED TODAY

0630 – Task Order and safety meeting at office
0645 – Checking instruments
0700 – Teams departing for field
0800 – Start Kick-out investigations
1200 – Break for lunch
1230 – Return to work
1300 – Kickoff meeting at Bldg 31 with Zuni and Navaho Tribal representatives, Cory Woods, Paul Hanneman
1530 – Meeting adjourned
1600 – Team meeting for pre-operational issues
1700 – Secure for the day

Transects Completed: **00**
Transects to Date: **00**

VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED

UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS

QA/QC INSPECTION RESULTS AND COMMENTS

Grids QC checked: **00** Grids QA checked: **00**
Total Grids: **00** Total Grids: **00**

SAFETY INSPECTION RESULTS AND COMMENTS

CHANGE ORDER(S): NA

Original Scope:
Proposed Change(s):
Rational for Change(s):
Approved by:

COMING WORK PREPARATIONS AND ARRANGEMENTS

Start Kick out investigations

NOTES/COMMENTS

SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)


Gerald Stone/PIKA PM



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS	
USACOE Safety/Slappy Harmon on site	
VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.	
SIGNATURE: 	DATE: 8/12/08



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 8/13/08		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Reott		
WEATHER: Partly cloudy			TEMPERATURE: High: 84 Low: 50		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
Continue Kick out /Transect Investigation					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	8/13/08
2	John Reott	SSHO/QC	10	PIKA	8/13/08
3	Mike Fiedler	Tech 3/Team Leader	10	PIKA	8/13/08
4	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	8/13/08
5	John Clifford	Tech 2	10	PIKA	8/13/08
6	Joel Pullem	Tech 2	10	PIKA	8/13/08
7	Thomas Holland	Tech 1	10	PIKA	8/13/08
8	Dennis Anaya	Tech 1	10	PIKA	8/13/08
9	Michael Bradford	Tech 1	10	PIKA	8/13/08
10	Geneveve Pino	Archeologist	10	Navaho Tribes	8/13/08
11	Eugene Bowekaty	Archeologist	10	Zuni Tribes	8/13/08
12					
13					
14					
15					
16					
17					
18					
19					
20					
Total work hours on this job this date			110	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			2490	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			2600	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					
N/A					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137


WORK PERFORMED TODAY	
0630 – Task Order and safety meeting at office	
0645 – Checking instruments	
0700 – Teams departing for field	
0800 – Start Kick-out investigations	
0830 – Start Igloo/ATF pre- Audit	
0930 – Complete Audit	
1200 – Break for lunch	
1230 – Return to work	
1700 – Secure for the day	
Transects Completed: <u>22</u>	
Transects to Date: <u>22</u>	
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED	
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS	
QA/QC INSPECTION RESULTS AND COMMENTS	
Grids QC checked: <u>00</u>	Grids QA checked: <u>00</u>
Total Grids: <u>00</u>	Total Grids: <u>00</u>
SAFETY INSPECTION RESULTS AND COMMENTS	
CHANGE ORDER(S): NA	
Original Scope:	
Proposed Change(s):	
Rational for Change(s):	
Approved by:	
COMING WORK PREPARATIONS AND ARRANGEMENTS	
Continue Kick out investigations	
NOTES/COMMENTS	
SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)	
Gerald Stone/PIKA PM	
Rick Holthouser/PIKA Ammo Mgr	



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS	
USACOE Safety/Slappy Harmon on site	
VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.	
SIGNATURE: 	DATE: 8/13/08



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 8/14/08		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Reott		
WEATHER: Partly cloudy			TEMPERATURE: High: 84 Low: 51		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
Continue Kick out /Transect Investigation					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	8/14/08
2	John Reott	SSHO/QC	10	PIKA	8/14/08
3	Mike Fiedler	Tech 3/Team Leader	10	PIKA	8/14/08
4	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	8/14/08
5	John Clifford	Tech 2	10	PIKA	8/14/08
6	Joel Pullem	Tech 2	10	PIKA	8/14/08
7	Thomas Holland	Tech 1	10	PIKA	8/14/08
8	Dennis Anaya	Tech 1	10	PIKA	8/14/08
9	Michael Bradford	Tech 1	10	PIKA	8/14/08
10	Geneveve Pino	Archeologist	10	Navaho Tribes	8/14/08
11	Eugene Bowekaty	Archeologist	10	Zuni Tribes	8/14/08
12					
13					
14					
15					
16					
17					
18					
19					
20					
Total work hours on this job this date			110	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			2600	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			2710	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					
N/A					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137


WORK PERFORMED TODAY	
0630 – Task Order and safety meeting at office	
0645 – Checking instruments	
0700 – Teams departing for field	
0800 – Start Kick-out investigations	
0830 – Start Igloo/ATF pre- Audit	
0930 – Complete Audit	
1200 – Break for lunch	
1230 – Return to work	
1530 – Return to office	
1600 – Start vehicle/equipment maintenance	
1700 – Secure for the day	
Transects Completed: <u>41</u>	
Transects to Date: <u>63</u>	
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED	
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS	
QA/QC INSPECTION RESULTS AND COMMENTS	
Grids QC checked: <u>00</u>	Grids QA checked: <u>00</u>
Total Grids: <u>00</u>	Total Grids: <u>00</u>
SAFETY INSPECTION RESULTS AND COMMENTS	
CHANGE ORDER(S): NA	
Original Scope:	
Proposed Change(s):	
Rational for Change(s):	
Approved by:	
COMING WORK PREPARATIONS AND ARRANGEMENTS	
Continue Kick out investigations	
NOTES/COMMENTS	
SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)	



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS	
USACOE Safety/Slappy Harmon on site	
VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.	
SIGNATURE: 	DATE: 8/14/08



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 8/18/08		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Reott		
WEATHER: Partly cloudy			TEMPERATURE: High: 81 Low: 47		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
Continue Kick out /Transect Investigation					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	8/18/08
2	John Reott	SSHO/QC	10	PIKA	8/18/08
3	Mike Fiedler	Tech 3/Team Leader	10	PIKA	8/18/08
4	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	8/18/08
5	John Clifford	Tech 2	10	PIKA	8/18/08
6	Joel Pullem	Tech 2	10	PIKA	8/18/08
7	Thomas Holland	Tech 1	10	PIKA	8/18/08
8	Dennis Anaya	Tech 1	10	PIKA	8/18/08
9	Michael Bradford	Tech 1	10	PIKA	8/18/08
10	Geneveve Pino	Archeologist	10	Navaho Tribes	8/18/08
11	Eugene Bowekaty	Archeologist	10	Zuni Tribes	8/18/08
12					
13					
14					
15					
16					
17					
18					
19					
20					
Total work hours on this job this date			110	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			2710	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			2820	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					
N/A					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137


WORK PERFORMED TODAY	
0630 – Task Order and safety meeting at office	
0645 – Checking instruments	
0700 – Teams departing for field	
0800 – Start Kick-out investigations	
1200 – Break for lunch	
1230 – Return to work	
1600 – Return to Office	
1700 – Secure for the day	
Transects Completed: <u>46</u>	
Transects to Date: <u>109</u>	
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED	
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS	
QA/QC INSPECTION RESULTS AND COMMENTS	
Grids QC checked: <u>00</u>	Grids QA checked: <u>00</u>
Total Grids: <u>00</u>	Total Grids: <u>00</u>
SAFETY INSPECTION RESULTS AND COMMENTS	
CHANGE ORDER(S): NA	
Original Scope:	
Proposed Change(s):	
Rational for Change(s):	
Approved by:	
COMING WORK PREPARATIONS AND ARRANGEMENTS	
Continue Kick out investigations	
NOTES/COMMENTS	
SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)	



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS	
USACOE Safety/Slappy Harmon on site	
VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.	
SIGNATURE: 	DATE: 8/18/08



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 8/19/08		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Reott		
WEATHER: Sunny			TEMPERATURE: High: 83 Low: 51		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
Continue Kick out /Transect Investigation					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	8/19/08
2	John Reott	SSHO/QC	10	PIKA	8/19/08
3	Mike Fiedler	Tech 3/Team Leader	10	PIKA	8/19/08
4	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	8/19/08
5	John Clifford	Tech 2	10	PIKA	8/19/08
6	Joel Pullem	Tech 2	10	PIKA	8/19/08
7	Thomas Holland	Tech 1	10	PIKA	8/19/08
8	Dennis Anaya	Tech 1	10	PIKA	8/19/08
9	Michael Bradford	Tech 1	10	PIKA	8/19/08
10	Geneveve Pino	Archeologist	10	Navaho Tribes	8/19/08
11					
12					
13					
14					
15					
16					
17					
18					
19					
20					
Total work hours on this job this date			100	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			2820	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			2920	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					
N/A					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

WORK PERFORMED TODAY

0630 – Task Order and safety meeting at office
0645 – Checking instruments
0700 – Teams departing for field
0800 – Start Kick-out investigations
0900 – Depauli Surveyors onsite to walk arroyo
1130 – Surveyors completed arroyo walk
1200 – Break for lunch
1230 – Return to work
1600 – Return to Office
1700 – Secure for the day

Transects Completed: **40**
Transects to Date: **149**

VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED

UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS

QA/QC INSPECTION RESULTS AND COMMENTS

Grids QC checked: **00** Grids QA checked: **00**
Total Grids: **00** Total Grids: **00**

SAFETY INSPECTION RESULTS AND COMMENTS

CHANGE ORDER(S): NA

Original Scope:
Proposed Change(s):
Rational for Change(s):
Approved by:

COMING WORK PREPARATIONS AND ARRANGEMENTS

Continue Kick out investigations

NOTES/COMMENTS

Eugene Bowekaty not on site today.

SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)


Mike Depauli/Depauli Eng. And Surveying Co



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS	
USACOE Safety/Slappy Harmon on site	
VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.	
SIGNATURE: 	DATE: 8/19/08



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 8/20/08		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Reott		
WEATHER: Partly Cloudy			TEMPERATURE: High: 81 Low: 51		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
Continue Kick out /Transect Investigation					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	8/20/08
2	John Reott	SSHO/QC	10	PIKA	8/20/08
3	Mike Fiedler	Tech 3/Team Leader	10	PIKA	8/20/08
4	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	8/20/08
5	John Clifford	Tech 2	10	PIKA	8/20/08
6	Joel Pullem	Tech 2	10	PIKA	8/20/08
7	Thomas Holland	Tech 1	10	PIKA	8/20/08
8	Dennis Anaya	Tech 1	10	PIKA	8/20/08
9	Michael Bradford	Tech 1	10	PIKA	8/20/08
10	Geneveve Pino	Archeologist	10	Navaho Tribes	8/20/08
11					
12					
13					
14					
15					
16					
17					
18					
19					
20					
Total work hours on this job this date			100	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			2920	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			3020	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					
N/A					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

WORK PERFORMED TODAY	
0630 – Task Order and safety meeting at office 0645 – Checking instruments 0700 – Teams departed for field 1200 – Break for lunch 1230 – Return to work 1630 – Teams return to Office 1700 – Secure for the day	
Transects Completed:	<u>64</u>
Transects to Date:	<u>213</u>
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED	
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS	
QA/QC INSPECTION RESULTS AND COMMENTS	
Grids QC checked:	<u>00</u>
Grids QA checked:	<u>00</u>
Total Grids:	<u>00</u>
Total Grids:	<u>00</u>
SAFETY INSPECTION RESULTS AND COMMENTS	
CHANGE ORDER(S): NA	
Original Scope:	
Proposed Change(s):	
Rational for Change(s):	
Approved by:	
COMING WORK PREPARATIONS AND ARRANGEMENTS	
Continue Kick out investigations	
NOTES/COMMENTS	
Eugene Bowekaty not on site today. He did not call or show up.	
SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)	
OTHER REMARKS	
USACOE Safety/Slappy Harmon on site	



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.


SIGNATURE: DATE: 8/20/08



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 8/21/08		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Reott		
WEATHER: Partly Cloudy			TEMPERATURE: High: 81 Low: 51		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
Continue Kick out /Transect Investigation					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	8/21/08
2	John Reott	SSHO/QC	10	PIKA	8/21/08
3	Mike Fiedler	Tech 3/Team Leader	10	PIKA	8/21/08
4	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	8/21/08
5	John Clifford	Tech 2	10	PIKA	8/21/08
6	Joel Pullem	Tech 2	10	PIKA	8/21/08
7	Thomas Holland	Tech 1	10	PIKA	8/21/08
8	Dennis Anaya	Tech 1	10	PIKA	8/21/08
9	Michael Bradford	Tech 1	10	PIKA	8/21/08
10	Geneveve Pino	Archeologist	10	Navaho Tribes	8/21/08
11	Eugene Bowekaty	Archeologist	10	Zuni Tribes	8/21/08
12					
13					
14					
15					
16					
17					
18					
19					
20					
Total work hours on this job this date			110	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			3020	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			3130	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					
N/A					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

WORK PERFORMED TODAY	
0630 – Task Order and safety meeting at office 0645 – Checking instruments 0700 – Teams departed for field 1200 – Break for lunch 1230 – Return to work 1600 – Teams return to Office 1605 – Teams conducting vehicle/equipment maintenance 1700 – Secure for the day	
Transects Completed:	<u>56</u>
Transects to Date:	<u>269</u>
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED	
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS	
QA/QC INSPECTION RESULTS AND COMMENTS	
Grids QC checked:	<u>00</u>
Grids QA checked:	<u>00</u>
Total Grids:	<u>00</u>
Total Grids:	<u>00</u>
SAFETY INSPECTION RESULTS AND COMMENTS	
CHANGE ORDER(S): NA	
Original Scope:	
Proposed Change(s):	
Rational for Change(s):	
Approved by:	
COMING WORK PREPARATIONS AND ARRANGEMENTS	
Continue Kick out investigations	
NOTES/COMMENTS	
Eugene Bowekaty returned to work today.	
SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)	
OTHER REMARKS	




**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

USACOE Safety/Slappy Harmon on site

VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.

	
SIGNATURE:	DATE:8/21/08



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 8/27/08		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Reott		
WEATHER: Partly Cloudy			TEMPERATURE: High: 79 Low: 50		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
* Continue Kick out /Transect Investigation					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	8/27/08
2	John Reott	SSHO/QC	10	PIKA	8/27/08
3	Mike Fiedler	Tech 3/Team Leader	10	PIKA	8/27/08
4	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	8/27/08
5	John Clifford	Tech 2	10	PIKA	8/27/08
6	Joel Pullem	Tech 2	10	PIKA	8/27/08
7	Thomas Holland	Tech 1	10	PIKA	8/27/08
8	Dennis Anaya	Tech 1	10	PIKA	8/27/08
9	Michael Bradford	Tech 1	10	PIKA	8/27/08
10	Michael Ahmu	Tech 1	10	PIKA	8/27/08
11	Geneveve Pino	Archeologist	10	Navaho Tribes	8/27/08
12	Eugene Bowekaty	Archeologist	10	Zuni Tribes	8/27/08
13					
14					
15					
16					
17					
18					
19					
20					
Total work hours on this job this date			120	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			3370	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			3490	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					
N/A					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137


WORK PERFORMED TODAY	
0630 – Task Order and safety meeting at office 0645 – Checking instruments 0700 – Teams departed for field 0845 – DePauli Surveyors on site to survey arroyo for grid system 1200 – Break for lunch 1230 – Return to work 1530 – DePauli Surveyors completed arroyo survey. Will have data for review after Labor Day. 1630 – Teams return to Office 1700 – Secure for the day	
Transects Completed:	<u>34</u>
Transects to Date:	<u>410</u>
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED	
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS	
QA/QC INSPECTION RESULTS AND COMMENTS	
Grids QC checked: <u>00</u>	Grids QA checked: <u>00</u>
Total Grids: <u>00</u>	Total Grids: <u>00</u>
SAFETY INSPECTION RESULTS AND COMMENTS	
CHANGE ORDER(S): NA	
Original Scope:	
Proposed Change(s):	
Rational for Change(s):	
Approved by:	
COMING WORK PREPARATIONS AND ARRANGEMENTS	
Continue Kick out investigations	
NOTES/COMMENTS	
SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)	
Marc DePauli/Surveyor/ Arroyo Survey/Yes	
Jason Irvine/Surveyor/Arroyo survey/Yes	
Virgil Hudson/Surveyor/Arroyo survey/Yes	



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS	
USACOE Safety/Slappy Harmon on site	
VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.	
SIGNATURE: 	DATE: 8/27/08



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 8/28/08		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Reott		
WEATHER: Partly Cloudy			TEMPERATURE: High: 79 Low: 50		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
* Continue Kick out /Transect Investigation					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	8/28/08
2	John Reott	SSHO/QC	10	PIKA	8/28/08
3	Mike Fiedler	Tech 3/Team Leader	10	PIKA	8/28/08
4	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	8/28/08
5	John Clifford	Tech 2	10	PIKA	8/28/08
6	Joel Pullem	Tech 2	10	PIKA	8/28/08
7	Thomas Holland	Tech 1	10	PIKA	8/28/08
8	Dennis Anaya	Tech 1	10	PIKA	8/28/08
9	Michael Bradford	Tech 1	10	PIKA	8/28/08
10	Michael Ahmu	Tech 1	10	PIKA	8/28/08
11	Geneveve Pino	Archeologist	10	Navaho Tribes	8/28/08
12	Eugene Bowekaty	Archeologist	10	Zuni Tribes	8/28/08
13					
14					
15					
16					
17					
w18					
19					
20					
Total work hours on this job this date			120	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			3490	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			3610	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					
N/A					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137


WORK PERFORMED TODAY	
0630 – Task Order and safety meeting at office 0645 – Checking instruments 0700 – Teams departed for field 1200 – Break for lunch 1230 – Return to work 1530 – Return to the office.. 1600 – Teams return to Office 1615 – Teams conducting maintenance on vehicles and equipment 1700 – Secure for the day	
Transects Completed: <u>24</u> Transects to Date: <u>434</u>	
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED	
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS	
QA/QC INSPECTION RESULTS AND COMMENTS	
Grids QC checked: <u>00</u>	Grids QA checked: <u>00</u>
Total Grids: <u>00</u>	Total Grids: <u>00</u>
SAFETY INSPECTION RESULTS AND COMMENTS	
CHANGE ORDER(S): NA	
Original Scope:	
Proposed Change(s):	
Rational for Change(s):	
Approved by:	
COMING WORK PREPARATIONS AND ARRANGEMENTS	
Continue Kick out investigations	
NOTES/COMMENTS	
SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)	



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS	
USACOE Safety/Slappy Harmon on site	
VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.	
SIGNATURE: 	DATE: 8/28/08



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 9/3/2008		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Reott		
WEATHER: Partly Cloudy			TEMPERATURE: High: 77 Low: 48		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
* Continue Kick out /Transect Investigation					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	9/3/08
2	John Reott	SSHO/QC	10	PIKA	9/3/08
3	Mike Fiedler	Tech 3/Team Leader	10	PIKA	9/3/08
4	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	9/3/08
5	John Clifford	Tech 2	10	PIKA	9/3/08
6	Joel Pullem	Tech 2	10	PIKA	9/3/08
7	Thomas Holland	Tech 1	10	PIKA	9/3/08
8	Dennis Anaya	Tech 1	10	PIKA	9/3/08
9	Michael Bradford	Tech 1	10	PIKA	9/3/08
10	Michael Ahmu	Tech 1	10	PIKA	9/3/08
11	Geneveve Pino	Archeologist	10	Navaho Tribes	9/3/08
12	Eugene Bowekaty	Archeologist	10	Zuni Tribes	9/3/08
13					
14					
15					
16					
17					
w18					
19					
20					
Total work hours on this job this date			120	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			3610	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			3730	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					
N/A					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

WORK PERFORMED TODAY

0630 – Task Order and safety meeting at office
0645 – Checking instruments
0700 – Teams departed for field
1200 – Break for lunch
1230 – Return to work
1630 – Return to the office
1700 – Secure for the day

Transects Completed: **36**
Transects to Date: **470**

VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED

UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS

QA/QC INSPECTION RESULTS AND COMMENTS

Grids QC checked: **00** Grids QA checked: **00**
Total Grids: **00** Total Grids: **00**

SAFETY INSPECTION RESULTS AND COMMENTS

CHANGE ORDER(S): NA

Original Scope:
Proposed Change(s):
Rational for Change(s):
Approved by:

COMING WORK PREPARATIONS AND ARRANGEMENTS

Continue Kick out investigations

NOTES/COMMENTS

SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS

VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.


SIGNATURE: _____ DATE: 9/3/08



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 9/4/2008		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Reott		
WEATHER: Sunny			TEMPERATURE: High: 79 Low: 50		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
* Continue Kick out /Transect Investigation					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	9/4/08
2	John Reott	SSHO/QC	10	PIKA	9/4/08
3	Mike Fiedler	Tech 3/Team Leader	10	PIKA	9/4/08
4	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	9/4/08
5	John Clifford	Tech 2	10	PIKA	9/4/08
6	Joel Pullem	Tech 2	10	PIKA	9/4/08
7	Thomas Holland	Tech 1	10	PIKA	9/4/08
8	Dennis Anaya	Tech 1	10	PIKA	9/4/08
9	Michael Bradford	Tech 1	10	PIKA	9/4/08
10	Michael Ahmu	Tech 1	10	PIKA	9/4/08
11	Geneveve Pino	Archeologist	10	Navaho Tribes	9/4/08
12	Eugene Bowekaty	Archeologist	10	Zuni Tribes	9/4/08
13					
14					
15					
16					
17					
w18					
19					
20					
Total work hours on this job this date			120	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			3730	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			3850	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					
N/A					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

WORK PERFORMED TODAY	
0630 – Task Order and safety meeting at office 0645 – Checking instruments 0700 – Teams departed for field 1200 – Break for lunch 1230 – Return to work 1630 – Return to the office 1700 – Secure for the day	
Transects Completed:	<u>38</u>
Transects to Date:	<u>508</u>
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED	
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS	
QA/QC INSPECTION RESULTS AND COMMENTS	
Grids QC checked: <u>00</u>	Grids QA checked: <u>00</u>
Total Grids: <u>00</u>	Total Grids: <u>00</u>
SAFETY INSPECTION RESULTS AND COMMENTS	
CHANGE ORDER(S): NA	
Original Scope:	
Proposed Change(s):	
Rational for Change(s):	
Approved by:	
COMING WORK PREPARATIONS AND ARRANGEMENTS	
Continue Kick out investigations	
NOTES/COMMENTS	
SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)	



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS

VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.


SIGNATURE: DATE:9/4/08



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 9/4/2008		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Reott		
WEATHER: Sunny			TEMPERATURE: High: 81 Low: 49		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
* Continue Kick out /Transect Investigation					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	9/5/08
2	John Reott	SSHO/QC	10	PIKA	9/5/08
3	Mike Fiedler	Tech 3/Team Leader	10	PIKA	9/5/08
4	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	9/5/08
5	John Clifford	Tech 2	10	PIKA	9/5/08
6	Joel Pullem	Tech 2	10	PIKA	9/5/08
7	Thomas Holland	Tech 1	10	PIKA	9/5/08
8	Dennis Anaya	Tech 1	10	PIKA	9/5/08
9	Michael Bradford	Tech 1	10	PIKA	9/5/08
10	Michael Ahmu	Tech 1	10	PIKA	9/5/08
11	Geneveve Pino	Archeologist	10	Navaho Tribes	9/5/08
12	Eugene Bowekaty	Archeologist	10	Zuni Tribes	9/5/08
13					
14					
15					
16					
17					
w18					
19					
20					
Total work hours on this job this date			120	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			3850	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			3970	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					
N/A					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

WORK PERFORMED TODAY	
0630 – Task Order and safety meeting at office 0645 – Checking instruments 0700 – Teams departed for field 1200 – Break for lunch 1230 – Return to work 1630 – Return to the office 1700 – Secure for the day	
Transects Completed:	<u>53</u>
Transects to Date:	<u>561</u>
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED	
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS	
QA/QC INSPECTION RESULTS AND COMMENTS	
Grids QC checked: <u>00</u>	Grids QA checked: <u>00</u>
Total Grids: <u>00</u>	Total Grids: <u>00</u>
SAFETY INSPECTION RESULTS AND COMMENTS	
CHANGE ORDER(S): NA	
Original Scope:	
Proposed Change(s):	
Rational for Change(s):	
Approved by:	
COMING WORK PREPARATIONS AND ARRANGEMENTS	
Continue Kick out investigations	
NOTES/COMMENTS	
SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)	




**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS

VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.



SIGNATURE: _____ DATE: 9/5/08



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 9/8/2008		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Reott		
WEATHER: Sunny			TEMPERATURE: High: 80 Low: 51		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
* Continue Kick out /Transect Investigation					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	9/8/08
2	John Reott	SSHO/QC	10	PIKA	9/8/08
3	Mike Fiedler	Tech 3/Team Leader	10	PIKA	9/8/08
4	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	9/8/08
5	John Clifford	Tech 2	10	PIKA	9/8/08
6	Joel Pullem	Tech 2	10	PIKA	9/8/08
7	Thomas Holland	Tech 1	10	PIKA	9/8/08
8	Dennis Anaya	Tech 1	10	PIKA	9/8/08
9	Michael Bradford	Tech 1	10	PIKA	9/8/08
10	Michael Ahmu	Tech 1	10	PIKA	9/8/08
11	Geneveve Pino	Archeologist	10	Navaho Tribes	9/8/08
12	Eugene Bowekaty	Archeologist	0	Zuni Tribes	9/8/08
13					
14					
15					
16					
17					
w18					
19					
20					
Total work hours on this job this date			110	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			3970	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			4080	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					
N/A					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

WORK PERFORMED TODAY	
0630 – Task Order and safety meeting at office 0645 – Checking instruments 0700 – Teams departed for field 1200 – Break for lunch 1230 – Return to work 1630 – Return to the office 1700 – Secure for the day	
Transects Completed:	<u>32</u>
Transects to Date:	<u>593</u>
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED	
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS	
QA/QC INSPECTION RESULTS AND COMMENTS	
Grids QC checked: <u>00</u>	Grids QA checked: <u>00</u>
Total Grids: <u>00</u>	Total Grids: <u>00</u>
SAFETY INSPECTION RESULTS AND COMMENTS	
CHANGE ORDER(S): NA	
Original Scope:	
Proposed Change(s):	
Rational for Change(s):	
Approved by:	
COMING WORK PREPARATIONS AND ARRANGEMENTS	
Continue Kick out investigations	
NOTES/COMMENTS	
USACOE Safety Representative/Harmon Slappy not on site. Will return tomorrow. Eugene Bowekaty not on site today. He did not notify us that he would not be here today.	
SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)	



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS

VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.


SIGNATURE: _____ DATE: 9/8/08



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 9/9/2008		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Reott		
WEATHER: Sunny			TEMPERATURE: High: 72 Low: 45		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
* Continue Kick out /Transect Investigation					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	9/9/08
2	John Reott	SSHO/QC	10	PIKA	9/9/08
3	Mike Fiedler	Tech 3/Team Leader	10	PIKA	9/9/08
4	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	9/9/08
5	John Clifford	Tech 2	10	PIKA	9/9/08
6	Joel Pullem	Tech 2	10	PIKA	9/9/08
7	Thomas Holland	Tech 1	10	PIKA	9/9/08
8	Dennis Anaya	Tech 1	10	PIKA	9/9/08
9	Michael Bradford	Tech 1	10	PIKA	9/9/08
10	Michael Ahmu	Tech 1	10	PIKA	9/9/08
11	Geneveve Pino	Archeologist	10	Navaho Tribes	9/9/08
12	Eugene Bowekaty	Archeologist	10	Zuni Tribes	9/9/08
13					
14					
15					
16					
17					
w18					
19					
20					
Total work hours on this job this date			120	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			4080	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			4200	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					
N/A					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

WORK PERFORMED TODAY

0630 – Task Order and safety meeting at office
0645 – Checking instruments
0700 – Teams departed for field
1200 – Break for lunch
1230 – Return to work
1630 – Return to the office
1700 – Secure for the day

Transects Completed: 26
Transects to Date: 619

VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED

UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS

QA/QC INSPECTION RESULTS AND COMMENTS

Grids QC checked: 00 Grids QA checked: 00
Total Grids: 00 Total Grids: 00

SAFETY INSPECTION RESULTS AND COMMENTS

CHANGE ORDER(S): NA

Original Scope:
Proposed Change(s):
Rational for Change(s):
Approved by:

COMING WORK PREPARATIONS AND ARRANGEMENTS

Continue Kick out investigations

NOTES/COMMENTS

USACOE Safety Representative/Harmon Slappy on site.
Eugene Bowekaty returned to work .

SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS

VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.


SIGNATURE: DATE:9/9/08



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 9/10/2008		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Reott		
WEATHER: Sunny			TEMPERATURE: High: 70 Low: 46		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
* Continue Kick out /Transect Investigation					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	9/10/08
2	John Reott	SSHO/QC	10	PIKA	9/10/08
3	Mike Fiedler	Tech 3/Team Leader	10	PIKA	9/10/08
4	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	9/10/08
5	John Clifford	Tech 2	10	PIKA	9/10/08
6	Joel Pullem	Tech 2	10	PIKA	9/10/08
7	Thomas Holland	Tech 1	10	PIKA	9/10/08
8	Dennis Anaya	Tech 1	10	PIKA	9/10/08
9	Michael Bradford	Tech 1	10	PIKA	9/10/08
10	Michael Ahmu	Tech 1	10	PIKA	9/10/08
11	Geneveve Pino	Archeologist	10	Navaho Tribes	9/10/08
12	Eugene Bowekaty	Archeologist	10	Zuni Tribes	9/10/08
13					
14					
15					
16					
17					
w18					
19					
20					
Total work hours on this job this date			120	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			4200	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			4320	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					
N/A					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

WORK PERFORMED TODAY	
0630 – Task Order and safety meeting at office	
0645 – Checking instruments	
0700 – Teams departed for field	
1200 – Break for lunch	
1230 – Return to work	
1630 – Return to the office	
1700 – Secure for the day	
Transects Completed:	<u>37</u>
Transects to Date:	<u>656</u>
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED	
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS	
QA/QC INSPECTION RESULTS AND COMMENTS	
Grids QC checked: <u>00</u>	Grids QA checked: <u>00</u>
Total Grids: <u>00</u>	Total Grids: <u>00</u>
SAFETY INSPECTION RESULTS AND COMMENTS	
CHANGE ORDER(S): NA	
Original Scope:	
Proposed Change(s):	
Rational for Change(s):	
Approved by:	
COMING WORK PREPARATIONS AND ARRANGEMENTS	
Continue Kick out investigations	
NOTES/COMMENTS	
USACOE Safety Representative/Harmon Slappy on site.	
SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)	



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS

VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.


SIGNATURE: DATE:9/10/08



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 9/11/2008		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Reott		
WEATHER: Sunny			TEMPERATURE: High: 70 Low: 48		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
* Continue Kick out /Transect Investigation					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	9/11/08
2	John Reott	SSHO/QC	10	PIKA	9/11/08
3	Mike Fiedler	Tech 3/Team Leader	10	PIKA	9/11/08
4	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	9/11/08
5	John Clifford	Tech 2	10	PIKA	9/11/08
6	Joel Pullem	Tech 2	10	PIKA	9/11/08
7	Thomas Holland	Tech 1	10	PIKA	9/11/08
8	Dennis Anaya	Tech 1	10	PIKA	9/11/08
9	Michael Bradford	Tech 1	10	PIKA	9/11/08
10	Michael Ahmu	Tech 1	10	PIKA	9/11/08
11	Curtis Yazzie	Archeologist	10	Navaho Tribes	9/11/08
12	Eugene Bowekaty	Archeologist	10	Zuni Tribes	9/11/08
13					
14					
15					
16					
17					
w18					
19					
20					
Total work hours on this job this date			120	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			4320	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			4440	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					
N/A					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

WORK PERFORMED TODAY	
0630 – Task Order and safety meeting at office 0645 – Checking instruments 0700 – Teams departed for field 1200 – Break for lunch 1230 – Return to work 1630 – Return to the office 1700 – Secure for the day	
Transects Completed:	<u>2</u>
Transects to Date:	<u>658</u>
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED	
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS	
QA/QC INSPECTION RESULTS AND COMMENTS	
Grids QC checked: <u>00</u>	Grids QA checked: <u>00</u>
Total Grids: <u>00</u>	Total Grids: <u>00</u>
SAFETY INSPECTION RESULTS AND COMMENTS	
CHANGE ORDER(S): NA	
Original Scope:	
Proposed Change(s):	
Rational for Change(s):	
Approved by:	
COMING WORK PREPARATIONS AND ARRANGEMENTS	
Continue Kick out investigations	
NOTES/COMMENTS	
USACOE Safety Representative/Harmon Slappy on site.	
Curtis Yazzie replaced Genevieve Pino as the Navaho representative	
Completed 1200' step out investigation along base line between E-64 through E-76 per W/P	
SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)	




**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS

VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.


SIGNATURE: _____ DATE: 9/11/08



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 9/15/2008		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Reott		
WEATHER: Sunny			TEMPERATURE: High: 74 Low: 41		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
* Continue Kick out /Transect Investigation					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	9/15/08
2	John Reott	SSHO/QC	10	PIKA	9/15/08
3	Mike Fiedler	Tech 3/Team Leader	10	PIKA	9/15/08
4	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	9/15/08
5	John Clifford	Tech 2	10	PIKA	9/15/08
6	Joel Pullem	Tech 2	10	PIKA	9/15/08
7	Thomas Holland	Tech 1	10	PIKA	9/15/08
8	Dennis Anaya	Tech 1	10	PIKA	9/15/08
9	Michael Ahmu	Tech 1	10	PIKA	9/15/08
10					
11					
12					
13					
14					
15					
16					
17					
18					
19					
20					
Total work hours on this job this date			90	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			4440	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			4530	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					
N/A					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137


WORK PERFORMED TODAY	
0630 – Task Order and safety meeting at office	
0645 – Checking instruments	
0700 – Teams departed for field	
0700 – Depauli Surveyors on site to put in grid stakes in arroyo	
1200 – Break for lunch	
1230 – Return to work	
1630 – Return to the office	
1700 – Secure for the day	
Transects Completed:	<u>0</u>
Transects to Date:	<u>658</u>
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED	
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS	
QA/QC INSPECTION RESULTS AND COMMENTS	
Grids QC checked: <u>00</u>	Grids QA checked: <u>00</u>
Total Grids: <u>00</u>	Total Grids: <u>00</u>
SAFETY INSPECTION RESULTS AND COMMENTS	
CHANGE ORDER(S): NA	
Original Scope:	
Proposed Change(s):	
Rational for Change(s):	
Approved by:	
COMING WORK PREPARATIONS AND ARRANGEMENTS	
Continue Kick out investigations	
NOTES/COMMENTS	
USACOE Safety Representative/Harmon Slappy on site.	
Tribal representatives will not be on site this week	
SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)	



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS	
VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.	
SIGNATURE: 	DATE: 9/15/08



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 9/16/2008		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Reott		
WEATHER: Sunny			TEMPERATURE: High: 70 Low: 48		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
* Continue Kick out /Transect Investigation					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	9/16/08
2	John Reott	SSHO/QC	10	PIKA	9/16/08
3	Mike Fiedler	Tech 3/Team Leader	10	PIKA	9/16/08
4	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	9/16/08
5	John Clifford	Tech 2	10	PIKA	9/16/08
6	Joel Pullem	Tech 2	10	PIKA	9/16/08
7	Thomas Holland	Tech 1	10	PIKA	9/16/08
8	Dennis Anaya	Tech 1	10	PIKA	9/16/08
9	Michael Ahmu	Tech 1	10	PIKA	9/16/08
10	Wendy Church	Geophysicist	9	PIKA	9/16/08
11	Eric Stoffel	Geophysicist	9	PIKA	9/16/08
12	Mike Milne	Tech 1	9	PIKA	9/16/08
13					
14					
15					
16					
17					
18					
19					
20					
Total work hours on this job this date			117	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			4530	<input type="checkbox"/> Yes	<input checked="" type="checkbox"/> No
Total work hours from start of project			4647	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					
N/A					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137


WORK PERFORMED TODAY	
<p>0630 – Task Order and safety meeting at office. 0645 – Checking instruments. 0700 – Team 1 departed for field to check for any accessible areas on South side. 0800 – EM-62 crew reported onboard. 0805 – Depauli survey crew arrived and departed for arroyo. 0930 – EM-62 crew departed office to GPO area to check instruments. 1200 – Break for lunch 1230 – Return to work 1530 – Depauli completed staking arroyo grid sReturn to work 1630 – Return to the office 1700 – Secure for the day</p> <p>Transects Completed: <u>19</u> Transects to Date: <u>677</u></p>	
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED	
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS	
QA/QC INSPECTION RESULTS AND COMMENTS	
Grids QC checked: <u>00</u>	Grids QA checked: <u>00</u>
Total Grids: <u>00</u>	Total Grids: <u>00</u>
Linear feet of QC audit completed: 4010	
Total Linear feet of QC audited: <u>4010</u>	
SAFETY INSPECTION RESULTS AND COMMENTS	
CHANGE ORDER(S): NA	
Original Scope:	
Proposed Change(s):	
Rational for Change(s):	
Approved by:	
COMING WORK PREPARATIONS AND ARRANGEMENTS	
Continue Kick out investigations	
NOTES/COMMENTS	
USACOE Safety Representative/Harmon Slappy on site.	
Tribal representatives will not be on site this week	



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)	
OTHER REMARKS	
VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.	
SIGNATURE: 	DATE: 9/16/08



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 9/17/2008		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Reott		
WEATHER: Sunny			TEMPERATURE: High: 75 Low: 42		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
* Continue Kick out /Transect Investigation					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	9/17/08
2	John Reott	SSHO/QC	10	PIKA	9/17/08
3	Mike Fiedler	Tech 3/Team Leader	10	PIKA	9/17/08
4	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	9/17/08
5	John Clifford	Tech 2	10	PIKA	9/17/08
6	Joel Pullem	Tech 2	10	PIKA	9/17/08
7	Thomas Holland	Tech 1	10	PIKA	9/17/08
8	Dennis Anaya	Tech 1	10	PIKA	9/17/08
9	Michael Ahmu	Tech 1	10	PIKA	9/17/08
10	Wendy Church	Geophysicist	10	PIKA	9/17/08
11	Eric Stoffel	Geophysicist	10	PIKA	9/17/08
12	Mike Milne	Tech 1	10	PIKA	9/17/08
13				PIKA	9/17/08
14					
15					
16					
17					
18					
19					
20					
Total work hours on this job this date			120	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			4647	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			4767	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					
N/A					



PIKA International, Inc.
Daily Field Activity Report

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

WORK PERFORMED TODAY

0630 – Task Order and safety meeting at office.
0645 – Checking instruments.
0700 – Team 1 departed for field to redo East 63 to East 92 transects.
0900 – EM-62 crew departed office to perform QC audits
1200 – Break for lunch
1230 – Return to work
1630 – Return to the office
1700 – Secure for the day

Transects Completed: 18
Transects to Date: 695

VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED

Eric Kirwan approved the use of the EM-61 in the litter mode vice wheel mode to collect data.

UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS

QA/QC INSPECTION RESULTS AND COMMENTS

Grids QC checked: 00 Grids QA checked: 00
Total Grids: 00 Total Grids: 00

Linear feet of QC audit completed: 5245
Total Linear feet of QC audited: 9255

SAFETY INSPECTION RESULTS AND COMMENTS

CHANGE ORDER(S): NA

Original Scope:
Proposed Change(s):
Rational for Change(s):
Approved by:

COMING WORK PREPARATIONS AND ARRANGEMENTS

Continue Kick out investigations

NOTES/COMMENTS

USACOE Safety Representative/Harmon Slappy on site.

SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)

Eric Kirwin, USACE PM, Assist in EM-61 audits, yes.




**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS

VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.


SIGNATURE: _____ DATE: 9/17/08

--



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 9/17/2008		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Reott		
WEATHER: Sunny			TEMPERATURE: High: 75 Low: 42		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
* Continue Kick out /Transect Investigation					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	9/18/08
2	John Reott	SSHO/QC	10	PIKA	9/18/08
3	Mike Fiedler	Tech 3/Team Leader	10	PIKA	9/18/08
4	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	9/18/08
5	John Clifford	Tech 2	10	PIKA	9/18/08
6	Joel Pullem	Tech 2	10	PIKA	9/18/08
7	Thomas Holland	Tech 1	10	PIKA	9/18/08
8	Dennis Anaya	Tech 1	10	PIKA	9/18/08
9	Michael Ahmu	Tech 1	10	PIKA	9/18/08
10	Wendy Church	Geophysicist	10	PIKA	9/18/08
11	Eric Stoffel	Geophysicist	10	PIKA	9/18/08
12	Mike Milne	Tech 1	10	PIKA	9/18/08
13					
14					
15					
16					
17					
18					
19					
20					
Total work hours on this job this date			120	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			4767	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			4887	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					
N/A					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

WORK PERFORMED TODAY	
0630 – Task Order and safety meeting at office. 0645 – Checking instruments. 0700 – Team 1 departed for field to work the western sections 0715 – EM-62 crew departed office to perform QC audits 1200 – Break for lunch 1230 – Return to work 1630 – Return to the office 1700 – Secure for the day	
Transects Completed:	<u>29</u>
Transects to Date:	<u>724</u>
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED	
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS	
QA/QC INSPECTION RESULTS AND COMMENTS	
Grids QC checked: <u>00</u>	Grids QA checked: <u>00</u>
Total Grids: <u>00</u>	Total Grids: <u>00</u>
Linear feet of QC audit completed: <u>5245</u>	
Total Linear feet of QC audited: <u>9255</u>	
SAFETY INSPECTION RESULTS AND COMMENTS	
CHANGE ORDER(S): NA	
Original Scope:	
Proposed Change(s):	
Rational for Change(s):	
Approved by:	
COMING WORK PREPARATIONS AND ARRANGEMENTS	
Continue Kick out investigations	
NOTES/COMMENTS	
USACOE Safety Representative/Harmon Slappy on site.	
All data collected on Western transects was lost. Corrupted file could not be recovered /converted.	
SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)	
Eric Kirwin, USACE PM, Assist in EM-61 audits, yes.	




**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS

VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.


SIGNATURE: DATE: 9/18/08



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 9/22/2008		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Reott		
WEATHER: Sunny			TEMPERATURE: High: 75 Low: 43		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
* Continue Kick out /Transect Investigation					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	9/22/08
2	John Reott	SSHO/QC	10	PIKA	9/22/08
3	Mike Fiedler	Tech 3/Team Leader	10	PIKA	9/22/08
4	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	9/22/08
5	Thomas Holland	Tech 1	10	PIKA	9/22/08
6	Dennis Anaya	Tech 1	10	PIKA	9/22/08
7	Michael Ahmu	Tech 1	10	PIKA	9/22/08
8	Eric Stoffel	Geophysicist	10	PIKA	9/22/08
9	Mike Milne	Tech 1	10	PIKA	9/22/08
10					
11					
12					
13					
14					
15					
16					
17					
18					
19					
20					
Total work hours on this job this date			90	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			4887	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			4977	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					
N/A					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

WORK PERFORMED TODAY	
0630 – Task Order and safety meeting at office. 0645 – Checking instruments. 0700 – Team 1 & EM-61 crews departed for field 0715 – EM-62 crew collecting data for QC audits on South Transects 1200 – Break for lunch 1230 – Return to work 1630 – Return to the office 1700 – Secure for the day	
Transects Completed:	<u>29</u>
Transects to Date:	<u>724</u>
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED	
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS	
QA/QC INSPECTION RESULTS AND COMMENTS	
Grids QC checked: <u>00</u>	Grids QA checked: <u>00</u>
Total Grids: <u>00</u>	Total Grids: <u>00</u>
Linear feet of QC audit completed: <u>8400</u>	
Total Linear feet of QC audited: <u>17655</u>	
SAFETY INSPECTION RESULTS AND COMMENTS	
CHANGE ORDER(S): NA	
Original Scope:	
Proposed Change(s):	
Rational for Change(s):	
Approved by:	
COMING WORK PREPARATIONS AND ARRANGEMENTS	
Continue Kick out QC audits and anomaly investigations	
NOTES/COMMENTS	
USACOE Safety Representative/Harmon Slappy on site.	
SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)	




**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS

VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.

SIGNATURE: _____ DATE: 9/22/08



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 9/23/2008		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Reott		
WEATHER: Sunny			TEMPERATURE: High: 76 Low: 40		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
* Continue Anomaly Investigations					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	9/23/08
2	John Reott	SSHO/QC	10	PIKA	9/23/08
3	Mike Fiedler	Tech 3/Team Leader	10	PIKA	9/23/08
4	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	9/23/08
5	Thomas Holland	Tech 1	10	PIKA	9/23/08
6	Dennis Anaya	Tech 1	10	PIKA	9/23/08
7	Michael Ahmu	Tech 1	10	PIKA	9/23/08
8	Eric Stoffel	Geophysicist	10	PIKA	9/23/08
9	Mike Milne	Tech 1	10	PIKA	9/23/08
10					
11					
12					
13					
14					
15					
16					
17					
18					
19					
20					
Total work hours on this job this date			90	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			4977	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			5067	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					
N/A					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

WORK PERFORMED TODAY

0630 – Task Order and safety meeting at office.
0645 – Checking instruments.
0700 – Team 1 & EM-61 crew departed for field
0715 – EM-61 crew collecting data for QC audits
 Team 2 investigating anomalies
1000 – Hertz picked up ATV's
1200 – Break for lunch
1230 – Return to work
1600 – EM-61 completed data collection
1630 – Return to the office
1700 – Secure for the day

Transects Completed: 29
Transects to Date: 724

VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED

USACOE/Eric Kirwin/PM is satisfied data points are IAW WP and no Surveyors are required.

UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS

QA/QC INSPECTION RESULTS AND COMMENTS

Grids QC checked: 00 Grids QA checked: 00
Total Grids: 00 Total Grids: 00

Linear feet of QC audit completed: 1400
Total Linear feet of QC audited: 19055

SAFETY INSPECTION RESULTS AND COMMENTS

CHANGE ORDER(S): NA

Original Scope:
Proposed Change(s):
Rational for Change(s):
Approved by:

COMING WORK PREPARATIONS AND ARRANGEMENTS

Continue Kick out QC audits and anomaly investigations

NOTES/COMMENTS


USACOE Safety Representative/Harmon Slappy on site.
MD/Non-MD will remain in Igloo B-1039



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

MEC will be turned over to FWAD caretaker personnel
SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)
OTHER REMARKS
VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.

SIGNATURE: _____ DATE: 9/23/08



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 9/24/2008		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Reott		
WEATHER: Sunny			TEMPERATURE: High: 76 Low: 40		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
* Continue Kick out /Transect Investigation					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	9/24/08
2	John Reott	SSHO/QC	10	PIKA	9/24/08
3	Mike Fiedler	Tech 3/Team Leader	10	PIKA	9/24/08
4	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	9/24/08
5	Thomas Holland	Tech 1	10	PIKA	9/24/08
6	Dennis Anaya	Tech 1	10	PIKA	9/24/08
7	Michael Ahmu	Tech 1	10	PIKA	9/24/08
8	Eric Stoffel	Geophysicist	10	PIKA	9/24/08
9	Mike Milne	Tech 1	10	PIKA	9/24/08
10					
11					
12					
13					
14					
15					
16					
17					
18					
19					
20					
Total work hours on this job this date			90	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			5067	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			5157	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					
N/A					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137


WORK PERFORMED TODAY	
0630 – Task Order and safety meeting at office. 0645 – Checking instruments. 0700 – Team 2 departed for field 0730 – Team 2 investigating EM-61 hits 1200 – Break for lunch 1230 – Return to work 1245 – EM-61 crew reacquiring anomalies on East side no contacts Team 1 providing Ordnance avoidance for EM-61 crew 1615 – Team 2 completed anomaly investigations EM-61 crew completed reacquiring data. 1630 – Return to the office 1700 – Secure for the day	
Transects Completed:	<u>29</u>
Transects to Date:	<u>724</u>
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED	
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS	
QA/QC INSPECTION RESULTS AND COMMENTS	
Grids QC checked: <u>00</u>	Grids QA checked: <u>00</u>
Total Grids: <u>00</u>	Total Grids: <u>00</u>
Linear feet of QC audit completed: <u>0</u>	Total Linear feet of QC audited: <u>19055</u>
SAFETY INSPECTION RESULTS AND COMMENTS	
CHANGE ORDER(S): NA	
Original Scope:	
Proposed Change(s):	
Rational for Change(s):	
Approved by:	
COMING WORK PREPARATIONS AND ARRANGEMENTS	
Completed all operations	
NOTES/COMMENTS	
USACOE Safety Representative/Harmon Slappy on site.	



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)	
OTHER REMARKS	
VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.	
SIGNATURE: 	DATE: 9/24/08



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 9/25/2008		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Reott		
WEATHER: Sunny			TEMPERATURE: High: 75 Low: 40		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
* Continue Kick out /Transect Investigation					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	9/25/08
2	John Reott	SSHO/QC	10	PIKA	9/25/08
3	Mike Fiedler	Tech 3/Team Leader	10	PIKA	9/25/08
4	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	9/25/08
5	Thomas Holland	Tech 1	10	PIKA	9/25/08
6	Dennis Anaya	Tech 1	10	PIKA	9/25/08
7	Michael Ahmu	Tech 1	10	PIKA	9/25/08
8	Eric Stoffel	Geophysicist	10	PIKA	9/25/08
9	Mike Milne	Tech 1	10	PIKA	9/25/08
10					
11					
12					
13					
14					
15					
16					
17					
18					
19					
20					
Total work hours on this job this date			90	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			5157	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			5247	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					
N/A					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137


WORK PERFORMED TODAY	
<p>0630 – Task Order and safety meeting at office. 0645 – Started packing instruments and gear for shipment to Stafford. 0800 – R & R Trucking arrived on-site to pick up Demolition materials 0930 – R & R completed load-out and departed FT Wingate 1000 – Keys from BIA are returned by Mike Feidler 1200 – Break for lunch 1230 – Return to work 1245 – Cleaning vehicles for turn in to Enterprise 1300 – Turned over MEC items to FWAD personnel Mike Scoville/Mike Chee 1630 – Return to the office 1700 – Secure for the day/Tasks completed</p> <p>Transects Completed: <u>29</u> Transects to Date: <u>724</u></p>	
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED	
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS	
QA/QC INSPECTION RESULTS AND COMMENTS	
Grids QC checked: <u>00</u>	Grids QA checked: <u>00</u>
Total Grids: <u>00</u>	Total Grids: <u>00</u>
Linear feet of QC audit completed: <u>0</u>	
Total Linear feet of QC audited: <u>19055</u>	
SAFETY INSPECTION RESULTS AND COMMENTS	
CHANGE ORDER(S): NA	
Original Scope:	
Proposed Change(s):	
Rational for Change(s):	
Approved by:	
COMING WORK PREPARATIONS AND ARRANGEMENTS	
Completed all operations	
NOTES/COMMENTS	
USACOE Safety Representative/Harmon Slappy on site.	



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)	
OTHER REMARKS	
VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.	
SIGNATURE: 	DATE: 9/25/08



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 3/31/09		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Kochefko		
WEATHER: Sunny			TEMPERATURE: High: 54 Low: 21		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
* Kick Off Meeting					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	3/31/09
2	John Kochefko	SSHO/QC	10	PIKA	3/31/09
3	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	3/31/09
4	Mike Fiedler	Tech 3/Team Leader	10	PIKA	3/31/09
5	John Reott	Tech 2	10	PIKA	3/31/09
6	Mark Dalton	Tech 2	10	PIKA	3/31/09
7	Justin Ellis	Tech 1	10	PIKA	3/31/09
8	Dennis Anaya	Tech 1	10	PIKA	3/31/09
9	Brandon Guthrie	Tech 1	10	PIKA	3/31/09
10	Mathew Thompson	Tech 1	10	PIKA	3/31/09
11	Austin Galusha	Tech 1	10	PIKA	3/31/09
12	Ty Hetzel	Tech 1	10	PIKA	3/31/09
13	Eugene Bowekaty	Archeologist	10	Zuni Tribes	3/31/09
14	Paul Hanneman	PM	10	PIKA	3/31/09
15	Cory Woods	PM	10	PIKA	3/31/09
16	Wendy Church	Geophysicist	10	PIKA	3/31/09
17					
18					
19					
20					
Total work hours on this job this date			160	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			5247	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			5407	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					
N/A					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

WORK PERFORMED TODAY
0730 – Personnel mustered at Bldg 30 for in-briefs 0800 – SUXOS/Safety/Team Leaders attended kick off meeting by Paul Hanneman and Corps PM and Safety 0900 – Paul/Doc/Wendy/Team Leaders went to site to walk no access areas from previous efforts Teams started equipment check out and setting up Team gear 1200 – Break for lunch 1230 – Return to work Teams continuing gear load outs 1400 – Personnel returned from field 1700 – Secure for the day
Transects Completed: <u>00</u> Transects to Date: <u>726</u>
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS
QA/QC INSPECTION RESULTS AND COMMENTS
Linear feet of QC audits completed: <u>0</u>
Total linear feet of QC audits: <u>19055</u>
SAFETY INSPECTION RESULTS AND COMMENTS
CHANGE ORDER(S): NA
Original Scope:
Proposed Change(s):
Rational for Change(s):
Approved by:
COMING WORK PREPARATIONS AND ARRANGEMENTS
Commence Kick out investigations
NOTES/COMMENTS
SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS

Computer problems have plagued us upon start-up again. Laptop sent from Stafford

We had a problem with maps. The points did not line up from previous maps. The East side was shifted approximately 200/300 feet to the East.

VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.

SIGNATURE:

DATE:3/31/09



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 4/1/09		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Kochefko		
WEATHER: Cloudy			TEMPERATURE: High: 51 Low: 20		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
We started transect investigations from the original starting points and working inboard towards OB/OD grounds.					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	4/1/09
2	John Kochefko	SSHO/QC	10	PIKA	4/1/09
3	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	4/1/09
4	Mike Fiedler	Tech 3/Team Leader	10	PIKA	4/1/09
5	John Reott	Tech 2	10	PIKA	4/1/09
6	Mark Dalton	Tech 2	10	PIKA	4/1/09
7	Justin Ellis	Tech 1	10	PIKA	4/1/09
8	Dennis Anaya	Tech 1	10	PIKA	4/1/09
9	Brandon Guthrie	Tech 1	10	PIKA	4/1/09
10	Mathew Thompson	Tech 1	10	PIKA	4/1/09
11	Austin Galusha	Tech 1	10	PIKA	4/1/09
12	Ty Hetzel	Tech 1	10	PIKA	4/1/09
13	Eugene Bowekaty	Zuni Rep	10	Zuni Nation	4/1/09
14	Curtis Yazzie	Navajo Rep	10	Navajo Nation	4/1/09
15	Cory Woods	PM	10	PIKA	4/1/09
16	Wendy Church	Geophysicist	10	PIKA	4/1/09
17					
18					
19					
20					
Total work hours on this job this date			160	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			5407	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			5567	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					
One ATV was delivered bbut gear shifter broke when moving to building 33. We will operate without any ATV's.					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137


WORK PERFORMED TODAY
0630 – Conducted Task Order and Safety briefing 0645 – Teams conducting load out of gear and Instrument checks 0715 – Teams departed to field to commence transect investigations SSHO/QC setting up Safety/QC files and reviewing personnel qualifications Wendy and SUSOS working on maps and Geophysical data 1200 – Break for lunch 1230 – Return to work 1400 – Personnel returned from field 1700 – Secure for the day Transects Completed: <u>21</u> Transects to Date: <u>747</u>
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS
QA/QC INSPECTION RESULTS AND COMMENTS
Linear feet of QC audits completed: <u>0</u>
Total linear feet of QC audits: <u>19055</u>
SAFETY INSPECTION RESULTS AND COMMENTS
CHANGE ORDER(S): NA
Original Scope:
Proposed Change(s):
Rational for Change(s):
Approved by:
COMING WORK PREPARATIONS AND ARRANGEMENTS
Commence Kick out investigations
NOTES/COMMENTS
SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS	
The laptop sent from Stafford has gone down. We are on the phone with Jessie trying to resolve problem.	
A new laptop will be sent overnight to replace original laptop. Hard drive collapsed.	
VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.	
SIGNATURE: 	DATE:4/1/09



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 4/2/09		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Kochefko		
WEATHER: Cloudy			TEMPERATURE: High: 62 Low: 28		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
We started transect investigations from the original starting points and working inboard towards OB/OD grounds.					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	4/2/09
2	John Kochefko	SSHO/QC	10	PIKA	4/2/09
3	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	4/2/09
4	Mike Fiedler	Tech 3/Team Leader	10	PIKA	4/2/09
5	John Reott	Tech 2	10	PIKA	4/2/09
6	Mark Dalton	Tech 2	10	PIKA	4/2/09
7	Justin Ellis	Tech 1	10	PIKA	4/2/09
8	Dennis Anaya	Tech 1	10	PIKA	4/2/09
9	Brandon Guthrie	Tech 1	10	PIKA	4/2/09
10	Mathew Thompson	Tech 1	10	PIKA	4/2/09
11	Austin Galusha	Tech 1	10	PIKA	4/2/09
12	Ty Hetzel	Tech 1	10	PIKA	4/2/09
13	Eugene Bowekaty	Zuni Rep	10	Zuni Nation	4/2/09
14	Curtis Yazzie	Navajo Rep	10	Navajo Nation	4/2/09
15	Wendy Church	Geophysicist	10	PIKA	4/2/09
16					
17					
18					
19					
20					
Total work hours on this job this date			150	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			5567	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			5717	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

WORK PERFORMED TODAY
0630 – Conducted Task Order and Safety briefing 0645 – Teams conducting load out of gear and Instrument checks 0715 – Teams departed to field to commence transect investigations 1200 – Break for lunch 1230 – Return to work 1600 – Personnel returned from field Downloading and cleaning equipment 1700 – Secure for the day
Transects Completed: <u>24</u> Transects to Date: <u>771</u>
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS
QA/QC INSPECTION RESULTS AND COMMENTS
Linear feet of QC audits completed: <u>0</u>
Total linear feet of QC audits: <u>19055</u>
SAFETY INSPECTION RESULTS AND COMMENTS
CHANGE ORDER(S): NA
Original Scope:
Proposed Change(s):
Rational for Change(s):
Approved by:
COMING WORK PREPARATIONS AND ARRANGEMENTS
Continue Kick out investigations
NOTES/COMMENTS
Received new laptop from Stafford. Checked out and running well. Slow data transfer when performing corrections to data. Wendy is looking into problem.
SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)




**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS

VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.


SIGNATURE: DATE:4/2/09



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 4/3/09		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Kochefko		
WEATHER: Cloudy			TEMPERATURE: High: 56 Low: 25		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
Continue Transect investigations					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	4/3/09
2	John Kochefko	SSHO/QC	10	PIKA	4/3/09
3	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	4/3/09
4	Mike Fiedler	Tech 3/Team Leader	10	PIKA	4/3/09
5	John Reott	Tech 2	10	PIKA	4/3/09
6	Mark Dalton	Tech 2	10	PIKA	4/3/09
7	Justin Ellis	Tech 1	10	PIKA	4/3/09
8	Dennis Anaya	Tech 1	10	PIKA	4/3/09
9	Brandon Guthrie	Tech 1	10	PIKA	4/3/09
10	Mathew Thompson	Tech 1	10	PIKA	4/3/09
11	Austin Galusha	Tech 1	10	PIKA	4/3/09
12	Ty Hetzel	Tech 1	10	PIKA	4/3/09
13	Eugene Bowekaty	Zuni Rep	10	Zuni Nation	4/3/09
14	Patricia Chee	Navajo Rep	10	Navajo Nation	4/3/09
15					
16					
17					
18					
19					
20					
Total work hours on this job this date			140	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			5717	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			5857	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137


WORK PERFORMED TODAY
0630 – Conducted Task Order and Safety briefing 0645 – Teams conducting load out of gear and Instrument checks 0715 – Teams departed to field to commence transect investigations 1200 – Break for lunch 1230 – Return to work 1530 – Personnel returned from field Downloading and cleaning equipment Field day and equipment/vehicle maintenance 1700 – Secure for the day
Transects Completed: <u>29</u> Transects to Date: <u>800</u>
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS
QA/QC INSPECTION RESULTS AND COMMENTS
Linear feet of QC audits completed: <u>0</u>
Total linear feet of QC audits: <u>19055</u>
SAFETY INSPECTION RESULTS AND COMMENTS
CHANGE ORDER(S): NA
Original Scope:
Proposed Change(s):
Rational for Change(s):
Approved by:
COMING WORK PREPARATIONS AND ARRANGEMENTS
Continue Kick out investigations
NOTES/COMMENTS
SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS	
Personnel are getting acclimatized to site conditions and no problems to date	
VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.	
SIGNATURE: 	DATE:4/3/09



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 4/6/09		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Kochefko		
WEATHER: Sunny			TEMPERATURE: High: 65 Low: 23		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
Continue Transect investigations					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	4/6/09
2	John Kochefko	SSHO/QC	10	PIKA	4/6/09
3	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	4/6/09
4	Mike Fiedler	Tech 3/Team Leader	10	PIKA	4/6/09
5	John Reott	Tech 2	10	PIKA	4/6/09
6	Mark Dalton	Tech 2	10	PIKA	4/6/09
7	Justin Ellis	Tech 1	10	PIKA	4/6/09
8	Dennis Anaya	Tech 1	10	PIKA	4/6/09
9	Brandon Guthrie	Tech 1	10	PIKA	4/6/09
10	Mathew Thompson	Tech 1	10	PIKA	4/6/09
11	Austin Galusha	Tech 1	10	PIKA	4/6/09
12	Ty Hetzel	Tech 1	10	PIKA	4/6/09
13	Eugene Bowekaty	Zuni Rep	10	Zuni Nation	4/6/09
14	Patricia Chee	Navajo Rep	10	Navajo Nation	4/6/09
15	Jim King	Project Coordinator	10	PIKA	4/6/09
16					
17					
18					
19					
20					
Total work hours on this job this date			150	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			5857	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			6007	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137


WORK PERFORMED TODAY
0630 – Conducted Task Order and Safety briefing 0645 – Teams conducting load out of gear and Instrument checks 0715 – Teams departed to field to commence transect investigations 1200 – Break for lunch 1230 – Return to work 1600 – Personnel returned from field 1700 – Secure for the day
Transects Completed: <u>23</u> Transects to Date: <u>823</u>
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS
QA/QC INSPECTION RESULTS AND COMMENTS
Linear feet of QC audits completed: <u>0</u>
Total linear feet of QC audits: <u>19055</u>
SAFETY INSPECTION RESULTS AND COMMENTS
CHANGE ORDER(S): NA
Original Scope:
Proposed Change(s):
Rational for Change(s):
Approved by:
COMING WORK PREPARATIONS AND ARRANGEMENTS
Continue Kick out investigations
NOTES/COMMENTS
SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS	
John Reott suffered heat stress and was brought back to office for evaluation. He was monitored by Justin Ellis, a qualified EMT, and first aid administered immediately. A near miss report was filled out and forwarded to Drew Bryson.	
VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.	
SIGNATURE: 	DATE:4/6/09



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 4/7/09		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Kochevko		
WEATHER: Sunny			TEMPERATURE: High: 72 Low: 17		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
Continue Transect investigations					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	4/7/09
2	John Kochevko	SSHO/QC	10	PIKA	4/7/09
3	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	4/7/09
4	Mike Fiedler	Tech 3/Team Leader	10	PIKA	4/7/09
5	John Reott	Tech 2	2	PIKA	4/7/09
6	Mark Dalton	Tech 2	10	PIKA	4/7/09
7	Justin Ellis	Tech 1	10	PIKA	4/7/09
8	Dennis Anaya	Tech 1	10	PIKA	4/7/09
9	Brandon Guthrie	Tech 1	10	PIKA	4/7/09
10	Mathew Thompson	Tech 1	10	PIKA	4/7/09
11	Austin Galusha	Tech 1	10	PIKA	4/7/09
12	Ty Hetzel	Tech 1	10	PIKA	4/7/09
13	Eugene Bowekaty	Zuni Rep	10	Zuni Nation	4/7/09
14	Curtis Yazzie	Navajo Rep	10	Navajo Nation	4/7/09
15	Jim King	Project Coordinator	10	PIKA	4/7/09
16					
17					
18					
19					
20					
Total work hours on this job this date			142	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			6007	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			6149	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

WORK PERFORMED TODAY
0630 – Conducted Task Order and Safety briefing 0645 – Teams conducting load out of gear and Instrument checks 0715 – Teams departed to field to commence transect investigations 1200 – Break for lunch 1230 – Return to work 1600 – Personnel returned from field 1700 – Secure for the day
Transects Completed: <u>17</u> Transects to Date: <u>840</u>
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS
QA/QC INSPECTION RESULTS AND COMMENTS
Linear feet of QC audits completed: <u>0</u>
Total linear feet of QC audits: <u>19055</u>
SAFETY INSPECTION RESULTS AND COMMENTS
CHANGE ORDER(S): NA
Original Scope:
Proposed Change(s):
Rational for Change(s):
Approved by:
COMING WORK PREPARATIONS AND ARRANGEMENTS
Continue Kick out investigations
NOTES/COMMENTS
Reott was out sick today He attended the morning Safety brief and stayed for 2 hours and then went to his hotel to rest. Called him at 1400 and he was doing ok. Will return to work tomorrow.
SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS

VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.


SIGNATURE: _____ DATE: 4/7/09



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 4/8/09		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Kochefko		
WEATHER: Sunny			TEMPERATURE: High: 68 Low: 29		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
Continue Transect investigations					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	4/8/09
2	John Kochefko	SSHO/QC	10	PIKA	4/8/09
3	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	4/8/09
4	Mike Fiedler	Tech 3/Team Leader	10	PIKA	4/8/09
5	John Reott	Tech 2	10	PIKA	4/8/09
6	Mark Dalton	Tech 2	10	PIKA	4/8/09
7	Justin Ellis	Tech 1	10	PIKA	4/8/09
8	Dennis Anaya	Tech 1	10	PIKA	4/8/09
9	Brandon Guthrie	Tech 1	10	PIKA	4/8/09
10	Mathew Thompson	Tech 1	10	PIKA	4/8/09
11	Austin Galusha	Tech 1	10	PIKA	4/8/09
12	Ty Hetzel	Tech 1	10	PIKA	4/8/09
13	Eugene Bowekaty	Zuni Rep	10	Zuni Nation	4/8/09
14	Patricia Chee	Navajo Rep	10	Navajo Nation	4/8/09
15	Jim King	Project Coordinator	10	PIKA	4/8/09
16					
17					
18					
19					
20					
Total work hours on this job this date			150	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			6149	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			6299	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137


WORK PERFORMED TODAY
0630 – Conducted Task Order and Safety briefing 0645 – Teams conducting load out of gear and Instrument checks 0715 – Teams departed to field to commence transect investigations 1200 – Break for lunch 1230 – Return to work 1600 – Personnel returned from field 1700 – Secure for the day
Transects Completed: <u>25</u> Transects to Date: <u>865</u>
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS
QA/QC INSPECTION RESULTS AND COMMENTS
Linear feet of QC audits completed: <u>0</u>
Total linear feet of QC audits: <u>19055</u>
SAFETY INSPECTION RESULTS AND COMMENTS
CHANGE ORDER(S): NA
Original Scope:
Proposed Change(s):
Rational for Change(s):
Approved by:
COMING WORK PREPARATIONS AND ARRANGEMENTS
Continue Kick out investigations
NOTES/COMMENTS
SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS	
Issued keys to Cibola National Forest gates by Fern Becenti/USDI/BIA representative	
VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.	
SIGNATURE: 	DATE: 4/8/09



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 4/9/09		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Kochefko		
WEATHER: Sunny			TEMPERATURE: High: 70 Low: 33		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
Continue Transect investigations					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	4/9/09
2	John Kochefko	SSHO/QC	10	PIKA	4/9/09
3	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	4/9/09
4	Mike Fiedler	Tech 3/Team Leader	10	PIKA	4/9/09
5	John Reott	Tech 2	10	PIKA	4/9/09
6	Mark Dalton	Tech 2	10	PIKA	4/9/09
7	Justin Ellis	Tech 1	10	PIKA	4/9/09
8	Dennis Anaya	Tech 1	10	PIKA	4/9/09
9	Brandon Guthrie	Tech 1	10	PIKA	4/9/09
10	Mathew Thompson	Tech 1	10	PIKA	4/9/09
11	Austin Galusha	Tech 1	10	PIKA	4/9/09
12	Ty Hetzel	Tech 1	10	PIKA	4/9/09
13	Eugene Bowekaty	Zuni Rep	10	Zuni Nation	4/9/09
14	Patricia Chee	Navajo Rep	10	Navajo Nation	4/9/09
15	Jim King	Project Coordinator	10	PIKA	4/9/09
16					
17					
18					
19					
20					
Total work hours on this job this date			150	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			6299	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			6449	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

WORK PERFORMED TODAY
0630 – Conducted Task Order and Safety briefing 0645 – Teams conducting load out of gear and Instrument checks 0715 – Teams departed to field to commence transect investigations 1200 – Break for lunch 1230 – Return to work 1530 – Personnel returned from field Field Day and Equipment/Vehicle maintenance 1700 – Secure for the day
Transects Completed: <u>24</u> Transects to Date: <u>889</u>
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS
QA/QC INSPECTION RESULTS AND COMMENTS
Linear feet of QC audits completed: <u>0</u>
Total linear feet of QC audits: <u>19055</u>
SAFETY INSPECTION RESULTS AND COMMENTS
CHANGE ORDER(S): NA
Original Scope:
Proposed Change(s):
Rational for Change(s):
Approved by:
COMING WORK PREPARATIONS AND ARRANGEMENTS
Continue Kick out investigations
NOTES/COMMENTS
SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)




**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS

VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.


SIGNATURE: DATE:4/9/09



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 4/13/09		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Kochefko		
WEATHER: Sunny			TEMPERATURE: High:68 Low: 28		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
Continue Transect investigations					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	4/13/09
2	John Kochefko	SSHO/QC	10	PIKA	4/13/09
3	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	4/13/09
4	Mike Fiedler	Tech 3/Team Leader	10	PIKA	4/13/09
5	John Reott	Tech 2	10	PIKA	4/13/09
6	Mark Dalton	Tech 2	10	PIKA	4/13/09
7	Justin Ellis	Tech 1	10	PIKA	4/13/09
8	Dennis Anaya	Tech 1	10	PIKA	4/13/09
9	Brandon Guthrie	Tech 1	10	PIKA	4/13/09
10	Mathew Thompson	Tech 1	10	PIKA	4/13/09
11	Austin Galusha	Tech 1	10	PIKA	4/13/09
12	Ty Hetzel	Tech 1	10	PIKA	4/13/09
13	Eugene Bowekaty	Zuni Rep	10	Zuni Nation	4/13/09
14	Curtis Yazee	Navajo Rep	10	Navajo Nation	4/13/09
15	Jim King	Project Coordinator	10	PIKA	4/13/09
16					
17					
18					
19					
20					
Total work hours on this job this date			150	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			6449	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			6599	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

WORK PERFORMED TODAY
0630 – Conducted Task Order and Safety briefing 0645 – Teams conducting load out of gear and Instrument checks 0715 – Teams departed to field to commence transect investigations 1200 – Break for lunch 1230 – Return to work 1600 – Personnel returned from field 1700 – Secure for the day Transects Completed: <u>28</u> Transects to Date: <u>917</u>
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS
QA/QC INSPECTION RESULTS AND COMMENTS
Linear feet of QC audits completed: <u>0</u>
Total linear feet of QC audits: <u>19055</u>
SAFETY INSPECTION RESULTS AND COMMENTS
CHANGE ORDER(S): NA
Original Scope:
Proposed Change(s):
Rational for Change(s):
Approved by:
COMING WORK PREPARATIONS AND ARRANGEMENTS
Continue Kick out investigations
NOTES/COMMENTS
SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS

Mike Fiedler/Team Leader and Justin Ellis/EMT qualified UXO Tech 1 expressed their concern about John Reott. He has not shown the physical ability to cope with the extreme demands of transect investigations. He has trouble keeping up and tires easily and the Team has to carry his gear out at the close of operations.

VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.

SIGNATURE:

DATE:4/13/09



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 4/14/09		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Kochefko		
WEATHER: Sunny			TEMPERATURE: High: 68 Low: 38		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
Continue Transect investigations					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	4/14/09
2	John Kochefko	SSHO/QC	10	PIKA	4/14/09
3	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	4/14/09
4	Mike Fiedler	Tech 3/Team Leader	10	PIKA	4/14/09
5	John Reott	Tech 2	4	PIKA	4/14/09
6	Mark Dalton	Tech 2	10	PIKA	4/14/09
7	Justin Ellis	Tech 1	10	PIKA	4/14/09
8	Dennis Anaya	Tech 1	10	PIKA	4/14/09
9	Brandon Guthrie	Tech 1	10	PIKA	4/14/09
10	Mathew Thompson	Tech 1	10	PIKA	4/14/09
11	Austin Galusha	Tech 1	10	PIKA	4/14/09
12	Ty Hetzel	Tech 1	0	PIKA	4/14/09
13	Eugene Bowekaty	Zuni Rep	0	Zuni Nation	4/14/09
14	Patricia Chee	Navajo Rep	10	Navajo Nation	4/14/09
15	Jim King	Project Coordinator	10	PIKA	4/14/09
16					
17					
18					
19					
20					
Total work hours on this job this date			124	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			6599	<input type="checkbox"/> Yes	<input checked="" type="checkbox"/> No
Total work hours from start of project			6723	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137


WORK PERFORMED TODAY
0630 – Conducted Task Order and Safety briefing 0645 – Teams conducting load out of gear and Instrument checks 0715 – Teams departed to field to commence transect investigations 1200 – Break for lunch 1230 – Return to work 1600 – Personnel returned from field 1700 – Secure for the day Transects Completed: <u>19</u> Transects to Date: <u>936</u>
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS
QA/QC INSPECTION RESULTS AND COMMENTS
Linear feet of QC audits completed: <u>0</u>
Total linear feet of QC audits: <u>19055</u>
SAFETY INSPECTION RESULTS AND COMMENTS
CHANGE ORDER(S): NA
Original Scope:
Proposed Change(s):
Rational for Change(s):
Approved by:
COMING WORK PREPARATIONS AND ARRANGEMENTS
Continue Kick out investigations
NOTES/COMMENTS
SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)



PIKA International, Inc.
Daily Field Activity Report

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS	
Aerotek has John Reott scheduled for a physical exam at 0830 tomorrow morning. He can not return to work until the Aerotek Doctor approves his return	
VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.	
SIGNATURE: 	DATE:4/14/09



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 4/15/09		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Kochefko		
WEATHER: Sunny			TEMPERATURE: High:42 Low: 57		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
Continue Transect investigations					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	4/15/09
2	John Kochefko	SSHO/QC	10	PIKA	4/15/09
3	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	4/15/09
4	Mike Fiedler	Tech 3/Team Leader	10	PIKA	4/15/09
5	John Reott	Tech 2	0	PIKA	4/15/09
6	Mark Dalton	Tech 2	10	PIKA	4/15/09
7	Justin Ellis	Tech 1	10	PIKA	4/15/09
8	Dennis Anaya	Tech 1	10	PIKA	4/15/09
9	Brandon Guthrie	Tech 1	10	PIKA	4/15/09
10	Mathew Thompson	Tech 1	10	PIKA	4/15/09
11	Austin Galusha	Tech 1	10	PIKA	4/15/09
12	Ty Hetzel	Tech 1	0	PIKA	4/15/09
13	Eugene Bowekaty	Zuni Rep	10	Zuni Nation	4/15/09
14	Patricia Chee	Navajo Rep	10	Navajo Nation	4/15/09
15	Jim King	Project Coordinator	10	PIKA	4/15/09
16	Eric Stoffel	Project Manager	10	PIKA	4/15/09
17					
18					
19					
20					
Total work hours on this job this date			140	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			6723	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			6863	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137


WORK PERFORMED TODAY
0630 – Conducted Task Order and Safety briefing 0645 – Teams conducting load out of gear and Instrument checks 0715 – Teams departed to field to commence transect investigations 1200 – Break for lunch 1230 – Return to work 1600 – Personnel returned from field 1700 – Secure for the day Transects Completed: <u>26</u> Transects to Date: <u>962</u>
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS
QA/QC INSPECTION RESULTS AND COMMENTS
Linear feet of QC audits completed: <u>0</u>
Total linear feet of QC audits: <u>19055</u>
SAFETY INSPECTION RESULTS AND COMMENTS
CHANGE ORDER(S): NA
Original Scope:
Proposed Change(s):
Rational for Change(s):
Approved by:
COMING WORK PREPARATIONS AND ARRANGEMENTS
Continue Kick out investigations
NOTES/COMMENTS
SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS	
John Reott passed his Physical and will report to work tomorrow, 4/16/09.	
VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.	
SIGNATURE: 	DATE:4/15/09



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 4/16/09		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Kochevko		
WEATHER: Sunny			TEMPERATURE: High:42 Low: 57		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
Continue Transect investigations					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	4/16/09
2	John Kochevko	SSHO/QC	10	PIKA	4/16/09
3	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	4/16/09
4	Mike Fiedler	Tech 3/Team Leader	10	PIKA	4/16/09
5	John Reott	Tech 2	10	PIKA	4/16/09
6	Mark Dalton	Tech 2	10	PIKA	4/16/09
7	Justin Ellis	Tech 1	10	PIKA	4/16/09
8	Dennis Anaya	Tech 1	10	PIKA	4/16/09
9	Brandon Guthrie	Tech 1	10	PIKA	4/16/09
10	Mathew Thompson	Tech 1	10	PIKA	4/16/09
11	Austin Galusha	Tech 1	10	PIKA	4/16/09
12	Ty Hetzel	Tech 1	0	PIKA	4/16/09
13	Eugene Bowekaty	Zuni Rep	10	Zuni Nation	4/16/09
14	Patricia Chee	Navajo Rep	10	Navajo Nation	4/16/09
15	Jim King	Project Coordinator	10	PIKA	4/16/09
16	Eric Stoffel	Project Manager	10	PIKA	4/16/09
17					
18					
19					
20					
Total work hours on this job this date			150	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			6863	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			7013	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137


WORK PERFORMED TODAY
0630 – Conducted Task Order and Safety briefing 0645 – Teams conducting load out of gear and Instrument checks 0715 – Teams departed to field to commence transect investigations 0830 – EM-61 crew to field to check out GPO area 1200 – Break for lunch 1230 – Return to work 1545 – Personnel returned from field Equipment/Vehicle inspections and field day 1700 – Secure for the day
Transects Completed: <u>19</u> Transects to Date: <u>981</u>
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS
QA/QC INSPECTION RESULTS AND COMMENTS
Linear feet of QC audits completed: <u>0</u>
Total linear feet of QC audits: <u>19055</u>
SAFETY INSPECTION RESULTS AND COMMENTS
CHANGE ORDER(S): NA
Original Scope:
Proposed Change(s):
Rational for Change(s):
Approved by:
COMING WORK PREPARATIONS AND ARRANGEMENTS
Continue Kick out investigations
NOTES/COMMENTS
SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS	
John Reott reported for work today and was assigned to help Eric Stoffel with the EM-61 checkout.	
VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.	
SIGNATURE: 	DATE:4/16/09



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 4/20/09		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Kochevko		
WEATHER: Sunny			TEMPERATURE: High:76 Low: 39		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
Continue Transect investigations					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	4/20/09
2	John Kochevko	SSHO/QC	10	PIKA	4/20/09
3	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	4/20/09
4	Mike Fiedler	Tech 3/Team Leader	10	PIKA	4/20/09
5	John Reott	Tech 2	10	PIKA	4/20/09
6	Mark Dalton	Tech 2	10	PIKA	4/20/09
7	Justin Ellis	Tech 1	10	PIKA	4/20/09
8	Dennis Anaya	Tech 1	10	PIKA	4/20/09
9	Brandon Guthrie	Tech 1	10	PIKA	4/20/09
10	Mathew Thompson	Tech 1	10	PIKA	4/20/09
11	Austin Galusha	Tech 1	10	PIKA	4/20/09
12	Ty Hetzel	Tech 1	0	PIKA	4/20/09
13	Eugene Bowekaty	Zuni Rep	10	Zuni Nation	4/20/09
14	Patricia Chee	Navajo Rep	10	Navajo Nation	4/20/09
15	Jim King	Project Coordinator	10	PIKA	4/20/09
16	Eric Stoffel	Project Manager	10	PIKA	4/20/09
17	Mike Milne	EM-61 Operator	10	PIKA	4/20/09
18	Rusty Tracy	EM-61 Operator	10	PIKA	4/20/09
19					
20					
Total work hours on this job this date			170	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			7013	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			7183	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

WORK PERFORMED TODAY
0630 – Conducted Task Order and Safety briefing 0645 – Teams conducting load out of gear and Instrument checks 0715 – Teams departed to field to commence transect investigations 0730 – EM-61 crew to field to check out GPO area 1100 – EM-61 crew to field to start data collection 1200 – Break for lunch 1230 – Return to work 1615 – Personnel returned from field 1700 – Secure for the day
Transects Completed: <u>10</u> Transects to Date: <u>991</u>
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS
QA/QC INSPECTION RESULTS AND COMMENTS
Linear feet of QC audits completed: <u>0</u>
Total linear feet of QC audits: <u>19055</u>
SAFETY INSPECTION RESULTS AND COMMENTS
CHANGE ORDER(S): NA
Original Scope:
Proposed Change(s):
Rational for Change(s):
Approved by:
COMING WORK PREPARATIONS AND ARRANGEMENTS
Continue Kick out investigations
NOTES/COMMENTS
Started EM-61 QC operations
SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS

VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.


SIGNATURE: DATE:4/20/09



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 4/21/09		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Kochevko		
WEATHER: Sunny			TEMPERATURE: High:76 Low: 37		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
Continue Transect investigations					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	4/21/09
2	John Kochevko	SSHO/QC	10	PIKA	4/21/09
3	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	4/21/09
4	Mike Fiedler	Tech 3/Team Leader	10	PIKA	4/21/09
5	John Reott	Tech 2	10	PIKA	4/21/09
6	Mark Dalton	Tech 2	10	PIKA	4/21/09
7	Justin Ellis	Tech 1	10	PIKA	4/21/09
8	Dennis Anaya	Tech 1	10	PIKA	4/21/09
9	Brandon Guthrie	Tech 1	10	PIKA	4/21/09
10	Mathew Thompson	Tech 1	10	PIKA	4/21/09
11	Austin Galusha	Tech 1	10	PIKA	4/21/09
12	Ty Hetzel	Tech 1	0	PIKA	4/21/09
13	Eugene Bowekaty	Zuni Rep	10	Zuni Nation	4/21/09
14	Curtis Yazee	Navajo Rep	10	Navajo Nation	4/21/09
15	Jim King	Project Coordinator	10	PIKA	4/21/09
16	Eric Stoffel	Project Manager	10	PIKA	4/21/09
17	Mike Milne	EM-61 Operator	10	PIKA	4/21/09
18	Rusty Tracy	EM-61 Operator	10	PIKA	4/21/09
19					
20					
Total work hours on this job this date			170	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			7183	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			7353	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

WORK PERFORMED TODAY
0630 – Conducted Task Order and Safety briefing 0645 – Teams conducting load out of gear and Instrument checks 0715 – Teams departed to field to commence transect investigations 0730 – EM-61 crew to field 1200 – Break for lunch 1230 – Return to work 1615 – Personnel returned from field 1700 – Secure for the day
Transects Completed: <u>7</u> Transects to Date: <u>998</u>
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS
QA/QC INSPECTION RESULTS AND COMMENTS
Linear feet of QC audits completed: <u>0</u>
Total linear feet of QC audits: <u>19055</u>
SAFETY INSPECTION RESULTS AND COMMENTS
CHANGE ORDER(S): NA
Original Scope:
Proposed Change(s):
Rational for Change(s):
Approved by:
COMING WORK PREPARATIONS AND ARRANGEMENTS
Completed Kick out investigations
NOTES/COMMENTS
SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)




**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS

VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.


SIGNATURE: DATE:4/21/09



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 4/22/09		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Kochevko		
WEATHER: Sunny			TEMPERATURE: High:75 Low: 38		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
Reacquire and investigate anomalies					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	4/22/09
2	John Kochevko	SSHO/QC	10	PIKA	4/22/09
3	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	4/22/09
4	Mike Fiedler	Tech 3/Team Leader	10	PIKA	4/22/09
5	John Reott	Tech 2	10	PIKA	4/22/09
6	Mark Dalton	Tech 2	10	PIKA	4/22/09
7	Justin Ellis	Tech 1	10	PIKA	4/22/09
8	Dennis Anaya	Tech 1	10	PIKA	4/22/09
9	Brandon Guthrie	Tech 1	10	PIKA	4/22/09
10	Mathew Thompson	Tech 1	10	PIKA	4/22/09
11	Austin Galusha	Tech 1	10	PIKA	4/22/09
12	Ty Hetzel	Tech 1	10	PIKA	4/22/09
13	Eugene Bowekaty	Zuni Rep	0	Zuni Nation	4/22/09
14	Curtis Yazee	Navajo Rep	0	Navajo Nation	4/22/09
15	Jim King	Project Coordinator	10	PIKA	4/22/09
16	Eric Stoffel	Project Manager	10	PIKA	4/22/09
17	Mike Milne	EM-61 Operator	10	PIKA	4/22/09
18	Rusty Tracy	EM-61 Operator	10	PIKA	4/22/09
19					
20					
Total work hours on this job this date			160	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			7353	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			7513	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

WORK PERFORMED TODAY
0630 – Conducted Task Order and Safety briefing 0645 – Team One conducting load out of gear and Instrument checks for Target Investigations 0800 – EM-61 Team and Team One departed to Reacquire/Investigate anomalies 1200 – Break for lunch 1230 – Return to work 1615 – Personnel returned from field 1700 – Secure for the day
Transects Completed: <u>00</u> Transects to Date: <u>998</u>
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS
QA/QC INSPECTION RESULTS AND COMMENTS
Linear feet of QC audits completed: <u>4194</u>
Total linear feet of QC audits: <u>23249</u>
SAFETY INSPECTION RESULTS AND COMMENTS
CHANGE ORDER(S): NA
Original Scope:
Proposed Change(s):
Rational for Change(s):
Approved by:
COMING WORK PREPARATIONS AND ARRANGEMENTS
Completed Kick out investigations
NOTES/COMMENTS
SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)




**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS

VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.


SIGNATURE: DATE:4/22/09



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 4/23/09		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Kochevko		
WEATHER: Sunny			TEMPERATURE: High :76 Low: 37		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
Collect/Reacquire and investigate anomalies					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	4/23/09
2	John Kochevko	SSHO/QC	10	PIKA	4/23/09
3	Cameron Wenzel	Tech 3/Team Leader	0	PIKA	4/23/09
4	Mike Fiedler	Tech 3/Team Leader	10	PIKA	4/23/09
5	John Reott	Tech 2	10	PIKA	4/23/09
6	Mark Dalton	Tech 2	10	PIKA	4/23/09
7	Justin Ellis	Tech 1	10	PIKA	4/23/09
8	Dennis Anaya	Tech 1	0	PIKA	4/23/09
9	Brandon Guthrie	Tech 1	0	PIKA	4/23/09
10	Mathew Thompson	Tech 1	10	PIKA	4/23/09
11	Austin Galusha	Tech 1	10	PIKA	4/23/09
12	Ty Hetzel	Tech 1	10	PIKA	4/23/09
13	Eugene Bowekaty	Zuni Rep	0	Zuni Nation	4/23/09
14	Curtis Yazee	Navajo Rep	0	Navajo Nation	4/23/09
15	Jim King	Project Coordinator	10	PIKA	4/23/09
16	Eric Stoffel	Project Manager	10	PIKA	4/23/09
17	Mike Milne	EM-61 Operator	10	PIKA	4/23/09
18	Rusty Tracy	EM-61 Operator	10	PIKA	4/23/09
19					
20					
Total work hours on this job this date			130	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			7513	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			7643	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137


WORK PERFORMED TODAY
0630 – Conducted Task Order and Safety briefing 0645 – Team Two conducting load out of gear and Instrument checks for Target Investigations Team One packing out gear for shipment to Stafford 0800 – EM-61 Team and Team One departed to collect/Reacquire/Investigate anomalies 1200 – Break for lunch 1230 – Return to work 1615 – Personnel returned from field Completed EM-61 operations 1700 – Secure for the day
Transects Completed: <u>00</u> Transects to Date: <u>998</u>
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS
QA/QC INSPECTION RESULTS AND COMMENTS
Linear feet of QC audits completed: <u>2624</u>
Total linear feet of QC audits: <u>25873</u>
SAFETY INSPECTION RESULTS AND COMMENTS
CHANGE ORDER(S): NA
Original Scope:
Proposed Change(s):
Rational for Change(s):
Approved by:
COMING WORK PREPARATIONS AND ARRANGEMENTS
Demobilization
NOTES/COMMENTS
Completed all operations for Transect Kick-out Investigations
SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS
VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.

SIGNATURE: DATE:4/23/09



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

PIKA Project Manager: Corey Woods			Date: 4/24/09		
SUXOS: Dewey Thedford			PIKA UXOSOS: John Kochevko		
WEATHER: Sunny			TEMPERATURE: High :74 Low: 35		
SITE CONDITIONS: Good			Health & Safety: Detailed safety brief before leaving office, site specific task/hazardous review at the site.		
GENERAL REMARKS – Plan of the Day (POD):					
Packing gear for shipment to Stafford					
Take gear to Airport for FedEx shipping					
Clean and move all gear into one Office space					
Secure windows to prevent breakin					
PERSONNEL ON-SITE					
Number	Name	Position	Hours	EMPLOYER	DATE
1	Dewey Thedford	SUXOS	10	PIKA	4/24/09
2	Cameron Wenzel	Tech 3/Team Leader	10	PIKA	4/24/09
3	Brandon Guthrie	Tech 1	10	PIKA	4/24/09
4					
5					
6					
7					
8					
9					
10					
11					
12					
13					
14					
15					
16					
17					
18					
19					
20					
Total work hours on this job this date			30	Were there any loss time accidents this date?	
Cumulative total of work hours from previous report			7513	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
Total work hours from start of project			7543	If yes, attach summary of incident or OSHA report	
HEAVY EQUIPMENT ON-SITE: (type, model, source [rental/own], subcontractor owned/operated)					



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

WORK PERFORMED TODAY
0630 – Conducted Task Order and Safety briefing 0645 – Continued packing gear for shipment to Stafford 1200 – Break for lunch 1230 – Return to work 1600 – Secure for the day
Transects Completed: <u>00</u> Transects to Date: <u>998</u>
VERBAL OR WRITTEN INSTRUCTIONS GIVEN OR RECEIVED
UNFORESEEN SITE CONDITIONS AND/OR POTENTIAL PROBLEMS
QA/QC INSPECTION RESULTS AND COMMENTS
Linear feet of QC audits completed: <u>2624</u>
Total linear feet of QC audits: <u>25873</u>
SAFETY INSPECTION RESULTS AND COMMENTS
CHANGE ORDER(S): NA
Original Scope:
Proposed Change(s):
Rational for Change(s):
Approved by:
COMING WORK PREPARATIONS AND ARRANGEMENTS
Demobilization
NOTES/COMMENTS
Shipping all Trimble items to Stafford for sorting and ensuring correct items are returned to Western Data
SITE VISITORS: (Name, Title, Reason for visit, Trained on HSP?)



**PIKA International, Inc.
Daily Field Activity Report**

Project Name: Kick out Investigation
Pika Contract Number: W912BV-04-D-2016-DY02

Project Location: Ft Wingate, New Mexico
PIKA Project Number: 08-12-137

OTHER REMARKS

VERIFICATION BY FIELD SUPERINTENDENT: The above report is, to the best of my knowledge, complete and correct.


SIGNATURE: DATE:4/24/09

APPENDIX G
WEEKLY REPORTS

Kick-Out Investigation

WEEKLY REPORT

Contract No:	W912BV-04-D-2016	Report No.	01
PIKA Project #:	08-12-137	Date:	08-10-08 to 08-16-08
Project:	Kick-out Investigation, Parcel 3 Boundary, Ft Wingate Army Activity Depot, McKinley County, New Mexico		

Summary of Activities:

- Kickoff meeting held in Bldg 1 on Monday, 8/11/08
- Started Transect Investigation
- Rick Holthouser and Jerry Stone conducted a Magazine Inspection and Site Audit. Minor issues noted and corrected.

Remarks: (include directions received from client's representative or regulators, visitors, compliance notices received, pertinent information)

Work Completed:	This Week	Cumulative	% Complete
Number of Transects completed	63	63	6
Number of QC audits completed	0	0	0
Number of QA audits completed	0	0	0
Number of Targets Dug	134	134	N/A
MEC Items recovered	0	0	N/A
Munitions Debris (MD) recovered (lbs estimate)	44	44	N/A
Scrap Metal/Metals Waste (MW) recovered (lbs estimate)	0	0	N/A

Health and Safety

- Conducted health and safety meetings and task order meetings every morning, prior to commencement of daily activities.

Were there any lost time accidents this week? No Yes .

If "yes", refer attached summary of incident or OSHA report.

Kick-Out Investigation

Quality Control			
Inspections Performed	Non-Conformances	Corrective Action (CA)	Follow-up on CA
Schonstedts	None		
Whites all metal detectors	None		
Vehicle Inspections	None		
<p>Notes:</p> <ul style="list-style-type: none"> • USACE Safety representative Harmon Slappy on site • Received repaired Whites All-Metals Detector 			
<p>Schedule for Next Week</p> <ul style="list-style-type: none"> • Continue Transect/Kick-out investigation. • NM licensed surveyors/Depauli Engineering & Surveying Co to set in grids stakes at SW corner of 84 Arroyo grids. <p>Refer attached Schedule for percentage of work completed and projected completion dates.</p>			
SUXOS	Dewey Thedford	Safety/QC Officer	John Reott
UXO Team Lead	Mike Fiedler	Project Manager	Corey Woods

Kick-Out Investigation

PHOTO DOCUMENTATION



Navigating to Transect Points with Trimble



Pinpointing Grid Stake Location

Kick-Out Investigation



Checking Point before Hammering in Grid Stake




Hammering in Grid Stakes



Project Schedule for Kickout Delineation, Parcel 3,
Fort Wingate Army Activity Depot, McKinley County, New Mexico

Contract #W912BV-04-D-2016 / DY02

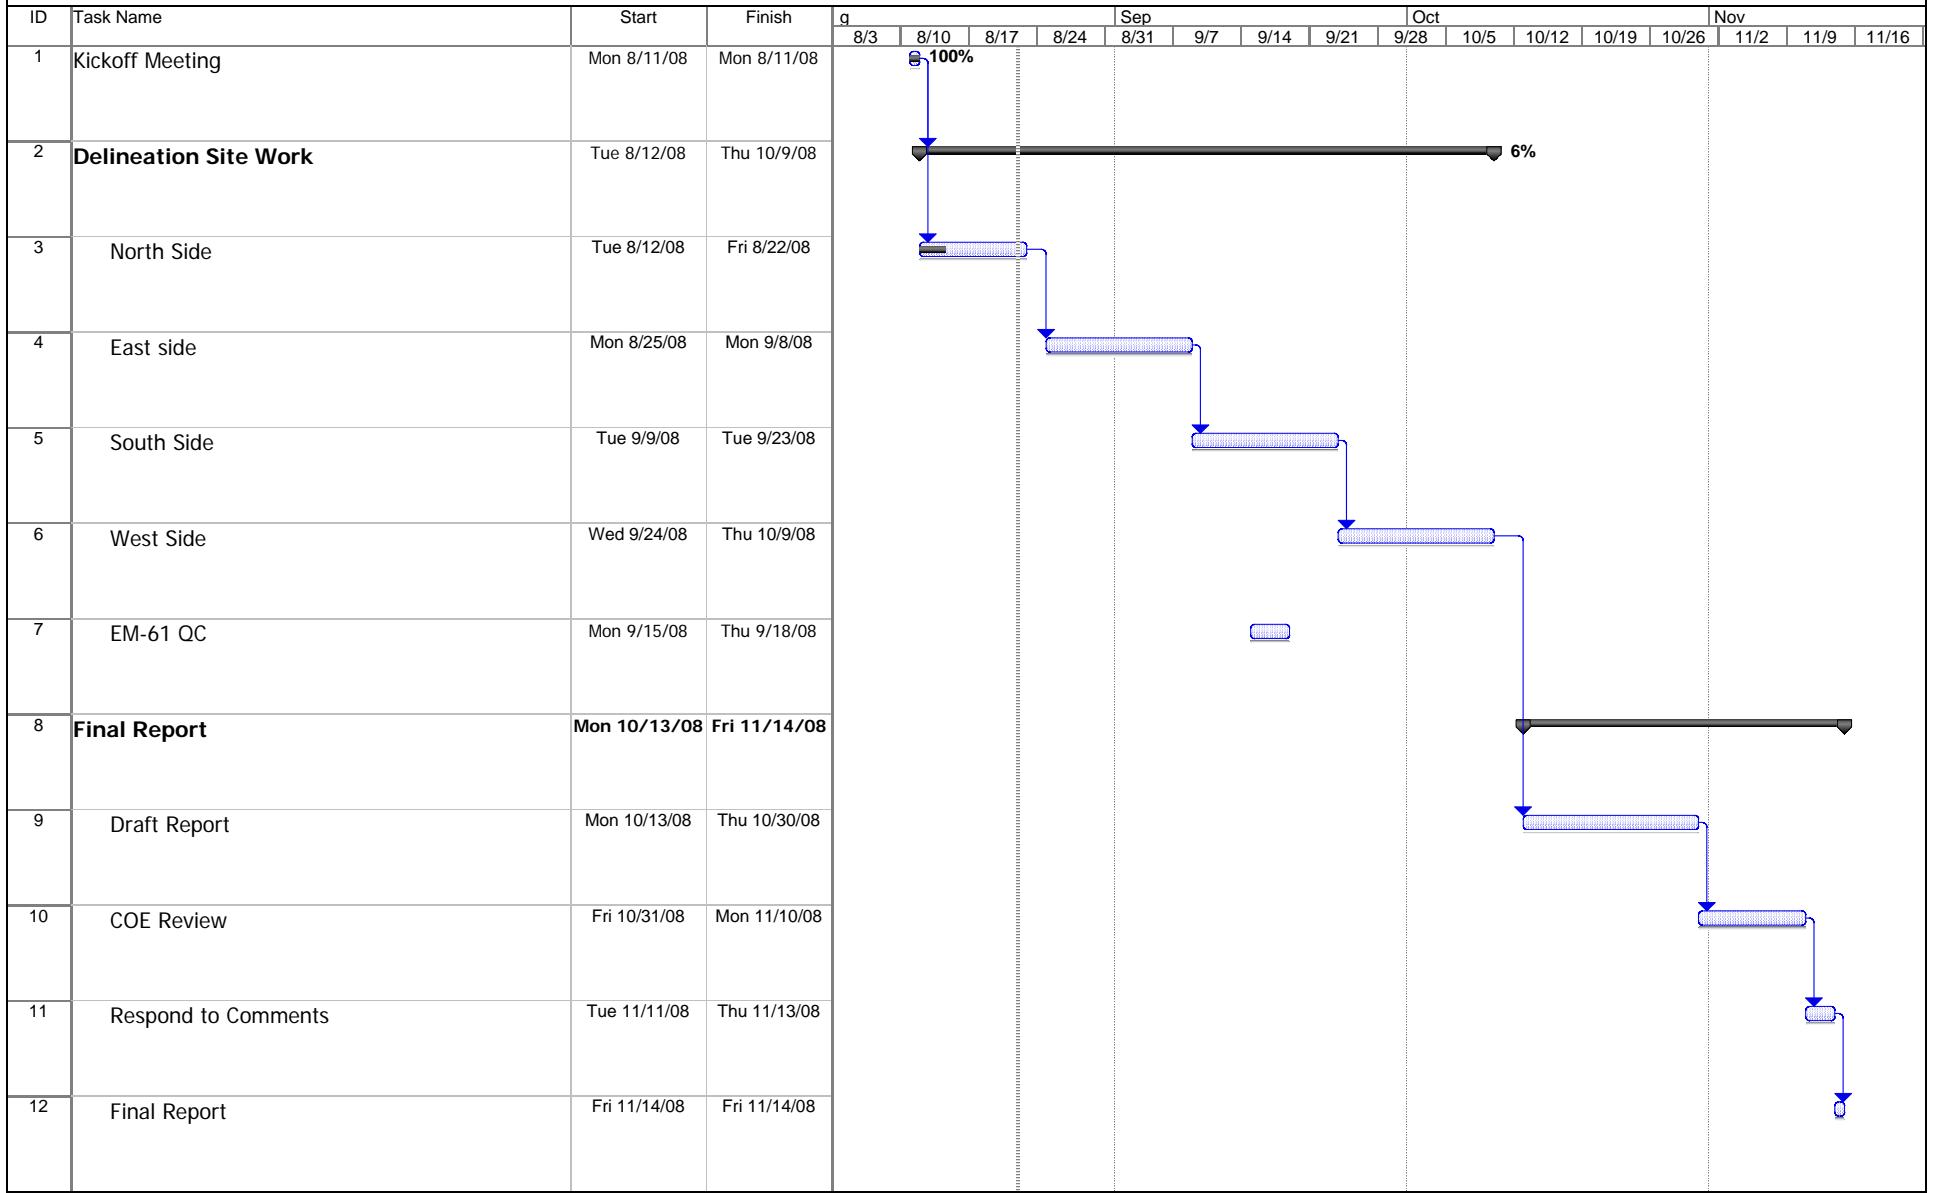

Prepared By: PIKA International, Inc.
Date: 08/16/08

Task		Milestone		External Tasks	
Split		Summary		External MileTask	
Progress		Project Summary		Split	

Kick-Out Investigation

WEEKLY REPORT

Contract No:	W912BV-04-D-2016	Report No.	2
PIKA Project #:	08-12-137	Date:	08-17-08 to 08-23-08
Project:	Kick-out Investigation, Parcel 3 Boundary, Ft Wingate Army Activity Depot, McKinley County, New Mexico		

Summary of Activities:

- Kickoff Transect Investigations
- Escorting surveyor putting in SW corner grid stakes in Arroyo

Remarks: (include directions received from client's representative or regulators, visitors, compliance notices received, pertinent information)

Work Completed:	This Week	Cumulative	% Complete
Number of Transects completed	206	275	29%
Number of QC audits completed	0	0	0
Number of QA audits completed	0	0	0
Number of Targets Dug	402	536	N/A
MEC Items recovered	0	0	N/A
Munitions Debris (MD) recovered (lbs estimate)	71	115	N/A
Scrap Metal/Metals Waste (MW) recovered (lbs estimate)	0	3	N/A

Health and Safety

- Conducted health and safety meetings and task order meetings every morning, prior to commencement of daily activities.

Were there any lost time accidents this week? No Yes .

If "yes", refer attached summary of incident or OSHA report.

Kick-Out Investigation

Quality Control			
Inspections Performed	Non-Conformances	Corrective Action (CA)	Follow-up on CA
Schonstedts	None		
Whites all metal detectors	None		
Vehicle Inspections	None		
<p>Notes:</p> <ul style="list-style-type: none"> • USACE Safety representative Harmon Slappy on site • Eugene Bowekaty/Zuni Representative did not work on Tuesday and Wednesday of this week. 			
<p>Schedule for Next Week</p> <ul style="list-style-type: none"> • Continue Transect/Kick-out investigation. • Continue escorting surveyors putting in SW corner grid stakes in Arroyo 			
<p>Refer attached Schedule for percentage of work completed and projected completion dates.</p>			
SUXOS	Dewey Thedford	Safety/QC Officer	John Reott
UXO Team Lead	Mike Fiedler	Project Manager	Corey Woods

Kick-Out Investigation

PHOTO DOCUMENTATION



Teams Loading Gear for Transect Investigations



Navigating to Transect Points with Trimble

Kick-Out Investigation



Investigating Transect for Anomalies




QC/Safety Assisting Teams in Field




Project Schedule for Kickout Delineation, Parcel 3,
Fort Wingate Army Activity Depot, McKinley County, New Mexico

Contract #W912BV-04-D-2016 / DY02

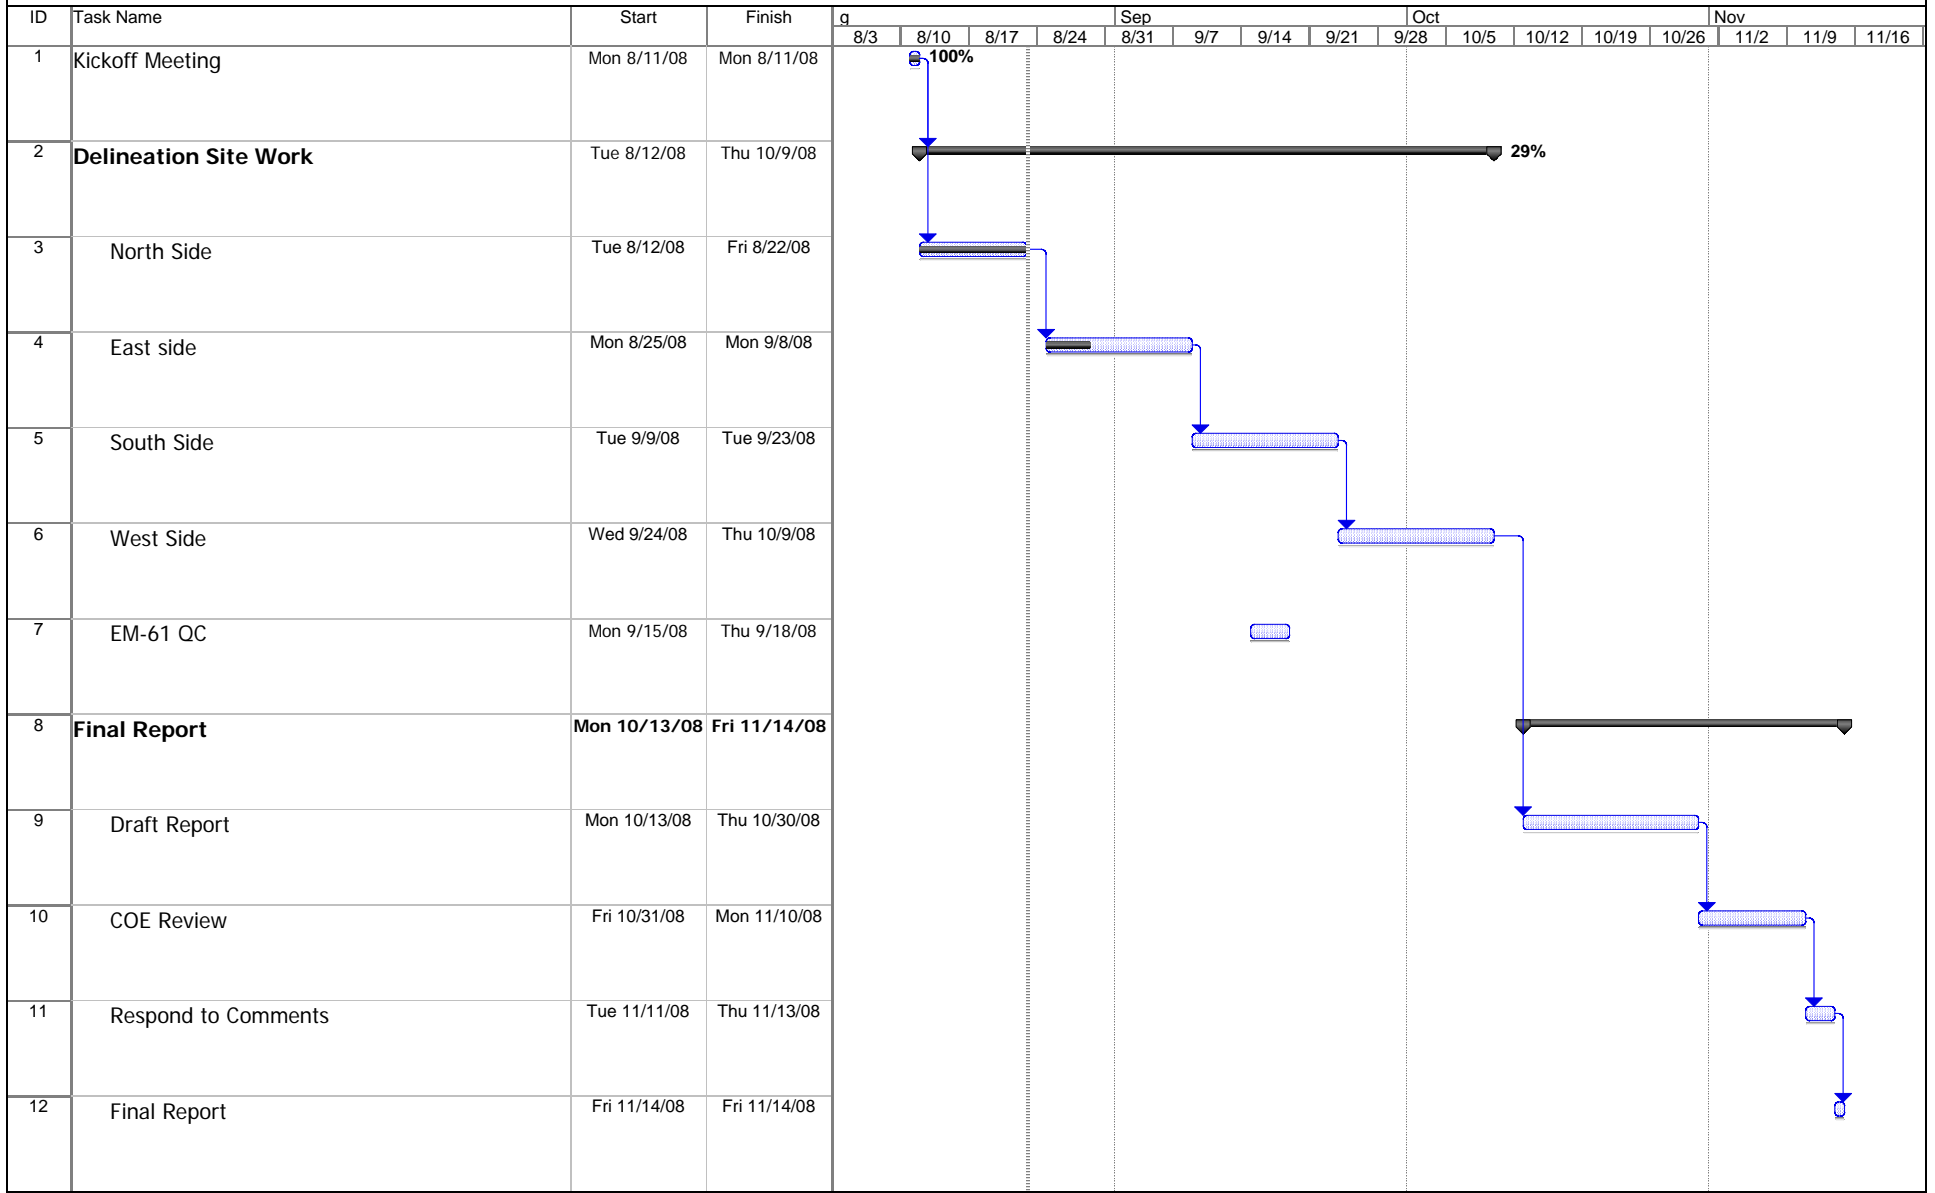

Prepared By: PIKA International, Inc.
Date: 08/23/08



Kick-Out Investigation

WEEKLY REPORT

Contract No:	W912BV-04-D-2016	Report No.	3
PIKA Project #:	08-12-137	Date:	08-24-08 to 08-30-08
Project:	Kick-out Investigation, Parcel 3 Boundary, Ft Wingate Army Activity Depot, McKinley County, New Mexico		
Summary of Activities:			
<ul style="list-style-type: none"> Continued Transect Investigations 			
Remarks: (include directions received from client's representative or regulators, visitors, compliance notices received, pertinent information)			

Work Completed:	This Week	Cumulative	% Complete
Number of Transects completed	159	434	45%
Number of QC audits completed	0	0	0
Number of QA audits completed	0	0	0
Number of Targets Dug	713	1249	N/A
MEC Items recovered	0	0	N/A
Munitions Debris (MD) recovered (lbs estimate)	331	446	N/A
Scrap Metal/Metals Waste (MW) recovered (lbs estimate)	158	171	N/A

Health and Safety

- Conducted health and safety meetings and task order meetings every morning, prior to commencement of daily activities.

Were there any lost time accidents this week? No Yes .

If "yes", refer attached summary of incident or OSHA report.

Kick-Out Investigation

Quality Control			
Inspections Performed	Non-Conformances	Corrective Action (CA)	Follow-up on CA
Schonstedts	None		
Whites all metal detectors	None		
Vehicle Inspections	None		
<p>Notes:</p> <ul style="list-style-type: none"> • USACE Safety representative Harmon Slappy on site • Michael Ahmu (Tech 1) reported onboard today to fill vacancy on Team One. 			
<p>Schedule for Next Week</p> <ul style="list-style-type: none"> • Continue Transect/Kick-out investigation. 			
<p>Refer attached Schedule for percentage of work completed and projected completion dates.</p>			
SUXOS	Dewey Thedford	Safety/QC Officer	John Reott
UXO Team Lead	Mike Fiedler	Project Manager	Corey Woods

Kick-Out Investigation

PHOTO DOCUMENTATION



Sweeping Transects Lanes for Anomalies



Hand Excavating an Anomaly

Kick-Out Investigation



Burnt Out 57-mm Projectile/Munitions Debris




Loading Gear at End of Work Day



Project Schedule for Kickout Delineation, Parcel 3,
Fort Wingate Army Activity Depot, McKinley County, New Mexico

Contract #W912BV-04-D-2016 / DY02

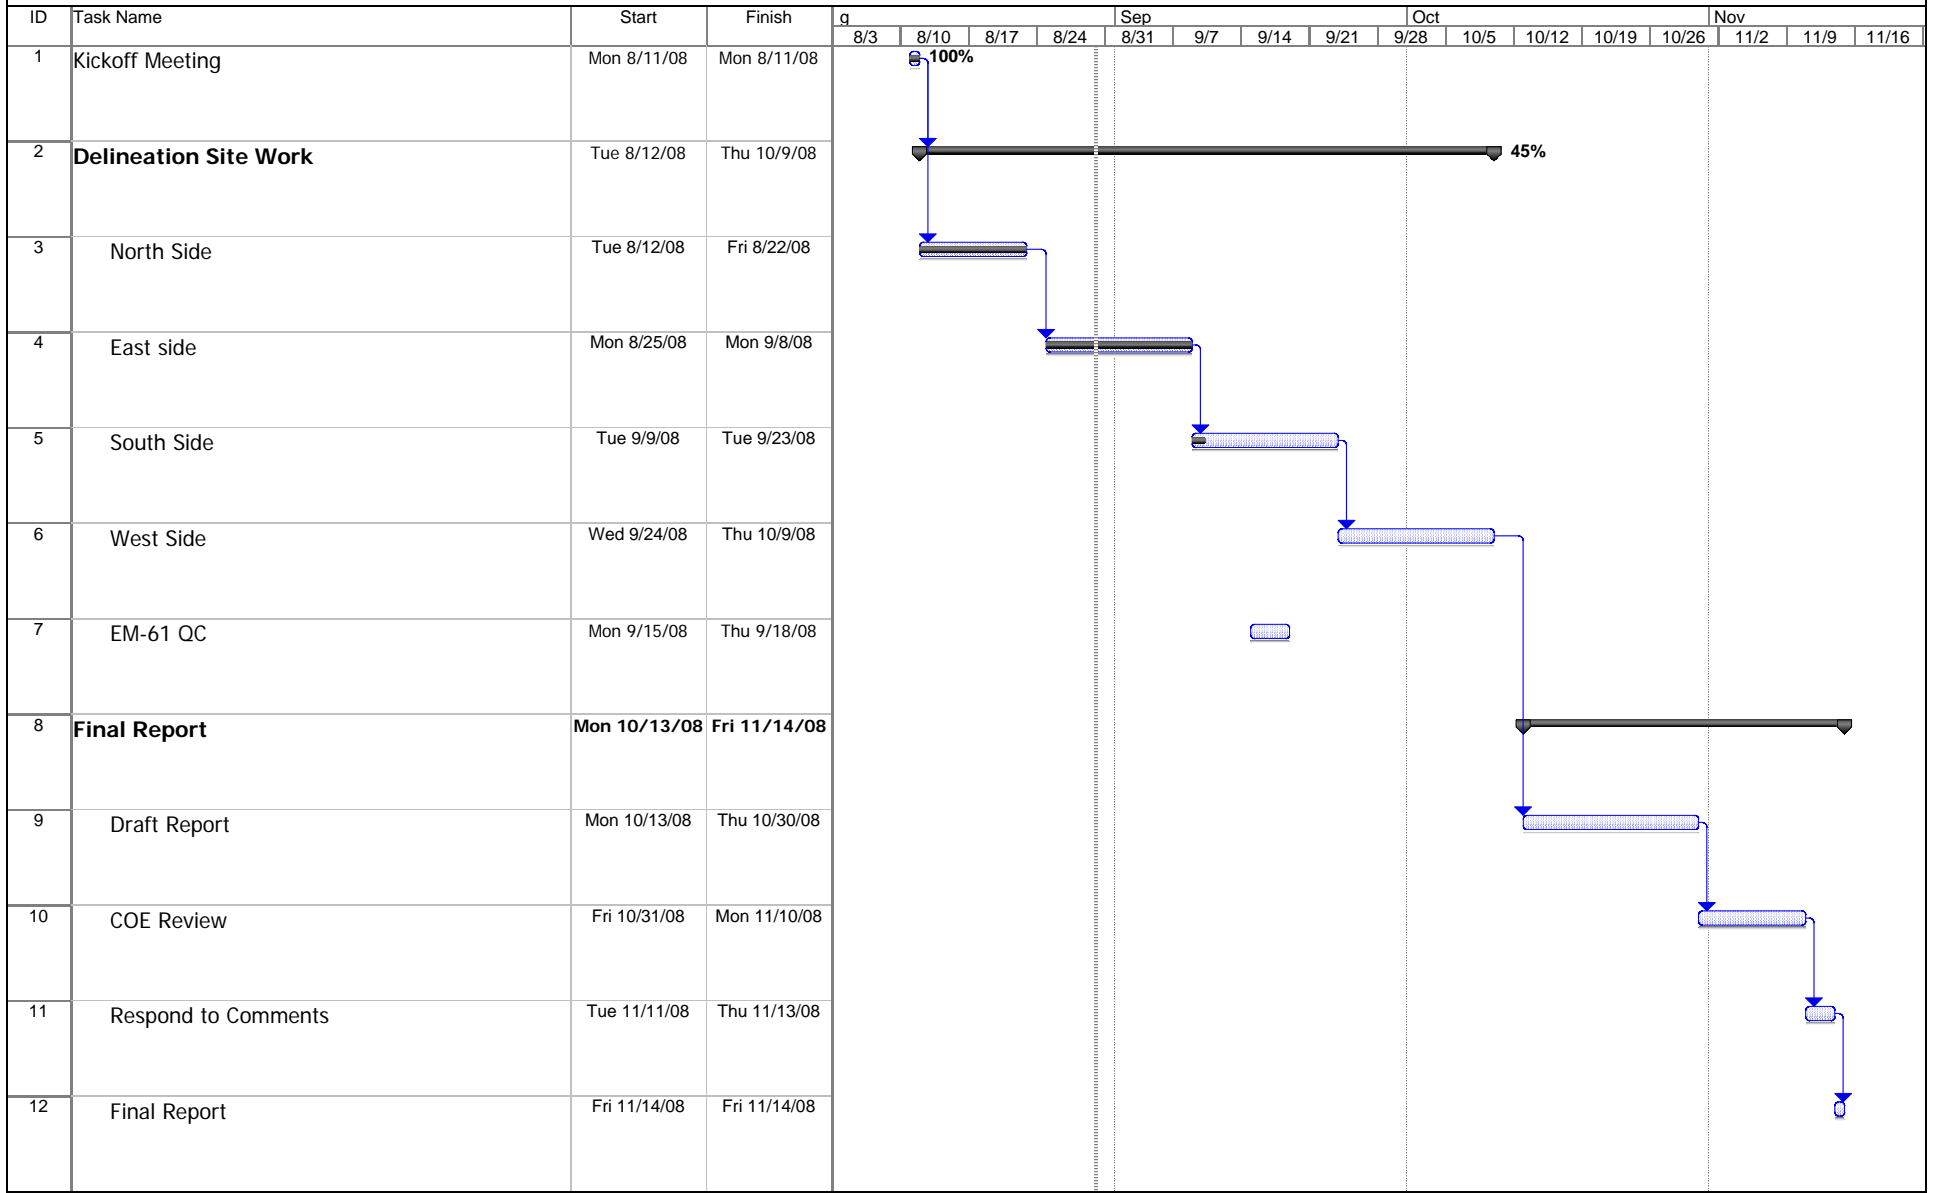

Prepared By: PIKA International, Inc.
Date: 08/30/08



Kick-Out Investigation

WEEKLY REPORT

Contract No:	W912BV-04-D-2016	Report No.	4
PIKA Project #:	08-12-137	Date:	08-31-08 to 09-06-08
Project:	Kick-out Investigation, Parcel 3 Boundary, Ft Wingate Army Activity Depot, McKinley County, New Mexico		
Summary of Activities:			
<ul style="list-style-type: none"> Kickout Transect Investigations 			
Remarks: (include directions received from client's representative or regulators, visitors, compliance notices received, pertinent information)			

Work Completed:	This Week	Cumulative	% Complete
Number of Transects completed	127	561	61%
Number of QC audits completed	0	0	0
Number of QA audits completed	0	0	0
Number of Targets Dug	131	1380	N/A
MEC Items recovered	0	0	N/A
Munitions Debris (MD) recovered (lbs estimate)	57	503	N/A
Scrap Metal/Metals Waste (MW) recovered (lbs estimate)	28	199	N/A

Health and Safety

- Conducted health and safety meetings and task order meetings every morning, prior to commencement of daily activities.

Were there any lost time accidents this week? No Yes .

If "yes", refer attached summary of incident or OSHA report.

Kick-Out Investigation

Quality Control			
Inspections Performed	Non-Conformances	Corrective Action (CA)	Follow-up on CA
Schonstedts	None		
Whites all metal detectors	None		
Vehicle Inspections	None		
<p>Notes:</p> <ul style="list-style-type: none"> USACE Safety representative Harmon Slappy was not on site this week 			
<p>Schedule for Next Week</p> <ul style="list-style-type: none"> Continue Transect/Kick-out investigation. <p>Refer attached Schedule for percentage of work completed and projected completion dates.</p>			
SUXOS	Dewey Thedford	Safety/QC Officer	John Reott
UXO Team Lead	Mike Fiedler	Project Manager	Corey Woods

Kick-Out Investigation

PHOTO DOCUMENTATION



Looking for Access to Transect Lanes



Navigating along Transect Lanes

Kick-Out Investigation



Climbing up Mountain Side




Inserting Grid Stake on Transect Lane Point



Project Schedule for Kickout Delineation, Parcel 3,
Fort Wingate Army Activity Depot, McKinley County, New Mexico

Contract #W912BV-04-D-2016 / DY02

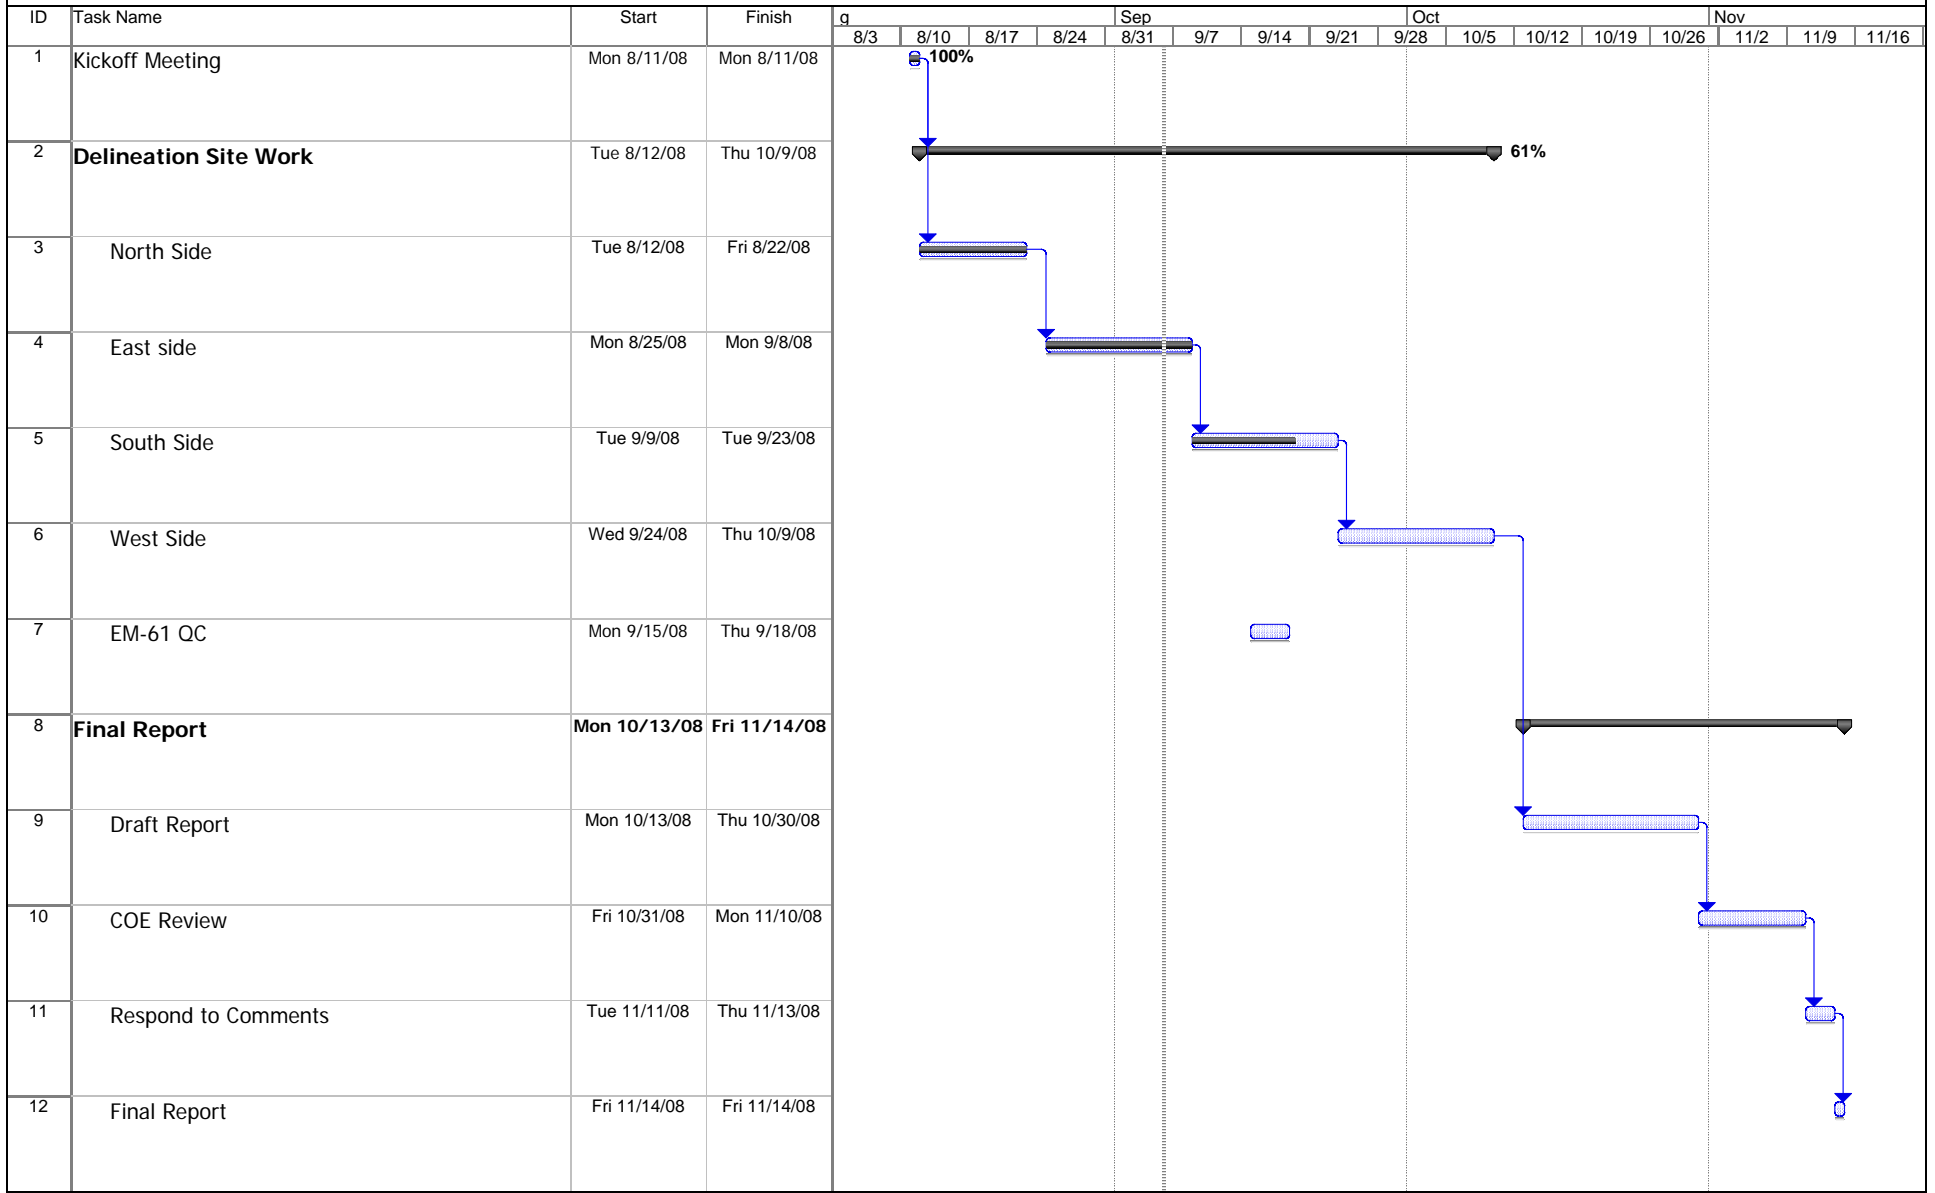

Prepared By: PIKA International, Inc.
Date: 09/06/08

Task		Milestone		External Tasks	
Split		Summary		External MileTask	
Progress		Project Summary		Split	

Kick-Out Investigation

WEEKLY REPORT

Contract No:	W912BV-04-D-2016	Report No.	5
PIKA Project #:	08-12-137	Date:	09-07-08 to 09-13-08
Project:	Kick-out Investigation, Parcel 3 Boundary, Ft Wingate Army Activity Depot, McKinley County, New Mexico		

Summary of Activities:

- Continued Transect Investigations

Remarks: (include directions received from client's representative or regulators, visitors, compliance notices received, pertinent information)

Several potential archeological sites were identified and investigated by the tribal archeologists, photos are included under Photo Documentation; did not affect work progress.

Work Completed:	This Week	Cumulative	% Complete
Number of Transects completed	99	660	66%
Number of QC audits completed	0	0	0
Number of QA audits completed	0	0	0
Number of Targets Dug	8	1388	N/A
MEC Items recovered	0	0	N/A
Munitions Debris (MD) recovered (lbs estimate)	0	503	N/A
Scrap Metal/Metals Waste (MW) recovered (lbs estimate)	5	204	N/A

Health and Safety

- Conducted health and safety meetings and task order meetings every morning, prior to commencement of daily activities.

Were there any lost time accidents this week? No Yes .

If "yes", refer attached summary of incident or OSHA report.

Kick-Out Investigation

Quality Control			
Inspections Performed	Non-Conformances	Corrective Action (CA)	Follow-up on CA
Schonstedts	None		
Whites all metal detectors	None		
Vehicle Inspections	None		
<p>Notes:</p> <ul style="list-style-type: none"> • USACE Safety representative Harmon Slappy on site this week • Eugene Bowekaty/Zuni Archeologist did not report for work on Monday, 9/8/08. 			
<p>Schedule for Next Week</p> <ul style="list-style-type: none"> • Continue Transect/Kick-out investigation. • Conduct EM-61 QC audits • Escort DePauli surveyors into arroyo to stake in South West grid stakes. <p>Refer attached Schedule for percentage of work completed and projected completion dates.</p>			
SUXOS	Dewey Thedford	Safety/QC Officer	John Reott
UXO Team Lead	Mike Fiedler	Project Manager	Corey Woods

Kick-Out Investigation

PHOTO DOCUMENTATION



Archeological Site



Archeological Site

Kick-Out Investigation



Archeological Site




Archeological Site



Project Schedule for Kickout Delineation, Parcel 3,
Fort Wingate Army Activity Depot, McKinley County, New Mexico

Contract #W912BV-04-D-2016 / DY02

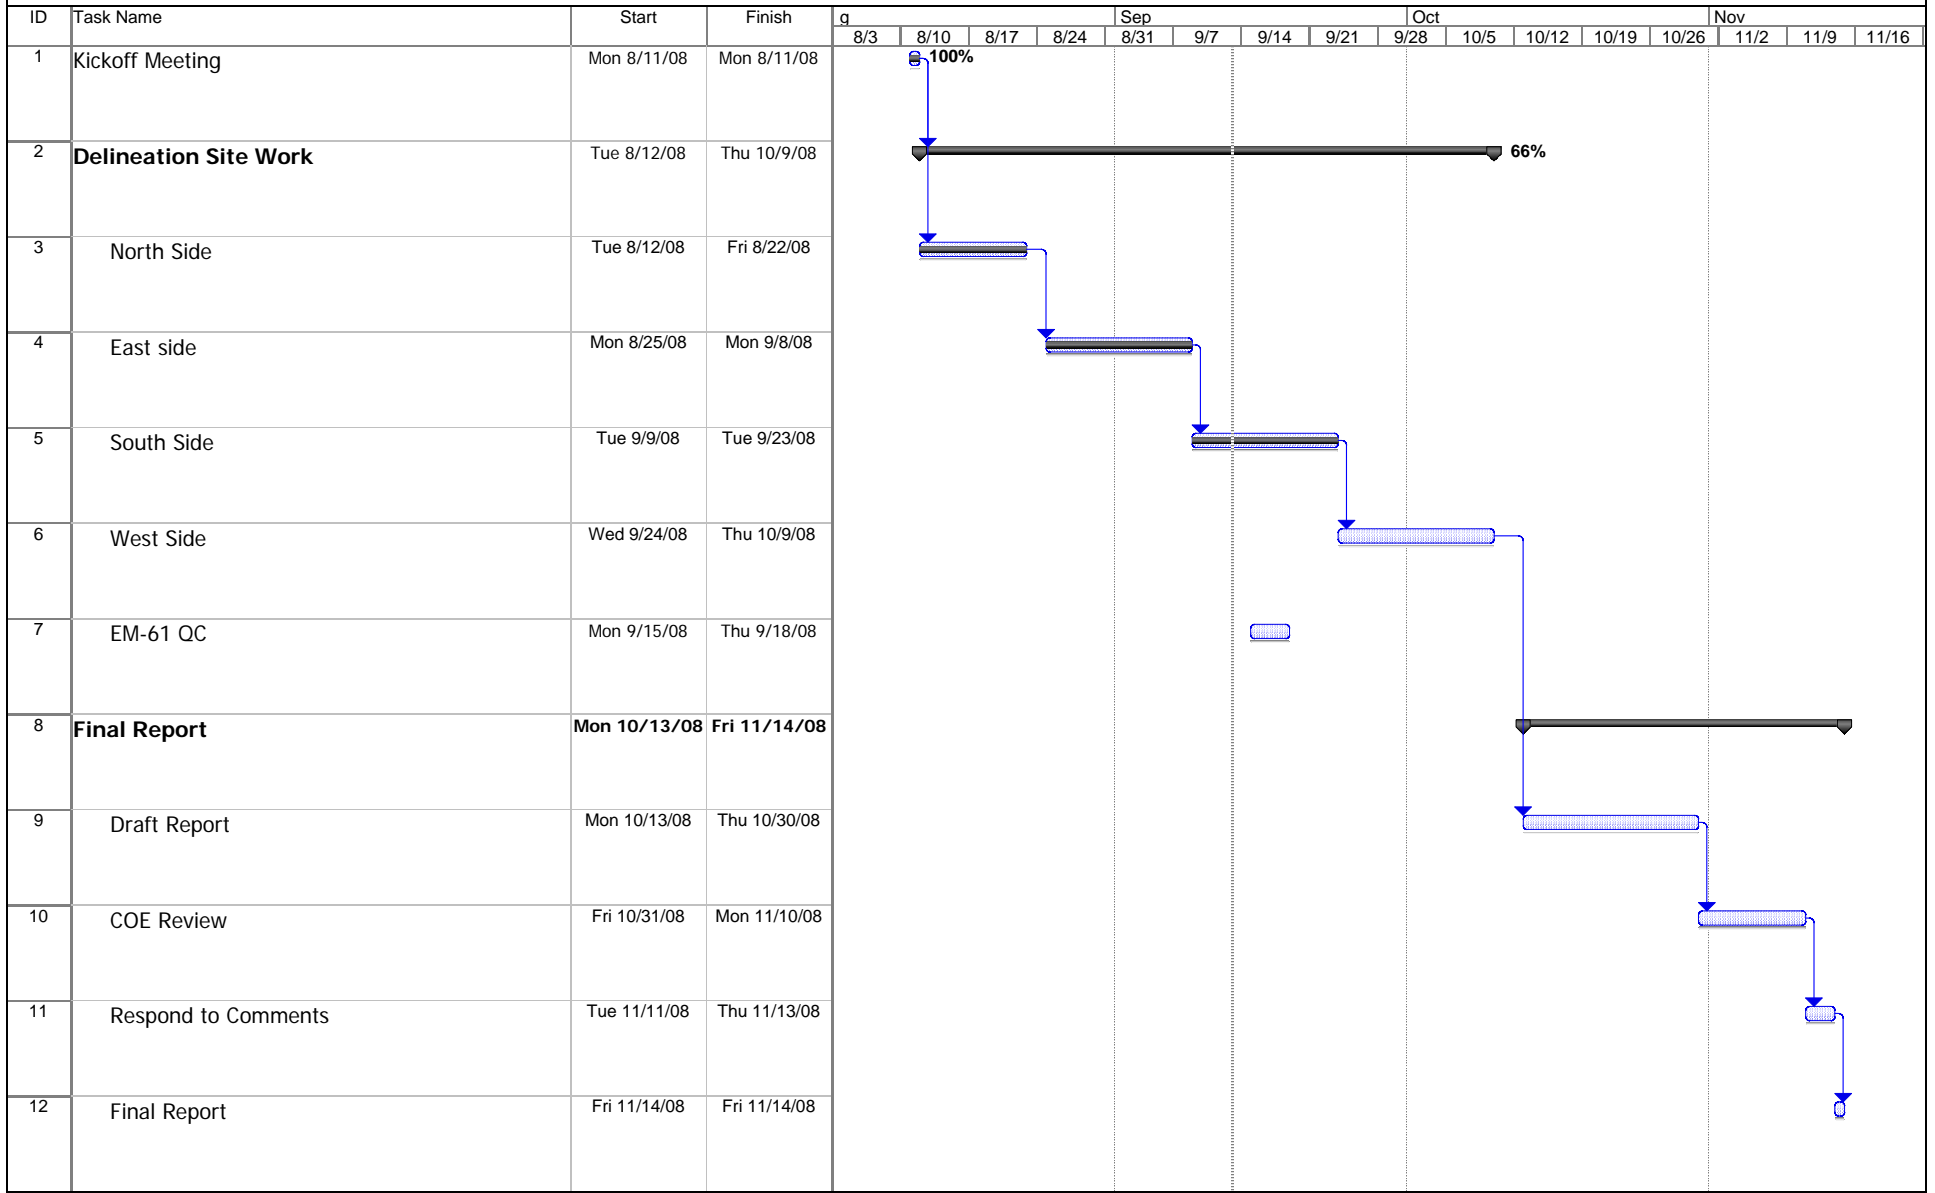

Prepared By: PIKA International, Inc.
Date: 09/13/08

Task		Milestone		External Tasks	
Split		Summary		External MileTask	
Progress		Project Summary		Split	

Kick-Out Investigation

WEEKLY REPORT

Contract No:	W912BV-04-D-2016	Report No.	6
PIKA Project #:	08-12-137	Date:	09-14-08 to 09-20-08
Project:	Kick-out Investigation, Parcel 3 Boundary, Ft Wingate Army Activity Depot, McKinley County, New Mexico		

Summary of Activities:

- Completed all kick out Transects
- Started EM-61 QC operations

Remarks: (include directions received from client's representative or regulators, visitors, compliance notices received, pertinent information)

Work Completed:	This Week	Cumulative	% Complete
Number of Transects completed	66	726	100
Linear Feet of Transects completed	13,986	140,863	100
Linear Feet of Transect QC audits completed	9255	9255	66
Number of Targets Dug	2	1390	N/A
MEC Items recovered	0	0	N/A
Munitions Debris (MD) recovered (lbs estimate)	0	503	N/A
Scrap Metal/Metals Waste (MW) recovered (lbs estimate)	1	205	N/A

Health and Safety

- Conducted health and safety meetings and task order meetings every morning, prior to commencement of daily activities.

Were there any lost time accidents this week? No Yes .

If "yes", refer attached summary of incident or OSHA report.

Kick-Out Investigation

Quality Control			
Inspections Performed	Non-Conformances	Corrective Action (CA)	Follow-up on CA
Schonstedts	None		
Whites all metal detectors	None		
Vehicle Inspections	None		
<p>Notes:</p> <ul style="list-style-type: none"> • USACE Safety representative Harmon Slappy and PM Eric Kirwan on site this week • Navajo and Zuni Archeologists were not utilized this week. 			
<p>Schedule for Next Week.</p> <ul style="list-style-type: none"> • Continue EM-61 QC audits • Investigate anomalies acquired by EM-61 audits • Ship all explosives to Camp Bonneville • Pack and ship equipment/instruments to Stafford <p>Refer attached Schedule for percentage of work completed and projected completion dates.</p>			
SUXOS	Dewey Thedford	Safety/QC Officer	John Reott
UXO Team Lead	Mike Fiedler	Project Manager	Corey Woods

Kick-Out Investigation

PHOTO DOCUMENTATION



MEC in Igloo B-1038



MEC in Igloo B-1038

Kick-Out Investigation



Jet Perforators, Detonating Cord and Boosters stored in Igloo B-1029



Electric Blasting Caps stored in Igloo B-1028

Kick-Out Investigation



205 Pounds of Scrap Metal Recovered in Arroyo




503 Pounds of Munitions Debris Recovered in Arroyo



Project Schedule for Kickout Delineation, Parcel 3,
Fort Wingate Army Activity Depot, McKinley County, New Mexico

Contract #W912BV-04-D-2016 / DY02

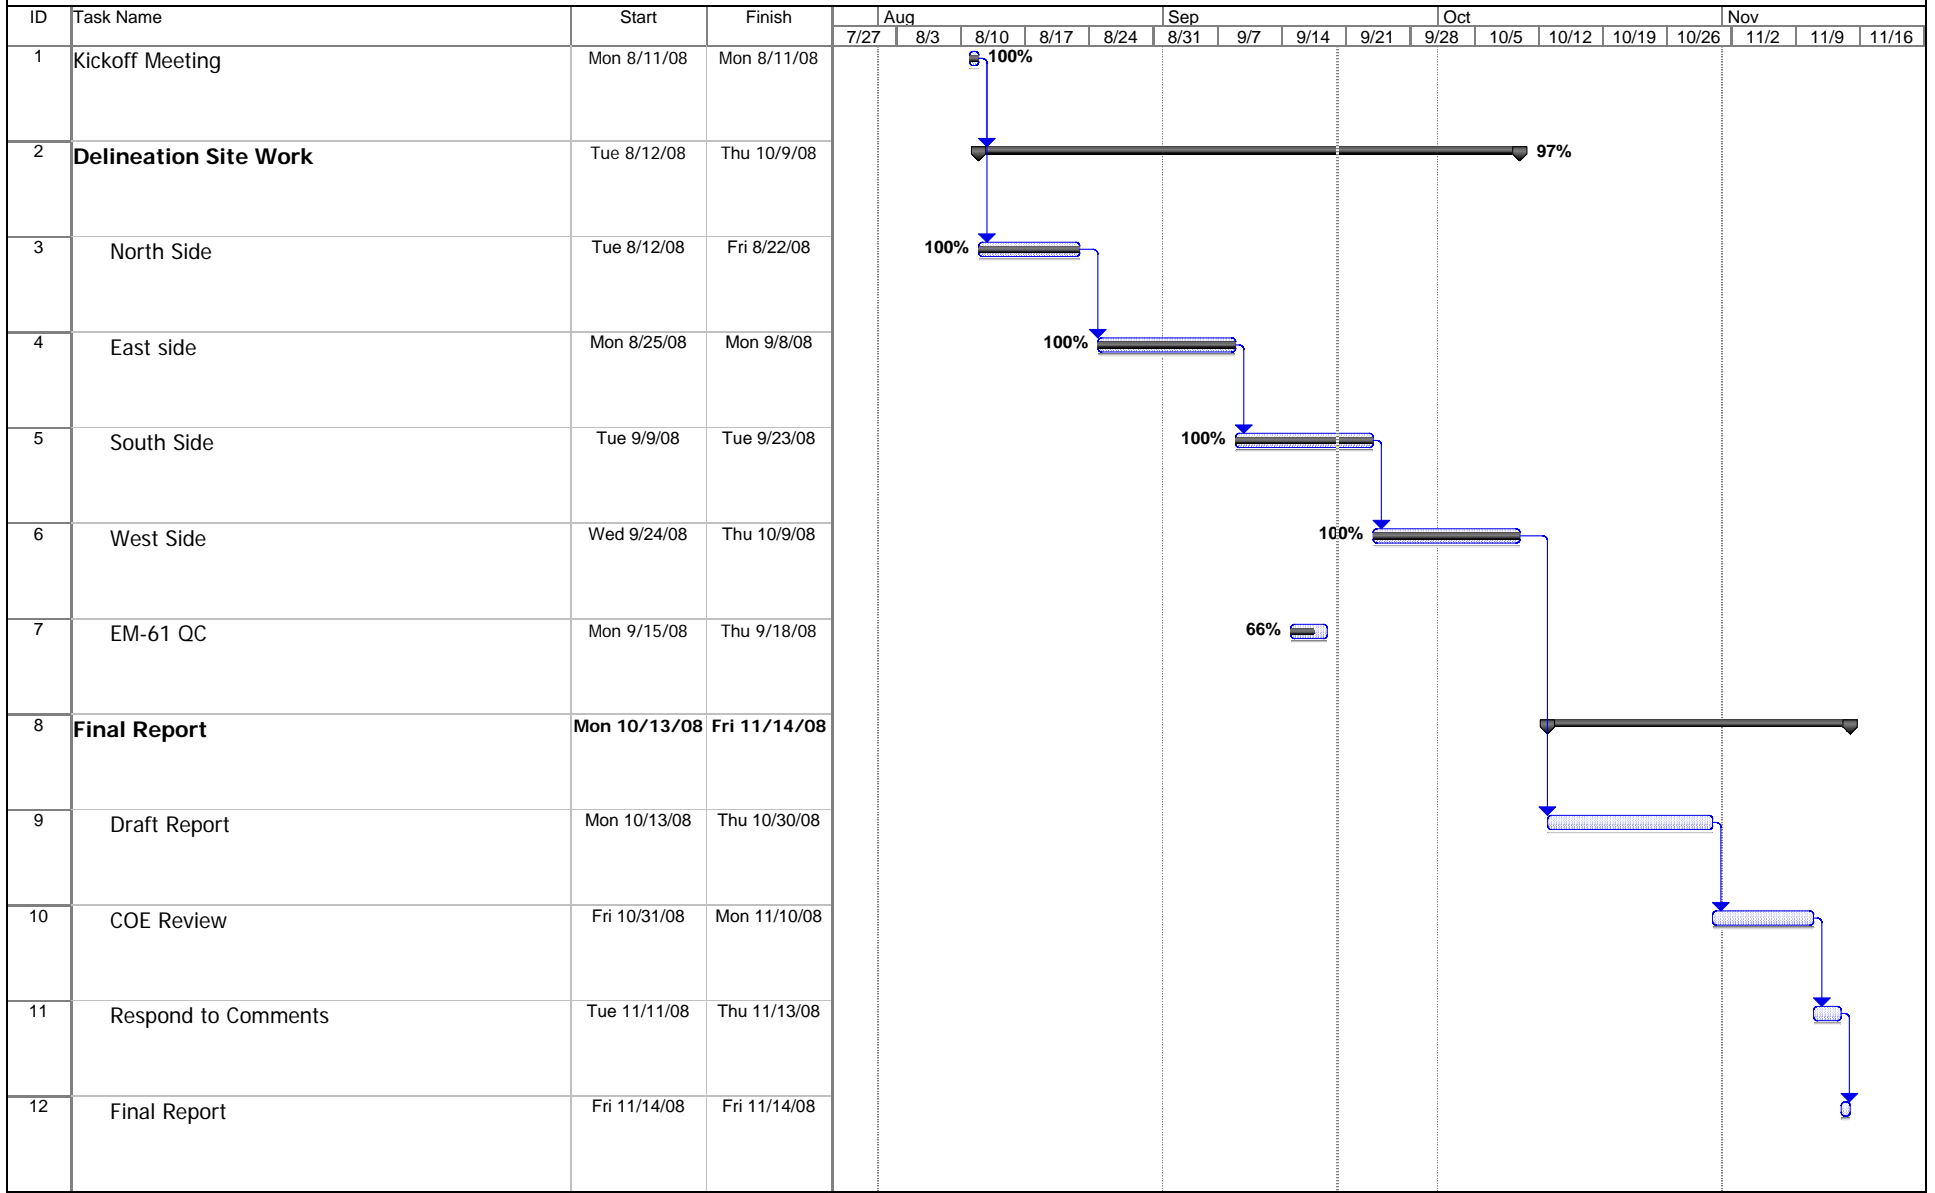

Prepared By: PIKA International, Inc.
Date: 09/20/08



Kick-Out Investigation

WEEKLY REPORT

Contract No:	W912BV-04-D-2016	Report No.	7
PIKA Project #:	08-12-137	Date:	09-21-08 to 09-27-08
Project:	Kick-out Investigation, Parcel 3 Boundary, Ft Wingate Army Activity Depot, McKinley County, New Mexico		
Summary of Activities:			
<ul style="list-style-type: none"> Completed EM-61 QC operations Shipped Demolition materials Shipped Instruments/gear to Stafford, TX Turned over MEC inventory to FWAD personnel Turned over MD/Non-MD scrap to FWAD personnel 			
Remarks: (include directions received from client's representative or regulators, visitors, compliance notices received, pertinent information)			

Work Completed:	This Week	Cumulative	% Complete
Number of Transects completed	0	726	100
Linear Feet of Transects completed	13,986	140,863	100
Linear Feet of Transect QC audits completed	9800	19,055	100
Number of Targets Dug	76	1466	N/A
MEC Items recovered	0	0	N/A
Munitions Debris (MD) recovered (lbs estimate)	0	503	N/A
Scrap Metal/Metals Waste (MW) recovered (lbs estimate)	1	206	N/A

Health and Safety

- Conducted health and safety meetings and task order meetings every morning, prior to commencement of daily activities.

Kick-Out Investigation

Were there any lost time accidents this week? No Yes .
If "yes", refer attached summary of incident or OSHA report.

Quality Control

Inspections Performed	Non-Conformances	Corrective Action (CA)	Follow-up on CA
Schonstedts	None		
Whites all metal detectors	None		
Vehicle Inspections	None		

Notes:

- USACE Safety representative Harmon Slappy on site this week
- Navajo and Zuni Archeologists were not utilized this week.

Schedule for Next Week.

- Complete Final Report for Arroyo Clearance, begin Final Report for Kickout Delineation.

Refer attached **Schedule** for percentage of work completed and projected completion dates.

SUXOS	Dewey Thedford	Safety/OC Officer	John Reott
UXO Team Lead	Mike Fiedler	Project Manager	Corey Woods

Kick-Out Investigation

PHOTO DOCUMENTATION



Breaking Out Base Station Components




Setting Up GPS Base Station for QC Operations

Kick-Out Investigation



Setting Up Base Station

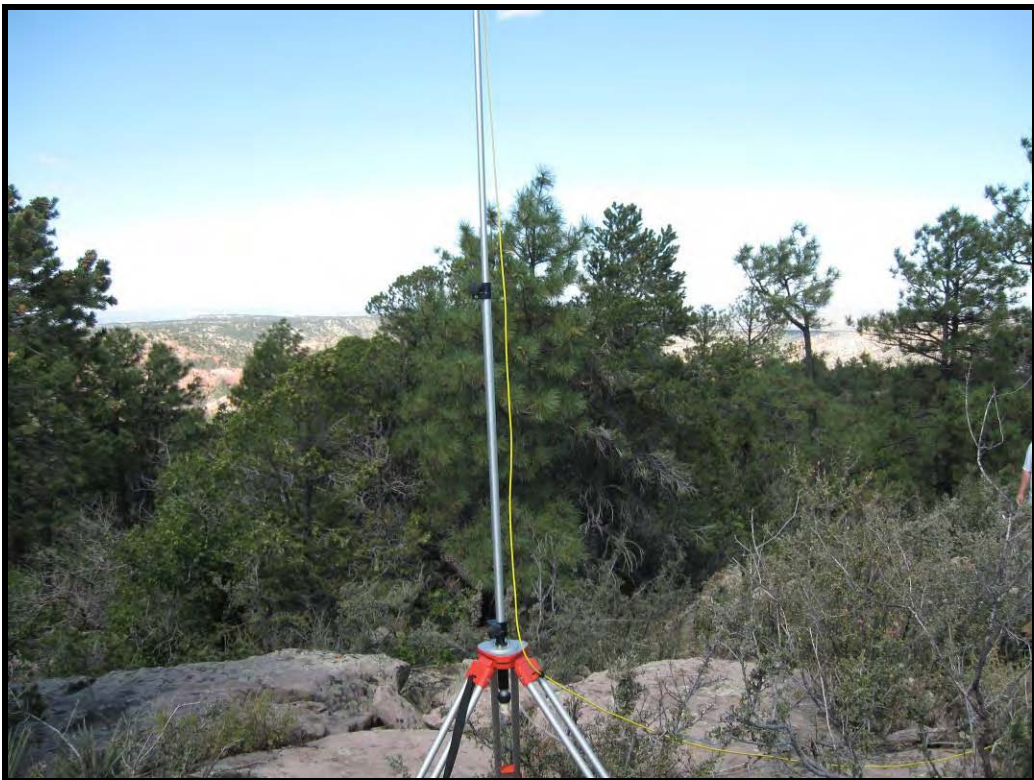


Base Station Set Up




Project Schedule for Kickout Delineation, Parcel 3,
Fort Wingate Army Activity Depot, McKinley County, New Mexico

Contract #W912BV-04-D-2016 / DY02

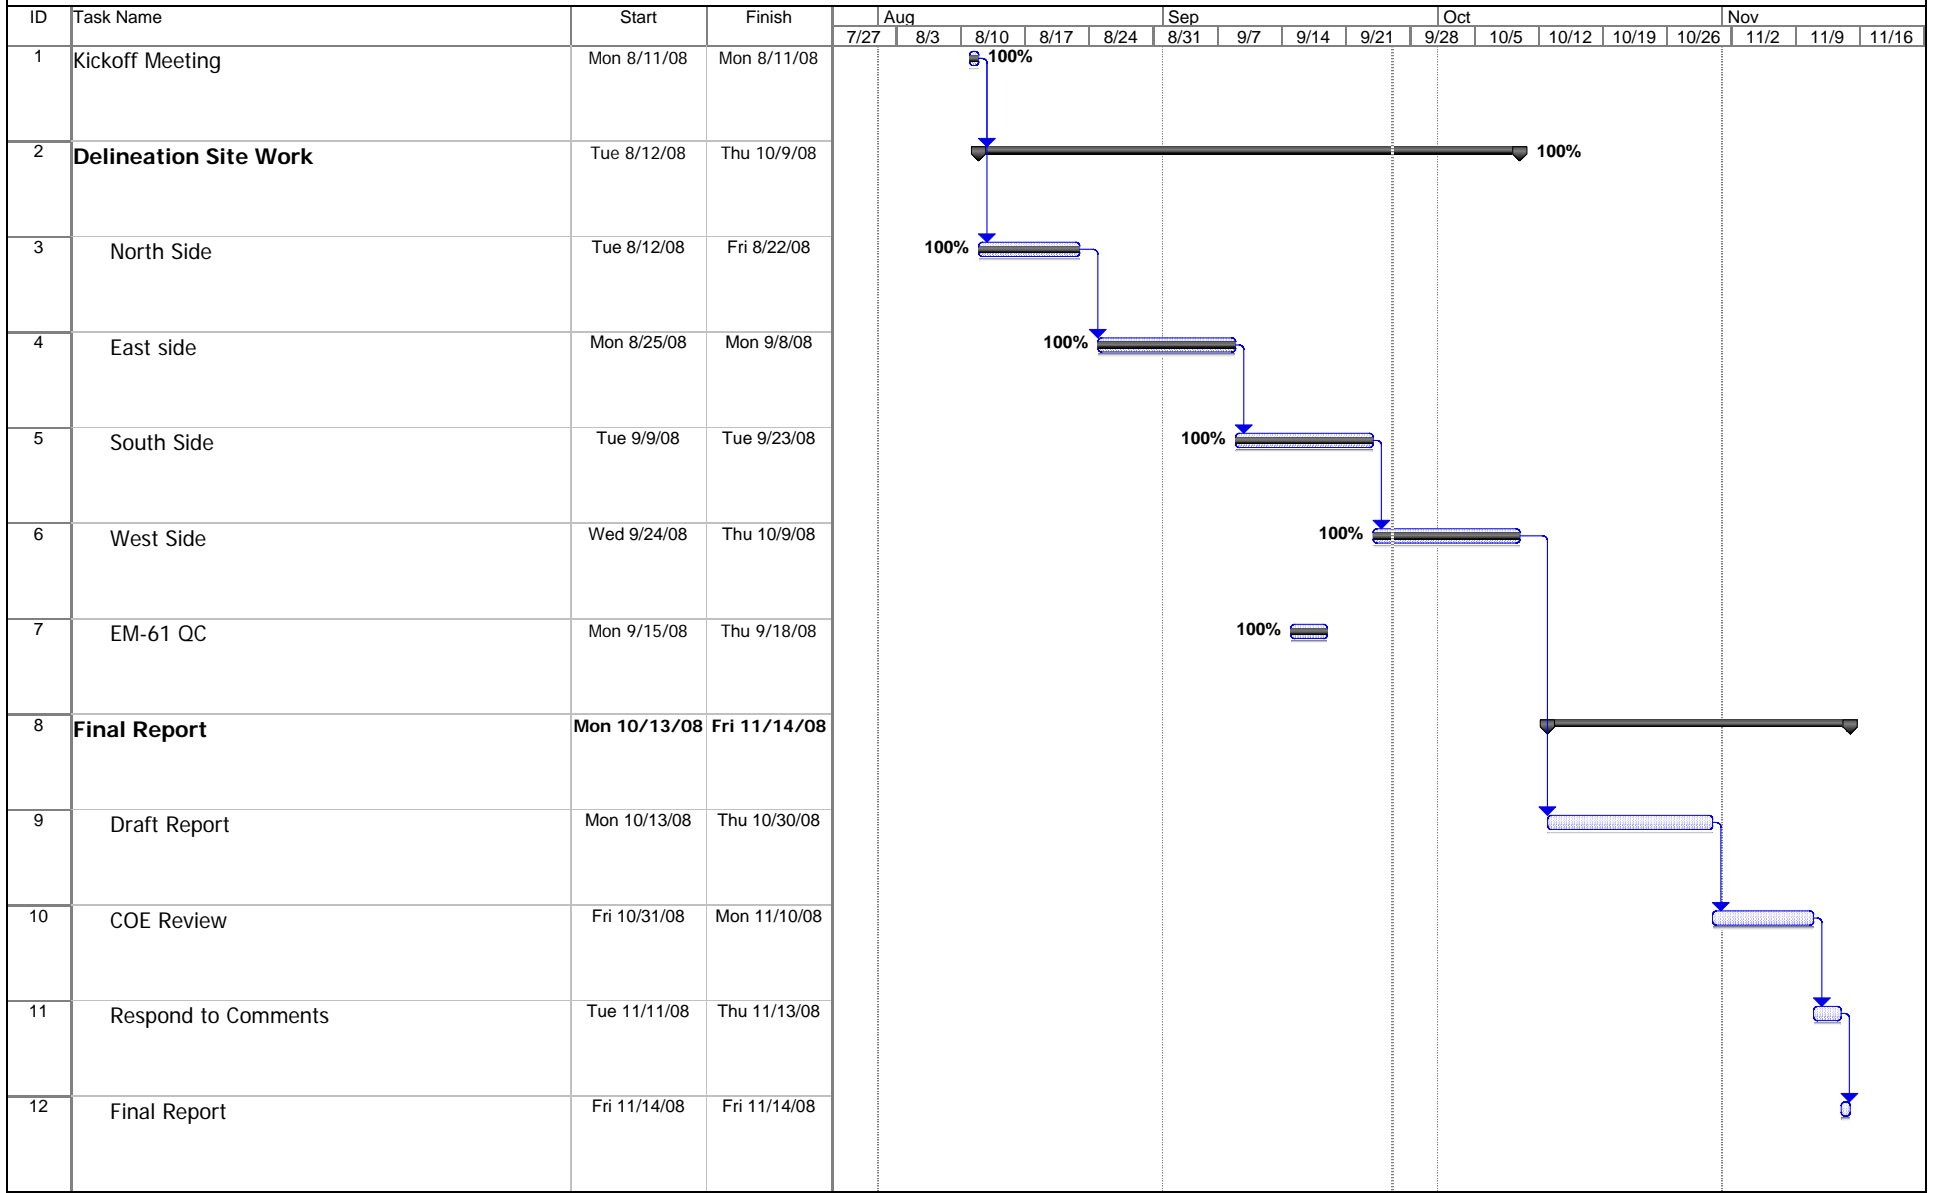

Prepared By: PIKA International, Inc.
Date: 09/26/08



Kick-Out Investigation

WEEKLY REPORT

Contract No:	W912BV-04-D-2016	Report No.	16
PIKA Project #:	08-12-137	Date:	03-29-09 to 04-04-09
Project:	Kick-out Investigation of <u>920</u> Transects		

Summary of Activities:

- Received, inspected and checked equipment and Vehicles
- Walked areas that were classified as Unsafe to transit from previous operations
- Started Transect investigations working inward to OB/OD area

Remarks: (include directions received from client's representative or regulators, visitors, compliance notices received, pertinent information)

We are to investigate and identify all anomalies in the areas that the Tribes allow us to enter.

Work Completed:	This Week	Cumulative	% Complete
Number of Transects completed	74	800	86
Linear Feet of Transects completed	14,394	155,257	61
Linear Feet of Transect QC audits completed	0	19,055	19,055
Number of Targets Dug	297	1687	N/A
MEC Items recovered	0	0	0
Munitions Debris (MD) recovered (lbs estimate)	62.3	565.3	565.3
Scrap Metal/Metals Waste (MW) recovered (lbs estimate)	0	205	N/A

Health and Safety

- Conducted health and safety meetings and task order meetings every morning, prior to commencement of daily activities.

Were there any lost time accidents this week? No Yes .

If "yes", refer attached summary of incident or OSHA report.

Kick-Out Investigation

Quality Control			
Inspections Performed	Non-Conformances	Corrective Action (CA)	Follow-up on CA
Schonstedts	None		
Whites all metal detectors	None		
Vehicle Inspections	None		
<p>Notes:</p> <ul style="list-style-type: none"> • Navajo and Zuni Archeologists escorts onboard all week. • ATV's will not be utilized for this evolution. 			
<p>Schedule for Next Week.</p> <ul style="list-style-type: none"> • Continue Transect Investigations <p>Refer attached Schedule for percentage of work completed and projected completion dates.</p>			
SUXOS	Dewey Thedford	Safety/QC Officer	John Kochefko
UXO Team Lead	Mike Fiedler	Project Manager	Corey Woods

Kick-Out Investigation

PHOTO DOCUMENTATION



Conducting Transect Investigations



Investigating Anomaly with Whites All Metal Detector

Kick-Out Investigation



Looking Down into Valley



Working up a Steep Incline

Kick-Out Investigation

WEEKLY REPORT

Contract No:	W912BV-04-D-2016	Report No.	17
PIKA Project #:	08-12-137	Date:	04-05-09 to 04-11-09
Project:	Kick-out Investigation of <u>920</u> Transects		

Summary of Activities:

- Received (2) replacement trucks for extended cab F-150's
- Continued Transect investigations on West and South transects

Remarks: (include directions received from client's representative or regulators, visitors, compliance notices received, pertinent information)

Submit a weekly report to COE/OESS to include any Transects that could not be investigated due to Safety or Cultural issues.

Work Completed:	This Week	Cumulative	% Complete
Number of Transects completed	89	889	95
Linear Feet of Transects completed	21,419	176,676	70
Linear Feet of Transect QC audits completed	0	19,055	19,055
Number of Targets Dug	94	1781	1763
MEC Items recovered	0	0	0
Munitions Debris (MD) recovered (lbs estimate)	60	625.3	565.3
Scrap Metal/Metals Waste (MW) recovered (lbs estimate)	0	205	N/A

Health and Safety

- Conducted health and safety meetings and task order meetings every morning, prior to commencement of daily activities.
- John Reott displayed symptoms of heat stress while conducting Transect investigations. Immediate first Aid measures were administered and symptoms subsided. Near Miss Report was submitted.

Kick-Out Investigation

Were there any lost time accidents this week? No Yes .
If "yes", refer attached summary of incident or OSHA report.

Quality Control

Inspections Performed	Non-Conformances	Corrective Action (CA)	Follow-up on CA
Schonstedts	None		
Whites all metal detectors	None		
Vehicle Inspections	None		

Notes:

- Navajo and Zuni Archeologists escorts onboard all week.

Schedule for Next Week.

- Continue Transect Investigations

Refer attached **Schedule** for percentage of work completed and projected completion dates.

SUXOS	Dewey Thedford	Safety/OC Officer	John Kochefko
UXO Team Lead	Mike Fiedler	Project Manager	Corey Woods

Kick-Out Investigation

PHOTO DOCUMENTATION



Navigating Transects



Investigating Anomaly

Kick-Out Investigation



Pinpointing Anomaly with Schonstedt and Whites



Fragmentation Found in Hole

Kick-Out Investigation

WEEKLY REPORT

Contract No:	W912BV-04-D-2016	Report No.	18
PIKA Project #:	08-12-137	Date:	04-12-09 to 04-18-09
Project:	Kick-out Investigation of <u>920</u> Transects		
Summary of Activities:			
<ul style="list-style-type: none"> Continued Transect investigations on East and South transects Eric Stoffel reported onboard Wednesday morning to set up and check EM-61 gear. Escorted to field to look at sites that we will conduct EM-61 operations for QA checks. 			
Remarks: (include directions received from client's representative or regulators, visitors, compliance notices received, pertinent information)			

Work Completed:	This Week	Cumulative	% Complete
Number of Transects completed	92	981	100
Linear Feet of Transects completed	24,855	201,531	80
Linear Feet of Transect QC audits completed	0	19,055	19,055
Number of Targets Dug	36	1817	N/A
MEC Items recovered	0	0	0
Munitions Debris (MD) recovered (lbs estimate)	13	638.3	N/A
Scrap Metal/Metals Waste (MW) recovered (lbs estimate)	0	205	N/A

Health and Safety

- Conducted health and safety meetings and task order meetings every morning, prior to commencement of daily activities.
- John Reott has been directed by Aerotek to have a physical evaluation conducted on 4/15/09. He passed the physical and was assigned to EM-61 crew on 4/16/09.

Were there any lost time accidents this week? No Yes .

If "yes", refer attached summary of incident or OSHA report.

Kick-Out Investigation

Quality Control

Inspections Performed	Non-Conformances	Corrective Action (CA)	Follow-up on CA
Schonstedts	None		
Whites all metal detectors	None		
Vehicle Inspections	None		

Notes:

- Navajo and Zuni Archeologists escorts onboard all week.

Schedule for Next Week.

- Continue Transect Investigations

Refer attached **Schedule** for percentage of work completed and projected completion dates.

SUXOS	Dewey Thedford	Safety/QC Officer	John Kochefko
UXO Team Lead	Mike Fiedler	Project Manager	Corey Woods

Kick-Out Investigation

PHOTO DOCUMENTATION



Navigating Transects



Investigating Anomaly

Kick-Out Investigation



Digging Anomaly



Empty Slap Flare Found in Hole

Kick-Out Investigation

WEEKLY REPORT

Contract No:	W912BV-04-D-2016	Report No.	19
PIKA Project #:	08-12-137	Date:	04-19-09 to 04-25-09
Project:	Kick-out Investigation of <u>920</u> Transects		

Summary of Activities:

- Completed Transect investigations
- Completed EM-61 QA/QC operations

Remarks: (include directions received from client's representative or regulators, visitors, compliance notices received, pertinent information)

Doc Holliday/COE OESS will send us a letter for the Transects we could not transit due to Safety concerns.

Work Completed:	This Week	Cumulative	% Complete
Number of Transects completed	17	998	100
Linear Feet of Transects completed	4189	205720	100
Linear Feet of Transect QC audits completed	6818	25873	
Number of Targets Dug	14	1831	N/A
MEC Items recovered	0	0	0
Munitions Debris (MD) recovered (lbs estimate)	38.95	677.25	N/A
Scrap Metal/Metals Waste (MW) recovered (lbs estimate)	0	205	N/A

Health and Safety

- Conducted health and safety meetings and task order meetings every morning, prior to commencement of daily activities.

Were there any lost time accidents this week? No Yes .

If "yes", refer attached summary of incident or OSHA report.

Kick-Out Investigation


Quality Control			
Inspections Performed	Non-Conformances	Corrective Action (CA)	Follow-up on CA
Schonstedts	None		
Whites all metal detectors	None		
Vehicle Inspections	None		
<p>Notes:</p> <ul style="list-style-type: none"> Navajo and Zuni Archeologists escorts released at COB on Tuesday, 4/21/09. 			
<p>Schedule for Next Week.</p> <ul style="list-style-type: none"> Demobilization <p>Refer attached Schedule for percentage of work completed and projected completion dates.</p>			
SUXOS	Dewey Thedford	Safety/QC Officer	John Kochefko
UXO Team Lead	Mike Fiedler	Project Manager	Corey Woods

Kick-Out Investigation

PHOTO DOCUMENTATION



Setting Up EM-61

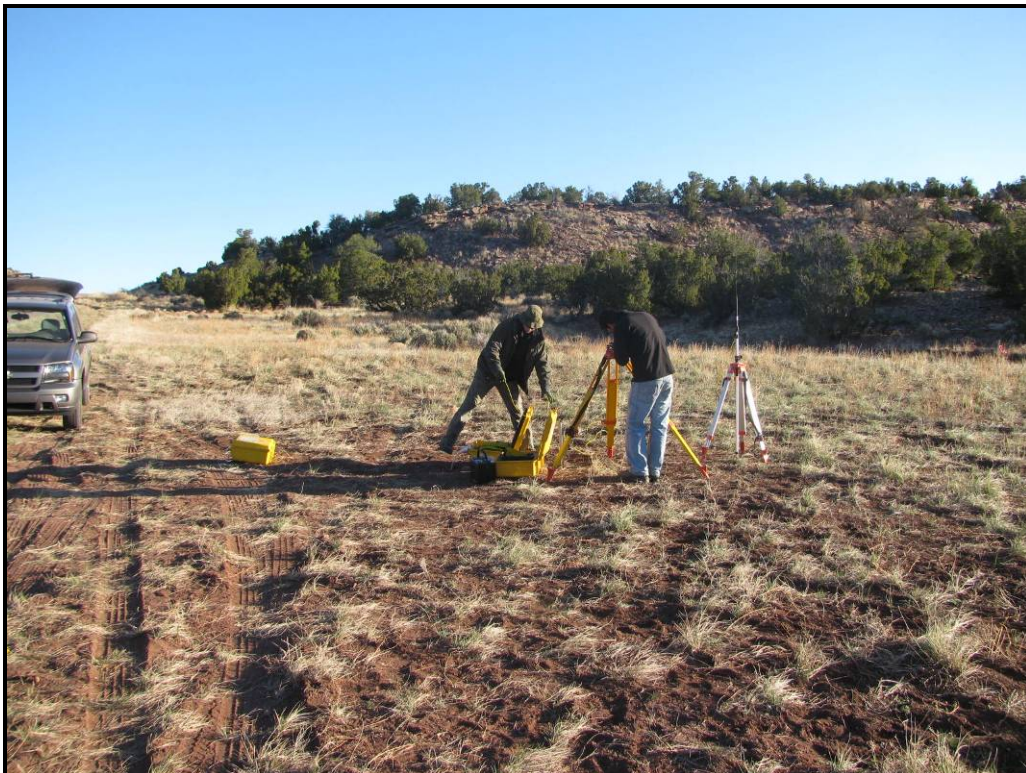

Setting Up Tripod/Base Station for EM-61 Operations

Kick-Out Investigation



Collecting Data



Checking Field Data Collection Settings
